City Council Meeting
City of Greenacres, Florida
Monday, August 17, 2026 at 6:00 PM
City Hall Council Chambers | 5800 Melaleuca Lane

Agenda

Mayor and City Council
Chuck Shaw, Mayor
John Tharp, Deputy Mayor
Peter Noble, Councilmember District II
Judith Dugo, Councilmember, District III
Susy Diaz, Councilmember, District IV
Elisa Leheny, Councilmember, District V
Administration
Andrea McCue, City Manager
Christy Goddeau, City Attorney
Glen J. Torcivia, City Attorney
Quintella Moorer, City Clerk

Call to Order and Roll Call

Pledge of Allegiance

Agenda Approval

Comments From the Public for Agenda Items Only

Special Business

1. **Proclamation:** Hunger Action Month, September 2026. - Tony Hopper, Feeding South Florida.

Consent Agenda

2. **Official City Council Meeting Minutes:** City Council Meeting Minutes, August 3, 2026. - Quintella L. Moorer, City Clerk.

3. **Resolution 2026-39:** Approving an increase to Purchase Order No. 26-161 with C.A.P. Government Inc. for building inspection services in the amount of $90,000, for a revised total Purchase Order amount not to exceed $280,000, utilizing the City of Delray Beach ITB No. 2024-041.- Monica Powery, Director of Purchasing.

Regular Agenda

4. **PUBLIC HEARING: Ordinance 2026-07: Second Reading:** Amending the City of Greenacres Budget for the fiscal year beginning October 1, 2025, and ending September 30, 2026, inclusive; providing for repeal of conflicting ordinances; providing for severability; and providing for an effective date. - Teri Beiriger, Director of Finance.

5. **Resolution No. 2026-40:** Approving the design-build amendment between the City of Greenacres and Kaufman Lynn Construction, Inc. for the Municipal Operations Center; establishing a guaranteed maximum price of $33,681,849.00; authorizing the appropriate city officials to execute the amendment. - Monica Powery, Director of Purchasing

Discussion Items

6. Rambo Park Parking. - Andrea McCue, City Manager.

Comments From the Public on Non-Agenda Items

City Manager's Report

7. Community Recreation Services.
8. Development and Neighborhood Services.
9. Economic Development.
10. Fire Rescue.
11. Finance.
12. Information Technology.
13. Palm Beach Sheriff's Office, District 16.
14. Public Works.
15. Purchasing.
16. Youth Programs.

City Attorney's Report

Mayor and City Council Report

Adjournment

Future City Council Meetings

September 8, 2026. (Budget Hearing)

September 21, 2026. (Budget Hearing)

Meeting Records Request

Any person requesting the appeal of a decision of the City Council will require a verbatim record of the proceedings and for that purpose will need to ensure that such verbatim record is made. Pursuant to FS. 286.0105, the record must include the testimony and evidence upon which the appeal is to be based. The City of Greenacres does not prepare or provide such verbatim record.

Notice of Council Meetings and Agendas

The first and third Monday of each month are regular meeting dates for the City Council; special or workshop meetings may be called, whenever necessary. Council Agendas are posted on the City's website on the Friday prior to each Council meeting. A copy of the meeting audio and the complete agenda may be requested by sending an email or calling at 561-642-2006.

Americans with Disabilities Act

In accordance with the provisions of the Americans with Disabilities Act (ADA), this document can be made available in an alternate format upon request. Special accommodations can be provided upon request with 3 days advance notice of any meeting, by contacting City Clerk Quintella Moorer at Greenacres City Hall, 5800 Melaleuca Lane, Greenacres, Florida. Phone No. 561-642-2006. Hearing Assistance: If any person wishes to use a Listen Aid Hearing Device, please contact the City Clerk prior to any meeting held in the Council Chambers.

Item Summary

Meeting Date: August 17, 2026

From:

Subject: **Proclamation:** Hunger Action Month, September 2026. - Tony Hopper, Feeding South Florida.

Background

Analysis

Financial Information

Legal

Staff Recommendation

Attachments:

None

City Council Meeting
City of Greenacres, Florida
Monday, August 3, 2026, at 6:00 PM
City Hall Council Chambers | 5800 Melaleuca Lane

Minutes

Mayor and City Council
Chuck Shaw, Mayor
John Tharp, Deputy Mayor
Peter Noble, Councilmember District II
Judith Dugo, Councilmember, District III
Susy Diaz, Councilmember, District IV
Elisa Leheny, Councilmember, District V
Administration
Andrea McCue, City Manager
Christy Goddeau, City Attorney
Glen J. Torcivia, City Attorney
Quintella Moorer, City Clerk

Call to Order and Roll Call

Mayor Shaw called the meeting to order at 6:00 PM. City Clerk Moorer called the roll. Councilmember Peter Noble and Councilmember Judy Dugo were absent. All other Councilmembers were present.

Mayor Shaw asked for a Moment of Silence for the late Officer Elizbeth "Liz" Ortega, previous City of Greenacres, Palm Beach County Sheriff's Office.

Pledge of Allegiance

Agenda Approval

Motion made by Councilmember Diaz, Seconded by Councilmember Leheny to Approve the agenda.
Voting Yea: Deputy Mayor Tharp, Councilmember Diaz, Councilmember Leheny.

Comments From the Public for Agenda Items Only

None.

Special Business

Mayor Shaw congratulated Councilmember Diaz on her amazing performance in the Play, "In the Heights".

1. **Presentation:** Legislative Update. - The Honorable House of Representative Debra Tendrich, District 89.
   Rep. Tendrich provided a brief history of her background. She highlighted the five Bills she was able to pass during the session, which included issues such as domestic violence, pension plans and a property tax plan. Rep. Tendrich highlighted the City's great responsibility towards the City's handling of the budget. Rep Tendrich encouraged residents to review the property tax and to educate themselves.

   Rep. Tendrich mentioned a few concerns she had related to the property tax bill and the legislative process.

   Rep. Tendrich thanked the Council and mentioned she loved the City.

2. **Proclamation:** India Independence Day, August 15, 2026. - Neil Zutshi
   Councilmember Leheny read the proclamation into the record.

   Mr. Zutshi thanked the Council and Mr. Austin Lee, Communications and Legislative Affairs Director, for their recognition.

   Photos were taken.

Consent Agenda

3. **Official City Council Meeting Minutes:** City Council Meeting and Special Budget Meeting Minutes, July 20, 2026. - Quintella L. Moorer, City Clerk.

4. **Resolution 2026-38:** Approving and authorizing the execution of the First Amendment to the Interlocal Agreement for Information Technology Services between the City of Greenacres and Palm Beach County (R2026-0699) for additional telephone lines; and providing for an effective date. - Georges Bayard, Director of Information Technology Services.

   Motion made by Deputy Mayor Tharp, Seconded by Councilmember Diaz to Approve the Consent Agenda.

   Voting Yea: Deputy Mayor Tharp, Councilmember Diaz, Councilmember Leheny.

Regular Agenda

5. **PUBLIC HEARING: Ordinance 2026-01: Second Reading:** Annexing two parcels of land totaling approximately 8.91 acres, located approximately 0.5 miles south of Melaleuca Lane, at 5163 and 5217 South Military Trail, as requested by Jeanne Ducharme of Cotleur & Hearing, agent for the owners Mizner Dell Lake Worth LLC, and Palm Beach Baptist Church Inc., in accordance with Chapter 171.0413 of the Florida Statutes; providing for redefining the boundary lines of the City of Greenacres to include the subject property in the City's official boundary map; providing for repeal of conflicting ordinances; providing for severability; and providing for an effective date. - Gionni Gallier, Assistant Director of Development and Neighborhood Services.

   Ms. Moorer read the ordinance by title.

   Mr. Gallier stated no changes had been made since the First Reading on July 20, 2026.

   Staff recommended approval.

   Motion made by Councilmember Diaz, Seconded by Deputy Mayor Tharp to Approve Ordinance 2026-01 on Second Reading.
   Voting Yea: Deputy Mayor Tharp, Councilmember Diaz, Councilmember Leheny.

6. **PUBLIC HEARING: Ordinance 2026-03: Second Reading:** Amending the Future Land Use Map of the Future Land Use Element of the City's Comprehensive Plan, to change the Future Land Use designation of two parcels of land totaling approximately 8.91 acres, located at 5163 and 5217 South Military Trail from a Palm Beach County MR-5, Medium Residential, 5 units per acre to City of Greenacres Residential High Density (RS-HD), as requested by Jeanne Ducharme of Cotleur & Hearing, agent for the owners Mizner Dell Lake Worth LLC, and Palm Beach Baptist Church Inc.; providing for repeal of conflicting ordinances; providing for severability; providing for transmittal to the Florida Department of Commerce (FDOC); providing for inclusion in the Comprehensive Plan; and providing for an effective date. - Gionni Gallier, Assistant Director of Development and Neighborhood Services.
   Ms. Moorer read the ordinance by title.

   Mr. Gallier stated no changes had been made since the First Reading on July 20, 2026.

   Staff recommended approval.

   Motion made by Councilmember Leheny, Seconded by Deputy Mayor Tharp to Approve Ordinance 2026-03 on Second Reading.
   Voting Yea: Deputy Mayor Tharp, Councilmember Diaz, Councilmember Leheny.

7. **PUBLIC HEARING: Ordinance 2026-04: Second Reading**: Rezoning for two parcels of land totaling approximately 8.91 acres, located at 5163 and 5217 South Military Trail, from a Palm Beach County Agricultural Residential (AR) zoning designation to a City of Greenacres Residential High (RH) zoning designation, as requested by Jeanne Ducharme of Cotleur & Hearing, agent for the owners Mizner Dell Lake Worth LLC, and Palm Beach Baptist Church Inc.; providing for changes to the official zoning map; providing for repeal of conflicting ordinances; providing for severability; and providing for an effective date. - Gionni Gallier, Assistant Director of Development and Neighborhood Services.
Ms. Moorer read the ordinance by title.

   Mr. Gallier stated no changes had been made since the First Reading on July 20, 2026.

   Staff recommended approval.

   Ms. Ducharme thanked the Council and especially the DNS Staff for the great partnership and assistance during the process.

   Motion made by Deputy Mayor Tharp, Seconded by Councilmember Diaz to Approve Ordinance 2026-04 on Second Reading.
   Voting Yea: Deputy Mayor Tharp, Councilmember Diaz, Councilmember Leheny.

8. **Ordinance 2026-07: First Reading:** Amending the City of Greenacres Budget for the fiscal year beginning October 1, 2025, and ending September 30, 2026, inclusive; providing for repeal of conflicting ordinances; providing for severability; and providing for an effective date. - Teri Beiriger, Director of Finance.
Mr. Todd Taylor, Budget Manager, requested two budget amendments for the purchase of land on 10th Avenue and the Youth Programs playground. The total was $2.280 million.

   Staff recommended approval.

   Motion made by Councilmember Leheny, Seconded by Deputy Mayor Tharp to Approve Ordinance 2026-07 on First Reading.
   Voting Yea: Deputy Mayor Tharp, Councilmember Diaz, Councilmember Leheny.

Discussion Items - None.

Comments From the Public on Non-Agenda Items

Ms. Kathy Higgins was running for Florida House District 89, which covers Greenacres. She wanted to introduce herself and share her passion for education and service to the Council and residents.

Representative Tendrich introduced herself and mentioned she would be running for District 89 again. She shared her passion for the community, and the work she had completed during her tenure.

Mr. Benjamin Wade questioned the illegal parking on 57th Avenue and hoped a solution could be found.

City Manager's Report

Ms. McCue reminded the Council about the upcoming Principals Luncheon.

City Attorney's Report

No report.

Mayor and City Council Report

Deputy Mayor Tharp congratulated Councilmember Diaz on her performance in the play. He questioned the school zone camera start date. Ms. McCue mentioned there would be a warning before the additional school zone camera begins.

Councilmember Diaz congratulated CRS on the school supply drive. She was thankful for their support. She also questioned the school zone camera program. She advised everyone to be safe.

Councilmember Leheny wished everyone a great new school year.

Mayor Shaw advised all to review the impact of the property tax issue and welcomed anyone to review our budget to see how well we used funds.

Adjournment

6:48PM.

_____

Chuck Shaw
Mayor

_____

Quintella Moorer, MMC
City Clerk

Date Approved: _____

Item Summary

Meeting Date: August 17, 2026

From: Monica Powery, Director

Subject: **Resolution 2026-39:** Approving an increase to Purchase Order No. 26-161 with C.A.P. Government Inc. for building inspection services in the amount of $90,000, for a revised total Purchase Order amount not to exceed $280,000, utilizing the City of Delray Beach ITB No. 2024-041.- Monica Powery, Director of Purchasing.

Background

The City currently utilizes C.A.P. Government, Inc. for building inspection services on an as-needed basis. The original purchase order was issued for Fiscal Year 2026 for building inspection, plan review, and other related services for the Development and Neighborhood Services Department, utilizing the terms and conditions of the City of Delray Beach ITB No. 2024-041, which is effective from August 19, 2024 through August 18, 2027.

On June 1, 2026 the City council approved an increase to Purchase Order No. 26-161, bringing the total authorized amount to $190,000. Since the approval, the City has continued to rely on C.A.P. Government, Inc. to provide building inspection services due to the vacancy of the Building Official position and the continued operational needs of the Development and Neighborhood Services Department.

Due to the continued need for building inspection services, staff is requesting authorization to increase Purchase Order 26-161 by $90,000, for a revised total not-to-exceed amount of $280,000, to cover outstanding invoices and continue providing building inspection services through the remainder of the fiscal year.

Analysis

C.A.P. Government, Inc. continues to provide professional building inspection, plan review, and related development services on an as-needed basis. These services have been essential in maintaining timely permit review, inspection scheduling, and customer service levels during the vacancy of the City's Building Official position.
The requested increase is necessary to pay outstanding invoices for services already rendered and to ensure adequate funding remains available until permanent staffing is restored or additional services are no longer required. Approval of this increase will allow the City to utilize the existing piggyback contract without interruption and ensure

sufficient funding remains available for building inspection services through the fiscal year.

Financial Information

Purchase Order No. 26-161 is currently $190,000. Staff is requesting approval to increase the purchase order by $90,000, for a revised total not to exceed amount of $280,000. Funding is available and will be charged to account 001-30-34-34-4, Other Contractual Services.

Legal

The purchase is being made in accordance with the City's Procurement Code and utilizes the terms and conditions of the City of Delray Beach ITB No. 2024-041. Council approval is requested in accordance with the revised Procurement Code requirements for piggyback purchases.

Staff Recommendation

Approval of Resolution No. 2026-39 authorizing an increase to Purchase Order No. 26-161 with C.A.P. Government, Inc. for building inspection services in the amount of $90,000, increasing the total purchase order amount from $190,000 to an amount not to exceed $280,000, utilizing the City of Delray Beach ITB No. 2024-041.

Attachments:

1. Resolution 2026-39
2. PO 26-161
3. City of Delray Beach- ITB 2024-041

RESOLUTION NO. 2026-39

A RESOLUTION OF THE CITY COUNCIL OF THE CITY OF GREENACRES, FLORIDA, APPROVING AN INCREASE TO PURCHASE ORDER NO. 26-161 WITH C.A.P. GOVERNMENT, INC. FOR BUILDING INSPECTION SERVICES IN THE AMOUNT OF $90,000, FOR A REVISED TOTAL PURCHASE ORDER AMOUNT NOT TO EXCEED $280,000, UTILIZING THE CITY OF DELRAY BEACH ITB NO. 2024-041; AND PROVIDING FOR AN EFFECTIVE DATE.

WHEREAS, the City of Greenacres (the "City") utilizes C.A.P. Government, Inc. to provide building inspection, plan review, and related services on an as-needed basis for the Development of Neighborhood Services Department; and

WHEREAS, Purchase Order No. 26-161 was issued utilizing the terms and conditions of the City of Delray Beach Invitation to Bid (ITB) No. 2024-041, effective August 19, 2024, through August 18, 2027; and

WHEREAS, City Council has previously approved increases to Purchase Order No. 26-161 to address the continued operational need for building inspection services; and

WHEREAS, the City continues to rely on C.A.P. Government, Inc. to provide these services due to the vacancy of the Building Official position and the ongoing need to maintain building inspection operations; and

WHEREAS, additional funding is necessary to pay outstanding invoices for services rendered and to ensure the continued availability of building inspection services through the remainder of the fiscal year; and

WHEREAS, City staff recommend that the City Council approve an increase to Purchase Order No. 26-161 with C.A.P. Government, Inc. by $90,000, for a revised total amount not to exceed $280,000, as being in the best interest of the City.

NOW, THEREFORE, BE IT RESOLVED BY THE CITY COUNCIL OF THE CITY OF GREENACRES, FLORIDA, THAT:

SECTION 1. The City Council hereby approves an increase to Purchase Order No. 26-161 with C.A.P. Government, Inc. for building inspection services in the amount of $90,000, for a revised total purchase order amount not to exceed $280,000, utilizing the terms and conditions of the City of Delray Beach ITB No. 2024-041.

SECTION 2. The City Council authorizes the appropriate City officials to execute the purchase orders and related documents necessary for these services.

SECTION 3. This Resolution shall become effective immediately upon adoption.

RESOLVED AND ADOPTED this 17 of day of August 2026

Chuck Shaw, Mayor

Voted:

John Tharp, *Deputy Mayor*

Attest:

Quintella Moorer, City Clerk

Voted:

Peter Noble, Council Member, *District II*

Voted:

Judith Dugo, *Council Member, District III*

Voted:

Susy Diaz, Council Member, *District IV*

Voted:

Elisa Leheny, *Council Member, District V*

Approved as to Form and Legal Sufficiency:

Glen J. Torcivia, City Attorney

Ship To City of Greenacres
Building Department
5800 Melaleuca Lane
Greenacres, FL 33463

Bill To 5800 Melaleuca Lane
GREENACRES, FL 33463

Purchase Order
No. 2026-00000161

DATE 06/09/2026

CITY OF GREENACRES

PURCHASE ORDER NUMBER MUST APPEAR ON ALL INVOICES, SHIPPERS, BILLS OF LADING AND CORRESPONDENCE

VENDOR 20379 - C.A.P. Government, Inc.

Changed Purchase Order

Contact
C.A.P. Government, Inc. (ACH)
343 Almeria Avenue
CORAL GABLES, FL 33134

DELIVER BY 09/30/2026
SHIP VIA
FREIGHT TERMS FOB
PAGE 1 of 1
ORIGINATOR: Sasha Burrell
TERMS: NET 30 DAYS

REFERENCE #

QUANTITY	UNIT	DESCRIPTION	STATUS	UNIT COST	TOTAL COST
190,000.0000	DL	BUILDING INSPECTION SERVICES - On call as needed Building inspection, plan review & Dev. srvs On call as needed services for FY 2026 . The Consultant shall provide inspection, plan review, and development services. All terms and conditions per City of Delray Beach contract with C.A.P. Government, Inc. dated August 19, 2024. Rates are provided for in the Professional Services Agreement . Rates do not include travel time. This Purchase Order is an estimate of payments to be made. Itemized invoices for services rendered must be submitted for payment. 3/17/2026 additional funds of 50,000 were added to cover invoices for plan review, inspections and other applicable building services for FY26. 6/5/2026 additional funds of $90,000 was added to cover invoices for plan review, inspections and other applicable building services for FY26. 001-30-34-34-4 - Other Contractual Services 190,000.00	Item Changed	1.0000	$190,000.00
				TOTAL DUE	$190,000.00

Direct inquiries to Buyer at (561) 649-5403 or purchasing@greenacresfl.gov

The terms and conditions on the City's website - (https://greenacresfl.gov/purchasing/page/terms-conditions) are hereby incorporated as an integral part of this order.

Special Instructions

All terms and conditions per the City of Delray Beach ITB No.2024-041. Effective dates 8/19/2024 through 8/18/2027.

Submit all invoices to:
Accounts Payable
5800 Melaleuca Lane
Greenacres, FL 33463
ap@greenacresfl.gov

TAX EXEMPTION NUMBER
85-8012683670C-0

AUTHORIZED BY CITY OF GREENACRES

BY: _____
Authorized Purchasing Official

AGREEMENT

THIS AGREEMENT is hereby made and entered into this 14th day of August, 2024, (the "effective date") by and between the City of Delray Beach, a Florida municipal corporation ("City"), whose address is 100 N.W. 1st Avenue, Delray Beach, Florida 33444, and CAP Government, Inc., a Florida Corporation (hereafter referred to as ("Consultant"), whose address is 343 Almeria Avenue, Coral Gables, Fl 33134.

WHEREAS, the City desires to retain the Consultant to provide inspection, plan review, and development services in accordance with the City's Invitation to Bid No. 2024-041, and the Consultant's response thereto, all of which are incorporated herein by reference.

NOW, THEREFORE, in consideration of the mutual covenants and promises hereafter set forth, the Consultant and the City agree as follows:

ARTICLE 1. INCORPORATION OF INVITATION TO BID

The terms and conditions of this Agreement shall include and incorporate the terms, conditions, and specifications set forth in the City's Invitation to Bid No. 2024-041, and the Consultant's response to the Invitation to Bid, including all documentation required thereunder.

ARTICLE 2. DESCRIPTION OF GOODS OR SCOPE OF SERVICES

The Consultant shall provide inspection, plan review, and development services as identified in the specifications accompanying the City's Invitation to Bid, which are incorporated herein by reference.

ARTICLE 3. COMPENSATION

The City shall pay the Consultant, in compliance with the Pricing Schedule attached hereto and incorporated herein, according to the terms and specifications of the referenced Invitation to Bid.

ARTICLE 4. MISCELLANEOUS PROVISIONS

a. Notice Format. All notices or other written communications required, contemplated, or permitted under this Agreement shall be in writing and shall be hand delivered, telecommunicated, or mailed by registered or certified mail (postage prepaid), return receipt requested, to the following addresses:

i. As to the City: City of Delray Beach
100 N.W. 1st Avenue
Delray Beach, Florida 33444
Attn: City Manager

ii. with a copy to: City of Delray Beach
100 N.W. 1st Avenue
Delray Beach, Florida 33444
Attn: City Attorney

iii. As to the Consultant: C.A.P. Government, Inc.
343 Almeria Avenue
Coral Gables, Fl 33134
Attn.: Carlos A. Penin, PE- President
Email: capenin@capfla.com
Phone: 305-448-1712

b. Headings. The headings contained in this Agreement are for convenience of reference only and shall not limit or otherwise affect in any way the meaning or interpretation of this Agreement.

c. Effective Date. The effective date of this Agreement shall be as of the date it has been executed by both the parties hereto.

ARTICLE 5. E-VERIFY

By entering into this Agreement, Consultant acknowledges its obligation to comply with the provisions of Section 448.095, Fla. Stat., "Employment Eligibility." Consultant affirms and represents it is registered with the E-Verify system, utilizing same, and will continue to utilize same as required by law. Compliance with this section includes, but is not limited to, utilization of the E-Verify System to verify the work authorization status of all newly hired employees and requiring all subcontractors to provide an affidavit attesting that the subcontractor does not employ, contract with, or subcontract with, an unauthorized alien. Failure to comply with this section will result in the termination of this Agreement, or if your subcontractor knowingly violates the statute, the subcontract must be terminated immediately. Any challenge to termination under this provision must be filed in the Circuit Court no later than 20 calendar days after the date of termination. If terminated for a violation of the statute by Consultant, the Consultant may be prohibited from conducting future business with the City or awarded a solicitation or contract for a period of 1 year after the date of termination. All costs incurred to initiate and sustain the aforementioned programs shall be the responsibility of the Consultant.

ARTICLE 6. CONTRACT TERM

The term of this Agreement shall remain in effect for a term of three (3) years and may be renewed for (2) two additional (1) one-year period(s), unless terminated earlier in accordance with the terms set forth in the ITB.

ARTICLE 7. PRECEDENCE

The documents listed below are a part of this Agreement and are hereby incorporated by reference. In the event of inconsistency between the documents, unless otherwise provided herein, the terms of the following documents will govern in the following order of precedence:

a. Terms and conditions as contained in this Agreement.

b. Terms and Conditions of the City's Invitation to Bid No. 2024-041, and the Consultant's response to the Invitation to Bid.

c. Consultant's response to the City's Invitation to Bid No. 2024-041, and any subsequent information submitted by Consultant during the evaluation and negotiation process.

[Remainder of the Page Intentionally Left Blank]

IN WITNESS WHEREOF, the parties have executed this Agreement as of the day and year first above written.

CITY OF DELRAY BEACH, FLORIDA

ATTEST:

By: _____
Katerri Johnson, City Clerk

By: _____
Thomas F. Carney Jr., Mayor

CITY OF DELRAY BEACH SEAL FLORIDA

APPROVED AS TO FORM AND LEGAL SUFFICIENCY

By: _____
Lynn Gelin, City Attorney

[SEAL]

C.A.P. GOVERNMENT, INC.

By: _____

Carlos A. Penin, PE
Printed Name

President
Title

STATE OF Florida

COUNTY OF Miami-Dade

The foregoing instrument was acknowledged before me by means of ☒ physical presence or ☐ online notarization, this 22 day of July, 2024, by Carlos A. Penin, PE (name of person), as President (type of authority) for C.A.P. Government, Inc (name of party on behalf of whom instrument was executed).

Personally known X OR Produced Identification ___
Type of Identification Produced _____

MONICA DE CASTRO
Notary Public - State of Florida
Commission # HH 295746
My Comm. Expires Aug 1, 2026
Bonded through National Notary Assn.

_____
Notary Public – State of Florida

SECTION 4
BID SUBMITTAL SIGNATURE PAGE

This Page and all following pages comprise your original Bid Submittal package.

Please also attach any additional information or documentation requested in this Invitation to Bid. There is no need to include the preceding Sections 1 and 2 in your Bid Submittal package.

By signing this Bid the Bidder certifies that it satisfies all legal requirements as an entity to do business with the City, including all Conflict of Interest and Code of Ethics provisions.

Firm Name: C.A.P. Government, Inc.

Street Address: 1910 N. Florida Mango Rd., West Palm Beach, 33409

Mailing Address (if different than Street Address):

Telephone Number(s): (305) 448-1711

Fax Number(s): NA

Email Address: capenin@capfla.com

Federal Employer Identification Number: 65-0121594

Signature: _____
(Signature of authorized agent)

Print Name: Carlos A. Penin, PE

Title: President

By signing this document, the Bidder agrees to all Terms and Conditions of this Solicitation and the resulting Contract/Agreement.

THE EXECUTION OF THIS FORM CONSTITUTES THE UNEQUIVOCAL OFFER OF BIDDER TO BE BOUND BY THE TERMS OF ITS OFFER, FOR NOT LESS THAN 120 DAYS, AND THE BIDDER'S UNEQUIVOCAL OFFER TO BE BOUND BY THE TERMS AND CONDITIONS SET FORTH IN THIS INVITATION TO BID. FAILURE TO SIGN THIS SOLICITATION WHERE INDICATED ABOVE, BY AN AUTHORIZED REPRESENTATIVE, SHALL RENDER THE BID NON-RESPONSIVE. THE CITY MAY, HOWEVER, IN ITS SOLE DISCRETION, ACCEPT ANY BID THAT INCLUDES AN EXECUTED DOCUMENT WHICH UNEQUIVOCALLY BINDS THE BIDDER TO THE TERMS OF ITS OFFER.

END OF SECTION 4

SECTION 5
PRICING SCHEDULE

5.1 PRICES AND RATES

Bids will be accepted through a secure mailbox at Periscope S2G (www.PeriscopeS2G.com) until the Deadline for Submission as indicated in this ITB. The City will only accept electronic bids for this ITB. Late Bids will not be accepted.

In addition to the "Place Offer" bid submission section, the Bidder shall indicate in the spaces provided, the firm and fixed prices and rates offered to the City for the goods and/or services described below.

Description	Estimated Quantities Yearly (Hours)	Hourly Rate	Yearly Total Cost
Building Inspector	150	$82.50	$12,375.00
Electrical Inspector	75	$82.50	$6,187.50
Plumbing Inspector	75	$82.50	$6,187.50
Mechanical Inspector	100	$80.00	$8,000.00
Plan Reviewer	5	$110.00	$550.00
Landscape Plan Reviewer	5	$100.00	$500.00
Fire Plan Reviewer	5	$100.00	$500.00
Plan Review Technician	5	$55.00	$275.00
Building Official	5	$120.00	$600.00

TOTAL BID PRICE $ 35,175.00

END OF SECTION 5

ii. C.A.P. Government, Inc.'s proposed staff have valid licenses, and all licenses will be maintained during the performance of the contract. (We have enclosed on the following pages, proof of licenses of all personnel that will be engaged in performing City's contract)

vi. C.A.P. Government, Inc. has no conflicts of interests in relation to this ITB.

i. Entity Name: Palm Beach County

ii. Entity's Primary Contact for contract: Mr. Doug Wise, Building Official

iii. Phone Number: (561) 233-5192

iv. Email Address: dwise@pbcgov.org

v. Project Term: (Start/End Date): 2015 - Ongoing

vi. Types of Work: Building Inspection, Plan Review and Permit Technicians on an "As needed Basis"

vii. Beginning and ending contract/PO amounts: $8.2M

---

i. Entity Name: Town of Highland Beach

ii. Entity's Primary Contact for contract: Mr. Marshall Labadie, Town Manager

iii. Phone Number: (561) 278-4548

iv. Email Address: mlabadie@highlandbeach.us

v. Project Term (Start/End Date): 2019 - Ongoing

vi. Types of Work: Supplemental Building Inspections and Plan Review Services

vii. Beginning and ending contract/PO amounts: $1.5M

---

i. Entity Name: City of South Bay

ii. Entity's Primary Contact for contract: Mr. Leondrae D. Camel, City Manager

iii. Phone Number: (561) 996-6751

iv. Email Address: camell@southbaycity.com

v. Project Term (Start/End Date): 2010 - Ongoing

vi. Types of Work: Plan Review and Inspections

vii. Beginning and ending contract/PO amounts: $630K

ACKNOWLEDGEMENT OF ADDENDA

INSTRUCTIONS: COMPLETE PART I OR PART II, WHICHEVER APPLIES

PART I:

List below the dates of issue for each addendum received in connection with this Solicitation:

Addendum #1, Dated 06/24/2024

Addendum #2, Dated _____

Addendum #3, Dated _____

Addendum #4, Dated _____

Addendum #5, Dated _____

Addendum #6, Dated _____

Addendum #7, Dated _____

Addendum #8, Dated _____

PART II:

☐ NO ADDENDUM WAS RECEIVED IN CONNECTION WITH THIS SOLICITATION

C.A.P Government, Inc.
Firm Name

Signature

Carlos A. Penin, PE, President
Name and Title (Print or Type)

06/18/2024
Date

CONFLICT OF INTEREST DISCLOSURE FORM

The award of this contract is subject to the provisions of Chapter 112, *Florida Statutes*. All Bidders must disclose within their Bids: the name of any officer, director, or agent who is also an employee of the City of Delray Beach.

Furthermore, all Bidders must disclose the name of any City employee who owns, directly, or indirectly, an interest of more than five percent (5%) in the Bidder's firm or any of its branches.

The purpose of this disclosure form is to give the City the information needed to identify potential conflicts of interest for evaluation team members and other key personnel involved in the award of this contract.

The term "conflict of interest" refers to situations in which financial or other personal considerations may adversely affect, or have the appearance of adversely affecting, an employee's professional judgment in exercising any City duty or responsibility in administration, management, instruction, research, or other professional activities.


Please check one of the following statements and attach additional documentation if necessary:

__X__ To the best of our knowledge, the undersigned firm has no potential conflict of interest due to any other Cities, Counties, contracts, or property interest for this Bid.

_____ The undersigned firm, by attachment to this form, submits information which may be a potential conflict of interest due to other Cities, Counties, contracts, or property interest for this Bid.

Acknowledged by:

C.A.P. Government, Inc.
Firm Name


Signature

Carlos A. Penin, PE, President
Name and Title (Print or Type)


06/18/2024
Date

NOTIFICATION OF PUBLIC ENTITY CRIMES LAW

Pursuant to Section 287.133, *Florida Statutes*, you are hereby notified that a person or affiliate who has been placed on the convicted contractors list following a conviction for a public entity crime may not submit a Bid on a contract to provide any goods or services to a public entity, may not submit a Bid on a contract with a public entity for the construction or repair of a public building or public work, may not submit Bids on leases or real property to a public entity, may not be awarded or perform work as a contractor, supplier, sub-vendor, or consultant under a contract with any public entity, and may not transact business with any public entity in excess of the threshold amount provided in Section 287.017 [F.S.] for Category Two [$35,000.00] for a period of thirty-six (36) months from the date of being placed on the convicted contractors list.

Acknowledged by:

C.A.P. Government, Inc.
Firm Name


Signature

Carlos A. Penin, PE, President
Name and Title (Print or Type)

06/18/2024
Date


Notification of Public Records Law Pertaining to Public Contracts and Requests for Contractor Records Pursuant to Chapter 119, *Florida Statutes*

Pursuant to Chapter 119, *Florida Statutes*, Contractor shall comply with the public records law by keeping and maintaining public records required by the City of Delray Beach in order to perform the service. Upon request from the City of Delray Beach' custodian of public records, contract shall provide the City of Delray Beach with a copy of the requested records or allow the records to be inspected or copied within a reasonable time at a cost that does not exceed the cost provided in Chapter 119, *Florida Statutes* or as otherwise provided by law. Contractor shall ensure that public records that are exempt or confidential and exempt from public records disclosure requirements are not disclosed except as authorized by law for the duration of the contract term and following completion of the contract If the Contractor does not transfer the records to the City of Delray Beach. Contractor upon completion of the contract, shall transfer, at no cost, to the City of Delray Beach all public records in possession of the Contractor or keep and maintain public records required by the City of Delray Beach in order to perform the service. If the Contractor transfers all public records to the City of Delray Beach upon completion of the contract, the Contractor shall destroy any duplicate public records that are exempt or confidential and exempt from public records disclosure requirements. If the Contractor keeps and maintains public records upon completion of the contract, the Contractor shall meet all applicable requirements for retaining public records. All records stored electronically must be provided to the City of Delray Beach, upon request from the City of Delray Beach' custodian of public records, in a format that is compatible with the information technology systems of the City of Delray Beach.

IF THE SUCCESSFUL BIDDER HAS QUESTIONS REGARDING THE APPLICATION OF CHAPTER 119, FLORIDA STATUTES, TO THE SUCCESSFUL BIDDER'S DUTY TO PROVIDE PUBLIC RECORDS RELATING TO THIS AGREEMENT, CONTACT THE CUSTODIAN OF PUBLIC RECORDS AT CITY OF DELRAY BEACH, CITY CLERK, 100 N.W. 1ST AVE., DELRAY BEACH FLORIDA. THE CITY CLERK'S OFFICE MAY BE CONTACTED BY PHONE AT 561-243-7050 OR VIA EMAIL AT CITYCLERK@MYDELRAYBEACH.COM.

Acknowledged:

C.A.P. Government, Inc.
Firm Name


Signature

Carlos A. Penin, PE, President
Name and Title (Print or Type)


06/18/2024
Date

DRUG-FREE WORKPLACE

C.A.P. Government, Inc. is a drug-free workplace and has
(Company Name)
a substance abuse policy in accordance with and pursuant to Section 440.102, *Florida Statutes*.

Acknowledged by:

Carlos A. Penin, PE
Firm Name


Signature

Carlos A. Penin, PE, President
Name and Title (Print or Type)

06/18/2024
Date

NON-COLLUSION AFFIDAVIT

STATE OF Florida
COUNTY OF Miami-Dade

Before me, the undersigned authority, personally appeared Carlos A. Penin, PE, who, after being by me first duly sworn, deposes and says of his/her personal knowledge that:

a. He/She is President of C.A.P. Government, Inc., the Bidder that has submitted a Bid to perform work for the following:

ITB No.: 2024-041 Title: Inspection, Planning Review, and Development Review Services

b. He/She is fully informed respecting the preparation and contents of the attached Request for Bids, and of all pertinent circumstances respecting such Solicitation.

Such Bid is genuine and is not a collusive or sham Bid.

c. Neither the said Bidder nor any of its officers, partners, owners, agents, representatives, employees, or parties in interest, including this affiant, has in any way colluded, conspired, connived, or agreed, directly or indirectly, with any other Bidder, firm, or person to submit a collusive or sham Bid in connection with the Solicitation and contract for which the attached Bid has been submitted or to refrain from proposing in connection with such Solicitation and contract, or has in any manner, directly or indirectly, sought by agreement or collusion or communication or conference with any other Bidder, firm, or person to fix the price or prices in the attached Bid or any other Bidder, or to fix any overhead, profit, or cost element of the Bid price or the Bid price of any other Bidder, or to secure through any collusion, conspiracy, connivance, or unlawful agreement any advantage against the City or any person interested in the proposed contract.

d. The price or prices quoted in the attached Bid are fair and proper and are not tainted by any collusion, conspiracy, connivance, or unlawful agreement on the part of the Bidder or any of its agents, representatives, owners, employees, or parties in interest, including this affiant.

Signature

Subscribed and sworn to (or affirmed) before me this 18th day of June 2024 by Carlos A. Penin, PE, who is personally known to me or who has produced _____ as identification.

SEAL

MONICA DE CASTRO
Notary Public - State of Florida
Commission # HH 295746
My Comm. Expires Aug 1, 2026
Bonded through National Notary Assn.

Notary Signature Monica de Castro
Notary Name: Monica De Castro
Notary Public (State): Florida
My Commission No: HH 295746
Expires on: 08/01/2026

TRUTH – IN – NEGOTIATION CERTIFICATE

The undersigned warrants (i) that it has not employed or retained any company or person, other than bona fide employees working solely for the undersigned, to solicit or secure the Agreement and (ii) that it has not paid or agreed to pay any person, company, corporation, individual, or firm other than its bona fide employees working solely for the undersigned or agreed to pay any fee, commission, percentage, gift, or any other consideration contingent upon or resulting from the award or making of the Agreement.

The undersigned certifies that the wage rates and other factual unit costs used to determine the compensation provided for in the Agreement are accurate, complete, and current as of the date of the Agreement.

(This document must be executed by a Corporate Officer.)

Name: Carlos A. Penin, PE

Title: President

Date: 06/18/2024

Signature:

Scrutinized Company Certification

This certification is required pursuant to Florida State Statute Section 287.135.

As of July 1, 2011, a company that, at the time of bidding or submitting a proposal for a new contract or renewal of an existing contract, is on the Scrutinized Companies with Activities in Sudan List or the Scrutinized Companies with Activities in the Iran Petroleum Energy Sector List is ineligible for, and may not bid on, submit a proposal for, or enter into or renew a contract with an agency or local governmental entity for goods or services of $1 million or more.


Companies must complete and return this form with its response.

Company. C.A.P. Government, Inc. FID or EIN No. 65-0121594

Address. 1910 N. Florida Mango Rd., West Palm Beach, FL 33409

City. Coral Gables State. FL Zip. 33409

I, Carlos A. Penin, PE, as a representative of C.A.P. Goverment, Inc. certify and affirm that this company is not on the Scrutinized Companies with Activities in Sudan List or the Scrutinized Companies with Activities in the Iran Petroleum Energy Sector List.



Signature

President
Title

Carlos A. Penin, PE
Printed Name

06/18/2024
Date



Florida dbpr Department of Business & Professional Regulation

ONLINE SERVICES

Apply for a License
Verify a Licensee
View Food & Lodging Inspections
File a Complaint
Continuing Education Course Search
View Application Status
Find Exam Information
Unlicensed Activity Search
AB&T Delinquent Invoice & Activity List Search

LICENSEE DETAILS

11:01:10 AM 2/21/2023

Licensee Information

Name:	**PENIN, CARLOS ANTONIO (Primary Name)**
Main Address:	**343 ALMERIA AVENUE CORAL GABLES Florida 33134**
County:	**DADE**
License Mailing:	**343 ALMERIA AVENUE CORAL GABLES FL 33134**
County:	**DADE**

License Information

License Type:	**Professional Engineer**
Rank:	**Prof Engineer**
License Number:	**33216**
Status:	**Current,Active**
Licensure Date:	**03/25/1983**
Expires:	**02/28/2025**

Special Qualifications	**Qualification Effective**

Alternate Names

View Related License Information
View License Complaint

The State of Florida is an AA/EEO employer. **Copyright 2007-2010 State of Florida. Privacy Statement**

Under Florida law, email addresses are public records. If you do not want your email address released in response to a public-records request, do not send electronic mail to this entity. Instead, contact the office by phone or by traditional mail. If you have any questions, please contact 850.487.1395. *Pursuant to Section 455.275(1), Florida Statutes, effective October 1, 2012, licensees licensed under Chapter 455, F.S. must provide the Department with an email address if they have one. The emails provided may be used for official communication with the licensee. However email addresses are public record. If you do not wish to supply a personal address, please provide the Department with an email address which can be made available to the public. Please see our **Chapter 455** page to determine if you are affected by this change.



Florida dbpr Department of Business & Professional Regulation

ONLINE SERVICES

Apply for a License

Verify a Licensee

View Food & Lodging Inspections

File a Complaint

Continuing Education Course Search

View Application Status

Find Exam Information

Unlicensed Activity Search

AB&T Delinquent Invoice & Activity List Search

LICENSEE DETAILS

11:45:55 AM 12/15/2023

Licensee Information

Name:	**NUTTER, DEBORAH ANN (Primary Name)**
Main Address:	***Private Address* *Private Address*** ***Private Address*** ***Private Address*** ***Private Address***
License Location:	***Private Address* *Private Address*** ***Private Address*** ***Private Address*** ***Private Address***

License Information

License Type:	**Standard Inspector**
Rank:	**Inspector**
License Number:	**BN5093**
Status:	**Current,Active**
Licensure Date:	**09/23/2005**
Expires:	**11/30/2025**

Special Qualifications	Qualification Effective
Building	**08/09/2006**
Electrical Inspector	**09/23/2005**
Residential	**05/05/2006**
Mechanical	**08/09/2006**

Alternate Names

View Related License Information

View License Complaint

The State of Florida is an AA/EEO employer. **Copyright 2007-2010 State of Florida. Privacy Statement**



Florida dbpr Department of Business & Professional Regulation

ONLINE SERVICES

Apply for a License

Verify a Licensee

View Food & Lodging Inspections

File a Complaint

Continuing Education Course Search

View Application Status

Find Exam Information

Unlicensed Activity Search

AB&T Delinquent Invoice & Activity List Search

LICENSEE DETAILS

11:46:45 AM 12/15/2023

Licensee Information

Name:	**NUTTER, DEBORAH ANN (Primary Name)**
Main Address:	***Private Address* *Private Address*** ***Private Address*** ***Private Address*** ***Private Address***
License Location:	***Private Address* *Private Address*** ***Private Address*** ***Private Address*** ***Private Address***

License Information

License Type:	**Building Code Administrator**
Rank:	**Building Code A**
License Number:	**BU1478**
Status:	**Current,Active**
Licensure Date:	**05/02/2006**
Expires:	**11/30/2025**

Special Qualifications — **Qualification Effective**

Alternate Names

View Related License Information

View License Complaint

2601 Blair Stone Road, Tallahassee FL 32399 :: Email: **Customer Contact Center** :: Customer Contact Center: 850.487.1395

The State of Florida is an AA/EEO employer. **Copyright 2007-2010 State of Florida. Privacy Statement**

Under Florida law, email addresses are public records. If you do not want your email address released in response to a public-records request, do not send electronic mail to this entity. Instead, contact the office by phone or by traditional mail. If you have any questions, please contact 850.487.1395. *Pursuant to Section 455.275(1), Florida Statutes, effective October 1, 2012, licensees licensed under Chapter 455, F.S. must provide the Department with an email address if they have one. The emails provided may be used for official communication with the licensee.

THE OFFICIAL SITE OF THE FLORIDA DEPARTMENT OF BUSINESS & PROFESSIONAL REGULATION



Florida dbpr Department of Business & Professional Regulation

HOME CONTACT US MY ACCOUNT

ONLINE SERVICES

- Apply for a License
- Verify a Licensee
- View Food & Lodging Inspections
- File a Complaint
- Continuing Education Course Search
- View Application Status
- Find Exam Information
- Unlicensed Activity Search
- AB&T Delinquent Invoice & Activity List Search

LICENSEE DETAILS

11:44:52 AM 12/15/2023

Licensee Information

Name:	**NUTTER, DEBORAH ANN (Primary Name)**
Main Address:	***Private Address* *Private Address*** ***Private Address*** ***Private Address*** ***Private Address***
License Location:	***Private Address* *Private Address*** ***Private Address*** ***Private Address*** ***Private Address***

License Information

License Type:	**Standard Plans Examiner**
Rank:	**Plans Examiner**
License Number:	**PX2657**
Status:	**Current,Active**
Licensure Date:	**03/13/2006**
Expires:	**11/30/2025**

Special Qualifications	**Qualification Effective**
Electrical	**03/13/2006**

Alternate Names

View Related License Information

View License Complaint

The State of Florida is an AA/EEO employer. **Copyright 2007-2010 State of Florida. Privacy Statement**

Under Florida law, email addresses are public records. If you do not want your email address released in response to a public-records request, do not send electronic mail to this entity. Instead, contact the office by phone or by traditional mail. If you have any questions, please contact 850.487.1395. *Pursuant to Section 455.275(1), Florida Statutes, effective October 1, 2012, licensees licensed under Chapter 455, F.S. must provide the Department with an email address if they have one. The emails provided may be used for official communication with the licensee.



Florida dbpr Department of Business & Professional Regulation

ONLINE SERVICES

- Apply for a License
- Verify a Licensee
- View Food & Lodging Inspections
- File a Complaint
- Continuing Education Course Search
- View Application Status
- Find Exam Information
- Unlicensed Activity Search
- AB&T Delinquent Invoice & Activity List Search

LICENSEE DETAILS

4:53:59 PM 12/15/2023

Licensee Information

Name:	**DULANY, JUDSON DEWITT** (Primary Name)
Main Address:	***Private Address* *Private Address*** ***Private Address*** ***Private Address*** ***Private Address***

License Information

License Type:	**Building Code Administrator**
Rank:	**Building Code A**
License Number:	**BU1990**
Status:	**Current,Active**
Licensure Date:	**02/26/2018**
Expires:	**11/30/2025**

Special Qualifications **Qualification Effective**

Alternate Names

View Related License Information

View License Complaint

2601 Blair Stone Road, Tallahassee FL 32399 :: Email: **Customer Contact Center** :: Customer Contact Center: 850 487.1395

The State of Florida is an AA/EEO employer **Copyright 2007-2010 State of Florida. Privacy Statement**

Under Florida law, email addresses are public records. If you do not want your email address released in response to a public-records request, do not send electronic mail to this entity. Instead, contact the office by phone or by traditional mail. If you have any questions, please contact 850.487.1395. *Pursuant to Section 455.275(1), Florida Statutes, effective October 1, 2012, licensees licensed under Chapter 455, F.S. must provide the Department with an email address if they have one. The emails provided may be used for official communication with the licensee. However email addresses are public record. If you do not wish to supply a personal address, please provide the Department with an email address which can be made available to the public. Please see our **Chapter 455** page to determine if you are affected by this change.



Florida dbpr Department of Business & Professional Regulation

ONLINE SERVICES

Apply for a License

Verify a Licensee

View Food & Lodging Inspections

File a Complaint

Continuing Education Course Search

View Application Status

Find Exam Information

Unlicensed Activity Search

AB&T Delinquent Invoice & Activity List Search

LICENSEE DETAILS

4:54:46 PM 12/15/2023

Licensee Information

Name:	**DULANY, JUDSON DEWITT (Primary Name)**
Main Address:	***Private Address* *Private Address* *Private Address* *Private Address* *Private Address***

License Information

License Type:	**Standard Plans Examiner**
Rank:	**Plans Examiner**
License Number:	**PX3626**
Status:	**Current,Active**
Licensure Date:	**07/30/2015**
Expires:	**11/30/2025**

Special Qualifications	**Qualification Effective**
Building	**07/30/2015**

Alternate Names

View Related License Information

View License Complaint

The State of Florida is an AA/EEO employer. **Copyright 2007-2010 State of Florida. Privacy Statement**

Under Florida law, email addresses are public records. If you do not want your email address released in response to a public-records request, do not send electronic mail to this entity. Instead, contact the office by phone or by traditional mail. If you have any questions, please contact 850.487.1395. *Pursuant to Section 455.275(1), Florida Statutes, effective October 1, 2012, licensees licensed under Chapter 455, F.S. must provide the Department with an email address if they have one. The emails provided may be used for official communication with the licensee. However email addresses are public record. If you do not wish to supply a personal address, please provide the Department with an email address which can be made available to the public. Please see our **Chapter 455** page to determine if you are affected by this change.

THE OFFICIAL SITE OF THE FLORIDA DEPARTMENT OF BUSINESS & PROFESSIONAL REGULATION

Florida dbpr Department of Business & Professional Regulation

HOME CONTACT US

ONLINE SERVICES

Apply for a License

Verify a Licensee

View Food & Lodging Inspections

File a Complaint

Continuing Education Course Search

View Application Status

Find Exam Information

Unlicensed Activity Search

AB&T Delinquent Invoice & Activity List Search

LICENSEE DETAILS

4:52:52 PM 12/15/2023

Licensee Information

Name:	**DULANY, JUDSON DEWITT (Primary Name)**
Main Address:	***Private Address* *Private Address*** ***Private Address*** ***Private Address*** ***Private Address***

License Information

License Type:	**Standard Inspector**
Rank:	**Inspector**
License Number:	**BN6644**
Status:	**Current,Active**
Licensure Date:	**03/27/2015**
Expires:	**11/30/2025**

Special Qualifications	**Qualification Effective**
Building	**03/27/2015**

Alternate Names

View Related License Information

View License Complaint

2601 Blair Stone Road, Tallahassee FL 32399 :: Email: **Customer Contact Center** :: Customer Contact Center: 850.487.1395

The State of Florida is an AA/EEO employer. **Copyright 2007-2010 State of Florida. Privacy Statement**

Under Florida law, email addresses are public records. If you do not want your email address released in response to a public-records request, do not send electronic mail to this entity. Instead, contact the office by phone or by traditional mail. If you have any questions, please contact 850.487.1395. *Pursuant to Section 455.275(1), Florida Statutes, effective October 1, 2012, licensees licensed under Chapter 455, F.S. must provide the Department with an email address if they have one. The emails provided may be used for official communication with the licensee. However email addresses are public record. If you do not wish to supply a personal address, please provide the Department with an email address which can be made available to the public. Please see our **Chapter 455** page to determine if you are affected by this change.



Florida dbpr Department of Business & Professional Regulation

ONLINE SERVICES

- Apply for a License
- Verify a Licensee
- View Food & Lodging Inspections
- File a Complaint
- Continuing Education Course Search
- View Application Status
- Find Exam Information
- Unlicensed Activity Search
- AB&T Delinquent Invoice & Activity List Search

LICENSEE DETAILS

1:52:02 PM 12/20/2023

Licensee Information

Name:	**STEPHEN, ZEALUS BUTTLER (Primary Name)**
Main Address:	**4301 SOUTH FLAMINGO RD SUITE 106 UNIT 172 DAVIE Florida 33330**
County:	**BROWARD**

License Information

License Type:	**Standard Inspector**
Rank:	**Inspector**
License Number:	**BN8335**
Status:	**Current,Active**
Licensure Date:	**10/11/2021**
Expires:	**11/30/2025**

Special Qualifications	**Qualification Effective**
Building	**10/11/2021**

Alternate Names

View Related License Information

View License Complaint

2601 Blair Stone Road, Tallahassee FL 32399 :: Email: **Customer Contact Center** :: Customer Contact Center: 850.487.1395

The State of Florida is an AA/EEO employer. **Copyright 2007-2010 State of Florida. Privacy Statement**

Under Florida law, email addresses are public records. If you do not want your email address released in response to a public-records request, do not send electronic mail to this entity. Instead, contact the office by phone or by traditional mail. If you have any questions, please contact 850.487.1395. *Pursuant to Section 455.275(1), Florida Statutes, effective October 1, 2012, licensees licensed under Chapter 455, F.S. must provide the Department with an email address if they have one. The emails provided may be used for official communication with the licensee. However email addresses are public record. If you do not wish to supply a personal address, please provide the Department with an email address which can be made available to the public. Please see our **Chapter 455** page to determine if you are affected by this change.

LICENSEE DETAILS

1:46:23 PM 12/20/2023

Licensee Information

Name:	**REY, XAIRO (Primary Name)**
Main Address:	**5722 DEWBERRY WAY** **WEST PALM BEACH Florida 33415**
County:	**PALM BEACH**

License Information

License Type:	**Standard Plans Examiner**
Rank:	**Plans Examiner**
License Number:	**PX4112**
Status:	**Current,Active**
Licensure Date:	**07/09/2018**
Expires:	**11/30/2025**

Special Qualifications	**Qualification Effective**
Building	**07/09/2018**

Alternate Names

View Related License Information

View License Complaint

The State of Florida is an AA/EEO employer. **Copyright 2007-2010 State of Florida. Privacy Statement**

Under Florida law, email addresses are public records. If you do not want your email address released in response to a public-records request, do not send electronic mail to this entity. Instead, contact the office by phone or by traditional mail. If you have any questions, please contact 850.487.1395. *Pursuant to Section 455.275(1), Florida Statutes, effective October 1, 2012, licensees licensed under Chapter 455, F.S. must provide the Department with an email address if they have one. The emails provided may be used for official communication with the licensee. However email addresses are public record. If you do not wish to supply a personal address, please provide the Department with an email address which can be made available to the public. Please see our **Chapter 455** page to determine if you are affected by this change.



Florida dbpr Department of Business & Professional Regulation

ONLINE SERVICES

Apply for a License

Verify a Licensee

View Food & Lodging Inspections

File a Complaint

Continuing Education Course Search

View Application Status

Find Exam Information

Unlicensed Activity Search

AB&T Delinquent Invoice & Activity List Search

LICENSEE DETAILS

1:45:07 PM 12/20/2023

Licensee Information

Name:	**REY, XAIRO (Primary Name)**
Main Address:	**5722 DEWBERRY WAY WEST PALM BEACH Florida 33415**
County:	**PALM BEACH**

License Information

License Type:	**Standard Inspector**
Rank:	**Inspector**
License Number:	**BN7926**
Status:	**Current,Active**
Licensure Date:	**01/16/2020**
Expires:	**11/30/2025**

Special Qualifications	**Qualification Effective**
Building	**01/16/2020**

Alternate Names

View Related License Information

View License Complaint

2601 Blair Stone Road, Tallahassee FL 32399 :: Email: **Customer Contact Center** :: Customer Contact Center: 850.487.1395

The State of Florida is an AA/EEO employer. **Copyright 2007-2010 State of Florida. Privacy Statement**

Under Florida law, email addresses are public records. If you do not want your email address released in response to a public-records request, do not send electronic mail to this entity. Instead, contact the office by phone or by traditional mail. If you have any questions, please contact 850.487.1395. *Pursuant to Section 455.275(1), Florida Statutes, effective October 1, 2012, licensees licensed under Chapter 455, F.S. must provide the Department with an email address if they have one. The emails provided may be used for official communication with the licensee. However email addresses are public record. If you do not wish to supply a personal address, please provide the Department with an email address which can be made available to the public. Please see our **Chapter 455** page to determine if you are affected by this change.

THE OFFICIAL SITE OF THE FLORIDA DEPARTMENT OF BUSINESS & PROFESSIONAL REGULATION

Florida dbpr Department of Business & Professional Regulation

HOME CONTACT US MY ACCOUNT

ONLINE SERVICES

- Apply for a License
- Verify a Licensee
- View Food & Lodging Inspections
- File a Complaint
- Continuing Education Course Search
- View Application Status
- Find Exam Information
- Unlicensed Activity Search
- AB&T Delinquent Invoice & Activity List Search

LICENSEE DETAILS

5:23:09 PM 12/15/2023

Licensee Information

Name:	**ESPINOSA, MANUEL E (Primary Name)**
Main Address:	**169 WEST TRAIL DRIVE WEST PALM BEACH Florida 33415**
County:	**PALM BEACH**

License Information

License Type:	**Standard Plans Examiner**
Rank:	**Plans Examiner**
License Number:	**PX4694**
Status:	**Current,Active**
Licensure Date:	**12/08/2021**
Expires:	**11/30/2025**

Special Qualifications	**Qualification Effective**
Electrical	**10/06/2023**
Mechanical	**12/08/2021**

Alternate Names

View Related License Information

View License Complaint

2601 Blair Stone Road, Tallahassee FL 32399 :: Email: **Customer Contact Center** :: Customer Contact Center: 850.487.1395

The State of Florida is an AA/EEO employer. **Copyright 2007-2010 State of Florida. Privacy Statement**

Under Florida law, email addresses are public records. If you do not want your email address released in response to a public-records request, do not send electronic mail to this entity. Instead, contact the office by phone or by traditional mail. If you have any questions, please contact 850.487.1395. *Pursuant to Section 455.275(1), Florida Statutes, effective October 1, 2012, licensees licensed under Chapter 455, F.S. must provide the Department with an email address if they have one. The emails provided may be used for official communication with the licensee. However email addresses are public record. If you do not wish to supply a personal address, please provide the Department with an email address which can be made available to the public. Please see our **Chapter 455** page to determine if you are affected by this change.

THE OFFICIAL SITE OF THE FLORIDA DEPARTMENT OF BUSINESS & PROFESSIONAL REGULATION

Florida dbpr Department of Business & Professional Regulation

HOME CONTACT US MY ACCOUNT

ONLINE SERVICES

- Apply for a License
- Verify a Licensee
- View Food & Lodging Inspections
- File a Complaint
- Continuing Education Course Search
- View Application Status
- Find Exam Information
- Unlicensed Activity Search
- AB&T Delinquent Invoice & Activity List Search

LICENSEE DETAILS

5:21:47 PM 12/15/2023

Licensee Information

Name:	**ESPINOSA, MANUEL E (Primary Name)**
Main Address:	**169 WEST TRAIL DRIVE WEST PALM BEACH Florida 33415**
County:	**PALM BEACH**

License Information

License Type:	**Standard Inspector**
Rank:	**Inspector**
License Number:	**BN8214**
Status:	**Current,Active**
Licensure Date:	**04/16/2021**
Expires:	**11/30/2025**

Special Qualifications	**Qualification Effective**
Electrical Inspector	**12/27/2022**
Mechanical	**04/16/2021**

Alternate Names

View Related License Information

View License Complaint

2601 Blair Stone Road, Tallahassee FL 32399 :: Email: **Customer Contact Center** :: Customer Contact Center: 850.487.1395

The State of Florida is an AA/EEO employer. **Copyright 2007-2010 State of Florida. Privacy Statement**

Under Florida law, email addresses are public records. If you do not want your email address released in response to a public-records request, do not send electronic mail to this entity. Instead, contact the office by phone or by traditional mail. If you have any questions, please contact 850.487.1395. *Pursuant to Section 455.275(1), Florida Statutes, effective October 1, 2012, licensees licensed under Chapter 455, F.S. must provide the Department with an email address if they have one. The emails provided may be used for official communication with the licensee. However email addresses are public record. If you do not wish to supply a personal address, please provide the Department with an email address which can be made available to the public. Please see our **Chapter 455** page to determine if you are affected by this change.



ONLINE SERVICES

- Apply for a License
- Verify a Licensee
- View Food & Lodging Inspections
- File a Complaint
- Continuing Education Course Search
- View Application Status
- Find Exam Information
- Unlicensed Activity Search
- AB&T Delinquent Invoice & Activity List Search

LICENSEE DETAILS

4:28:55 PM 12/15/2023

Licensee Information

Name:	**HENNESSEY, JOSEPH THOMAS** (Primary Name)
Main Address:	***Private Address* *Private Address*** ***Private Address*** ***Private Address*** ***Private Address***

License Information

License Type:	**Standard Plans Examiner**
Rank:	**Plans Examiner**
License Number:	**PX4547**
Status:	**Current,Active**
Licensure Date:	**12/14/2020**
Expires:	**11/30/2025**

Special Qualifications	**Qualification Effective**
Mechanical	**10/05/2021**
Plumbing	**12/14/2020**

Alternate Names

View Related License Information

View License Complaint

2601 Blair Stone Road, Tallahassee FL 32399 :: Email: **Customer Contact Center** :: Customer Contact Center: 850.487.1395

The State of Florida is an AA/EEO employer. **Copyright 2007-2010 State of Florida. Privacy Statement**

Under Florida law, email addresses are public records. If you do not want your email address released in response to a public-records request, do not send electronic mail to this entity. Instead, contact the office by phone or by traditional mail. If you have any questions, please contact 850.487.1395. *Pursuant to Section 455.275(1), Florida Statutes, effective October 1, 2012, licensees licensed under Chapter 455, F.S. must provide the Department with an email address if they have one. The emails provided may be used for official communication with the licensee. However email addresses are public record. If you do not wish to supply a personal address, please provide the Department with an email address which can be made available to the public. Please see our **Chapter 455** page to determine if you are affected by this change.



dbpr Florida Department of Business & Professional Regulation

ONLINE SERVICES

Apply for a License

Verify a Licensee

View Food & Lodging Inspections

File a Complaint

Continuing Education Course Search

View Application Status

Find Exam Information

Unlicensed Activity Search

AB&T Delinquent Invoice & Activity List Search

LICENSEE DETAILS

4:15:48 PM 12/15/2023

Licensee Information

Name:	**HENNESSEY, JOSEPH THOMAS (Primary Name)**
Main Address:	***Private Address* *Private Address*** ***Private Address*** ***Private Address*** ***Private Address***

License Information

License Type:	**Standard Inspector**
Rank:	**Inspector**
License Number:	**BN7885**
Status:	**Current,Active**
Licensure Date:	**11/20/2019**
Expires:	**11/30/2025**

Special Qualifications	**Qualification Effective**
Residential	**10/25/2023**
Mechanical	**11/20/2019**
Plumbing	**02/10/2020**

Alternate Names

View Related License Information

View License Complaint

2601 Blair Stone Road, Tallahassee FL 32399 :: Email: **Customer Contact Center** :: Customer Contact Center: 850.487.1395

The State of Florida is an AA/EEO employer. **Copyright 2007-2010 State of Florida. Privacy Statement**

Under Florida law, email addresses are public records. If you do not want your email address released in response to a public-records request, do not send electronic mail to this entity. Instead, contact the office by phone or by traditional mail. If you have any questions, please contact 850.487.1395. *Pursuant to Section 455.275(1), Florida Statutes, effective October 1, 2012, licensees licensed under Chapter 455, F.S. must provide the Department with an email address if they have one. The emails provided may be used for official communication with the licensee. However email addresses are public record. If you do not wish to supply a personal address, please provide the Department with an email address which can be made available to the public. Please see our **Chapter 455** page to determine if you are affected by this change.



Florida dbpr Department of Business & Professional Regulation

ONLINE SERVICES

Apply for a License
Verify a Licensee
View Food & Lodging Inspections
File a Complaint
Continuing Education Course Search
View Application Status
Find Exam Information
Unlicensed Activity Search
AB&T Delinquent Invoice & Activity List Search

LICENSEE DETAILS

10:17:48 AM 10/26/2023

Licensee Information

Name:	**GOMES, LECIO DO (Primary Name)**
Main Address:	***Private Address* *Private Address* *Private Address* *Private Address* *Private Address***

License Information

License Type:	**Provisional Electrical Plans Examiner**
Rank:	**Prov. Elec Plan**
License Number:	**PEP634**
Status:	**Current,Active**
Licensure Date:	**06/12/2023**
Expires:	**06/11/2025**

Special Qualifications **Qualification Effective**

Alternate Names

View Related License Information
View License Complaint

2601 Blair Stone Road, Tallahassee FL 32399 :: Email: **Customer Contact Center** :: Customer Contact Center: 850.487.1395

The State of Florida is an AA/EEO employer. **Copyright 2007-2010 State of Florida. Privacy Statement**

Under Florida law, email addresses are public records. If you do not want your email address released in response to a public-records request, do not send electronic mail to this entity. Instead, contact the office by phone or by traditional mail. If you have any questions, please contact 850.487.1395. *Pursuant to Section 455.275(1), Florida Statutes, effective October 1, 2012, licensees licensed under Chapter 455, F.S. must provide the Department with an email address if they have one. The emails provided may be used for official communication with the licensee. However email addresses are public record. If you do not wish to supply a personal address, please provide the Department with an email address which can be made available to the public. Please see our **Chapter 455** page to determine if you are affected by this change.

THE OFFICIAL SITE OF THE FLORIDA DEPARTMENT OF BUSINESS & PROFESSIONAL REGULATION

dbpr Florida Department of Business & Professional Regulation

HOME CONTACT US MY ACCOUNT

ONLINE SERVICES

- Apply for a License
- Verify a Licensee
- View Food & Lodging Inspections
- File a Complaint
- Continuing Education Course Search
- View Application Status
- Find Exam Information
- Unlicensed Activity Search
- AB&T Delinquent Invoice & Activity List Search

LICENSEE DETAILS

10:15:26 AM 10/26/2023

Licensee Information

Name:	**GOMES, LECIO DO (Primary Name)**
Main Address:	***Private Address* *Private Address* *Private Address* *Private Address* *Private Address***

License Information

License Type:	**Standard Inspector**
Rank:	**Inspector**
License Number:	**BN8845**
Status:	**Current,Active**
Licensure Date:	**07/06/2023**
Expires:	**11/30/2025**

Special Qualifications	Qualification Effective
Electrical Inspector	**07/06/2023**

Alternate Names

View Related License Information

View License Complaint

2601 Blair Stone Road, Tallahassee FL 32399 :: Email: **Customer Contact Center** :: Customer Contact Center: 850.487.1395

The State of Florida is an AA/EEO employer. **Copyright 2007-2010 State of Florida. Privacy Statement**

Under Florida law, email addresses are public records. If you do not want your email address released in response to a public-records request, do not send electronic mail to this entity. Instead, contact the office by phone or by traditional mail. If you have any questions, please contact 850.487.1395. *Pursuant to Section 455.275(1), Florida Statutes, effective October 1, 2012, licensees licensed under Chapter 455, F.S. must provide the Department with an email address if they have one. The emails provided may be used for official communication with the licensee. However email addresses are public record. If you do not wish to supply a personal address, please provide the Department with an email address which can be made available to the public. Please see our **Chapter 455** page to determine if you are affected by this change.



Florida dbpr Department of Business & Professional Regulation

ONLINE SERVICES

Apply for a License

Verify a Licensee

View Food & Lodging Inspections

File a Complaint

Continuing Education Course Search

View Application Status

Find Exam Information

Unlicensed Activity Search

AB&T Delinquent Invoice & Activity List Search

LICENSEE DETAILS

11:33:53 AM 12/19/2023

Licensee Information

Name:	**CEDENO, WILLIAM (Primary Name)**
Main Address:	***Private Address* *Private Address*** ***Private Address*** ***Private Address*** ***Private Address***

License Information

License Type:	**Standard Inspector**
Rank:	**Inspector**
License Number:	**BN7817**
Status:	**Current,Active**
Licensure Date:	**09/06/2019**
Expires:	**11/30/2025**

Special Qualifications	Qualification Effective
Electrical Inspector	**09/06/2019**
Mechanical	**03/10/2023**
Plumbing	**08/07/2023**

Alternate Names

View Related License Information

View License Complaint

2601 Blair Stone Road, Tallahassee FL 32399 :: Email: **Customer Contact Center** :: Customer Contact Center: 850.487.1395

The State of Florida is an AA/EEO employer. **Copyright 2007-2010 State of Florida. Privacy Statement**

Under Florida law, email addresses are public records. If you do not want your email address released in response to a public-records request, do not send electronic mail to this entity. Instead, contact the office by phone or by traditional mail. If you have any questions, please contact 850.487.1395. *Pursuant to Section 455.275(1), Florida Statutes, effective October 1, 2012, licensees licensed under Chapter 455, F.S. must provide the Department with an email address if they have one. The emails provided may be used for official communication with the licensee. However email addresses are public record. If you do not wish to supply a personal address, please provide the Department with an email address which can be made available to the public. Please see our **Chapter 455** page to determine if you are affected by this change.



ONLINE SERVICES

- Apply for a License
- Verify a Licensee
- View Food & Lodging Inspections
- File a Complaint
- Continuing Education Course Search
- View Application Status
- Find Exam Information
- Unlicensed Activity Search
- AB&T Delinquent Invoice & Activity List Search

LICENSEE DETAILS

11:37:23 AM 12/19/2023

Licensee Information

Name:	**CEDENO, WILLIAM (Primary Name)**
Main Address:	***Private Address* *Private Address*** ***Private Address*** ***Private Address*** ***Private Address***

License Information

License Type:	**Standard Plans Examiner**
Rank:	**Plans Examiner**
License Number:	**PX4335**
Status:	**Current,Active**
Licensure Date:	**09/06/2019**
Expires:	**11/30/2025**

Special Qualifications	Qualification Effective
Electrical	**09/06/2019**
Mechanical	**03/10/2023**
Plumbing	**09/12/2023**

Alternate Names

View Related License Information

View License Complaint

The State of Florida is an AA/EEO employer. **Copyright 2007-2010 State of Florida. Privacy Statement**

Under Florida law, email addresses are public records. If you do not want your email address released in response to a public-records request, do not send electronic mail to this entity. Instead, contact the office by phone or by traditional mail. If you have any questions, please contact 850.487.1395. *Pursuant to Section 455.275(1), Florida Statutes, effective October 1, 2012, licensees licensed under Chapter 455, F.S. must provide the Department with an email address if they have one. The emails provided may be used for official communication with the licensee. However email addresses are public record. If you do not wish to supply a personal address, please provide the Department with an email address which can be made available to the public. Please see our **Chapter 455** page to determine if you are affected by this change.

ONLINE SERVICES

Apply for a License

Verify a Licensee

View Food & Lodging Inspections

File a Complaint

Continuing Education Course Search

View Application Status

Find Exam Information

Unlicensed Activity Search

AB&T Delinquent Invoice & Activity List Search

LICENSEE DETAILS

11:41:54 AM 1/17/2024

Licensee Information

Name:	**THARPE, PAUL ANTHONY (Primary Name)**
Main Address:	***Private Address* *Private Address* *Private Address* *Private Address* *Private Address***

License Information

License Type:	**Standard Inspector**
Rank:	**Inspector**
License Number:	**BN8059**
Status:	**Current,Active**
Licensure Date:	**08/31/2020**
Expires:	**11/30/2025**

Special Qualifications	**Qualification Effective**
Plumbing	**08/31/2020**

Alternate Names

View Related License Information

View License Complaint

2601 Blair Stone Road, Tallahassee FL 32399 :: Email: **Customer Contact Center** :: Customer Contact Center: 850.487.1395

The State of Florida is an AA/EEO employer. **Copyright 2007-2010 State of Florida. Privacy Statement**

Under Florida law, email addresses are public records. If you do not want your email address released in response to a public-records request, do not send electronic mail to this entity. Instead, contact the office by phone or by traditional mail. If you have any questions, please contact 850.487.1395. *Pursuant to Section 455.275(1), Florida Statutes, effective October 1, 2012, licensees licensed under Chapter 455, F.S. must provide the Department with an email address if they have one. The emails provided may be used for official communication with the licensee. However email addresses are public record. If you do not wish to supply a personal address, please provide the Department with an email address which can be made available to the public. Please see our **Chapter 455** page to determine if you are affected by this change.

THE OFFICIAL SITE OF THE FLORIDA DEPARTMENT OF BUSINESS & PROFESSIONAL REGULATION

Florida dbpr Department of Business & Professional Regulation

HOME CONTACT US MY ACCOUNT

ONLINE SERVICES

- Apply for a License
- Verify a Licensee
- View Food & Lodging Inspections
- File a Complaint
- Continuing Education Course Search
- View Application Status
- Find Exam Information
- Unlicensed Activity Search
- AB&T Delinquent Invoice & Activity List Search

LICENSEE DETAILS

11:43:10 AM 1/17/2024

Licensee Information

Name:	**THARPE, PAUL ANTHONY (Primary Name)**
Main Address:	***Private Address* *Private Address*** ***Private Address*** ***Private Address*** ***Private Address***

License Information

License Type:	**Standard Plans Examiner**
Rank:	**Plans Examiner**
License Number:	**PX4666**
Status:	**Current,Active**
Licensure Date:	**10/04/2021**
Expires:	**11/30/2025**

Special Qualifications	Qualification Effective
Plumbing	**10/04/2021**

Alternate Names

View Related License Information

View License Complaint

2601 Blair Stone Road, Tallahassee FL 32399 :: Email: **Customer Contact Center** :: Customer Contact Center: 850.487.1395

The State of Florida is an AA/EEO employer. **Copyright 2007-2010 State of Florida. Privacy Statement**

Under Florida law, email addresses are public records. If you do not want your email address released in response to a public-records request, do not send electronic mail to this entity. Instead, contact the office by phone or by traditional mail. If you have any questions, please contact 850.487.1395. *Pursuant to Section 455.275(1), Florida Statutes, effective October 1, 2012, licensees licensed under Chapter 455, F.S. must provide the Department with an email address if they have one. The emails provided may be used for official communication with the licensee. However email addresses are public record. If you do not wish to supply a personal address, please provide the Department with an email address which can be made available to the public. Please see our **Chapter 455** page to determine if you are affected by this change.



ONLINE SERVICES

- Apply for a License
- Verify a Licensee
- View Food & Lodging Inspections
- File a Complaint
- Continuing Education Course Search
- View Application Status
- Find Exam Information
- Unlicensed Activity Search
- AB&T Delinquent Invoice & Activity List Search

LICENSEE DETAILS

10:36:10 AM 12/15/2023

Licensee Information

Name:	**DAURIA, ANTHONY ALBINO (Primary Name)**
Main Address:	***Private Address* *Private Address*** ***Private Address*** ***Private Address*** ***Private Address***

License Information

License Type:	**Standard Inspector**
Rank:	**Inspector**
License Number:	**BN7353**
Status:	**Current,Active**
Licensure Date:	**03/05/2018**
Expires:	**11/30/2025**

Special Qualifications	Qualification Effective
Plumbing	**03/05/2018**

Alternate Names

View Related License Information

View License Complaint

THE OFFICIAL SITE OF THE FLORIDA DEPARTMENT OF BUSINESS & PROFESSIONAL REGULATION

Florida dbpr Department of Business & Professional Regulation

HOME CONTACT US MY ACCOUNT

ONLINE SERVICES

- Apply for a License
- Verify a Licensee
- View Food & Lodging Inspections
- File a Complaint
- Continuing Education Course Search
- View Application Status
- Find Exam Information
- Unlicensed Activity Search
- AB&T Delinquent Invoice & Activity List Search

LICENSEE DETAILS

10:37:29 AM 12/15/2023

Licensee Information

Name:	**DAURIA, ANTHONY ALBINO (Primary Name)**
Main Address:	***Private Address* *Private Address*** ***Private Address*** ***Private Address*** ***Private Address***

License Information

License Type:	**Standard Plans Examiner**
Rank:	**Plans Examiner**
License Number:	**PX4133**
Status:	**Current,Active**
Licensure Date:	**08/07/2018**
Expires:	**11/30/2025**

Special Qualifications	**Qualification Effective**
Plumbing	**08/07/2018**

Alternate Names

View Related License Information

View License Complaint

Division of State Fire Marshal

BUREAU OF FIRE STANDARDS AND TRAINING

Hereby Awards this

245604

FIRESAFETY INSPECTOR I

Certificate of Compliance

to

RYAN J MURPHY

Expires the 30th Day of September, 2025

By virtue of having met the requirements of Florida Statutes of the Rules and Regulation of the Division of State Fire Marshal.

State Fire Marshal

Bureau Chief

Director

DUPLICATE COPY

SECTION 11
SOLICITATION SUMMARY

The City of Delray Beach
100 N.W. 1st Avenue
Delray Beach, FL 33444

PURCHASING DIVISION

SOLICITATION SUMMARY

IMPORTANT NOTICE
The information you provide on this page will be read aloud at the PUBLIC OPENING for this Solicitation. It is VERY IMPORTANT that the summary information you provide below is exactly the same information contained in your Bid. If subsequent to the opening of Bids, the City determines that the information contained in the electronic version of your Bid is different from the information on this Solicitation Summary, the City reserves the right to deem your Bid NON-RESPONSIVE, and remove your Bid from further evaluation and consideration for contract award.

BID INFORMATION

Bid Number:	ITB No. 2024-041
Title:	Inspection, plan review and Development Review Services
Due Date and Time:	June 27, 2024, @ 2:00PM EST
Name of Bidder:	C.A.P. Government. Inc.
Address:	1910 N. Florida Mango Rd., West Palm Beach, FL 33409
Contact Person:	Carlos A. Penin, PE
Bid Amount:	$ 35,175.00
Authorized Signature:	
Date:	06/27/2024

By signing and submitting this Solicitation Summary, the Bidder affirms that the information provided above is an exact and correct summary of the information contained in the electronic version of the Bidder's Bid to the City of Delray Beach.

THIS SOLICITATION SUMMARY MUST BE SIGNED AND INCLUDED WITH YOUR SECURE ELECTRONIC BID SUBMITTAL THROUGH WWW.PERISCOPE S2G.COM.

Item Summary

Meeting Date: August 17, 2026

From:

Subject: **PUBLIC HEARING: Ordinance 2026-07: Second Reading:** Amending the City of Greenacres Budget for the fiscal year beginning October 1, 2025, and ending September 30, 2026, inclusive; providing for repeal of conflicting ordinances; providing for severability; and providing for an effective date. - Teri Beiriger, Director of Finance.

Background

Analysis

Financial Information

Legal

Staff Recommendation

Attachments:

1. Ord. 2026-07 FY 2026 3rd Budget Adj ord general funds and 305
2. Ord. 2026-07 FY 2026 3rd Budget Adjustment item summary 1st read

ORDINANCE NO. 2026-07

AN ORDINANCE ADOPTED BY THE CITY COUNCIL OF THE CITY OF GREENACRES, FLORIDA, AMENDING THE CITY OF GREENACRES' BUDGET FOR THE FISCAL YEAR BEGINNING OCTOBER 1, 2025, AND ENDING SEPTEMBER 30, 2026, INCLUSIVE; PROVIDING FOR REPEAL OF CONFLICTING ORDINANCES; PROVIDING FOR SEVERABILITY; AND PROVIDING FOR AN EFFECTIVE DATE.

WHEREAS, the City Council of the City of Greenacres, Florida adopted a budget for the 2025/2026 Fiscal Year; and

WHEREAS, the City Council has determined that an amendment needs to be made to the previously adopted Fiscal Year Budget; and

WHEREAS, the City Council deems approval of this Ordinance to be in the best interest of the residents and citizens of the City of Greenacres.

NOW, THEREFORE, BE IT ORDAINED BY THE CITY COUNCIL OF GREENACRES, FLORIDA, AS FOLLOWS:

Section 1. The City Council hereby amends the expenditures in the General Fund (001) fund, and expenditures in the Infrastructure Surtax (305) fund and the balances listed in attached Exhibit "A" and adopts such amendments to the Budget of the City of Greenacres for the Fiscal Year October 1, 2025, through September 30, 2026, inclusive.

Section 2. Repeal of Conflicting Ordinances.

All ordinances or parts thereof or parts of the Code conflicting or inconsistent with the provisions of this ordinance are hereby repealed.

Section 3. Severability.

If any section, part of a section, paragraph, sentence, clause, phrase or word of this Ordinance is for any reason held or declared to be unconstitutional, inoperative or void, such holdings of invalidity shall not affect the remaining portion of this Ordinance and it shall be construed to have been the legislative intent to pass the Ordinance without such unconstitutional, invalid or inoperative part therein, and the remainder of this Ordinance after the exclusion of such part or parts shall be deemed to be held valid as if such part or parts had not been included therein, or if this Ordinance or any of the provisions thereof shall be held inapplicable to any person, group of persons, property, kind of property, circumstances, or set of circumstances, such holdings shall not affect the applicability thereof to any other person, property or circumstances.

Section 4. Effective Date.

The provisions of this Ordinance shall become effective upon adoption.

Passed on the first reading this 3rd day of August 2026.

PASSED AND ADOPTED on the second reading this 17th day of August 2026.

Voted:

Chuck Shaw, Mayor

John Tharp, Deputy Mayor

Attest:

Voted:

Quintella Moorer, City Clerk

Peter Noble, Council Member, *District II*

Voted:

Judith Dugo, Council Member, *District III*

Voted:

Susy Diaz, Council Member, District IV

Voted:

Elisa Leheny, Council Member, *District V*

Approved as to Form and Legal Sufficiency:

_____

Glen J. Torcivia, City Attorney

FYE 9/30/2026
Exhibit "A"

Fund 001 General Fund

		Increase (Decrease)
Expense		
Land/ROW Acquisitions		
5280 10th Ave N (incl est closing cost)	001-30-31-61-3	$2,280,000
	Total Expense	**$2,280,000**
001 General Fund Change in Fund Balance		**($2,280,000)**
Playground	305-40-46-63-91	$710,691
YP Building		
	Total Expense	**$710,691**
305 Infrastructure Surtax Fund Balance		**($710,691)**

ITEM SUMMARY

MEETING DATE: August 17, 2025

FROM: Teri Lea Beiriger, Director of Finance

SUBJECT: Ord. No. 2026-07 Budget Adjustment – General Fund, and Infrastructure Surtax - 032 City Park

BACKGROUND

Council Policy No. 6 requires City Council action to authorize budget adjustments between cost centers, departments, and funds. A budget adjustment is required to account for the following un-budgeted items: the land purchase of 5280 10th Avenue N and build out of the Youth program playground. This affects the general fund (001) and the infrastructure fund (305) only.

The land purchase will be at 5280 10th Ave N in the amount of approximately $2,538,000 this includes an estimate for closing cost. This will affect fund balance of the general fund.

The playground is to be built near the youth program building – 032 City Parks improvement project - for approximately $710,691.

ANAYSIS

Ordinance 2026-07 is to authorize the net budget adjustment for the total amount of $3,248,691 that documents the movement of the funds from the general funds balance and infrastructure balance to cover the unbudgeted item.

FINANCIAL INFORMATION

The proposed ordinance increases the general fund expenditure by $2,538,000 and the infrastructure fund by $710,691 in FY 2026.

LEGAL

The proposed Budget Amendment has been prepared in accordance with the applicable State Statues and City Code Requirements

STAFF RECOMMENDATION

Approval of Ordinance 2026-07.

Item Summary

Meeting Date: August 17, 2026

From: Monica Powery, Director

Subject: **Resolution No. 2026-40:** Approving the design-build amendment between the City of Greenacres and Kaufman Lynn Construction, Inc. for the Municipal Operations Center; establishing a guaranteed maximum price of $33,681,849.00; authorizing the appropriate city officials to execute the amendment. - Monica Powery, Director of Purchasing

Background

On May 5, 2025, the City Council approved Resolution No. 2025-18 authorizing the award of RFQ No. 24-021, Progressive Design-Build for the Emergency Operations Center, to Kaufman Lynn Construction, Inc. The project has since been renamed the Municipal Operations Center. Under the progressive design-build delivery method, Kaufman Lynn has completed the design development and pricing process necessary to establish the Guaranteed Maximum Price (GMP) and advance the project into the construction phase.

Analysis

The proposed Design-Build Amendment establishes a Guaranteed Maximum Price of $33,681,849.00 and incorporates the approved construction documents, qualifications and assumptions, construction schedule, allowances, commissioning requirements, project staffing, and related exhibits into the original Design-Build Agreement. The GMP includes a $387,500.00 allowance for anticipated permit fees, a $416,371.00 Contractor's Construction Contingency, and a $268,626.00 City Contingency. Builder's Risk insurance will be purchased directly by the City and is excluded from the GMP. The construction schedule provides for City occupancy within 491 days, Substantial Completion within 521 days, and Final Completion within 551 days from commencement of the work. The Amendment also establishes liquidated damages of $4,931.00 per day, subject to a $1,000,000.00 cap; requires open-book documentation and City approval for allowance and construction contingency use; and includes detailed commissioning, closeout, audit, bond, change-order, and owner-direct purchase provisions. Once trade buyout is complete, the first $500,000.00 of aggregated buyout savings will be added to the Construction Contingency, with savings above $500,000.00 credited 100% to the City. Any unused Construction Contingency

remaining at final accounting will be returned 75% to the City and 25% to the Design-Builder.

Financial Information

Guaranteed Maximum Price for the construction phase is $33,681,849.00. Builder's Risk insurance is excluded from the GMP and will be purchased directly by the City. The GMP Summary identifies additional estimated Owner items outside the GMP, resulting in an estimated total project cost of $34,474,849.00. Funds are available in Capital Improvement Program account 301-50-55-62-26 (CIP 301-238).

Legal

The proposed Design-Build Amendment has been reviewed for legal sufficiency and form by the City Attorney.

Staff Recommendation

Approval of Resolution No. 2026-40 authorizing execution of the Design-Build Amendment with Kaufman Lynn Construction, Inc., establishing a Guaranteed Maximum Price of $33,681,849.00, acknowledging that Builder's Risk insurance will be purchased directly by the City and excluded from the GMP, and authorizing the construction phase of the Municipal Operations Center.

Attachments:

1. Resolution 2026-40 MOC Design Build Amendment and GMP
2. KL - Greenacres - DB Amendment

RESOLUTION NO. 2026-40

A RESOLUTION ADOPTED BY THE CITY COUNCIL OF THE CITY OF GREENACRES, FLORIDA, APPROVING THE DESIGN-BUILD AMENDMENT BETWEEN THE CITY OF GREENACRES AND KAUFMAN LYNN CONSTRUCTION, INC. FOR THE MUNICIPAL OPERATIONS CENTER; ESTABLISHING A GUARANTEED MAXIMUM PRICE OF $33,681,849.00; AUTHORIZING THE APPROPRIATE CITY OFFICIALS TO EXECUTE THE AMENDMENT; PROVIDING FOR AN EFFECTIVE DATE.

WHEREAS, On May 5, 2025, the City Council adopted Resolution No. 2025-18 approving an agreement with Kaufman Lynn Construction, Inc. for progressive design-build services pursuant to RFQ No. 24-021; and

WHEREAS, the project, formerly identified as the Emergency Operations Center, is now referred to as the Municipal Operations Center; and

WHEREAS, in accordance with the Design-Build Agreement, Kaufman Lynn Construction, Inc. has prepared the approved design, Guaranteed Maximum Price, construction schedule, and related documents necessary to proceed with the Construction Phase of the project; and

WHEREAS, the Design-Build Amendment establishes a Guaranteed Maximum Price of Thirty-Three Million Six Hundred Eighty-One Thousand Eight Hundred Forty-Nine Dollars and Zero Cents ($33,681,849.00); and

WHEREAS, the Guaranteed Maximum Price includes an allowance for anticipated permit fees in the amount of $387,500.00, a Contractor's Construction Contingency in the amount of $416,371.00, and a City Contingency in the amount of $268,626.00; and

WHEREAS, the City shall purchase Builder's Risk insurance for the Project, and the cost of such insurance is excluded from the Guaranteed Maximum Price; and

WHEREAS, the Design-Build Amendment establishes the Construction Phase schedule, including City occupancy at 491 days, Substantial Completion at 521 days, and Final Completion at 551 days from commencement of the work; and

WHEREAS, the City Council finds that approval of the Design-Build Amendment and authorization to proceed with the Construction Phase serves a valid public purpose and is in the best interests of the City.

NOW, THEREFORE, BE IT RESOLVED BY THE CITY COUNCIL OF THE CITY OF GREENACRES, FLORIDA, THAT:

SECTION 1. The City Council hereby approves the Design-Build Amendment between the City of Greenacres and Kaufman Lynn Construction, Inc. for the Municipal Operations Center, establishing a Guaranteed Maximum Price of $33,681,849.00 and authorizing the Construction Phase of the project.

SECTION 2. The City Council authorizes the appropriate City Officials to execute the Design-Build Amendment and take such actions as are necessary to implement the Amendment in accordance with its terms.

SECTION 3. This Resolution shall be effective upon its adoption.

RESOLVED AND ADOPTED this 17th day of August 2026

	Voted:
Chuck Shaw, Mayor	**John Tharp,** *Deputy Mayor*
Attest:	
	Voted:
Quintella Moorer, City Clerk	**Peter Noble,** Council Member, *District II*
	Voted:
	Judith Dugo, Council Member, *District III*
	Voted:
	Susy Diaz, Council Member, *District IV*
	Voted:
	Paula Bousquet, Council Member, *District V*

Approved as to Form and Legal Sufficiency:

Glen J. Torcivia, City Attorney

DESIGN-BUILD AMENDMENT TO AGREEMENT FOR DESIGN-BUILD SERVICES

This Design-Build Amendment to Design-Build Services Agreement ("Amendment") is entered into this 17th day of August, 2026 ("Effective Date"), by and between the **City of Greenacres** ("Owner" or "City"), a municipality, whose address is 5800 Melaleuca Lane, Greenacres, Florida, 33463, and **Kaufman Lynn Construction, Inc.** ("Design-Builder" or "DB"), a Florida corporation, whose address is 3185 S. Congress Avenue, Delray Beach, Florida, 33445 (all of whom shall collectively be referred to herein as the "Parties" or a "Party" if referring to only one of them).

RECITALS

WHEREAS, on about May 5, 2025, the Owner and Design-Builder entered into a contract for the design, construction, of the New Municipal Operations Center ("Project") pursuant to RFQ #24-021 ("Design-Build Agreement"); and

WHEREAS, as required by the Design-Build Agreement, Design-Builder has prepared the design for the Project approved by Owner and the Guaranteed Maximum Price for the Project, as well as other information and documents, which are stated herein or attached hereto; and

WHEREAS, the Guaranteed Maximum Price and documents attached hereto are intended to encompass the Design-Build Amendment as provided in the Design-Build Agreement; and

WHEREAS, Owner hereby authorizes Design-Builder to proceed with the Construction Phase, as more specifically set forth herein; and

WHEREAS, Owner and Design-Builder agree that the defined terms used herein shall be given the same meaning as set forth in the Design-Build Agreement; and,

WHEREAS, the Owner finds that entering this Amendment with the Design-Builder serves a valid public purpose and is in the best interests of the City of Greenacres.

NOW THEREFORE, for good and valuable consideration, the receipt and sufficiency of which is hereby acknowledged, the Parties agree as follows:

AMENDMENT

1. The foregoing Recitals are true and correct and are incorporated by reference into this Amendment as if fully set forth herein as operative terms of this Amendment.

2. The Design-Build Agreement remains in full force and effect and is amended only to the extent expressly set forth in this Amendment. In the event of a conflict of inconsistency between the Design-Build Agreement and this Amendment, this Amendment shall control. All capitalized and defined terms of the Design-Build Agreement and Design-Build Documents are incorporated herein by reference and shall herein have the same meaning.

3. The Guaranteed Maximum Price ("GMP") is $33,681,849.00 and the GMP summary, along with Design-Builder's Schedule of Values for all of the Cost of Work, are attached hereto as Exhibits "A". If a change in Work and/or an adjustment to the GMP or Construction Schedule is required due to, in whole or in part, an act, omission, breach or negligence on the part of Design-Builder or any of its employees, agents, Subcontractors, suppliers or other lower tiers then, to the proportional extent of such act, omission, breach or negligence, and further subject to Design-Builder's rights to use Contingency as detailed herein, the Work or services required to implement the change in Work shall be performed by Design-Builder and its Subcontractors, at no cost to Owner and there shall not be an adjustment to the GMP or Construction Schedule.

4. An Allowance for anticipated permit fees in the amount of $387,500.00 is included within the GMP.

5. A Contractor's Construction Contingency in the amount of $416,371.00 is included within the GMP for the Design-Builder's use as set forth herein.

6. A City Contingency in the amount of $268,626.00 is included within the GMP for use by the City per Article 6.4 of the Design-Build Agreement.

7. As part of the Guaranteed Maximum Price, Design-Builder's fixed General Conditions/General Requirements Costs are identified as part of the attached Exhibit "A."

8. A list of the approved Construction Documents used as the basis for the GMP, and which shall become a part of the Project Documents, is attached hereto as Exhibit "B."

9. The agreed upon Qualifications and Assumptions upon which the GMP is based are attached hereto as Exhibit "C". The parties agree that nothing in Exhibit "C" shall modify or diminish Design Builder's obligations to provide a complete (in accordance with the agreed upon Construction Documents), functional, and fully code-compliant Project.

10. The Construction Schedule, attached hereto as Exhibit D, shall provide for the following agreed upon critical date durations:

a. City Occupancy Date – 491 days from Commencement of the Work (per 2.3.2 Article of the Design-Build Agreement);
b. Substantial Completion – 521 days from Commencement of the Work (per 2.3.2 Article of the Design-Build Agreement);
c. Final Completion – 551 days from Commencement of the Work (per 2.3.2 Article of the Design-Build Agreement);
d. Guaranteed Completion Date – 551 days from Commencement of the Work (per 2.3.2 Article of the Design-Build Agreement).
e. The Construction Schedule shall also show interim milestone dates for, at a minimum, permit issuance, mobilization, dry-in, permanent power availability, major MEP rough-in completion, commissioning start, and owner training commencement and commissioning activities set forth in Section 30 below.
f. If Design-Builder falls behind the approved Construction Schedule by 14 days or any interim milestone through fault not attributable to the City, Design-Builder shall submit and implement a written recovery plan within seven (7) days after request by the City or after Design-Builder becomes aware of such slippage, at no additional cost to the City.
g. Failure to include an activity in the Construction Schedule shall not excuse Design-Builder from timely performance of such activity if required by the Project Documents.

11. The Second sentence of Section 23.9 is deleted and replaced as follows: "The GMP shall be increased by an amount equal to the daily general conditions four thousand nine hundred thirty-one dollars and 00 cents ($4,931.00) multiplied by the number of days of delay (as determined above) plus, after thirty (30) days of delay to the critical path for which Design-Builder would otherwise be entitled to an extension of time hereunder, Design-Builder shall be also entitled to any increased labor, material, or equipment costs that are directly attributable to the delay commencing on day 31, except to the extent that the DB has caused or contributed to the delay or has failed to take reasonable steps to mitigate the impacts (including costs) of the delay. Notwithstanding anything to the contrary, there shall be no compensation for concurrent delay.

12. The Allowance Items and Allowance Values (as stated in Exhibit "E"), and statement of their basis, are identified as part of Design-Builder's Allowances List attached hereto as Exhibit "E." Design-Builder shall obtain the City's written approval prior to committing or expending any allowance amount. Each allowance shall be reconciled to actual cost on an open-book basis with supporting documentation, and any unused allowance balance shall be credited to the City. Any fee, insurance costs, bond costs, SDI costs, or other markup that has been applied to an Allowance Value in the GMP shall be returned to Owner on any Allowance Item underruns.

13. The Parties' stipulated, non-auditable rates for Design-Builder's Fee, Design-Builder's Insurance, Design-Builder's Payment and Performance Bond, and Design-Builder's Subcontractor Default Insurance/Subcontractor Bonds are as follows:

a. Design-Builder's Fee – 5.0%

b. Design-Builder's Liability Insurance (other than Builder's Risk) – 1.45%
c. Design-Builder's Payment and Performance Bond 1.11%
d. Design-Builder's Subcontractor Default Insurance – 1.58%
e. General Conditions Costs – $2,426,644.00
f. Daily General Conditions – $4,931.00 per day

For avoidance of doubt, the City's audit, inspection, and review rights under the Design-Build Documents, including without limitation rights relating to accounting records, buyout savings, Cost of the Work, allowances, contingency usage, credits, rebates, refunds, and change documentation, shall continue to apply notwithstanding the stipulated nature of the percentages and rates set forth in this Section; provided however, where stipulated rates have been agreed upon, the audit shall be limited to the application of the rate and not to the underlying costs that make up the rate.

14. The stipulated percentage of Design Builder's Fee for Change Orders and Construction Change Directives (exclusive of general conditions, general requirements, insurance, and SDI and bond costs) shall be the percentage rate set forth in Section 13(a), above. The foregoing percentage shall apply only to additive changes in the Work approved in writing by the City and shall not apply to DB Construction contingency draws, correction of defective or non-conforming Work, redesign required due to Design-Builder error or omission, or costs otherwise not reimbursable under the Design-Build Documents. Design Builder's Fee shall not be reduced for deductive Change Orders and Construction Change Directives.

15. The City shall purchase Builder's Risk insurance, and the costs thereof are not Cost of the Work, and are excluded from the GMP. Notwithstanding the terms of the Design-Build Agreement to the contrary, with respect to the Builder's Risk Deductibles, the City shall assume responsibility to pay deductibles for a covered loss to the proportional extent the underlying loss is not caused by the Design-Builder or anyone working for, or under, the Design-Builder. For clarification, and by way of example and not as a limitation, in the event there is a covered loss arising from the impact of a hurricane, the City shall have the primary obligation to pay the Named Wind Storm deductible under the Builder's Risk Policy, however, if Design-Builder's failure to properly secure the Project site in advance of the storm caused a quarter of the value of the covered loss, than Design-Builder shall be responsible to pay for a quarter of the deductible amount.

16. Owner Direct Purchases. Section SC 7.2 of the Design-Build Agreement is supplemented with the following: In connection with the City Furnished Materials/Direct Purchase Program described in this Section, and in addition to the requirements set forth above: (a) City shall provide the applicable vendor with a copy of City's Florida Consumer's Certificate of Exemption and, where required to substantiate the exemption, a Certificate of Entitlement in the form required by Rule 12A-1.038, Florida Administrative Code; (b) no City Furnished Material shall be purchased directly by City from DB, or from the Subcontractor or Trade Contractor engaged to install the material in question, unless such direct purchase from the installing party is expressly permitted under applicable law; (c) DB shall promptly provide City with such additional documentation as City may reasonably request to support the tax-exempt status of a given direct purchase, the corresponding GMP credit, and City's audit trail for City Furnished Materials generally; (d) except solely for City's obligations to issue the Purchase Order directly to the vendor and to remit payment directly to the vendor, DB's responsibilities with respect to City Furnished Materials — including but not limited to coordination, scheduling, receiving, unloading, inspection, storage, protection, security, handling, installation, testing, start-up, commissioning, punchlist, warranty management, and correction of defective Work — shall be identical to DB's responsibilities for materials DB procures directly, and shall be performed to the same standard of care; (e) the Program shall not relieve DB of its responsibility to deliver a complete, coordinated, code-compliant, and fully functional Project, and no direct purchase of City Furnished Materials shall excuse any delay, omission, coordination gap, scope gap, incompatibility, warranty issue, or additional cost that DB could have avoided through proper planning, verification, receiving, storage, protection, or installation, regardless of any review, approval, comment, evaluation, or participation by City in the direct purchase process; provided however that the

foregoing does not relieve the City of its obligation to timely administer payment for any City Furnished Materials so as to cause no delay to the critical path of the Project; and (f) nothing in this Section obligates City to make any direct purchase, and City may decline to exercise, or may discontinue, the Program, in whole or in part and at any time, if City determines in its discretion that the anticipated Sales Tax savings do not justify the associated administrative burden or risk.

17. Design-Builder Warranty of Completeness of GMP. Design-Builder represents and warrants that it has carefully reviewed the Design-Build Documents, investigated the Project requirements to the extent required by the Design-Build Documents, coordinated the design and pricing information used to establish the GMP, and included within the GMP all costs reasonably necessary to achieve Final Completion of a complete (in accordance with the Contract Documents), code-compliant, and fully operational Project. The Design-Builder shall not be entitled to any increase in the GMP or extension of time on account of errors, omissions, inconsistencies, lack of coordination, scope gaps, or estimating assumptions that the Design-Builder knew or reasonably should have known prior to execution of this Amendment but shall be allowed to use the Construction Contingency as set forth herein.

18. Construction Contingency Controls.

a. The Construction Contingency is included within the GMP solely for unforeseen circumstances of the type permitted by the Design-Build Agreement as amended herein and shall be used only with the City's prior written approval, which may be granted or withheld in the City's reasonable discretion.

b. The Construction Contingency shall not be used for: (i) rework, to the extent the Design-Builder can identify the responsible party; (ii) defective Work; (iii) costs arising from the Design-Builder's failure to comply with the Project Documents; or (iv) costs otherwise excluded from Cost of the Work under the Design-Build Agreement.

c. Each request to use the Construction Contingency shall include sufficient backup documentation, including a description of the event, affected scope, reason the cost was not included elsewhere in the GMP, subcontractor or vendor support, and the impact, if any, on the Construction Schedule. The Construction Contingency shall not be replenished. Change Orders and Construction Change Directives shall not include additional markup to replenish the Construction Contingency amounts. Design-Builder shall not charge markup on Construction Contingency use because Design-Builder's Fee, insurance costs, bond costs, SDI costs and all other markups on the Construction Contingency are already included in the GMP.

19. Buyout Savings and Unused Contingency.

a. Once buyout is complete, all aggregated trade buyout savings exceeding $500,000.00 shall be credited to Owner 100% via a deductive Change Order to the GMP. The first $500,000.00 of aggregated trade buyout savings shall be added to Construction Contingency.

b. No trade buyout savings shall be reallocated to increase Design-Builder's Fee or any percentage-based markup.

c. Any unused portion of the Construction Contingency remaining at Final Completion and final accounting shall be returned seventy-five percent (75%) to the City and twenty-five percent (25%) to Design Builder.

20. Delay Cost Documentation. As a condition precedent to any request for additional compensation arising from delay, Design-Builder shall also provide contemporaneous schedule fragnet analysis, mitigation efforts, and a demonstration that the claimed impact affected the critical path and could not reasonably have been avoided or mitigated. No extension of time or increase in the GMP shall be due for concurrent delay attributable in whole or in part to Design-Builder or its subcontractors.

21. Redesign to Maintain Budget. Design-Builder shall not be entitled to an increase in the Design Fee for any redesign required due to incomplete coordination, estimating error, design inefficiency, omitted scope, or failure to design to budget but shall be allowed to use Construction Contingency to the extent permitted herein.

22. Audit and Open-Book Support. Notwithstanding any characterization of certain percentages or rates as non-auditable, the City shall have the right, upon reasonable notice, to review and audit all books, records, contracts, subcontracts, quotations, bid tabulations, takeoffs, contingency logs, allowance documentation, invoices, payment applications, the application of staff's stipulated rates, the application of the insurance rates to the Cost of Work, the application of the bond rate to the Cost of Work, the application of the SDI rate to the Cost of Work, owner-

direct purchase support, and other documents reasonably necessary to verify the GMP, Cost of the Work, savings, credits, and changes to the Work. Design-Builder shall include equivalent audit-right provisions in its subcontracts and purchase orders for the Project. Any overbilling or unsupported charge shall be promptly credited to the City.

23. Self-Perform and Affiliate Awards. Design-Builder shall not self-perform any trade work, nor award any portion of the Work to an affiliate or related entity, without the City's prior written approval after full disclosure of the proposed scope, pricing basis (including three separate bids where commercially reasonable), labor burden, equipment rates, overhead, profit, and competitive benchmark information reasonably requested by the City. Any approved self-performed or affiliate work shall remain subject to audit and shall be priced at rates no greater than fair market value.

24. Commissioning and Closeout as Conditions to Completion. Final Completion shall be subject to satisfaction of the closeout, testing, training, and commissioning requirements of the Design-Build Documents. Without limiting the foregoing, Design-Builder shall timely provide all record drawings, O&M manuals, warranties, training sessions, start-up and testing reports, equipment demonstrations, commissioning documentation, attic stock, keys, access credentials, and other closeout materials required for a complete and operational turnover of the Project. The City shall not be required to deem the Project Substantially Complete if critical building systems or life-safety, emergency power, HVAC controls, communications, security, or other operational systems are not functioning to allow beneficial use of the Project. Design Builder shall be responsible for obtaining all permits, coordination with all utilities, including FPL, and shall provide an agency coordination plan. Design Builder shall be responsible for commissioning and functionality of all systems.

25. No Waiver by Review or Approval. The City's review, comment upon, approval of, or failure to reject any schedule, nontechnical submittal, buyout, allowance use, contingency request, payment application, change proposal, or other submission shall not relieve the Design-Builder of responsibility for compliance with the Design-Build Documents and shall not constitute acceptance of defective, incomplete, non-conforming, or under-scoped Work.

26. Utilities. The City is responsible for the direct cost of utilities. There shall be no change in GMP or Construction Schedule for foreseeable permitting/utility coordination issues that a competent Florida design-builder should have identified pre-GMP Amendment, but Design-Builder shall be allowed to use Construction Contingency to the extent permitted herein.

27. Waiver of Consequential Damages. In addition to the carveouts set forth in Section GC73 of the Design Build Agreement, the parties agree that the following are also excluded from the waiver set forth in Section GC73 (i) any of the Design-Builder's indemnity obligations with respect to personal injury and property damage, and (ii) liquidated damages due to the City from the Design-Builder. Notwithstanding the foregoing, it is agreed that the following are not considered to be consequential damages: (i) costs of replacement design/procurement, (ii) costs to complete or correct defective Work, and (iii) statutory fines or penalties assessed as a result of Design-Builder's acts or omissions.

28. The following is added to GC 65.1:

a. Approved Commissioning Plan and Final Commissioning Report. Attached as Exhibit F is a Commissioning Plan Design-Builder shall furnish a Final Commissioning Report documenting the results of all commissioning activities, deficiencies identified, and confirmation that all deficiencies have been resolved to the City's satisfaction.

b. Pre-functional and Functional Testing. DB shall complete pre-functional checklists and functional performance testing for all commissioned systems and equipment, with results documented and submitted to the City for review and acceptance.

c. Integrated Systems Testing. DB shall complete integrated systems testing demonstrating the coordinated operation of all interdependent building systems (including but not limited to fire alarm, life safety, security, HVAC, electrical, and low-voltage systems) acting together as designed, with results documented and submitted to the City.

d. Generator/Load-Bank Testing. DB shall complete load-bank testing of the emergency generator(s) at the manufacturer's rated capacity, with test results, including run-time, transfer, and performance data, submitted to the City for review and acceptance.

e. UPS/ATS/Fuel System Testing. DB shall complete testing of the uninterruptible power supply, automatic transfer switch(es), and fuel storage/delivery systems, including simulated power failure and transfer sequences, with results documented and submitted to the City.

f. Lighting System Testing. DB shall complete testing of all interior and exterior lighting systems, including emergency/egress lighting, lighting controls, and any daylight-harvesting or occupancy-sensor systems, confirming proper operation in accordance with the Project Documents.

g. HVAC Testing, Adjusting, and Balancing (TAB) and Controls Optimization. DB shall complete TAB of all HVAC systems and shall complete optimization and sequence-of-operation verification of the building automation/controls system, with a final TAB report submitted to the City.

h. Cybersecurity and Access-Control Turnover for Electronic Systems. DB shall complete turnover of all electronic security, access-control, and networked building systems, including delivery of administrator credentials, system documentation, cybersecurity configuration details, and any required password/credential transfer protocols, to the City's designated representative.

i. Training for City Operations Staff. DB shall complete all training of City operations, maintenance, and security personnel on the operation and maintenance of building systems and equipment, with such training video and audio recorded and one copy of the recording provided to the City as required by the General Conditions.

j. Spare Parts and Attic Stock. DB shall deliver to the City all spare parts, attic stock, and special tools required under the Project Documents, with an itemized inventory list acknowledged by the City's Project Manager.

k. O&M Manuals in Digital and Hard Copy. DB shall furnish complete operations and maintenance manuals, in both digital and hard-copy (bound) format, for all equipment and systems, as required under the General Conditions.

l. As-Builts / Record BIM / GIS-Compatible Deliverables, if Applicable. DB shall furnish complete record (as-built) drawings and specifications, and, to the extent required under the Project Documents, record BIM models and GIS-compatible data deliverables, in both electronic and hard-copy format where required.

m. Warranties Log. DB shall furnish a comprehensive warranties log identifying all manufacturer, Subcontractor, and DB warranties applicable to the Project, including warranty commencement dates, durations, and points of contact, together with copies of all underlying warranty documents.

n. Final Asset Registry. DB shall furnish a final asset registry identifying all major equipment and systems installed on the Project, including manufacturer, model and serial numbers, locations, and installation dates, in an excel format.

29. Section 2.3.24 of the Design Build Agreement is clarified to include design documents, BIM models, specs, calculations, and related work product for construction, operation, maintenance, repair, additions, and completion by others. The reference to “amounts that are due” is hereby changed to “undisputed amounts that are due”.

30. To GC Section 59.13, the following is added “Within seven (7) days of Design-Builder learning of an occurrence of an event that gives rise to a basis for a Change Order that will be initiated by the Design-Builder (and not the City), Design-Builder shall notify the City of such an occurrence in writing. Within twenty-one (21) days of such an event, or a longer period if mutually agreed upon by the parties in writing, Design-Builder shall provide all available supporting documentation, pricing, information and detail to the City for purposes of the City’s review and consideration of Design-Builder’s Change Order request. Design-Builder’s failure to provide the initial notice of the supporting information in the foregoing time periods, respectively, shall be deemed a waiver by the Design-Builder to the right to receive such adjustment and of all claims related thereto. Further, with respect to Change Orders initiated first by the Design-Builder, execution of a Change Order shall also serve as release and waiver by the Design-Builder of any and all Design-Builder initiated Change Order requests not related to the Change Order, including, but not limited to, claims for equitable adjustments, except for (i) those Claims/Change Order requests timely and properly made in writing in accordance with the Design-Build Agreement to the City prior to the effective date of the Change Order, or (ii) those Claims/Change Orders for which contractual notice period has not yet run.

31. Section 27.3 of the Design Build Agreement is deleted and replaced with the following “DB shall require the Architect to also maintain professional liability insurance during the Design Phase and during the Construction Phase, and for 7 years following Substantial Completion of the Project at a $3,000,000 each claim and

$5,000,000 aggregate basis."

32. Design Builder shall not transfer any buyout savings until after all buyout has been completed and aggregated in accordance with Section 6.3 of the Design Build Agreement. City may attend openings, negotiations with Trade Contractors and must consent to awards, scope splits, and any negotiations. All buyout shall be open-book.

33. The following language is deleted from Section 23.7 "and an adjustment in the GMP for a compensable delay as provided in this Section.". Adverse Weather shall not entitle Design Builder to an adjustment in the GMP, but Design-Builder may be entitled to an extension of the Contract Time in accordance with the Design-Build Documents.

34. Receipt of lien waivers from Design-Builder's Subcontractors and other lower tiers having rights against the bond shall be a condition precedent to the making of final payment to Design Builder.

35. The reference to "to the extent caused by" in Section 26.1 is amended to state "to the proportional extent caused by".

36. Any disputes in connection with the Design Build Agreement and/or the Project shall be resolved in a court of competent jurisdiction in the Couty where the Project is located.

37. Design Builder shall be solely responsible for any and all design issues in connection with the Project. Owner hereby disclaims all warranties, including, without limitation, *Spearin*, in connection with any information provided by the Owner.

38. It is acknowledged that all Parties participated in the drafting of this Amendment and this language shall not be presumptively construed either in favor or against any of the Parties.

39. The Parties to this Amendment may execute the Amendment electronically and/or in counterparts, all of which shall constitute one agreement and be deemed an original.

40. The Design-Builder shall provide the Project with the DB staff identified in Exhibit "G" attached hereto.

41. The daily amount of Liquidated Damages agreed upon by the parties pursuant to GC 72 of the General Conditions to the Design-Build Agreement is Four Thousand Nine Hundred Thirty-One Dollars and Zero ($4,931.00) per day. Design Builder's total liability for Liquidated Damages under the Design Build Agreement shall be $1,000,000.00, as may be adjusted by Change Order. If, for any reason, the liquidated damages as set forth herein above are deemed unenforceable by a court of competent jurisdiction, the Owner shall be entitled to receive all of its actual damages incurred by the Owner as a result of the Design-Builder's failure to timely achieve Substantial Completion Dates as set forth above

42. The Parties further warrant and represent that: (1) they have full authority to enter into this Amendment; (2) no promise, inducement or agreement not expressed in this Amendment has been made; (3) this Amendment has been carefully read and they know the contents thereof; (4) they have either consulted with legal counsel or have chosen not to do so; (5) they (or their representative executing this Amendment) are of legal age and competent to execute this Amendment; and (6) in executing this Amendment, they have not been influenced by any misrepresentation of any other Party.

43. In the event that any provision of this Amendment is determined to be unenforceable, said determination shall not affect the remaining provisions hereof which shall remain in full force and effect. Any section or portion of a section so declared to be unenforceable shall, if possible, be construed in a manner which will give effect to the terms of such section or portion of a section to the fullest extent possible while remaining enforceable.

44. The Design-Builder and the City shall utilize administrative forms, including Requests for

Information, Change Orders, Submittals, and Transmittals, generated and executed within the Procore project management software; however, any standard terms and conditions set forth in such forms shall not supersede the procedures and requirements set forth in the Design Build Documents.

45. Design-Builder shall provide payment and performance bonds 7 days prior to performing work at the site.

46. COERCION OF LABOR AND SERVICES. The Design-Builder, by signing this Amendment, as set forth below, attests that the Design-Builder does not use coercion for labor or services as defined in section 787.06, Florida Statutes, as amended from time to time.

47. The Design-Builder shall maintain reasonable procedures for documenting personnel present at the Project consistent with customary construction industry practices. Each Subcontractor performing Work at the Site shall submit a daily report through Procore identifying the Subcontractor, the trade or scope of Work being performed, and the number of its personnel present at the Site that day. Each report shall be submitted by the Subcontractor's superintendent, foreman, or other on-site supervisory representative and incorporated into the Design-Builder's daily report. The Design-Builder shall post signage directing visitors and other non-trade personnel who are not regularly assigned to the Project to report to the Project field office upon arrival and sign the visitor log. The visitor log shall include, to the extent reasonably obtainable, the individual's printed name, company or entity represented, date, time of arrival, and time of departure. Routine delivery personnel, couriers, material and equipment vendors, service technicians, governmental authorities, building officials, inspectors, emergency responders, utility personnel, and other persons entering the Site temporarily in connection with deliveries, pickups, inspections, testing, governmental functions, utility services, emergencies, or similar incidental purposes shall not be required to sign in. The parties acknowledge that the Site is an active construction project and that the Design-Builder cannot guarantee that every individual entering or leaving the Site will be identified or recorded by name. The Design-Builder's implementation and reasonable administration of the Procore daily reporting and visitor sign-in procedures described above shall satisfy its obligations under this Section. The Design-Builder shall maintain the Procore daily reports and visitor logs in a legible and organized manner for the duration of the Project and shall make them available to the Owner upon reasonable request. The failure of any individual worker, visitor, delivery person, governmental representative, inspector, vendor, or other Site entrant to personally sign a log shall not constitute a breach by the Design-Builder.

48. The design for the Project job sign, as discussed in Section GC 69, shall be submitted to Owner for approval prior to submitting such sign for manufacturing.

49. The reference in Section 1.2.15 to City Manager is amended to include his/her authorized designee.

50. The SDI Policy shall provide coverage in the event that a Trade Contractor is enrolled in, or insured by, the SDI Policy defaults on its obligations under its respective Trade Contract. DB's SDI Policy shall have a direct cost limit of $25,000,000 per occurrence and $50,000,000 in the annual aggregate. DB is solely responsible to pay the deductibles and premiums applicable to the SDI Policy. Owner shall have no responsibility to pay, or otherwise satisfy, the deductibles or premiums applicable to the SDI Policy. The SDI Costs are those amounts that Owner shall pay to DB to insure its Trade Contractors under the SDI Policy, which shall be calculated as a rate of (1.58%) of enrolled Trade Contract values ("SDI Rate"). The percentage agreed to be used for the SDI rate is not subject to audit. DB may only charge Owner SDI Costs for a Trade Contractor that that is covered, and insured, by the SDI Policy and such SDI Costs shall be calculated by multiplying the Trade Contract sum of the Trade Contractor that is covered and insured by the SDI Policy by the SDI Rate. Contractor shall provide Owner with a SDI endorsement that evidences Trade Contractors are covered, and insured by, the SDI Policy.

51. The parties agree to use change orders in the form set forth as Exhibit H. The parties also agree to the forms in the Miscellaneous Forms Composite Exhibit I.

52. References in the Design-Build Agreement to "Emergency Operations Center" are changed to "Municipal Operations Center".

53. All material, equipment, or other special warranties required by the Design-Build Documents shall be issued in the name of the City, to the extent possible or, shall be assigned (if assignable) to the City at no additional cost and shall commence at the time of Substantial Completion.

54. The last sentence of Section 7.1.2 (Construction Phase) is replaced with the following "The DB's Fee will be paid each month proportionally on a percent complete basis of the Work in place that month, less retainage in an amount equal to five percent (5%) of the DB's Fee". Further, the parties agree that the elements of Project expenses set forth in Sections 6.6.2, 6.6.6, 6.6.7, 6.6.8, 6.6.9, 6.6.10, 6.6.11, 6.6.12 and 6.6.13 of the Design-Build Agreement are all included in Design-Builder's lump sum General Conditions costs and/or General Requirements costs and shall be considered a Cost of the Work under Article 8 of the Design-Build Agreement instead of as a part of Design-Builder's Fee.

IN WITNESS WHEREOF, the Owner and Design-Builder have made and executed this Amendment to the Design-Build Agreement as of the day and year first above written.

(Signature Page Follows)

CITY OF GREENACRES

ATTEST:

By: _____
Chuck Shaw, Mayor

By:_____
Quintella Moorer, City Clerk

Approved as to legal sufficiency and form:

By:_____
Glen J. Torcivia, City Attorney

Design-Builder: **KAUFMAN LYNN CONSTRUCTION, INC.**

By:_____

Print Name:_____

Print Position:_____

[CORPORATE SEAL]

STATE OF _____)
COUNTY OF _____)

THE FOREGOING instrument was acknowledged before me by means of ___ physical presence or ___ online notarization on this ____ day of _____ 2026, by _____, as the _____ [title] of **Kaufman Lynn Construction, Inc.**, who is personally known to me or who has produced_____ as identification, and who is personally known to me or who has produced_____ as identification, and who did take an oath under penalty of perjury that the facts stated with regard to section 787.06, Florida Statutes, are true and correct, and that he or she is duly authorized to execute the foregoing instrument and bind **Kaufman Lynn Construction, Inc.**, to the same.

Notary Public: _____

Print Name: _____

My commission expires: _____

Exhibit A

GMP Summary

Project Data

Project Name	**Greenacres Municipal Operations Center**	**Deliverable**	**GMP 8/10/26**
Location	5770 Melaleuca Ln, Greenacres, FL 33463	**Owner**	**City of Greenacres**
Plan Set Date	See Drawing Log	**Architect**	**Song & Associates**
Gross Project Area (Square Feet)	40826	**Document Level**	**Permitting Addendum #3**

Div	Description			Total Cost	$ / GSF	% / Total
1.1	GENERAL REQUIREMENTS		$	501,084	$ 12.27	1.49%
2	SITEWORK		$	4,324,885	$ 105.93	12.84%
3	CONCRETE		$	1,965,748	$ 48.15	5.84%
4	MASONRY		$	-	$ -	0.00%
5	METALS		$	2,749,617	$ 67.35	8.16%
6	WOODS, PLASTICS AND COMPOSITES		$	339,367	$ 8.31	1.01%
7	THERMAL AND MOISTURE PROTECTION		$	800,428	$ 19.61	2.38%
8	DOORS AND WINDOWS		$	1,439,798	$ 35.27	4.27%
9	FINISHES		$	1,931,517	$ 47.31	5.73%
10	SPECIALTIES		$	590,158	$ 14.46	1.75%
11	EQUIPMENT		$	882,953	$ 21.63	2.62%
12	FURNISHINGS		$	802,998	$ 19.67	2.38%
13	SPECIAL CONSTRUCTION		$	992,919	$ 24.32	2.95%
14	CONVEYING SYSTEMS		$	135,000	$ 3.31	0.40%
15	MECHANICAL		$	4,190,492	$ 102.64	12.44%
16	ELECTRICAL		$	5,215,660	$ 127.75	15.49%
	SUBTOTAL		**$**	**26,862,623**	$ 657.98	79.75%
1	GENERAL CONDITIONS		$	2,426,644	$ 59.44	7.20%
50	INSURANCE, TAXES & BONDS					
	Kaufman Lynn Insurance	1.45%	$	478,873	$ 11.73	1.42%
	Builder's Risk Insurance - By Owner	0.00%	$	-	$ -	
	Subcontractor Default Ins.	1.58%	$	424,429	$ 10.40	1.26%
	Design Build Construction Contingency	1.55%	$	416,371	$ 10.20	1.24%
	Construction Administration & Commissioning		$	495,000	$ 12.12	1.47%
	SUBTOTAL		**$**	**1,814,673**	$ 44.45	5.39%
	Contractor Overhead and Profit (Div 1 thru 50)	5.00%	$	1,555,197	$ 38.09	4.62%
	Contractor's Payment and Performance Bond	1.11%	$	366,586	$ 8.98	1.09%
	SUBTOTAL		**$**	**33,025,723**	**$ 809**	98%
	City Contingency	1.00%	$	268,626	$ 6.58	0.80%
	Permit Fee Allowance		$	387,500	$ 9.49	1.15%
GRAND TOTAL			**$**	**33,681,849**	**$ 825**	**100%**

Excluded by Kaufman Lynn. Estimates provided for Owner's use in determining project totals.

Construction Material Testing	$	50,000
FPL Overhead Line Removal, Primary, & Transformer	$	100,000
PBC Water Utilities	$	433,000
Fuel	$	10,000
Builder's Risk	$	150,000
Special Inspector	$	50,000
Project Total with Owner Items	**$**	**34,474,849**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP01000 - General Conditions	**2,426,644**			**2,426,644**			**0**			**0**			**0**			**0**	
	General Conditions	**2,426,644**			**2,426,644**			**0**			**0**			**0**			**0**	
	General Conditions	**2,426,644**	**KL Ops 8/6/26**	KL Ops 8/6/26	2,426,644			0			0			0			0	
	BP01001 - General Requirements	**501,084**			**501,084**			**0**			**0**			**0**			**0**	
	General Requirements	**501,084**			**501,084**			**0**			**0**			**0**			**0**	
100	Security System	**68,400**	**KL Ops 7/10/26**	KL Ops 7/10/26	68,400			0			0			0			0	
110	Water Holding Tank	**36,677**	**KL Ops 7/10/26**	KL Ops 7/10/26	36,677			0			0			0			0	
120	Document Reproduction Services	**17,040**	**KL Ops 7/10/26**	KL Ops 7/10/26	17,040			0			0			0			0	
125	Close Out/As Built Docs	**3,500**	**KL Ops 7/10/26**	KL Ops 7/10/26	3,500			0			0			0			0	
130	Dumpsters	**89,881**	**KL Ops 7/10/26**	KL Ops 7/10/26	89,881			0			0			0			0	
135	Final Clean Building	**22,400**	**KL Ops 7/10/26**	KL Ops 7/10/26	22,400			0			0			0			0	
140	Temp Fence Maintenance	**16,200**	**KL Ops 7/10/26**	KL Ops 7/10/26	16,200			0			0			0			0	
145	Temp Construction Fence	**43,116**	**KL Ops 7/10/26**	KL Ops 7/10/26	43,116			0			0			0			0	
150	Temp Toilets & Wash Stations	**22,012**	**KL Ops 7/10/26**	KL Ops 7/10/26	22,012			0			0			0			0	
160	Project Signage	**9,600**	**KL Ops 7/10/26**	KL Ops 7/10/26	9,600			0			0			0			0	
170	Temp Construction Electric	**10,366**	**KL Ops 7/10/26**	KL Ops 7/10/26	10,366			0			0			0			0	
173	Temp Trailer Electric	**10,175**	**KL Ops 7/10/26**	KL Ops 7/10/26	10,175			0			0			0			0	
178	By Owner: Permanent Power	**0**	**By Owner Per Owner 8/7/26**	By Owner Per Owner 8/7	0			0			0			0			0	
180	Temp Water	**33,916**	**KL Ops 7/10/26**	KL Ops 7/10/26	33,916			0			0			0			0	
185	Temp Water Connection & Meter	**15,000**	**KL Ops 7/10/26**	KL Ops 7/10/26	15,000			0			0			0			0	
202	By Owner: Threshold Inspector Allowance	**0**	**KL Ops IGMP**	KL Ops IGMP	0	N/A		0			0			0			0	
300	Surveying	**45,000**	**KL Ops 7/10/26**	KL Ops 7/10/26	45,000			0			0			0			0	
305	BBB Consultant	**57,800**	**KL Ops 7/10/26**	KL Ops 7/10/26	57,800			0			0			0			0	
900	Rev 1 Adjustments	**0**			0			0			0			0			0	
901	Excludes Vibration Monitoring	**0**	**KL Ops 8/6/26**	KL Ops 8/6/26	0			0			0			0			0	

***Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP02305 - Sitework	**3,224,538**			**3,407,594**			**3,453,464**			**3,224,538**			**0**			**0**	
	BP02305.0 - Sitework - General	**3,168,941**			**3,634,962**			**3,498,500**			**3,168,941**			**0**			**0**	
	Earthwork	**3,168,941**			3,634,962			3,498,500			3,168,941			0			0	
100	Sitework Base Bid	**3,168,941**	**Stanford**	Big D	3,634,962	Yes	EMS	3,498,500	Yes	Stanford	3,168,941	Yes		0			0	
102	Sales Taxes	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
106	Prequalified	**0**	**Stanford**	Big D	0		EMS	0		Stanford	0			0			0	
	BP02305.2 - Sitework - Scope	**55,597**			**-227,368**			**-45,036**			**55,597**			**0**			**0**	
	Earthwork	**55,597**			-137,332			45,000			55,597			0			0	
140	MOT	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
140	Visit the site	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
142	Survey & AS-builts	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
144	Existing rock piles are to be preserved and reused	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
146	Demo 2 Trailers, Wood Fence, Metal Swing Gate, Canopy, Chain Link Fence, 2 Metal Gates.	**-18,559**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	-18,559	Yes		0			0	
148	Demo Asphalt and Base Rock within Road ,1 Brick Fire Pit, Path, Asphalt,2 Sheds, Walls, Trash Pile, Driveway, Hex Driveway	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
150	Already Done- Underground Demo: Remove Existing Septic Tank.	**0**	**Stanford**	Big D	-4,620	No	EMS	0	Yes	Stanford	0	Yes		0			0	
152	Tree Removals	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
154	Refer to Add alternate - Tree Removals ILO RELOCATE	**0**	**Stanford**	Big D	-24,750	Yes	EMS	0	Sub +	Stanford	0	Sub +		0			0	
162	Tree Protection	**45,000**	**Stanford**	Big D	0	Yes	EMS	45,000	X Sub	Stanford	45,000	X Sub		0			0	
164	Sediment barrier; filter fabric and 57 stone.	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
166	Turbidity barriers (3) and silt fence around site.	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
168	Maintain silt fence and erosion control (inlet protection) through construction.	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
170	Stabilized rock construction entrance	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
172	Stabilized Rock access road Ramp to Pond	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
173	Crane Road 900'x 24' (8 inch)	**132,440**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	132,440	Yes		0			0	
174	Open cuts in existing pavement and restoration for utility connections to existing utilities	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
176	Export Fill for Site Balance & Using it for Building Pad	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
178	Proof Roll Building Pad	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
180	Rough Grading	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
182	8" compacted Lime rock minimum	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
184	Paver Base	**-103,284**	**Stanford**	Big D	-107,962	Yes	EMS	0	Yes	Stanford	-103,284	Yes		0			0	
188	NIC- Water Meter Pad- refer to concrete	**0**	**Stanford**	Big D	0	No	EMS	0	No	Stanford	0	No		0			0	
190	NIC- Generator Pad- refer to concrete	**0**	**Stanford**	Big D	0	No	EMS	0	No	Stanford	0	No		0			0	
	Utilities	**0**			0			0			0			0			0	
200	Drainage:	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
202	24" Exfiltration	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
204	HPDE Pipes	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
206	Drainage Structures	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
208	Drainage Manholes	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
210	Drainage Cleanout	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
212	Roof drain connection to storm; Site contractor to stub up for roofer connection	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
214	NIC Provide PVC "Boot" or hub for downspout connection per sheet A-450	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
216	Sewer:	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
216	NIC Oil Separator,Grease & Solids Interceptor - Refer to Plumbing	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
218	PVC Pipes	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
220	Clean Outs & manholes	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
222	NIC If ground water is encountered - 6" 57 stone installed above and below the pipe to stabilize.	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
224	DIP & PVC pipes	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
226	4" RPZ	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
228	Trench backfill and compacted in 12" lifts. One test per 100 LF of 12" lift.	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
230	Repair of existing structures and pavement for utility connections.	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
232	connect car wash to existing sewage & water	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
234	NIC Chlorination, testing, inspections, as-builts to be coordinated by Civil with PBCWUD.	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
236	Fire Line:	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
238	DIP pipes	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	
240	6" DDCV	**0**	**Stanford**	Big D	0	Yes	EMS	0	Yes	Stanford	0	Yes		0			0	

242	DDCA Assembly model 3000SS with thrust blocks.	0	Stanford	Big D	0	Yes	EMS	0	Yes	Stanford	0 Yes	0	0
244	6" FDC	0	Stanford	Big D	0	Yes	EMS	0	Yes	Stanford	0 Yes	0	0
	Bases, ballasts and pavement	0			-90,036			-90,036			0	0	0
299	Paving:	0	Stanford	Big D	0	Yes	EMS	0	Yes	Stanford	0 Yes	0	0
300	12" Subgrade	0	Stanford	Big D	0	Yes	EMS	0	Yes	Stanford	0 Yes	0	0
302	8" Limerock	0	Stanford	Big D	0	Yes	EMS	0	Yes	Stanford	0 Yes	0	0
304	2" Asphalt (2 Lifts)	0	Stanford	Big D	0	Yes	EMS	0	Yes	Stanford	0 Yes	0	0
304	Open Cut Repairs in Road	0	Stanford	Big D	0	Yes	EMS	0	Yes	Stanford	0 Yes	0	0
304	Mill and Pave Restoration of Road	0	Stanford	Big D	0	Yes	EMS	0	Yes	Stanford	0 Yes	0	0
306	Construct new median (curbs, etc.) restore roadway adjacent	0	Stanford	Big D	0	Yes	EMS	0	Yes	Stanford	0 Yes	0	0
308	Curbs D	0	Stanford	Big D	0	Yes	EMS	0	Yes	Stanford	0 Yes	0	0
310	Header Curbs	0	Stanford	Big D	0	Yes	EMS	0	Yes	Stanford	0 Yes	0	0
312	Concrete Sidewalks	0	Stanford	Big D	0	Yes	EMS	0	Yes	Stanford	0 Yes	0	0
314	6" 3000 PSI Concrete; 12" clean Subgrade; Sawcut 8 x 8 sections; provide joint plan; curbing.	0	Stanford	Big D	0	Yes	EMS	0	Yes	Stanford	0 Yes	0	0
316	Concrete Pavings	0	Stanford	Big D	0	Yes	EMS	0	Yes	Stanford	0 Yes	0	0
318	1 year warranty in lieu of 2 year warranty on paving. Paving Notes C-2	0	Stanford	Big D	-90,036	X Sub	EMS	-90,036	X Sub	Stanford	0 Yes	0	0
320	Striping & Signage:	0	Stanford	Big D	0	Yes	EMS	0	Yes	Stanford	0 Yes	0	0
322	Detectable warning strips, striping, ADA Signage, stops and wheel stops.	0	Stanford	Big D	0	Yes	EMS	0	Yes	Stanford	0 Yes	0	0
324	Striping and signage include RPMs (blue) as shown	0	Stanford	Big D	0	Yes	EMS	0	Yes	Stanford	0 Yes	0	0
326	By Plumbing- Oil Seperator:	0	Stanford	Big D	0	Yes	EMS	0	Yes	Stanford	0 Yes	0	0
326	Relocate boulders as shown at memorial garden; coordinate with AOR	0	Stanford	Big D	0	Yes	EMS	0	Yes	Stanford	0 X Sub	0	0
328	Ground floor slab should be rolled with at least 24 passes in static mode	0	Stanford	Big D	0	Yes	EMS	0	Yes	Stanford	0 Yes	0	0
330	NIC- already done- Relocate abandoned cars	0	Stanford	Big D	0	No	EMS	0	No	Stanford	0 No	0	0

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP02780 - Brick Pavers	**75,535**			**75,535**			**100,986**			**104,414**			**107,962**			**92,659**	
	BP02780.0 - Brick Pavers - General	**58,149**			**58,149**			**86,195**			**89,623**			**107,962**			**76,810**	
	Unit pavers	**58,149**			58,149			86,195			89,623			107,962			76,810	
100	Base Bid	**58,149**	**Crossroads Paving**	Crossroads Paving	58,149	Yes	Perfect Pavers	86,195	Yes	C.S.E.	89,623	Yes	Big D	107,962	Yes	GPC	76,810	Yes
102	Sales Taxes	**0**	**Crossroads Paving**	Crossroads Paving	0	Yes	Perfect Pavers	0	Yes	C.S.E.	0	Yes	Big D	0	Yes	GPC	0	Yes
106	Prequalified	**0**	**Crossroads Paving**	Crossroads Paving	0		Perfect Pavers	0		C.S.E.	0		Big D	0		GPC	0	
	BP02780.2 - Brick Pavers - Scope	**17,386**			**17,386**			**14,791**			**14,791**			**0**			**15,849**	
	Unit pavers	**17,386**			17,386			14,791			14,791			0			15,849	
100	MEMORIAL AREA:	**0**	**Crossroads Paving**	Crossroads Paving	0	Yes	Perfect Pavers	0	Yes	C.S.E.	0	Yes	Big D	0	Yes	GPC	0	Yes
101	Catalina Grana Mixed Pavers	**0**	**Crossroads Paving**	Crossroads Paving	0	Yes	Perfect Pavers	0	Yes	C.S.E.	0	Yes	Big D	0	Yes	GPC	0	Yes
102	See Div 3 for 8" x 8" Paver Perimeter Header Curb	**0**	**Crossroads Paving**	Crossroads Paving	0	Yes	Perfect Pavers	0	Yes	C.S.E.	0	Yes	Big D	0	Yes	GPC	0	Yes
103	Titanium Sand Bed	**0**	**Crossroads Paving**	Crossroads Paving	0	Yes	Perfect Pavers	0	Yes	C.S.E.	0	Yes	Big D	0	Yes	GPC	0	Yes
104	Charcoal Sand Bed - Perimeter Band	**0**	**Crossroads Paving**	Crossroads Paving	0	Yes	Perfect Pavers	0	Yes	C.S.E.	0	Yes	Big D	0	Yes	GPC	0	Yes
200	VEHICULAR PAVERS	**0**	**Crossroads Paving**	Crossroads Paving	0	Yes	Perfect Pavers	0	Yes	C.S.E.	0	Yes	Big D	0	Yes	GPC	0	Yes
201	Charcoal Sand Bed	**0**	**Crossroads Paving**	Crossroads Paving	0	Yes	Perfect Pavers	0	Yes	C.S.E.	0	Yes	Big D	0	Yes	GPC	0	Yes
202	Belgard - 4" x 8" Concrete Brick Pavers - Charcoal	**0**	**Crossroads Paving**	Crossroads Paving	0	Yes	Perfect Pavers	0	Yes	C.S.E.	0	Yes	Big D	0	Yes	GPC	0	Yes
203	Belgard - 4" x 8" Concrete Brick Pavers - Titanium	**0**	**Crossroads Paving**	Crossroads Paving	0	Yes	Perfect Pavers	0	Yes	C.S.E.	0	Yes	Big D	0	Yes	GPC	0	Yes
204	Belgard - 4" x 8" Concrete Brick Pavers - Soldier Course	**0**	**Crossroads Paving**	Crossroads Paving	0	Yes	Perfect Pavers	0	Yes	C.S.E.	0	Yes	Big D	0	Yes	GPC	0	Yes
205	Set in Herrinbone Layout.	**0**	**Crossroads Paving**	Crossroads Paving	0	Yes	Perfect Pavers	0	Yes	C.S.E.	0	Yes	Big D	0	Yes	GPC	0	Yes
300	NORTH ENTRY	**0**	**Crossroads Paving**	Crossroads Paving	0	Yes	Perfect Pavers	0	Yes	C.S.E.	0	Yes	Big D	0	Yes	GPC	0	Yes
300	Belgard - 4" x 8" Concrete Brick Pavers - Charcoal	**0**	**Crossroads Paving**	Crossroads Paving	0	Yes	Perfect Pavers	0	Yes	C.S.E.	0	Yes	Big D	0	Yes	GPC	0	Yes
300	Belgard - 4" x 8" Concrete Brick Pavers - Titanium	**0**	**Crossroads Paving**	Crossroads Paving	0	Yes	Perfect Pavers	0	Yes	C.S.E.	0	Yes	Big D	0	Yes	GPC	0	Yes
300	Charcoal Sand Bed	**0**	**Crossroads Paving**	Crossroads Paving	0	Yes	Perfect Pavers	0	Yes	C.S.E.	0	Yes	Big D	0	Yes	GPC	0	Yes
400	MISC	**0**	**Crossroads Paving**	Crossroads Paving	0	Yes	Perfect Pavers	0	Yes	C.S.E.	0	Yes	Big D	0	Yes	GPC	0	Yes
400	Site Prep-Final Grade +/-1"	**5,000**	**Crossroads Paving**	Crossroads Paving	5,000	Yes	Perfect Pavers	5,000	X Sub	C.S.E.	5,000	X Sub	Big D	0	Yes	GPC	0	Yes
401	Installation	**0**	**Crossroads Paving**	Crossroads Paving	0	Yes	Perfect Pavers	0	Yes	C.S.E.	0	Yes	Big D	0	Yes	GPC	0	Yes
402	Clean/Seal	**12,386**	**Crossroads Paving**	Crossroads Paving	12,386	Yes	Perfect Pavers	9,791	Yes	C.S.E.	9,791	X Sub	Big D	0	Yes	GPC	15,849	Yes
403	Shipping/Handling	**0**	**Crossroads Paving**	Crossroads Paving	0	Yes	Perfect Pavers	0	Yes	C.S.E.	0	Yes	Big D	0	Yes	GPC	0	Yes

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP02835 - Fence & Gates	**420,941**			**420,941**			**485,521**			**424,465**			**0**			**0**	
	BP02835.0 - Fence & Gates - General	**0**			**0**			**205,868**			**3,500**			**0**			**0**	
	Fences and gates	**0**			0			205,868			3,500			0			0	
100	Base Bid Fences & Gates	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	205,868	Yes	LTG Carlson Fence	0	Yes		0			0	
102	Sales Taxes	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0	Yes	LTG Carlson Fence	0	Yes		0			0	
104	Trade Permits	**0**	**Tropic Fence**	Tropic Fence	0	No	EJ Tropical - TAMP	0		LTG Carlson Fence	3,500	Sub +		0			0	
106	Prequalified	**0**	**Tropic Fence**	Tropic Fence	0		EJ Tropical - TAMP	0		LTG Carlson Fence	0			0			0	
	BP02835.2 - Fence & Gates - Scope	**420,941**			**420,941**			**279,653**			**420,965**			**0**			**0**	
	Fences and gates	**420,941**			420,941			279,653			420,965			0			0	
203	Aluminum Picket Fence	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0		LTG Carlson Fence	0	Yes		0			0	
204	Aluminum Picket Fence H: 6'-0" around Parking	**118,604**	**Tropic Fence**	Tropic Fence	118,604	Yes	EJ Tropical - TAMP	118,604	X Sub	LTG Carlson Fence	110,500	Yes		0			0	
205	Aluminum Picket Fence H: 6'-0" at Outdoor Patio	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0		LTG Carlson Fence	0			0			0	
206	Aluminum Picket Fence H: 6'-0" at South of property (new)	**107,600**	**Tropic Fence**	Tropic Fence	107,600	Yes	EJ Tropical - TAMP	0		LTG Carlson Fence	136,000	Yes		0			0	
206	Excludes New Aluminum Picket Fence H: 6'-0" at East of property (new) per RFI #GMP-13	**-50,287**	**Tropic Fence**	Tropic Fence	-50,287	No	EJ Tropical - TAMP	0		LTG Carlson Fence	0	Yes		0			0	
206	Aluminum Picket Fence: Fan at Aluminum picket fence at lake (new)	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0		LTG Carlson Fence	0	Yes		0			0	
207	Vehicular gates: V-track roll gates.	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0		LTG Carlson Fence	0	Yes		0			0	
214	(2) Picket gate (sliding) 12'-0" Lockable, Tag 2	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0		LTG Carlson Fence	0	Yes		0			0	
215	(2) Picket gate (sliding) (2) 12'-0" Lockable in position, Tag 3	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0		LTG Carlson Fence	0	Yes		0			0	
216	(2) Picket gate (swing) 3'-0" Lockable, Tag 4	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0		LTG Carlson Fence	0	Yes		0			0	
218	Perforated aluminum plat (0.093" thick) at picket gates (new)	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0		LTG Carlson Fence	0			0			0	
218	Mortise lock mechanism at picket single gates (new)	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0		LTG Carlson Fence	0			0			0	
220	New Chain Link Fence H: 6'-0" outside Generator Room (new)	**49,250**	**Tropic Fence**	Tropic Fence	49,250	Yes	EJ Tropical - TAMP	49,250	X Sub	LTG Carlson Fence	8,750	Yes		0			0	
220	(1) Chain link double gate (2) 3'-0" lockable at Generator Room, Tag 5 (new)	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0		LTG Carlson Fence	0	Yes		0			0	
220	Screen/ slats for Chain Link Fence at Generator (new)	**722**	**Tropic Fence**	Tropic Fence	722	Sub +	EJ Tropical - TAMP	722	X Sub	LTG Carlson Fence	722	X Sub		0			0	
221	(1) Chain link double gate (2) 10'-0" lockable at Access Road, Tag 1 (new)	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0		LTG Carlson Fence	4,250	Yes		0			0	
221	Mortise lock mechanism at chain link gates (new)	**0**	**Tropic Fence**	Tropic Fence	0	No	EJ Tropical - TAMP	0		LTG Carlson Fence	0	Yes		0			0	
221	Chain Link Fence - Black Vinyl Coated	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0		LTG Carlson Fence	0	Yes		0			0	
222	Chain Link Fence on structural beams at Chiller Area	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0		LTG Carlson Fence	14,500	Yes		0			0	
224	Chain Link Fence to deck and gate at Fire Supply / Bunker Gear (Addendum #2)	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0		LTG Carlson Fence	0			0			0	
224	Screen Enclosure at Canopy 3 around Fuel Tank - BOD Ametco Shadow 100	**130,336**	**Tropic Fence**	Tropic Fence	130,336	Yes	EJ Tropical - TAMP	19,260	Yes	LTG Carlson Fence	19,260	X Sub		0			0	
224	(1) Louvered gate at Canopy 3 Fuel Tank (new) - BOD Ametco Shadow 100	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0	Yes	LTG Carlson Fence	0			0			0	
225	Screen Enclosure at Mechanical Equipment - BOD Ametco- Eclipse Aluminum Louver Fence and Gate 6' high. - per RFI #PC-15	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0	Yes	LTG Carlson Fence	38,695	Yes		0			0	
225	(1) Louvered Gate at Mechanical Equipment	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0		LTG Carlson Fence	0	Yes		0			0	
226	Screen Enclosure at Dumpster - BOD Ametco Shadow 100	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0	Yes	LTG Carlson Fence	30,500	Yes		0			0	
228	(1) Dumpster double swing gate BOD Ametco Shadow 100	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0		LTG Carlson Fence	0	Yes		0			0	
230	(1) Dumpster single swing gate - BOD Ametco Shadow 100	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0	Yes	LTG Carlson Fence	0	Yes		0			0	
300	See Low Voltage - RFID readers included for vehicular gates	**-11,813**	**Tropic Fence**	Tropic Fence	-11,813	No	EJ Tropical - TAMP	0		LTG Carlson Fence	0	Yes		0			0	
302	Access Control - Gate Motor Operators	**76,529**	**Tropic Fence**	Tropic Fence	76,529	Yes	EJ Tropical - TAMP	76,529	X Sub	LTG Carlson Fence	37,500	Yes		0			0	
304	Knox Switch + CLICK2ENTER at access control gates (Addendum #2)	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0	X Sub	LTG Carlson Fence	0			0			0	
304	Concrete footing	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0		LTG Carlson Fence	0	Yes		0			0	
305	Concrete grade beam for V-track roll gates	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	15,288	X Sub	LTG Carlson Fence	15,288	X Sub		0			0	
306	Furnish and Installation	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0		LTG Carlson Fence	0	Yes		0			0	
307	Engineering and Shop Drawings	**0**	**Tropic Fence**	Tropic Fence	0	Yes	EJ Tropical - TAMP	0		LTG Carlson Fence	5,000	Sub +		0			0	

**Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP02850 - Landscape/Plantings/Irrigation/Exterior Improvements	**443,893**			**493,443**			**443,893**			**512,705**			**515,249**			**0**
	BP02850.0 - Landscape/Plantings / Irrigation /Exterior Improvements - General	**350,733**			**341,148**			**350,733**			**379,185**			**472,269**			**0**
	Landscape/Plantings	**350,733**			341,148			350,733			379,185			472,269			0
100	Landscaping Base Bid	**212,233**	**Amaro Landscape**	A Cut Above	198,648	Yes	Amaro Landscape	212,233	Yes	Arazoza Bros	200,185	Yes	Bermuda Landscape	276,465	Yes			0
100	Irrigation Base Bid	**138,500**	**Amaro Landscape**	A Cut Above	142,500	Yes	Amaro Landscape	138,500	Yes	Arazoza Bros	179,000	Yes	Bermuda Landscape	195,804	Yes			0
101	Sales Tax	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
103	Prequalified	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	No			0
	BP02850.2 - Landscape/Plantings / Irrigation /Exterior Improvements - Scope	**93,160**			**152,295**			**93,160**			**133,520**			**42,980**			**0**
	Landscape/Plantings	**93,160**			152,295			93,160			133,520			42,980			0
100	TREES	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
101	12' Green Buttonwood	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
102	12' Slash Pine	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
103	12' Southern Live Oak	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
103	12' Dahoon Holly	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
103	12' Verawood	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
103	12' Orange Geiger Tree	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
103	12' Cabbage Palm	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
103	12' Single Montgomery Palm	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
104	Tree Bracing/Staking/Guying	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
105	Excavate Planting Pit	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
106	Remove Existing Roots	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
107	Existing Tree Protection	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
200	SHRUB/SHRUB AREAS	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
200	24" Coco Plum	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
200	18" Silver Saw Palmetto	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
200	18" Dwarf Firebrush	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
200	24" Pink Muhly Grass	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
200	24" Dwarf Fagahatchee Grass	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
300	GROUND COVERAGE	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
300	12" Perennial Peanut	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
300	6" Green Island Ficus	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
300	12" Stokes Dwarf Yaupon Holly	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
300	12" Coontie Cycad	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
300	SOD - St. Augustine	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
400	IRRIGATION	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
400	Furnish and Install Irrigation System (Design Build)	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
400	100% Coverage w/ 50% Overlap	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
400	Rain Sensors	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
400	Start up and Test	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
500	MISC	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
500	Tree Bracing/Staking/Guying	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
500	Excavate Planting Pit	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
500	Remove Existing Roots	**14,000**	**Amaro Landscape**	A Cut Above	14,000	Yes	Amaro Landscape	14,000	X Sub	Arazoza Bros	0	Yes	Bermuda Landscape	14,000	X Sub			0
500	Existing Tree Protection	**0**	**Amaro Landscape**	A Cut Above	19,250	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
500	ALT: Tree Removal ilo Tree Relocation	**108,140**	**Amaro Landscape**	A Cut Above	143,025	Yes	Amaro Landscape	108,140	Yes	Arazoza Bros	162,500	Yes	Bermuda Landscape	0	Yes			0
500	Furtilizer	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
500	3" Malaluca Mulch	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
500	Root Barrier	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
500	Top Soil	**0**	**Amaro Landscape**	A Cut Above	0	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
500	Maintainence 30 Days after Completion	**0**	**Amaro Landscape**	A Cut Above	5,000	Yes	Amaro Landscape	0	Yes	Arazoza Bros	0	Yes	Bermuda Landscape	0	Yes			0
500	ALT: Furnish/Install Trees as New ILO Relocated	**0**	**Amaro Landscape**	A Cut Above	0	No	Amaro Landscape	0	No	Arazoza Bros	0	No	Bermuda Landscape	0	Yes			0
	Alternate Tree remove replace ilo relocation: See Qualifcations	**-28,980**	**Amaro Landscape**	A Cut Above	-28,980		Amaro Landscape	-28,980		Arazoza Bros	-28,980		Bermuda Landscape	-28,980				

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP02870 - Site Furnishing	**159,978**			**159,978**			**2,100**			**0**			**0**			**0**	
	BP02870.0 - Site Furnishing - General	**17,224**			**17,224**			**0**			**0**			**0**			**0**	
	Furnishings	**17,224**			17,224			0			0			0			0	
100	Site Furnishings	**17,224**	**Custome One Source**	Custome One Source	17,224	Yes		0			0			0			0	
102	Sales Taxes	**0**	**Custome One Source**	Custome One Source	0	Yes		0			0			0			0	
104	Prequalified	**0**	**Custome One Source**	Custome One Source	0	Yes		0			0			0			0	
	BP02870.2 - Site Furnishing - Scope	**142,754**			**142,754**			**2,100**			**0**			**0**			**0**	
	Furnishings	**142,754**			142,754			2,100			0			0			0	
100	See Div 10 for Flag Poles	**0**	**Custome One Source**	Custome One Source	0	No		0			0			0			0	
101	See Break out Divisions for Memorial Plaza	**0**	**Custome One Source**	Custome One Source	0	No		0			0			0			0	
102	North Entry Benches - No Spec.	**0**	**Custome One Source**	Custome One Source	0	Yes		0			0			0			0	
103	North Entry Bike Racks - No Spec.	**0**	**Custome One Source**	Custome One Source	0	Yes		0			0			0			0	
104	See Division 03 - Concrete Bridge	**0**	**Custome One Source**	Custome One Source	0	Yes		0			0			0			0	
105	Concrete Bridge Wood Composite Planking	**92,550**	**Custome One Source**	Custome One Source	92,550	Yes		0			0			0			0	
105	Memorial Bench Marine Grade Composite Wood Seat	**48,481**	**Custome One Source**	Custome One Source	48,481	Yes		0			0			0			0	
105	Memorial Bench Skate Board Deterrents	**2,100**	**KL Estimate**	KL Estimate	2,100	KLEst		0			0			0			0	
106	Trash & Recycle Bins on Site: Not currently shown in plans or specs	**0**	**Custome One Source**	Custome One Source	0	Yes		0			0			0			0	
901	Revise Benches & Trash to match specs and Amendment 3	**-377**	**KL Estimate**	KL Estimate	-377			0			0			0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP03300 - Cast in Place Concrete - Building	**1,965,748**			**2,164,176**			**1,965,748**			**0**			**0**			**0**	
	BP03300.0 - Cast in Place Concrete - Building - General	**1,947,748**			**1,952,199**			**1,947,748**			**0**			**0**			**0**	
	Concrete	**1,947,748**			1,952,199			1,947,748			0			0			0	
40	Concrete Base Bid	**1,947,748**	**RCX TILT UP**	Woodland	1,952,199	Yes	RCX TILT UP	1,947,748	Yes		0			0			0	
55	Sales Tax	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
70	Prequalified	**0**	**RCX TILT UP**	Woodland	0		RCX TILT UP	0			0			0			0	
	BP03300.2 - Cast in Place Concrete - Building - Scope	**18,000**			**211,977**			**18,000**			**0**			**0**			**0**	
	Concrete	**18,000**			211,977			18,000			0			0			0	
100	Excavation and backfill and compaction of all footings	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
100	Foundations and Slab on Grade	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
102	4" NWC Reinforced slab with WWR 6x6-W1.4xW1.4	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
104	6" NWC Reinforced slab with WWR 6x6-W2.9xW	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
106	2" MINIMUM NWC5 REINFORCED SLAB WITH #5@12" OC EACH WAY TOP & BOTTOM	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
108	Stepped Footing in coordination with MEP/BIM as shown.	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
110	Additional reinforcement at slab penetrations per structural details.	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
112	Formwork and reinforcement for floor trench drains as shown	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
114	Vapor Barrier	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
116	Termite Control	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
120	Air cooled chiller housekeeping pad on slab Detail 4/S-311	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
122	Generator 14" thick isolated housekeeping pad see 4/S-311	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
124	Slab Trench Drain Detail 8/S-311	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
126	Spread Footings	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
128	Wall Footings	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
130	See Div 5 for Steel Columns Supply	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
132	See Div 5 for Steel Columns Install	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
134	Install Embed plates; coordinate placement with Steel Shop Drawings	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
138	Grout at steel columns	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
138	Leaveout Panel	**18,000**	**RCX TILT UP**	Woodland	18,000	Yes	RCX TILT UP	18,000	X Sub		0			0			0	
140	Concrete Tilt up Walls	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
142	Concrete Slab on Metal Decks	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
144	Elevated Slabs	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
146	Precast Lintels	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
148	Elevator Pit Walls & slab	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
150	Isolation Joints Per Plans	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
152	Construction Joints Per plans	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
154	Control Joints Per Plans	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
156	CMU COLUMN outside of Building Sheet S-204- SEE 7/S-302	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
158	Connections from CMU to Tilt.	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
160	Concrete beams	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
162	Freestanding CMU Column Footings.	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
164	Fuel Station Foundation, Bollards Infill, thickened slab & 6" Slab & 12" Slab Sheet S-205	**0**	**RCX TILT UP**	Woodland	49,309	Yes	RCX TILT UP	0	Yes		0			0			0	
166	Parking Canopy Foundations	**0**	**RCX TILT UP**	Woodland	30,744	Yes	RCX TILT UP	0	Yes		0			0			0	
168	Pavilion Foundations	**0**	**RCX TILT UP**	Woodland	15,983	Yes	RCX TILT UP	0	Yes		0			0			0	
170	Car wash station Isolated footings and thickened slabs r	**0**	**RCX TILT UP**	Woodland	25,941	Yes	RCX TILT UP	0	Yes		0			0			0	
172	Dumpster Enclosure : Tilt Wall Dumpster Enclosure, 4" slab with thickened edge and bollards shown Sheet a 206	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
174	Infill & Footings For Bollards Detail 6/S-302	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
176	Concrete fill for Metal pan stairs	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
178	Memorial Concrete Bench sheet A -103 & S-302	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
179	Bridge columns, beams & slab	**0**	**RCX TILT UP**	Woodland	28,000	X Sub	RCX TILT UP	0	Yes		0			0			0	
179	EXCLUDED Precast Planks at Bridge detail Sheet A-151.	**0**	**RCX TILT UP**	Woodland	0	No	RCX TILT UP	0	No		0			0			0	
180	Housekeeping pad for fire pump room	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
180	Water meter pad per C-7	**0**	**RCX TILT UP**	Woodland	9,000	X Sub	RCX TILT UP	0	Yes		0			0			0	
181	Nlc - Refer to Metals - Footings for Fence	**0**	**RCX TILT UP**	Woodland	0	No	RCX TILT UP	0	No		0			0			0	
182	Fire Training Structure:	**0**	**RCX TILT UP**	Woodland	0	Yes	RCX TILT UP	0	Yes		0			0			0	
184	FTS Foundation 12" Thick X 6' Wide x 25' Length (2 Sides) #5 Rebar 12" OC both ways - 3000 PSI Concrete	**0**	**RCX TILT UP**	Woodland	35,000	X Sub	RCX TILT UP	0	Yes		0			0			0	

186 FTS 16 Spread Footings 2' x2' x2' #5 Rebar	0	RCX TILT UP	Woodland	0	Yes	RCX TILT UP	0	Yes	0	0	0
188 FTS 12" Slab on Grade	0	RCX TILT UP	Woodland	0	Yes	RCX TILT UP	0	Yes	0	0	0
200 See Civil for 6" Concrete Paving	0	RCX TILT UP	Woodland	0	No	RCX TILT UP	0	Yes	0	0	0

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP05500 - Structural Steel Framing/Joists/Cold Form	**1,550,147**			**1,616,197**			**1,570,980**			**2,309,003**			**1,550,147**			**0**	
	BP05500.0 - Structural Steel Framing/Joists/Cold Form - General	**1,395,523**			**1,616,197**			**1,570,980**			**2,309,003**			**1,395,523**			**0**	
	Structural framing	**1,227,768**			1,328,539			1,570,980			1,926,133			1,227,768			0	
100	Base Bid - Structural Steel	**1,227,768**	**East Coast Metals**	Steel Fabricators	1,328,539	Yes	Suncor	1,570,980	Yes	George's Welding	1,926,133	Yes	East Coast Metals	1,227,768	Yes			0
102	Sales Taxes	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes			0
106	Prequalified	**0**	**East Coast Metals**	Steel Fabricators	0		Suncor	0		George's Welding	0		East Coast Metals	0				0
	Metal fabrications	**167,755**			287,658			0			382,870			167,755				0
100	Base Bid - Misc Metals	**167,755**	**East Coast Metals**	Steel Fabricators	287,658	Yes	Suncor	0	Yes	George's Welding	382,870	Yes	East Coast Metals	167,755	Yes			0
102	Sales Taxes	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
106	Prequalified	**0**	**East Coast Metals**	Steel Fabricators	0		Suncor	0		George's Welding	0		East Coast Metals	0				0
	BP05500.2 - Structural Steel Framing/Joists/Cold Form - Scope	**154,624**			**0**			**0**			**0**			**154,624**				**0**
	Structural framing	**0**			0			0			0			0				0
100	Columns HSS8x8x5/8	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
102	Columns HSS8x8x1/2	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
104	Columns HSS8x8x3/8	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
106	Columns HSS10x10x1/2	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
108	Columns HSS8x8x1/4 - Post up	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
110	Columns base plates and anchor rods	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
111	Istallation of steel columns	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
112	Beams HSS6X6X1/4	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
114	Beams W12x16	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
116	Beams W14x22	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
118	Beams W14x26	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
120	Beams W16x26	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
122	Beams W16x31	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
124	Beams W18x35	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
126	Beams W18x50	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
128	Beams W21x44	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
130	Beams W21x48	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
132	Beams W21x50	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
134	Beams W21x55	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
136	Beams W24x55	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
140	Beams W24x62	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
142	Beams W24x68	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
144	Beams W24x76	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
146	Beams W33x118	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
148	Beams steel connections	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
150	Steel Floor Deck	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes			0
152	Steel Roof Deck and Joists	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes			0
153	1.5" Deep Type B 20GA Galv. vented non-composite steel roof deck	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
153	2.0" Deep 20GA Composite Steel Deck	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
153	3.0" Deep 20GA Composite Steel Deck	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
156	Perimeter angle	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
158	Bracing	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
160	Cross bridging	**0**	**East Coast Metals**	Steel Fabricators	0		Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
166	Folding Partition Support (Rooms: Breakout 1 & 2)	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes			0
168	Metal Pan Stair (Stair #1)	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes			0
170	Metal Pan Stair (Stair #2)	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes			0
172	Lifting equipment	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes			0
174	Engineering and Shop Drawings	**0**	**East Coast Metals**	Steel Fabricators	0		Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes			0
176	Delivery and Installation	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes			0
	Metal fabrications	**154,624**			0			0			0			154,624				0
100	(6) - 6" Steel Bollards at Dumpster	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes			0
102	(16) - 6" Steel Bollards at Bay Area - Interior	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes			0
103	(16) - 6" Steel Bollards at Bay Area - Exterior	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes			0
104	(2) - 4" Bollards at EV Charger location	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes			0
106	(30) - 6" Bollards at Canopy 3 Fuel Island	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes			0
107	(2) - 6" Steel Bollards at Canopy 1 Fire Training (new)	**0**	**East Coast Metals**	Steel Fabricators	0		Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
107	(4) - 6" Steel Bollards at Canopy 4 Covered Parking (new)	**0**	**East Coast Metals**	Steel Fabricators	0		Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
107	(2) Roof Ladders (new)	**0**	**East Coast Metals**	Steel Fabricators	0		Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
108	Stair Railings - Stair #1 - Cable Railing (new)	**0**	**East Coast Metals**	Steel Fabricators	0	No	Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes			0
110	Stair Railings - Stair #2 - Cable Railing (new)	**0**	**East Coast Metals**	Steel Fabricators	0	No	Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes			0
111	Railing at Pedestrian Bridge 8/A-151 (new)	**0**	**East Coast Metals**	Steel Fabricators	0		Suncor	0	Yes	George's Welding	0		East Coast Metals	0	Yes			0
111	See Div 2 Site Furniture for Skateboard deterrents at concrete seat wall 4/A-103 (new)	**0**	**East Coast Metals**	Steel Fabricators	0	No	Suncor	0	No	George's Welding	0	No	East Coast Metals	0	No			0
112	Elevator - Pit Ladder	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes			0
114	Elevator - Hoist Beam	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes			0

116	Elevator - Sill angles	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes	0
118	Elevator - Sump Pit Cover	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes	0
124	Grating support at trench drains (Bay Area) - hot dipped galvanized	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes	0
125	Overhead Door sill embeds 4B/A-851.	**0**	**East Coast Metals**	Steel Fabricators	0		Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes	0
129	See Div 2 Fences for Dumpster: (1) double swing gate H:7'-0"	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	No	George's Welding	0	No	East Coast Metals	0	No	0
129	See Div 2 Fences for Dumpster: (1) single swing gate	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	No	George's Welding	0	No	East Coast Metals	0	No	0
132	Canopy 2 - Car Wash Station - Stairs and Cat Walk w/ Railings	**154,624**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	154,624	Sub +	0
134	See Fuel Pump Systems for Canopy 3 - Fuel Island - Galvanized Platform Stairs and Railings	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	No	George's Welding	0	Yes	East Coast Metals	0	No	0
200	See Signage for Memorial Sculpture Allowance	**0**	**East Coast Metals**	Steel Fabricators	0	No	Suncor	0	No	George's Welding	0	No	East Coast Metals	0	No	0
202	Delivery and Installation	**0**	**East Coast Metals**	Steel Fabricators	0	Yes	Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes	0
204	Engineering and Shop Drawings	**0**	**East Coast Metals**	Steel Fabricators	0		Suncor	0	Yes	George's Welding	0	Yes	East Coast Metals	0	Yes	0

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP05700 - Ornamental/Decorative Metals	**1,199,470**			**1,586,318**			**1,199,470**			**0**			**0**			**0**
	BP05700.0 - Ornamental/Decorative Metals - General	**1,178,605**			**1,586,318**			**1,178,605**			**0**			**0**			**0**
	Ornamental metal	**1,178,605**			1,586,318			1,178,605			0			0			0
100	Base Bid Metal Awnings, Shutters	**350,425**	**EJ Tropical - TAMP**	Walker Design	554,574	Yes	EJ Tropical - TAMP	350,425	Yes	White Sign	0			0			0
100	Base Bid Metal Canopies	**828,180**	**EJ Tropical - TAMP**	Walker Design	1,031,744	Yes	EJ Tropical - TAMP	828,180	Yes	White Sign	0			0			0
102	Sales Taxes	**0**	**EJ Tropical - TAMP**	Walker Design	0	Yes	EJ Tropical - TAMP	0	Yes	White Sign	0			0			0
106	Prequalified	**0**	**EJ Tropical - TAMP**	Walker Design	0		EJ Tropical - TAMP	0		White Sign	0			0			0
	BP05700.2 - Ornamental/Decorative Metals - Scope	**20,865**			**0**			**20,865**			**0**			**0**			**0**
	Ornamental metal	**0**			0			0			0			0			0
100	Awning Overhead at North Elevation (Building Entrance Stair Tower)	**0**	**EJ Tropical - TAMP**	Walker Design	0	Yes	EJ Tropical - TAMP	0	Yes	White Sign	0			0			0
102	Awning Overhead at West and East Elevations	**0**	**EJ Tropical - TAMP**	Walker Design	0	Yes	EJ Tropical - TAMP	0	Yes	White Sign	0			0			0
104	Awning - Full perimeter gutters	**0**	**EJ Tropical - TAMP**	Walker Design	0	Yes	EJ Tropical - TAMP	0	Yes	White Sign	0			0			0
106	Aluminum Bahama Shutters	**0**	**EJ Tropical - TAMP**	Walker Design	0	Yes	EJ Tropical - TAMP	0	Yes	White Sign	0			0			0
106	Aluminum Bahama Shutters Color: MTL-5 COLOR: RAL 7032 KIESELGRAU (new)	**0**	**EJ Tropical - TAMP**	Walker Design	0	Yes	EJ Tropical - TAMP	0	Yes	White Sign	0			0			0
108	Delivery and Installation	**0**	**EJ Tropical - TAMP**	Walker Design	0	Yes	EJ Tropical - TAMP	0	Yes	White Sign	0			0			0
110	Engineering and Shop Drawings	**0**	**EJ Tropical - TAMP**	Walker Design	0	Yes	EJ Tropical - TAMP	0	Yes	White Sign	0			0			0
	Alumn. Walkway Canopy	**20,865**			0			20,865			0			0			0
200	Canopy 1 - Fire Training	**0**	**EJ Tropical - TAMP**	Walker Design	0	Yes	EJ Tropical - TAMP	0	Yes	White Sign	0			0			0
202	Canopy 2 - Car Wash Station	**0**	**EJ Tropical - TAMP**	Walker Design	0	Yes	EJ Tropical - TAMP	0	Yes	White Sign	0			0			0
206	Canopy 3 - Fuel Island	**0**	**EJ Tropical - TAMP**	Walker Design	0	Yes	EJ Tropical - TAMP	0	Yes	White Sign	0			0			0
207	See Div 2 Fences for Canopy 3 - Fuel Island Louvered Fence	**-19,260**	**EJ Tropical - TAMP**	Walker Design	0	No	EJ Tropical - TAMP	-19,260	No	White Sign	0			0			0
210	Canopy 4 - Covered Parking	**0**	**EJ Tropical - TAMP**	Walker Design	0	Yes	EJ Tropical - TAMP	0	Yes	White Sign	0			0			0
212	Curved Canopy at Main Entrance	**0**	**EJ Tropical - TAMP**	Walker Design	0	Yes	EJ Tropical - TAMP	0	Yes	White Sign	0			0			0
214	Side extrusions for Canopy at Main Entrance (both sides)	**0**	**EJ Tropical - TAMP**	Walker Design	0	Yes	EJ Tropical - TAMP	0	Yes	White Sign	0			0			0
216	Extrusions / Facade Accents at North and West elevations	**40,125**	**EJ Tropical - TAMP**	Walker Design	0	Yes	EJ Tropical - TAMP	40,125	Yes	White Sign	0			0			0
218	MTL-3 - COLOR: RAL 7039 QUARZGRAU (new)	**0**	**EJ Tropical - TAMP**	Walker Design	0	Yes	EJ Tropical - TAMP	0		White Sign	0			0			0
220	Full perimeter gutters for canopies	**0**	**EJ Tropical - TAMP**	Walker Design	0	Yes	EJ Tropical - TAMP	0	Yes	White Sign	0			0			0
222	Delivery and Installation	**0**	**EJ Tropical - TAMP**	Walker Design	0	Yes	EJ Tropical - TAMP	0	Yes	White Sign	0			0			0
224	Engineering and Shop Drawings	**0**	**EJ Tropical - TAMP**	Walker Design	0	Yes	EJ Tropical - TAMP	0	Yes	White Sign	0			0			0
226	Footings for Canopies - See Concrete	**0**	**EJ Tropical - TAMP**	Walker Design	0	No	EJ Tropical - TAMP	0	No	White Sign	0			0			0

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP07100 - Dampproofing/Waterproofing	**93,546**			**93,546**			**103,325**			**186,690**			**0**			**0**	
	BP07100.0 - Dampproofing/Waterproofing - General	**84,981**			**84,981**			**97,825**			**195,025**			**0**			**0**	
	Waterproofing and dampproofing	**84,981**			84,981			97,825			195,025			0			0	
100	Base Bid Waterproofing	**84,981**	**Above All Caulking**	Above All Caulking	84,981	Yes	Service Contracting Solu	97,825	Yes	Dennaoui	195,025	Yes		0			0	
200	Sales Tax	**0**	**Above All Caulking**	Above All Caulking	0	Yes	Service Contracting Solu	0	Yes	Dennaoui	0	Yes		0			0	
400	Prequalified	**0**	**Above All Caulking**	Above All Caulking	0		Service Contracting Solu	0		Dennaoui	0			0			0	
	BP07100.2 - Dampproofing/Waterproofing - Scope	**8,565**			**8,565**			**5,500**			**-8,335**			**0**			**0**	
	Waterproofing and dampproofing	**8,565**			8,565			5,500			-8,335			0			0	
100	Elevator Pit Walls - Exterior	**0**	**Above All Caulking**	Above All Caulking	0	Yes	Service Contracting Solu	0	Yes	Dennaoui	0	Yes		0			0	
100	Elevator Pit Walls - Interior	**0**	**Above All Caulking**	Above All Caulking	0	Yes	Service Contracting Solu	0	Yes	Dennaoui	3,330	Sub +		0			0	
102	Waterproofing layer at 2nd floor Patio	**0**	**Above All Caulking**	Above All Caulking	0	Yes	Service Contracting Solu	0	Yes	Dennaoui	0	Yes		0			0	
104	Waterproofing at Rough Openings	**0**	**Above All Caulking**	Above All Caulking	0	Yes	Service Contracting Solu	0	Yes	Dennaoui	0	Yes		0			0	
106	Fluid Applied Waterproofing behind stair tower metal paneling (aluminum cladding) - per RFI #PC-40.	**15,765**	**Above All Caulking**	Above All Caulking	15,765	Sub +	Service Contracting Solu	0	Yes	Dennaoui	0	Yes		0			0	
107	Joint Sealants / Caulking	**0**	**Above All Caulking**	Above All Caulking	0	Yes	Service Contracting Solu	0	Yes	Dennaoui	0	Yes		0			0	
108	Joint Sealants: Sealant and backer rod at joints between tilt panels	**0**	**Above All Caulking**	Above All Caulking	0	Yes	Service Contracting Solu	0	Yes	Dennaoui	0	Yes		0			0	
110	Joint Sealants: Blanket Insulation Ceramic Fiber at joints between tilt panels	**0**	**Above All Caulking**	Above All Caulking	0	Yes	Service Contracting Solu	0	Yes	Dennaoui	0	Yes		0			0	
111	Caulking sealant at dissimilar materials	**0**	**Above All Caulking**	Above All Caulking	0	Yes	Service Contracting Solu	4,000	Sub +	Dennaoui	0	Yes		0			0	
111	Caulking sealant at interior slab to walls	**0**	**Above All Caulking**	Above All Caulking	0	Yes	Service Contracting Solu	0	Yes	Dennaoui	0	Yes		0			0	
111	Caulking sealant at interior slab control joints	**0**	**Above All Caulking**	Above All Caulking	0	Yes	Service Contracting Solu	0	Yes	Dennaoui	0	Yes		0			0	
111	Caulking sealant at HM Doors	**0**	**Above All Caulking**	Above All Caulking	0	Yes	Service Contracting Solu	0	Yes	Dennaoui	0	Yes		0			0	
111	See Glazing for: Caulking sealant at exterior beauty bead windows and storefronts - See Glazing	**-7,200**	**Above All Caulking**	Above All Caulking	-7,200	No	Service Contracting Solu	0	No	Dennaoui	-11,665	No		0			0	
111	Caulking sealant at exterior sidewalk to building walls	**0**	**Above All Caulking**	Above All Caulking	0	Yes	Service Contracting Solu	0	Yes	Dennaoui	0	Yes		0			0	
112	Warranty: Correct defective work within a five year period after Date of Substantial Completion.	**0**	**Above All Caulking**	Above All Caulking	0	Yes	Service Contracting Solu	1,500	Sub +	Dennaoui	0			0			0	
115	Concrete sealer - See Painting	**0**	**Above All Caulking**	Above All Caulking	0	No	Service Contracting Solu	0	No	Dennaoui	0	No		0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP07300 - Roofing /Flashing/Roof Specialties	**465,932**			**555,567**			**465,932**			**484,877**			**599,567**				**0**
	BP07300.0 - Roofing /Flashing/Roof Specialties - General	445,365			**535,000**			**445,365**			**464,310**			**579,000**				**0**
	Membrane roofing	**445,365**			535,000			445,365			464,310			579,000				0
100	Base Bid - Roofing	**445,365**	**Paletz**	Latite	535,000	Yes	Paletz	445,365	Yes	Wolverine	464,310	Yes	Atlas-Apex	579,000	Yes			0
200	Sales Tax	**0**	**Paletz**	Latite	0	Yes	Paletz	0	Yes	Wolverine	0	Yes	Atlas-Apex	0	Yes			0
400	Prequalified	**0**	**Paletz**	Latite	0		Paletz	0		Wolverine	0		Atlas-Apex	0				0
	BP07300.2 - Roofing /Flashing/Roof Specialties - Scope	20,567			**20,567**			**20,567**			**20,567**			**20,567**				**0**
	Membrane roofing	**20,567**			20,567			20,567			20,567			20,567				0
100	EXCLUDED: Hybrid Roof System 40YR Warranted Roof, Min. R-20 Insulation, Composite/ Non composite steel deck with normal weight Concrete FL47798	**0**	**Paletz**	Latite	0	N/A	Paletz	0	N/A	Wolverine	0	N/A	Atlas-Apex	0	N/A			0
102	Hot-applied, 3-ply Modified Bitumen Roof System - RFI #PC-58	**0**	**Paletz**	Latite	0	Yes	Paletz	0	Yes	Wolverine	0	Yes	Atlas-Apex	0	Yes			0
104	R-20 Lightweight Insulated Concrete	**0**	**Paletz**	Latite	0	Yes	Paletz	0	Yes	Wolverine	0	Yes	Atlas-Apex	0	Yes			0
116	Warranty: 20-year NDL manufacturer's warranty	**0**	**Paletz**	Latite	0	Yes	Paletz	0	Yes	Wolverine	0	Yes	Atlas-Apex	0	Yes			0
118	Warranty: 2-year workmanship warranty.	**0**	**Paletz**	Latite	0	Yes	Paletz	0	Yes	Wolverine	0	Yes	Atlas-Apex	0	Yes			0
122	Downspouts - (Tag 1)	**0**	**Paletz**	Latite	0	Yes	Paletz	0	Yes	Wolverine	0	Yes	Atlas-Apex	0	Yes			0
124	Overflow Scupper (Stainless Steel Scuppers) - (Tag 2)	**0**	**Paletz**	Latite	0	Yes	Paletz	0	Yes	Wolverine	0	Yes	Atlas-Apex	0	Yes			0
126	Coping at parapet walls	**0**	**Paletz**	Latite	0	Yes	Paletz	0	Yes	Wolverine	0	Yes	Atlas-Apex	0	Yes			0
127	Coping, color to match RAL 7032 & RAL 9003 or equal - RFI #PC-27.	**0**	**Paletz**	Latite	0	No	Paletz	0	No	Wolverine	0	No	Atlas-Apex	0	No			0
128	Extend membrane up & over parapet	**0**	**Paletz**	Latite	0	Yes	Paletz	0	Yes	Wolverine	0	Yes	Atlas-Apex	0	Yes			0
130	Seal gap per Detail 6/A-450	**0**	**Paletz**	Latite	0		Paletz	0	Yes	Wolverine	0	Yes	Atlas-Apex	0	Yes			0
134	Lifting Equipment	**0**	**Paletz**	Latite	0	Yes	Paletz	0	Yes	Wolverine	0	Yes	Atlas-Apex	0	Yes			0
901	R25 minimu ilo R20	**20,567**	**Paletz**	Latite	20,567	X Sub	Paletz	20,567	Sub +	Wolverine	20,567	X Sub	Atlas-Apex	20,567	X Sub			0

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP07400 - Roof Panels/Wall Panels/Siding	**215,000**			**215,000**		**Not KL Qualified**	**178,700**			**0**			**0**			**0**	
	BP07400.0 - Roof Panels/Wall Panels/Siding - General	**215,000**			**215,000**			**178,700**			**0**			**0**			**0**	
	Metal roof and wall panels	**215,000**			215,000			178,700			0			0			0	
100	Base Bid - Metal Facade Panel System	**215,000**	**Lotspeich**	Lotspeich	215,000	Yes	Kistler	178,700	Yes		0			0			0	
102	Sales Taxes	**0**	**Lotspeich**	Lotspeich	0	Yes	Kistler	0	Yes		0			0			0	
106	Prequalified	**0**	**Lotspeich**	Lotspeich	0	Yes	Kistler	0	No		0			0			0	
	BP07400.2 - Roof Panels/Wall Panels/Siding - Scope	**0**			**0**			**0**			**0**			**0**			**0**	
	Metal roof and wall panels	**0**			0			0			0			0			0	
100	Stair Tower Metal Paneling	**0**	**Lotspeich**	Lotspeich	0	Yes	Kistler	0	Yes		0			0			0	
102	Basis of design: 4MM Alucobond Plus System	**0**	**Lotspeich**	Lotspeich	0	Yes	Kistler	0	Yes		0			0			0	
104	MTL-1 - Alucobond Product, Color Krispy Green	**0**	**Lotspeich**	Lotspeich	0	Yes	Kistler	0	Yes		0			0			0	
106	MTL-2 - Alucobond Product, Color Botanic	**0**	**Lotspeich**	Lotspeich	0	Yes	Kistler	0	Yes		0			0			0	
111	Alucobond Metal Panel Coping at Stair tower - Color to match MTL-1 and MTL-2 - per RFI PC-26	**0**	**Lotspeich**	Lotspeich	0	Yes	Kistler	0	Yes		0			0			0	
112	Fluid Applied Waterproofing behind stair tower metal paneling - See Waterproofing	**0**	**Lotspeich**	Lotspeich	0	No	Kistler	0	No		0			0			0	
114	Material Warranty - 10 years from date of Substantial Completion.	**0**	**Lotspeich**	Lotspeich	0	Yes	Kistler	0	Yes		0			0			0	
116	Workmanship Warranty - 2 years from the date of Substantial Completion.	**0**	**Lotspeich**	Lotspeich	0	Yes	Kistler	0	Yes		0			0			0	
118	Warranty on Panel Finishes - 20 years from date of Substantial Completion.	**0**	**Lotspeich**	Lotspeich	0	Yes	Kistler	0	Yes		0			0			0	
120	See Div 10 for Install sign at Alucobond panels	**0**	**Lotspeich**	Lotspeich	0	No	Kistler	0	No		0			0			0	
122	Delivery and Installation	**0**	**Lotspeich**	Lotspeich	0	Yes	Kistler	0	Yes		0			0			0	
124	Engineering and Shop Drawings	**0**	**Lotspeich**	Lotspeich	0	Yes	Kistler	0	Yes		0			0			0	
126	Excluded - 10% Attic Stock per RFI #PC-43.	**0**	**Lotspeich**	Lotspeich	0	No	Kistler	0	No		0			0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP07800 - Fireproofing/Firestopping	**25,950**			**25,950**			**0**			**0**			**0**			**0**	
	BP07800.0 - Fireproofing/Firestopping - General	**23,330**			**23,330**			**0**			**0**			**0**			**0**	
	Waterproofing and dampproofing	**23,330**			23,330			0			0			0			0	
100	Fireproofing Base Bid Per Quote	**23,330**	**Southern Foam**	Southern Foam	23,330	Yes		0			0			0			0	
200	Sales Tax	**0**	**Southern Foam**	Southern Foam	0	Yes		0			0			0			0	
400	Prequalified	**0**	**Southern Foam**	Southern Foam	0			0			0			0			0	
	BP07800.2 - Fireproofing/Firestopping - Scope	**2,620**			**2,620**			**0**			**0**			**0**			**0**	
	Thermal protection	**2,620**			2,620			0			0			0			0	
	Spray Polyurethane Closed Cell Foam R-19 rating	**0**	**Southern Foam**	Southern Foam	0	Yes		0			0			0			0	
	Underside of the level 2 slab (ground floor ceiling) at Flam. Storage & Tire Storage.	**0**	**Southern Foam**	Southern Foam	0	Yes		0			0			0			0	
	Intumescent Thermal Barrier	**2,620**	**Southern Foam**	Southern Foam	2,620	Yes		0			0			0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP08100 - Doors/Frames/Hardware	**526,800**			**569,850**			**612,465**			**526,800**			**0**			**0**	
	BP08100.0 - Doors/Frames/Hardware - General	**524,000**			**498,800**			**0**			**524,000**			**0**			**0**	
	Doors and windows	**524,000**			498,800			0			524,000			0			0	
100	Doors & Hardware Base Bid per Quote	**524,000**	**Dash Doors**	Lotspeich	498,800	Yes	Atlantic Doors	0	Yes	Dash Doors	524,000	Yes		0			0	
200	Sales Tax	**0**	**Dash Doors**	Lotspeich	0	Yes	Atlantic Doors	0	Yes	Dash Doors	0	Yes		0			0	
400	Prequalified	**0**	**Dash Doors**	Lotspeich	0		Atlantic Doors	0		Dash Doors	0			0			0	
	BP08100.2 - Doors/Frames/Hardware - Scope	**2,800**			**71,050**			**612,465**			**2,800**			**0**			**0**	
	Doors and windows	**2,800**			71,050			612,465			2,800			0			0	
100	Meets design criteria Sheet S-002 (Level E impact - Risk Category IV)	**0**	**Dash Doors**	Lotspeich	0		Atlantic Doors	0	Yes	Dash Doors	0	Yes		0			0	
101	HM Doors	**0**	**Dash Doors**	Lotspeich	0	Yes	Atlantic Doors	158,190	Yes	Dash Doors	0	Yes		0			0	
102	Wood Doors	**0**	**Dash Doors**	Lotspeich	0	Yes	Atlantic Doors	57,505	Yes	Dash Doors	0	Yes		0			0	
102	WD-1 - Door (Solid Wood) Veneer: VT Industries Architectural Wood Doors, Select White Birch | A Grade, Quarter Sliced Veneer, Color Wheat WH18	**0**	**Dash Doors**	Lotspeich	0	Yes	Atlantic Doors	0	Yes	Dash Doors	0	Yes		0			0	
102	WD-1 - Door (Solid Wood) Veneer: Coverage for delamination of veneer, warping beyond specified installation tolerances, defective materials, and telegraphing core construction	**0**	**Dash Doors**	Lotspeich	0	Yes	Atlantic Doors	0	Yes	Dash Doors	0	Yes		0			0	
104	Fire Rated Doors	**0**	**Dash Doors**	Lotspeich	0	Yes	Atlantic Doors	0	Yes	Dash Doors	0	Yes		0			0	
106	Hollow metal frame, non-rated	**0**	**Dash Doors**	Lotspeich	0	Yes	Atlantic Doors	0	Yes	Dash Doors	0	Yes		0			0	
108	Hollow metal frame, rated	**0**	**Dash Doors**	Lotspeich	0	Yes	Atlantic Doors	0	Yes	Dash Doors	0	Yes		0			0	
114	Hardware included.	**0**	**Dash Doors**	Lotspeich	0	Yes	Atlantic Doors	296,930	Yes	Dash Doors	0	Yes		0			0	
115	Thermal Rated doors for the main doors separating the conditioned space from the unconditioned space - per RFI #PC-53.	**0**	**Dash Doors**	Lotspeich	0	Yes	Atlantic Doors	0	Yes	Dash Doors	0	Yes		0			0	
116	Warranty: five year after Date of Substantial Completion	**0**	**Dash Doors**	Lotspeich	45,000	Sub +	Atlantic Doors	0	Yes	Dash Doors	0	No		0			0	
118	3rd Floor: Double HM Door for future building addition - Door 250 per RFI PC-21	**0**	**Dash Doors**	Lotspeich	0	Yes	Atlantic Doors	0	Yes	Dash Doors	0	Yes		0			0	
124	Delivery	**0**	**Dash Doors**	Lotspeich	0	Yes	Atlantic Doors	0	Yes	Dash Doors	0	Yes		0			0	
124	Installation	**0**	**Dash Doors**	Lotspeich	0	Yes	Atlantic Doors	73,790	Yes	Dash Doors	0	Yes		0			0	
126	Handling and offloading	**0**	**Dash Doors**	Lotspeich	0	Yes	Atlantic Doors	0		Dash Doors	0	Yes		0			0	
128	Install Frames in tilt walls	**2,800**	**Dash Doors**	Lotspeich	2,800	Sub +	Atlantic Doors	2,800	X Sub	Dash Doors	2,800	X Sub		0			0	
129	Install grout filled frames	**0**	**Dash Doors**	Lotspeich	23,250	Sub +	Atlantic Doors	23,250	X Sub	Dash Doors	0	Yes		0			0	
130	Hanging doors	**0**	**Dash Doors**	Lotspeich	0	Yes	Atlantic Doors	0	Yes	Dash Doors	0	Yes		0			0	
132	Vision Lights	**0**	**Dash Doors**	Lotspeich	0	Yes	Atlantic Doors	0	Yes	Dash Doors	0	Yes		0			0	
134	Related NOAs	**0**	**Dash Doors**	Lotspeich	0	Yes	Atlantic Doors	0	Yes	Dash Doors	0	Yes		0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP08330 - OH Coiling/Sectional Doors	**142,600**			**143,950**			**142,600**			**160,000**			**0**			**0**	
	BP08330.0 - OH Coiling/Sectional Doors - General	**142,600**			**143,950**			**142,600**			**160,000**			**0**			**0**	
	Doors and windows	**142,600**			143,950			142,600			160,000			0			0	
100	Rolling Door Base Bid	**142,600**	**Door Systems of South FL**	Overhead Door Co. of S	143,950	Yes	Door Systems of South F	142,600	Yes	Coast to Coast Garage D	160,000	Yes	Rolling Door Manufactur	0			0	
200	Sales Tax	**0**	**Door Systems of South FL**	Overhead Door Co. of S	0	Yes	Door Systems of South F	0	Yes	Coast to Coast Garage D	0	Yes	Rolling Door Manufactur	0			0	
400	Prequaliied	**0**	**Door Systems of South FL**	Overhead Door Co. of S	0		Door Systems of South F	0		Coast to Coast Garage D	0		Rolling Door Manufactur	0			0	
	BP08330.2 - OH Coiling/Sectional Doors - Scope	**0**			**0**			**0**			**0**			**0**			**0**	
	Doors and windows	**0**			0			0			0			0			0	
100	(1) Roll -Up Door (Type D7) at Tire Storage	**0**	**Door Systems of South FL**	Overhead Door Co. of S	0	Yes	Door Systems of South F	0	Yes	Coast to Coast Garage D	0	Yes	Rolling Door Manufactur	0			0	
102	(8) Roll -Up Doors (Type D6) at Bay Area	**0**	**Door Systems of South FL**	Overhead Door Co. of S	0	Yes	Door Systems of South F	0	Yes	Coast to Coast Garage D	0	Yes	Rolling Door Manufactur	0			0	
104	Doors Type (D6) with approved Exterior NOA - (Exterior Doors)	**0**	**Door Systems of South FL**	Overhead Door Co. of S	0	Yes	Door Systems of South F	0	Yes	Coast to Coast Garage D	0		Rolling Door Manufactur	0			0	
106	Door Type (D7) is Roll-Up Door Light Gauge. - (Interior Door)	**0**	**Door Systems of South FL**	Overhead Door Co. of S	0	Yes	Door Systems of South F	0	Yes	Coast to Coast Garage D	0		Rolling Door Manufactur	0			0	
107	No insulation required for the (8) Bay Doors - per RFI #PC-53.	**0**	**Door Systems of South FL**	Overhead Door Co. of S	0	Yes	Door Systems of South F	0	Yes	Coast to Coast Garage D	0	Yes	Rolling Door Manufactur	0			0	
108	Electric Operators	**0**	**Door Systems of South FL**	Overhead Door Co. of S	0	Yes	Door Systems of South F	0	Yes	Coast to Coast Garage D	0	Yes	Rolling Door Manufactur	0			0	
110	Control Station	**0**	**Door Systems of South FL**	Overhead Door Co. of S	0	Yes	Door Systems of South F	0	Yes	Coast to Coast Garage D	0	Yes	Rolling Door Manufactur	0			0	
112	Safety Edge	**0**	**Door Systems of South FL**	Overhead Door Co. of S	0	Yes	Door Systems of South F	0	Yes	Coast to Coast Garage D	0		Rolling Door Manufactur	0			0	
113	Meets the wind load design criteria on Structural S-002	**0**	**Door Systems of South FL**	Overhead Door Co. of S	0	Yes	Door Systems of South F	0	Yes	Coast to Coast Garage D	0		Rolling Door Manufactur	0			0	
114	Furnish & Installation	**0**	**Door Systems of South FL**	Overhead Door Co. of S	0	Yes	Door Systems of South F	0	Yes	Coast to Coast Garage D	0	Yes	Rolling Door Manufactur	0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP08450 - Glass & Glazing Systems	**697,928**		**Not to Spec**	**583,490**			**697,928**			**999,619**			**0**			**0**	
	BP08450.0 - Glass & Glazing Systems - General	**669,722**			**351,948**			**669,722**			**855,594**			**0**			**0**	
	Doors and windows	**669,722**			351,948			669,722			855,594			0			0	
100	Glass & Glazing base bid	**665,723**	**Dash Door & Glass**	Infinite Windows	347,949	Yes	Dash Door & Glass	665,723	Yes	Palm Beach Glass	855,594	Yes		0			0	
200	Sales Tax	**0**	**Dash Door & Glass**	Infinite Windows	0	Yes	Dash Door & Glass	0	Yes	Palm Beach Glass	0	Yes		0			0	
400	Prequalified	**0**	**Dash Door & Glass**	Infinite Windows	0		Dash Door & Glass	0		Palm Beach Glass	0			0			0	
	BP08450.2 - Glass & Glazing Systems - Scope	**28,206**			**231,542**			**28,206**			**144,025**			**0**			**0**	
	Doors and windows	**-24,154**			193,410			-24,154			105,893			0			0	
100	Exterior Storefronts	**0**	**Dash Door & Glass**	Infinite Windows	0	Sub +	Dash Door & Glass	0	Yes	Palm Beach Glass	0	Yes		0			0	
100	Meets the wind load design criteria on Structural S-002	**0**	**Dash Door & Glass**	Infinite Windows	0	No	Dash Door & Glass	0	Yes	Palm Beach Glass	0	No		0			0	
100	Curtain Walls BOD: YKK AP; 300 OG - specs book	**0**	**Dash Door & Glass**	Infinite Windows	0	No	Dash Door & Glass	0	Yes	Palm Beach Glass	0			0			0	
101	Exterior Storefront Specification - Trulite Glass & Aluminum Solutions	**0**	**Dash Door & Glass**	Infinite Windows	0	No	Dash Door & Glass	0	No	Palm Beach Glass	0	Yes		0			0	
101	Meets the performance requirements on RFI #PC-14	**0**	**Dash Door & Glass**	Infinite Windows	30,412	Sub +	Dash Door & Glass	0	Yes	Palm Beach Glass	0			0			0	
102	Exterior Storefronts - Aluminum Frames Finish Color anodized.	**0**	**Dash Door & Glass**	Infinite Windows	0	No	Dash Door & Glass	0	Yes	Palm Beach Glass	0	Yes		0			0	
104	Exterior Storefronts - five (5) year manufacturer warranty	**0**	**Dash Door & Glass**	Infinite Windows	0	Yes	Dash Door & Glass	0	Yes	Palm Beach Glass	0			0			0	
108	Exterior - Necessary steel beams / columns for structural support of storefronts	**5,280**	**Dash Door & Glass**	Infinite Windows	5,280	Sub +	Dash Door & Glass	5,280	X Sub	Palm Beach Glass	5,280	X Sub		0			0	
110	Exterior - Windows S1, S2, S3, S3.1, S4, S5, S6, S7.	**0**	**Dash Door & Glass**	Infinite Windows	0	Yes	Dash Door & Glass	0	Yes	Palm Beach Glass	0			0			0	
112	Exterior - S8 Storefront at Stair Tower	**0**	**Dash Door & Glass**	Infinite Windows	0	Yes	Dash Door & Glass	0	Yes	Palm Beach Glass	0	Yes		0			0	
114	Exterior - Caulking for windows and storefronts	**0**	**Dash Door & Glass**	Infinite Windows	0	Yes	Dash Door & Glass	0	Yes	Palm Beach Glass	20,513	Sub +		0			0	
115	Exterior - Blue Max protection (exterior side)	**8,250**	**Dash Door & Glass**	Infinite Windows	0	Yes	Dash Door & Glass	8,250	Sub +	Palm Beach Glass	23,585	Sub +		0			0	
115	Exterior - Aluminum Railing with Integrated Glass Panels at 2nd Level Patio	**7,140**	**Dash Door & Glass**	Infinite Windows	7,140	Sub +	Dash Door & Glass	7,140	X Sub	Palm Beach Glass	7,140	X Sub		0			0	
115	Exterior - Approved NOA for glass railings	**0**	**Dash Door & Glass**	Infinite Windows	0		Dash Door & Glass	0		Palm Beach Glass	0			0			0	
116	Hardware - Weatherstripping	**0**	**Dash Door & Glass**	Infinite Windows	0		Dash Door & Glass	0	Yes	Palm Beach Glass	0			0			0	
118	Hardware - Sill sweep strip	**0**	**Dash Door & Glass**	Infinite Windows	0		Dash Door & Glass	0	Yes	Palm Beach Glass	0			0			0	
120	Hardware - Thresholds	**0**	**Dash Door & Glass**	Infinite Windows	0		Dash Door & Glass	0	Yes	Palm Beach Glass	0			0			0	
123	Hardware - Standard Panic Hardware	**0**	**Dash Door & Glass**	Infinite Windows	0		Dash Door & Glass	0	Yes	Palm Beach Glass	0			0			0	
200	Interior - Storefronts at Offices	**0**	**Dash Door & Glass**	Infinite Windows	61,587	Sub +	Dash Door & Glass	0	Yes	Palm Beach Glass	0			0			0	
201	Interior - W1 - Sliding Window Sheet A-201A.	**0**	**Dash Door & Glass**	Infinite Windows	0	Yes	Dash Door & Glass	0	Yes	Palm Beach Glass	0			0			0	
202	See Div 10 for - Nana Wall Partitions at Command Center	**0**	**Dash Door & Glass**	Infinite Windows	0	No	Dash Door & Glass	0	No	Palm Beach Glass	0			0			0	
204	See Div 5 for - Necessary steel support / column for Nana Wall Partitions at Command Center - See Div 5	**0**	**Dash Door & Glass**	Infinite Windows	0	No	Dash Door & Glass	0	No	Palm Beach Glass	0			0			0	
206	Interior - WF-1 Window Film at Command Center & Lobby 100 (new)	**0**	**Dash Door & Glass**	Infinite Windows	6,696	Sub +	Dash Door & Glass	0	Yes	Palm Beach Glass	6,696	X Sub		0			0	
207	Interior - WF-2 Window Film at Private Offices (new)	**0**	**Dash Door & Glass**	Infinite Windows	42,143	Sub +	Dash Door & Glass	0	Yes	Palm Beach Glass	42,143	X Sub		0			0	
207	Interior - Window Film at W1 Window (new)	**536**	**Dash Door & Glass**	Infinite Windows	536	Sub +	Dash Door & Glass	536	X Sub	Palm Beach Glass	536	X Sub		0			0	
208	Interior - Wall Mirrors at Gym - 1/4" thick Tempered Mirror Glass with safety backing film	**0**	**Dash Door & Glass**	Infinite Windows	13,200	Sub +	Dash Door & Glass	0	Yes	Palm Beach Glass	0	Yes		0			0	
209	See Furniture for Glass Writable Surface / Glass Boards (Tags E15 & E16)	**-52,360**	**Dash Door & Glass**	Infinite Windows	0	No	Dash Door & Glass	-52,360	No	Palm Beach Glass	0	No		0			0	
209	See Div 10 for 1/4" thick back painted glass w/ applied city of logo at reception area - 1/A-613. - See Div 10 Signage	**0**	**Dash Door & Glass**	Infinite Windows	0	No	Dash Door & Glass	0	No	Palm Beach Glass	0			0			0	
210	Interior - Vision Lites	**0**	**Dash Door & Glass**	Infinite Windows	5,018	Sub +	Dash Door & Glass	0	Yes	Palm Beach Glass	0			0			0	
212	Wood bucks (if required)	**0**	**Dash Door & Glass**	Infinite Windows	14,398	X Sub	Dash Door & Glass	0	N/A	Palm Beach Glass	0			0			0	
300	Furnish & Installation	**0**	**Dash Door & Glass**	Infinite Windows	0	Yes	Dash Door & Glass	0	Yes	Palm Beach Glass	0			0			0	
302	Enginering and Shop Drawings	**0**	**Dash Door & Glass**	Infinite Windows	0	Yes	Dash Door & Glass	0	Yes	Palm Beach Glass	0			0			0	
304	Lifting equipment	**0**	**Dash Door & Glass**	Infinite Windows	0	Yes	Dash Door & Glass	0	Yes	Palm Beach Glass	0			0			0	
901	Tempering of Wall mirrors at Gym	**7,000**	**KL Estimate**	KL Estimate	7,000		KL Estimate	7,000			0			0			0	
	Glass	**52,360**			38,132			52,360			38,132			0			0	
200	Glass Writable Surface / Glass Boards (Tags E15 & E16)	**52,360**	**Dash Door & Glass**	Infinite Windows	38,132	Sub +	Dash Door & Glass	52,360	Yes	Palm Beach Glass	38,132	X Sub		0			0	

****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP09100 - Cement Plastering/Stucco	**21,400**			**21,400**			**37,900**			**60,000**			**0**			**0**	
	BP09100.0 - Cement Plastering/Stucco - General	**21,400**			**21,400**			**37,900**			**60,000**			**0**			**0**	
	Plaster and gypsum board	**21,400**			21,400			37,900			60,000			0			0	
100	Stucco Base Bid Per Quote	**21,400**	**Atlantic Interior Contracting**	Atlantic Interior Contract	21,400	Yes	Atlantic Interior Services	37,900	Yes	Lotspeich	60,000	Yes		0			0	
200	Sales Tax	**0**	**Atlantic Interior Contracting**	Atlantic Interior Contract	0	Yes	Atlantic Interior Services	0		Lotspeich	0	Yes		0			0	
400	Prequalified	**0**	**Atlantic Interior Contracting**	Atlantic Interior Contract	0		Atlantic Interior Services	0		Lotspeich	0			0			0	
	BP09100.2 - Cement Plastering/Stucco - Scope	**0**			**0**			**0**			**0**			**0**			**0**	
	Plaster and gypsum board	**0**			0			0			0			0			0	
100	EXT. CEILINGS	**0**	**Atlantic Interior Contracting**	Atlantic Interior Contract	0	Yes	Atlantic Interior Services	0	Yes	Lotspeich	0	Yes		0			0	
101	5/8" Outdoor Patio Stucco Ceilings	**0**	**Atlantic Interior Contracting**	Atlantic Interior Contract	0	Yes	Atlantic Interior Services	0	Yes	Lotspeich	0	Yes		0			0	
102	5/8" Stair 2 Ext. Stucco Ceilings	**0**	**Atlantic Interior Contracting**	Atlantic Interior Contract	0	Yes	Atlantic Interior Services	0	Yes	Lotspeich	0	Yes		0			0	
103	5/8" West Breezeway Ext. Stucco Ceilings	**0**	**Atlantic Interior Contracting**	Atlantic Interior Contract	0	Yes	Atlantic Interior Services	0	Yes	Lotspeich	0	Yes		0			0	
104	EXT. FRAMING - Included in Div 09 - Drywall	**0**	**Atlantic Interior Contracting**	Atlantic Interior Contract	0	No	Atlantic Interior Services	0	No	Lotspeich	0	No		0			0	
200	3-5/8" 18GA Steel Stud Framing 24" O.C. - Outdoor Patio	**0**	**Atlantic Interior Contracting**	Atlantic Interior Contract	0	No	Atlantic Interior Services	0	No	Lotspeich	0	No		0			0	
201	3-5/8" 18GA Steel Stud Framing 24" O.C. - West Walkway	**0**	**Atlantic Interior Contracting**	Atlantic Interior Contract	0	No	Atlantic Interior Services	0	No	Lotspeich	0	No		0			0	
202	3-5/8" 18GA Steel Stud Framing 24" O.C. - 2nd Floor Balcony	**0**	**Atlantic Interior Contracting**	Atlantic Interior Contract	0	No	Atlantic Interior Services	0	No	Lotspeich	0	No		0			0	
202	Cutouts for Lighting/Electical/Jboxes	**0**	**Atlantic Interior Contracting**	Atlantic Interior Contract	0	Yes	Atlantic Interior Services	0	Yes	Lotspeich	0	Yes		0			0	
300	MISC	**0**	**Atlantic Interior Contracting**	Atlantic Interior Contract	0	Yes	Atlantic Interior Services	0	Yes	Lotspeich	0	Yes		0			0	
301	Control Joints/Reveals	**0**	**Atlantic Interior Contracting**	Atlantic Interior Contract	0	Yes	Atlantic Interior Services	0	Yes	Lotspeich	0	Yes		0			0	
302	Installation	**0**	**Atlantic Interior Contracting**	Atlantic Interior Contract	0	Yes	Atlantic Interior Services	0	Yes	Lotspeich	0	Yes		0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP09250 - Gypsum Board Assemblies	**761,668**			**942,900**			**761,668**			**955,300**			**0**			**0**	
	BP09250.0 - Gypsum Board Assemblies - General	**761,668**			**919,900**			**761,668**			**932,000**			**0**			**0**	
	Gypsum board assemblies	**761,668**			919,900			761,668			932,000			0			0	
100	Drywall & Framing Bid	**761,668**	**FL Crane**	Atlantic Interior Services	919,900	Yes	FL Crane	761,668	Yes	Atlantic Interior Contract	898,300	Yes		0			0	
102	Insulation	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
104	Exterior Framing	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	33,700	Yes		0			0	
106	Sales Tax	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
108	Prequalified	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
108	10% Attic Stock - RFI - PC-43	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	No		0			0	
	BP09250.2 - Gypsum Board Assemblies - Scope	**0**			**23,000**			**0**			**23,300**			**0**			**0**	
	Gypsum board assemblies	**0**			23,000			0			23,300			0			0	
100	FRAMING	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
102	Interior partitions: 1-5/8" metal furring studs	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
103	Interior partitions: 3-5/8" metal studs	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
104	Exterior wall stud framing supporting interior finishes	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
105	Exterior Framing for Stucco 16GA (G90)	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
106	20 GA steel studs @ 16" O.C. w/ G60 Coating	**0**	**FL Crane**	Atlantic Interior Services	23,000	X Sub	FL Crane	0	Yes	Atlantic Interior Contract	23,300	Yes		0			0	
107	Tracks, Runners, Bridges, and Bracing	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
108	Door Framing	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
109	Mechanical Chases	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
110	Installation of HM Door Frames in Drywall Partitions	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
200	DRYWALL/CEMENTBOARD	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
201	5/8" Drywall @ Walls/Ceilings	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
202	1/2" Drywall @ Soffit Linings	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
203	5/8" Cementboard @ Walls to receive tile	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
204	Corner Beads/Trims	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
206	Acoustical Sealants @ Top/Bottom of Partitions	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
207	Spray Texture @ Exterior Tilt Walls	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
208	Gypsum Ceiling ACT integration and Trims	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
208	EOC Command Center - Reglet Reveal	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
300	INSULATION	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
301	EXT. Wall Rigid Insulation 1-1/2" DOW THERMAX - OAE	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
302	Provide 3/8" Airspace in Required Wall Types	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
303	Mineral Wool Insulation in Acoustical Walls - STC 55-60	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
304	Form Fit Acoustical Batt Insulation	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
400	MISC	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
400	Installation	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
400	Clean up	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
400	Mobilization	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	
400	Level 4 Finish	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	FL Crane	0	Yes	Atlantic Interior Contract	0	Yes		0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP09500 - Ceilings - ACT/Linear Metal/Wood	**373,416**			**391,974**			**397,990**			**373,416**			**0**			**0**	
	BP09500.0 - Ceilings - ACT/Linear Metal/Wood - General	369,416			**235,000**			**304,016**			**369,416**			**0**			**0**	
	Gypsum board assemblies	**369,416**			235,000			304,016			369,416			0			0	
100	Ceilings Base Bid	**369,416**	**FL Crane**	Atlantic Interior Services	235,000	Yes	Residential Acoustics	304,016	Yes	FL Crane	369,416	Yes		0			0	
101	Sales Tax	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	Residential Acoustics	0	Yes	FL Crane	0	Yes		0			0	
103	Prequalified	**0**	**FL Crane**	Atlantic Interior Services	0		Residential Acoustics	0		FL Crane	0			0			0	
	BP09500.2 - Ceilings - ACT/Linear Metal/Wood - Scope	4,000			**156,974**			**93,974**			**4,000**			**0**			**0**	
	Gypsum board assemblies	**4,000**			156,974			93,974			4,000			0			0	
100	ACT CEILINGS	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	Residential Acoustics	0	Yes	FL Crane	0	Yes		0			0	
101	2x2 - Rockfon Koral (0.85 NRC, SLN edge, white)	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	Residential Acoustics	0	Yes	FL Crane	0	Yes		0			0	
102	2x2 - Rockfon CM Tempra 4000 (9/16" thick, white) OR Rockfon Sonar	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	Residential Acoustics	0	Yes	FL Crane	0	Yes		0			0	
103	2x4 - Rockfon Sonar (0.95 NRC, CDX edge) with Infinity Standard System	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	Residential Acoustics	0	Yes	FL Crane	0	Yes		0			0	
104	Armstrong 15/16" Grid	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	Residential Acoustics	0	Yes	FL Crane	0	Yes		0			0	
105	Edge Trim	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	Residential Acoustics	0	Yes	FL Crane	0	Yes		0			0	
200	METAL CEILINGS	**0**	**FL Crane**	Atlantic Interior Services	63,000	Yes	Residential Acoustics	0	Yes	FL Crane	0	Yes		0			0	
201	Rockfon Planar Macroplus Linear 8" Metal - Woodlook Panels	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	Residential Acoustics	0	Yes	FL Crane	0	Yes		0			0	
202	Rockfon Planar Macroplus Linear 8" - RAL 9016	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	Residential Acoustics	0	Yes	FL Crane	0	Yes		0			0	
203	Perforated + Acoutex Backer	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	Residential Acoustics	0	Yes	FL Crane	0	Yes		0			0	
203	VE: USG Planx ILO Rockfon Planar Macroplus	**0**	**FL Crane**	Atlantic Interior Services	0	No	Residential Acoustics	0	No	FL Crane	0	No		0			0	
300	ACOUSTICAL CEILINGS	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	Residential Acoustics	0	Yes	FL Crane	0	Yes		0			0	
300	Autex Acoustics Opera Grid Ceiling Tiles	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	Residential Acoustics	0	Yes	FL Crane	0	Yes		0			0	
300	Acoufelt Fracture Ceiling Panels	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	Residential Acoustics	0	Yes	FL Crane	0	Yes		0			0	
300	Acoustical Wall Panels 24x24 Zintra Etch Tile Squares	**0**	**FL Crane**	Atlantic Interior Services	89,974	X Sub	Residential Acoustics	89,974	X Sub	FL Crane	0	Yes		0			0	
300	Green Wall @ 1st Floor Reception/Lobby	**4,000**	**FL Crane**	Atlantic Interior Services	4,000	KLEst	Residential Acoustics	4,000	KLEst	FL Crane	4,000	KLEst		0			0	
301	15/16" Grids	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	Residential Acoustics	0	Yes	FL Crane	0	Yes		0			0	
500	MISC	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	Residential Acoustics	0	Yes	FL Crane	0	Yes		0			0	
500	Shipping & Handling	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	Residential Acoustics	0	Yes	FL Crane	0	Yes		0			0	
500	Installation	**0**	**FL Crane**	Atlantic Interior Services	0	Yes	Residential Acoustics	0	Yes	FL Crane	0	Yes		0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP09600 - Flooring Package	**418,846**			**418,846**			**589,300**			**467,446**			**0**			**0**	
	BP09600.0 - Flooring Package - General	**316,346**			**316,346**			**604,200**			**428,145**			**0**			**0**	
	Floors	**316,346**			316,346			604,200			428,145			0			0	
100	Flooring Bid	**271,080**	**American Flooring Services**	American Flooring Servi	271,080	Yes	O'Neill Brothers	604,200	Yes	GPC	397,705	Yes		0			0	
102	Sales Tax	**12,838**	**American Flooring Services**	American Flooring Servi	12,838	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
106	Prequalified	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
110	10% Attic Stock - RFI - PC-43	**32,428**	**American Flooring Services**	American Flooring Servi	32,428	Yes	O'Neill Brothers	0	Yes	GPC	30,440	Yes		0			0	
	BP09600.2 - Flooring Package - Scope	**102,500**			**102,500**			**-14,900**			**39,301**			**0**			**0**	
	Floors	**89,000**			89,000			-28,400			9,701			0			0	
300	PORCELAIN TILE	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
301	12" x 24" Porcelain Tile - Del Conca - (PT1)	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
302	12" x 12" Porcelain Tile Sheet - Mosaic Del Conca (PT1a)	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
303	4" x 12" Porcelain Tile Base - Del Conca (PT1b)	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
304	24" x 48" Porcelain Tile - Trinity - (PT2)	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
305	3" x 12" Porcelain Base - Trinity - (PT2b)	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
306	12" x 24" Porcelain Wall Tile - Trinity - (PT3)	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
307	Mud Set	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
308	Grout	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	-28,400	Yes	GPC	0	Yes		0			0	
309	Waterproofing Beneath Tile - Bathrooms	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
700	SEALED CONCRETE - IN PAINTING	**0**	**American Flooring Services**	American Flooring Servi	0	No	O'Neill Brothers	0	No	GPC	0	Yes		0			0	
903	MISC	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
904	Installation	**89,000**	**American Flooring Services**	American Flooring Servi	89,000	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
905	Floor Protection	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	9,701	Yes		0			0	
905	Includes Floor Transitions - Schluter	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
	Specialty floors	**0**			0			0			16,100			0			0	
400	ENTRANCE MATS	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	16,100	Yes		0			0	
401	EMAT 4' x 8' - American Floor Mats (BOD)	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
402	Frames/Rails	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
403	Recess Fill	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
	Wood floors	**0**			0			0			0			0			0	
900	HARDWOOD FLOORING	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
901	7.5" x 6' Hardwood Flooring - Storia (OAE) - (HW1)	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
902	Sound Underlayment.	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
	Resilient flooring	**0**			0			0			0			0			0	
200	LUXURY VINYL TILE	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
201	10" x 40" LVT Tile - Interface - (LVT 1)	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
202	Low/No VOC Glue Down	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
203	Floor Prep	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
500	RUBBER TILE	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
501	24" x 24" Rubber Tile - Tarkett - (RT1)	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
502	24" x 24" Rubber Tile Gym Floor Logo - Tarkett - (RT2)	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
503	Low/No VOC Glue Down	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
	Static control flooring	**0**			0			0			0			0			0	
600	STATIC CONTROL FLOORING	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
601	24" x 24" - Forbo Static Tile - (ESD1)	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
602	Copper Tape Grounding	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
603	Adhesive - Per Manufactures Spec.	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
604	Electrical Coordination	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
	Carpet	**13,500**			13,500			13,500			13,500			0			0	
100	CARPET TILE	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
101	2' x 2' Carpet Tile - Interface (CPT1/2)	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
102	10" x 40" Carpet Tile - Interface (CPT3)	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
103	Glue Down - LOW VAC	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
104	Product Testing	**0**	**American Flooring Services**	American Flooring Servi	0	Yes	O'Neill Brothers	0	Yes	GPC	0	Yes		0			0	
901	Add Turf Allowance in front of Gym only on patio. $15 per sf	**13,500**	**Allowance**	Allowance	13,500		Allowance	13,500		Allowance	13,500			0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP09660 - Specialty Flooring - Wood/Epoxy/Athletic	**162,043**			**162,043**			**174,950**			**173,891**			**0**			**0**	
	BP09660.0 - Specialty Flooring - Wood/Epoxy/Athletic - General	**51,333**			**51,333**			**168,910**			**173,891**			**0**			**0**	
	Specialty floors	**51,333**			51,333			168,910			173,891			0			0	
905	Epoxy Flooring Base Bid Per Quote	**51,333**	**Bay To Bay**	Bay To Bay	51,333	Yes	Dura Floor	168,910	Yes	GPC	173,891	Yes		0			0	
905	Sales Tax	**0**	**Bay To Bay**	Bay To Bay	0	Yes	Dura Floor	0	Yes	GPC	0	Yes		0			0	
905	Prequalified	**0**	**Bay To Bay**	Bay To Bay	0	Yes	Dura Floor	0		GPC	0			0			0	
	BP09660.2 - Specialty Flooring - Wood/Epoxy/Athletic - Scope	**110,710**			**110,710**			**6,040**			**0**			**0**			**0**	
	Specialty floors	**110,710**			110,710			6,040			0			0			0	
305	High Build 1 Coat / 15 Mils	**0**	**Bay To Bay**	Bay To Bay	0	Yes	Dura Floor	0	Yes	GPC	0	Yes		0			0	
305	Integral Cove Base	**0**	**Bay To Bay**	Bay To Bay	0	Yes	Dura Floor	0	Yes	GPC	0	Yes		0			0	
305	Moisture Mitigation	**29,805**	**Bay To Bay**	Bay To Bay	29,805	Yes	Dura Floor	0	Yes	GPC	0	Yes		0			0	
305	Maintenance Bay 1/2/3	**0**	**Bay To Bay**	Bay To Bay	0	Yes	Dura Floor	0	Yes	GPC	0	Yes		0			0	
305	Vehicle Storage Bay	**0**	**Bay To Bay**	Bay To Bay	0	Yes	Dura Floor	0	Yes	GPC	0	Yes		0			0	
305	Custodial 130	**0**	**Bay To Bay**	Bay To Bay	0	Yes	Dura Floor	0	Yes	GPC	0	Yes		0			0	
305	2nd Floor Custodial	**0**	**Bay To Bay**	Bay To Bay	0	Yes	Dura Floor	0	Yes	GPC	0	Yes		0			0	
305	MISC	**0**	**Bay To Bay**	Bay To Bay	0	Yes	Dura Floor	0	Yes	GPC	0	Yes		0			0	
305	Installation	**74,865**	**Bay To Bay**	Bay To Bay	74,865	Yes	Dura Floor	0	Yes	GPC	0	Yes		0			0	
306	Allowance for Sealing or finishing of Concrete Benches at Memorial Plaza	**0**	**Bay To Bay**	Bay To Bay	0	No	Dura Floor	0	No	GPC	0	Yes		0			0	
900	Urithane Based Coating	**0**	**Bay To Bay**	Bay To Bay	0	Yes	Dura Floor	0	Yes	GPC	0	Yes		0			0	
901	Stamped concrete at balcony	**6,040**	**KL Estimate**	KL Estimate	6,040		KL Estimate	6,040			0			0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP09900 - Painting/Wallcovering	**194,144**			**215,927**			**194,144**			**227,118**			**233,315**				**0**
	BP09900.0 - Painting/Wallcovering - General	**167,831**			**200,583**			**167,831**			**185,000**			**198,500**				**0**
	Paints and coatings	**167,831**			200,583			167,831			185,000			198,500				0
100	Painting Base Bid Per Quote	**167,831**	**Premier One Painting**	Service Contracting Solu	200,583	Yes	Premier One Painting	167,831	Yes	Dorado Painting	185,000	Yes	Advance Painting	198,500	Yes			0
105	Sales Tax	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	0	Yes	Advance Painting	0	Yes			0
115	Prequalified	**0**	**Premier One Painting**	Service Contracting Solu	0		Premier One Painting	0		Dorado Painting	0		Advance Painting	0				0
	BP09900.2 - Painting/Wallcovering - Scope	**26,313**			**15,344**			**26,313**			**42,118**			**34,815**				**0**
	Paints and coatings	**26,313**			15,344			26,313			42,118			34,815				0
100	Exterior - 1st Coat: Sherwin-Williams Loxon Concrete and Masonry Primer Sealer LX02W50	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	0	Yes	Advance Painting	0				0
102	Exterior - 2nd and 3rd Coat: Sherwin-Williams A-100 Exterior Latex Satin, A82 Series	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	0	Yes	Advance Painting	0				0
104	Exterior - PNT-1 - SW, Product: TBD, Color: SW 7003 Toque White, Finish: Satin, Spray texture coating: Fine	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	25,000	Sub +	Advance Painting	25,000	X Sub			0
106	Exterior - PNT-2 - SW, Product: TBD, Color: SW 7542 Naturel, Finish: Satin, Spray texture coating: Fine	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	0		Advance Painting	0				0
108	Texture on tilt panels	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	0		Advance Painting	0				0
200	Interior - 1st Coat: Sherwin-Williams Loxon Concrete and Masonry Primer Sealer, LX02W50 Series.	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	0		Advance Painting	0				0
202	Interior - 2nd and 3rd Coat: Sherwin-Williams ProMar 200 Zero VOC Egg-Shell, B20-2600 Series.	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	0		Advance Painting	0				0
204	Interior - Finish: Egg-Shell.	**1,181**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	1,181	Sub +	Dorado Painting	15,000	Sub +	Advance Painting	0				0
206	Interior - 1 coat primer, 2 top coats	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	0		Advance Painting	0				0
208	Interior - PNT-1 - Paint (Ceiling &/Or Soffits): Benjamin Moore, Silver Satin OC-26, LOW VOC / Flat Finish.	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	0		Advance Painting	0				0
210	Interior - PNT-2 - Paint (Primary Field): Benjamin Moore, Gray Mist OC-30, LOW VOC/Satin Finish.	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	0		Advance Painting	0				0
212	Interior - PNT-3 - Paint (Door Frames): Benjamin Moore, Gray Mist OC-30, Acrylic Latex / Semi-Gloss.	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	0		Advance Painting	0				0
214	(New) Interior - PNT-4 - Paint (Accent 1) Conference Rooms: Benjamin Moore, Slate Blue 1648, LOW VOC/Satin Finish.	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	0		Advance Painting	0				0
216	Interior - PNT-5 - Paint (Accent 2): Benjamin Moore, Vienna Green 538, LOW VOC/Satin Finish.	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	0		Advance Painting	0				0
218	Interior - PNT-6 - Paint (Custodial): Benjamin Moore, Gray Mist OC-30, Acrylic Latex / Semi-Gloss.	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	0		Advance Painting	0				0
220	Interior - PNT-7 - Paint (Restrooms Ceilings): Benjamin Moore, Silver Satin OC-26, Acrylic Latex / Semi-Gloss.	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	0		Advance Painting	0				0
222	Interior - PNT-8 - Paint (Accent 3) Gym: Benjamin Moore, Amber 168, LOW VOC/Satin Finish.	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	0		Advance Painting	0				0
224	(New) Interior - PNT-9 - Paint Stair Stringers + HM Doors: Benjamin Moore Stone Hearth 984 LOW VOC / Semi-gloss	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	0		Advance Painting	0				0
226	(New) Interior - PNT-10 - Paint (Accent 5) Command Center + Small Conference Rooms: Benjamin Moore, Revere Pewter HC-172, LOW VOC/Satin Finish.	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	0		Advance Painting	0				0
228	(New) Interior - PNT-11 - Paint Work Bays: Benjamin Moore, Silver Gray 70, Corotech V440 Epoxy Finish Coat, Semi-gloss	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	0		Advance Painting	0				0
229	(New) Interior - PNT-12 - Paint Work Bays: Benjamin Moore Terra Cotta 22, Corotech V440 Epoxy Finish Coat, Semi-gloss	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	0		Advance Painting	0				0
230	Interior - Wall paint band at specified rooms	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	0		Advance Painting	0				0
300	Sealed Concrete - At specified room floors.	**8,692**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	8,692	Sub +	Dorado Painting	0	Yes	Advance Painting	8,692	X Sub			0
302	Sealed Concrete - Spec: Nightengal PBG, UV Resistant, Polyurethane Protectant Coating.	**0**	**Premier One Painting**	Service Contracting Solu	0	No	Premier One Painting	0	No	Dorado Painting	0	No	Advance Painting	0				0
304	Sealer at Memorial benches	**1,123**	**Premier One Painting**	Service Contracting Solu	1,123	X Sub	Premier One Painting	1,123	Sub +	Dorado Painting	1,123	X Sub	Advance Painting	1,123	X Sub			0
400	Necessary equipment	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	0	Yes	Advance Painting	0				0
404	Beauty Bead	**0**	**Premier One Painting**	Service Contracting Solu	0	Yes	Premier One Painting	0	Yes	Dorado Painting	0	Yes	Advance Painting	0				0
406	10% Attic Stock per RFI #PC-43.	**5,034**	**Premier One Painting**	Service Contracting Solu	3,938	Yes	Premier One Painting	5,034	Yes	Dorado Painting	995	Sub +	Advance Painting	0				0
901	Interior Paint as Benjamin Moore	**10,283**	**Premier One Painting**		10,283	X Sub	Premier One Painting	10,283	Sub +		0			0				0

**Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP10140 - Signage/Visual Display	**229,797**			**229,797**			**246,473**			**0**			**0**			**0**	
	BP10140.0 - Signage/Visual Display - General	**229,797**			**229,797**			**246,473**			**0**			**0**			**0**	
	Identification devices	**229,797**			229,797			246,473			0			0			0	
100	Base Bid - Interior Signage	**59,546**	**White Sign Company**	White Sign Company	59,546	Yes	Baron Sign Manufacturir	246,473	Yes		0			0			0	
100	Base Bid - Exterior Signage	**122,513**	**White Sign Company**	White Sign Company	122,513	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
100	Base Bid - Memorial Sign	**36,125**	**White Sign Company**	White Sign Company	36,125	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
200	Sales Tax	**11,613**	**White Sign Company**	White Sign Company	11,613	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
300	Prequalified	**0**	**White Sign Company**	White Sign Company	0	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
	BP10140.2 - Signage/Visual Display - Scope	**0**			**0**			**0**			**0**			**0**			**0**	
	Identification devices	**0**			0			0			0			0			0	
100	INTERIOR SIGNAGE	**0**	**White Sign Company**	White Sign Company	0	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
101	Standard ADA Compliant Signage	**0**	**White Sign Company**	White Sign Company	0	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
102	Stair/Elevator Wayfinding Signage	**0**	**White Sign Company**	White Sign Company	0	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
103	Room ID	**0**	**White Sign Company**	White Sign Company	0	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
104	Room ID / Window Inserts	**0**	**White Sign Company**	White Sign Company	0	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
105	Evacuation Signage	**0**	**White Sign Company**	White Sign Company	0	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
106	Restroom Singage	**0**	**White Sign Company**	White Sign Company	0	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
107	Restroom - Occupied/Unoccupied Signage	**0**	**White Sign Company**	White Sign Company	0	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
108	Incase of Fire Signage	**0**	**White Sign Company**	White Sign Company	0	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
109	Area of Refuge Signage	**0**	**White Sign Company**	White Sign Company	0	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
109	Greenacres Logo 2nd Floor Lobby	**0**	**White Sign Company**	White Sign Company	0	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
109	Breakroom "Grow with you" LED Sign	**0**	**White Sign Company**	White Sign Company	0	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
200	EXTERIOR SIGNAGE	**0**	**White Sign Company**	White Sign Company	0	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
200	North Metal Memorial Sign - Outer Ring	**0**	**White Sign Company**	White Sign Company	0	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
200	North Metal Memorial Sign - Inner Ring	**0**	**White Sign Company**	White Sign Company	0	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
201	"City of Greenacres Municipal Operation Center" Entry Signage	**0**	**White Sign Company**	White Sign Company	0	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
202	Stair Tower - Greenacres Logo	**0**	**White Sign Company**	White Sign Company	0	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
203	Building Wayfinding Signage	**0**	**White Sign Company**	White Sign Company	0	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
300	MISC	**0**	**White Sign Company**	White Sign Company	0	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
301	Installation	**0**	**White Sign Company**	White Sign Company	0	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
302	Adhesives	**0**	**White Sign Company**	White Sign Company	0	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	
302	Mounting Plaqards	**0**	**White Sign Company**	White Sign Company	0	Yes	Baron Sign Manufacturir	0	Yes		0			0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP10160 - Bath Accessories	**82,671**			**82,671**			**100,964**			**0**			**0**			**0**	
	BP10160.0 - Bath Accessories - General	**81,372**			**81,372**			**99,665**			**0**			**0**			**0**	
	Toilet and laundry specialties	**81,372**			81,372			99,665			0			0			0	
100	Bath Accessories - Base Bid	**81,372**	**All Specialty Sales**	All Specialty Sales	81,372	Yes	Mardale Specialties	99,665			0			0			0	
200	Sales Tax	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0			0			0			0	
300	Prequalified	**0**	**All Specialty Sales**	All Specialty Sales	0		Mardale Specialties	0			0			0			0	
	BP10160.2 - Bath Accessories - Scope	**1,299**			**1,299**			**1,299**			**0**			**0**			**0**	
	Toilet and laundry specialties	**1,299**			1,299			1,299			0			0			0	
	Corner Guards	**1,299**	**All Specialty Sales**	All Specialty Sales	1,299	X Sub	Mardale Specialties	1,299	Yes		0			0			0	
100	TOILET PARTITIONS	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
101	Scranton Products (OAE)	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
102	HDPE Panels	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
103	25% Recycled	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
104	Floor Mounted / Over Head Braced	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
105	72" Panel Height	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
106	Bronze Hammered Color	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
200	BATHROOM ACCESSORIES	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
201	1-1/2" DIA. Grab Bars - 36"	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
202	1-1/2" DIA. Grab Bars - 48"	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
203	1-1/2" DIA. Grab Bars - 24" x 30"	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
204	24" x 36" LED Mirrors	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
204	Fitness Room Mirrors - 1/4" - Seamed Edges - in Division 08 Glass	**0**	**All Specialty Sales**	All Specialty Sales	0	No	Mardale Specialties	0	Yes		0			0			0	
205	SS - Sanitary Napkin Disposal	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
206	SS - Toilet Tissue Dispenser	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
207	SS - Toilet Seat Cover Dispenser	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
208	SS - Wall Mount ADA Soap Dispenser	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
209	SS - Paper Towel Dispenser	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
210	SS - Waste Receptical	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
211	Shower Curtains / Hooks	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
212	Shower Curtain Rods	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
213	ADA Wall Mounted Shower Bench	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
214	Towel Rack w/ 24" Bar	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
214	Restroom Mirrors - Sloan	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
300	MISC	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
301	Installation	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
302	Shipping and Handling	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
303	Clean Up	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP10500 - Fire Protection Specialties	**5,140**			**5,140**			**7,394**			**0**			**0**			**0**	
	BP10500.0 - Fire Protection Specialties - General	**5,140**			**5,140**			**7,394**			**0**			**0**			**0**	
	Fire protection specialties	**5,140**			5,140			7,394			0			0			0	
100	Fire Extinguisher Sub - Base Bid	**5,140**	**All Specialty Sales**	All Specialty Sales	5,140	Yes	Mardale Specialties	7,394	Yes		0			0			0	
200	Sales Tax	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
300	Prequalified	**0**	**All Specialty Sales**	All Specialty Sales	0		Mardale Specialties	0			0			0			0	
	BP10500.2 - Fire Protection Specialties - Scope	**0**			**0**			**0**			**0**			**0**			**0**	
	Fire protection specialties	**0**			0			0			0			0			0	
100	FIRE EXTINGUISHERS	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
101	Class 2-A:10B:C in all areas outside the Kitchen.	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
102	Class K and Fire Blanket in Breakroom Kitchen.	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
200	CABINETS	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
201	Wall Mounted Cabinets - White with Glass window	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
202	Bracket Mounted Fire Extinguishers - MEP rooms	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
203	Weather Resistance Cabinet at Fuel Island.	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
300	MISC	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
301	Sign and Date Tag	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
302	Trims/Seals	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	
303	Installation	**0**	**All Specialty Sales**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes		0			0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP10601 - Operable Wall System	**72,470**			**72,470**			**92,550**			**0**			**0**			**0**	
	BP10601.0 - General	**70,430**			**70,430**			**92,550**			**0**			**0**			**0**	
	Folding doors and grilles	**70,430**			70,430			92,550			0			0			0	
400	Operable Partitions - Base Bid	**70,430**	**Acousti Doors & Specialties**	Acousti Doors & Special	70,430	Yes	Precision Services	92,550	Yes		0			0			0	
400	Sales Tax	**0**	**Acousti Doors & Specialties**	Acousti Doors & Special	0	Yes	Precision Services	0	Yes		0			0			0	
400	Prequalification	**0**	**Acousti Doors & Specialties**	Acousti Doors & Special	0		Precision Services	0			0			0			0	
	BP10601.2 - Scope	**2,040**			**2,040**			**0**			**0**			**0**			**0**	
	Folding doors and grilles	**2,040**			2,040			0			0			0			0	
400	32' Glass Panel Operable Partition	**0**	**Acousti Doors & Specialties**	Acousti Doors & Special	0	Yes	Precision Services	0	Yes		0			0			0	
400	12'-6" Solid Panel Operable Partition	**0**	**Acousti Doors & Specialties**	Acousti Doors & Special	0	Yes	Precision Services	0	Yes		0			0			0	
400	44 STC Rating or Better	**0**	**Acousti Doors & Specialties**	Acousti Doors & Special	0	Yes	Precision Services	0	Yes		0			0			0	
400	Andoized Finish	**0**	**Acousti Doors & Specialties**	Acousti Doors & Special	0	Yes	Precision Services	0	Yes		0			0			0	
400	Inlet Passthrough Doors	**2,040**	**Acousti Doors & Specialties**	Acousti Doors & Special	2,040	Yes	Precision Services	0	Yes		0			0			0	
400	Manual Operation	**0**	**Acousti Doors & Specialties**	Acousti Doors & Special	0	Yes	Precision Services	0	Yes		0			0			0	
400	Installation	**0**	**Acousti Doors & Specialties**	Acousti Doors & Special	0	Yes	Precision Services	0	Yes		0			0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP10700 - Flagpoles	**27,284**			**36,522**			**27,284**			**31,511**			**0**			**0**	
	BP10700.0 - General	**17,399**			**32,742**			**17,399**			**31,511**			**0**			**0**	
	Flagpoles	**17,399**			32,742			17,399			31,511			0			0	
400	Flagpole Subcontractor - Base Bid	**17,399**	**Mardale Specialties**	All Specialty Sales	32,742	Yes	Mardale Specialties	17,399	Yes	Custome One Source	31,511	Yes		0			0	
400	Sales Tax	**0**	**Mardale Specialties**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes	Custome One Source	0	Yes		0			0	
400	Prequalification	**0**	**Mardale Specialties**	All Specialty Sales	0		Mardale Specialties	0		Custome One Source	0	Yes		0			0	
	BP10700.2 - Scope	**9,885**			**3,780**			**9,885**			**0**			**0**			**0**	
	Flagpoles	**9,885**			3,780			9,885			0			0			0	
100	Memorial Flagpole - 25'	**0**	**Mardale Specialties**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes	Custome One Source	0	Yes		0			0	
100	Memorial Flagpole - 20'	**0**	**Mardale Specialties**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes	Custome One Source	0	Yes		0			0	
100	Base Plate	**0**	**Mardale Specialties**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes	Custome One Source	0	Yes		0			0	
100	Revolvilng Track	**0**	**Mardale Specialties**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes	Custome One Source	0	Yes		0			0	
100	Flagpole Beacon 12v with two 3 Watt Bulbs	**0**	**Mardale Specialties**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes	Custome One Source	0	Yes		0			0	
100	Asphaltic Paint on Sub Grade Components	**0**	**Mardale Specialties**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes	Custome One Source	0	Yes		0			0	
100	Installation	**9,885**	**Mardale Specialties**	All Specialty Sales	3,780	Yes	Mardale Specialties	9,885	Yes	Custome One Source	0	Yes		0			0	
100	Flagpole Beacon 12v with two 3 Watt Bulbs	**0**	**Mardale Specialties**	All Specialty Sales	0	Yes	Mardale Specialties	0	Yes	Custome One Source	0	Yes		0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP11450 - Appliances	**101,179**	**Combination Package**		**84,519**			**20,313**			**18,760**			**0**			**0**	
	BP11450.0 - Appliances - General	**0**			**0**			**0**			**0**			**0**			**0**	
	Residential equipment	**0**			0			0			0			0			0	
100	Appliance Subcontractor - Base Bid	**0**	**Island Supply**	Island Supply	0	Yes	Commercial Laundry Eq	0	Yes	Ferguson	0	Yes		0			0	
105	Sales Tax	**0**	**Island Supply**	Island Supply	0	Yes	Commercial Laundry Eq	0	Yes	Ferguson	0	Yes		0			0	
120	Prequalification	**0**	**Island Supply**	Island Supply	0	No	Commercial Laundry Eq	0	No	Ferguson	0	Yes		0			0	
	BP11450.2 - Appliances - Scope	**101,179**			**84,519**			**20,313**			**18,760**			**0**			**0**	
	Equipment	**82,419**			82,419			18,213			0			0			0	
200	Commercial Appliances Furnish and Install (E2, E3, E6, E9, E10 & E11)	**82,419**	**Island Supply**	Island Supply	82,419	Yes	Commercial Laundry Eq	18,213	No	Ferguson	0	No		0			0	
205	E2 - Reach-In Solid Swing Door Refrigerator With Hydrocarbon Refrigerant	**0**	**Island Supply**	Island Supply	0	Yes	Commercial Laundry Eq	0	No	Ferguson	0	No		0			0	
210	E3 - Reach-In Solid Swing Door Freezer Hydrocarbon Refrigerant	**0**	**Island Supply**	Island Supply	0	Yes	Commercial Laundry Eq	0	No	Ferguson	0	No		0			0	
215	E6 - 60" Electric Range And Oven	**0**	**Island Supply**	Island Supply	0	Yes	Commercial Laundry Eq	0	No	Ferguson	0	No		0			0	
220	E9 - Commercial Dryer - 22.5 Lbs Capacity	**0**	**Island Supply**	Island Supply	0	Yes	Commercial Laundry Eq	0	Yes	Ferguson	0	No		0			0	
225	E10 - Commercial Washer-Extractor - 20 Lbs Capacity	**0**	**Island Supply**	Island Supply	0	Yes	Commercial Laundry Eq	0	Yes	Ferguson	0	No		0			0	
230	E11 - Sanitary Cubelet Ice Machine/Dispenser	**0**	**Island Supply**	Island Supply	0	Yes	Commercial Laundry Eq	0	No	Ferguson	0	No		0			0	
300	See HVAC for Kitchen Exhaust Hood w/ Fire Supression System (previously carried in HVAC)	**0**	**Island Supply**	Island Supply	0	N/A	Commercial Laundry Eq	0	No	Ferguson	0	No		0			0	
350	Ice Machine (No Callout) in Part Storage 117 Sheet A-701B	**0**	**Island Supply**	Island Supply	0	Yes	Commercial Laundry Eq	0	No	Ferguson	0	No		0			0	
	Residential equipment	**18,760**			2,100			2,100			18,760			0			0	
100	Residential Appliances Furnish and Install (E4, E5, E7, 14 & E24)	**16,660**	**Ferguson**	Island Supply	0	No	Commercial Laundry Eq	0	No	Ferguson	16,660	Yes		0			0	
105	E4 - Microwave Oven	**0**	**Ferguson**	Island Supply	0	No	Commercial Laundry Eq	0	No	Ferguson	0	Yes		0			0	
110	E5 - ADA Compliant Dishwasher With Sanitizing Setting	**0**	**Ferguson**	Island Supply	0	No	Commercial Laundry Eq	0	No	Ferguson	0	Yes		0			0	
115	E7 - Side-By-Side Refrigerator With Disp (One is not labeled in Breakroom 218)	**0**	**Ferguson**	Island Supply	0	No	Commercial Laundry Eq	0	No	Ferguson	0	Yes		0			0	
120	E14 - Microwave Oven (Under Counter)	**0**	**Ferguson**	Island Supply	0	No	Commercial Laundry Eq	0	No	Ferguson	0	Yes		0			0	
125	E24 - Mini Refrigerator 18"	**0**	**Ferguson**	Island Supply	0	No	Commercial Laundry Eq	0	No	Ferguson	0	Yes		0			0	
901	Match specs with Amendment 3 updates	**2,100**	**KL Estimate**	KL Estimate	2,100		KL Estimate	2,100		KL Estimate	2,100			0			0	

***Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP11485 - Exercise Equipment	**121,283**			**121,283**			**0**			**0**			**0**			**0**	
	BP11485.0 - General	**121,283**			**121,283**			**0**			**0**			**0**			**0**	
	Athletic and recreational equipment	**121,283**			121,283			0			0			0			0	
100	Base Bid - Fitness Equipment	**121,283**	**Fit Supply**	Fit Supply	121,283	Yes		0			0			0			0	
200	Sales Tax	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
400	Prequalified	**0**	**Fit Supply**	Fit Supply	0			0			0			0			0	
	BP11485.2 - Scope	**0**			**0**			**0**			**0**			**0**			**0**	
	Athletic and recreational equipment	**0**			0			0			0			0			0	
100	FITNESS EQUIPMENT	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
101	Core - Throwdown Rower	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
102	Core - Throwdown HIIT Bike	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
103	Core - Stairmaster	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
104	Core - Star Trac Treadmill	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
105	Core - Nautilus 3 Tier Dumbell Rack	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
106	Core - Nautilus Adjustable Bench	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
106	Core - Nautilus Adjustable Pulley	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
106	Core - Nautilus Multipress	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
107	Core - Decline Bench	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
108	Core - Nautilus Bamboo Platform	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
109	Core - Nautilus Barbell Rack	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
109	Core - Leg Extention	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
110	Prism Smart Training Center Bay	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
111	TKO 3 - Kettle Bell Rack	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
111	TKO - AirRaid Rower	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
112	Flying Pull up Bars	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
200	Vert. Dumbell Rack	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
200	Core -Alpha XTC Strength Station	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
300	WEIGHTS	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
301	5lb Medicine Balls	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
302	10lb Medicine Balls	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
303	15lb Medicine Balls	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
304	20lb Medicine Balls	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
305	10lb Plates	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
306	25lb Plates	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
307	35lb Plates	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
308	45lb Plates	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
308	Core - Dumbells 80lb	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
308	Core - Dumbells 85lb	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
308	Core - Dumbells 90lb	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
308	Core - Dumbells 95lb	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
308	Core - Dumbells 100lb	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
308	EZ - Curl Bars 20-110lb Set	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
308	10lb Grip Plate	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
308	25lb Grip Plate	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
308	45lb Grip Plate	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
308	8.8lb Kettle Bells	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
308	13.2lb Kettle Bells	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
308	17.6lb Kattle Bells	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
308	26.4lb Kettle Bells	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
308	35.2lb Kettle Bells	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
400	MISC	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
401	Shipping/Handling	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
402	Floor Mounting	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
403	Installation	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
404	Bar Collars	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
405	Stability Balls	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
406	Foam Rollers	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
407	Suspension Trainers	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
408	Plyo Set	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
408	Weight Power Bar	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
408	Battle Rope - 1.5" x 30'	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	
408	Step up Plateforms w/ 6 Risers	**0**	**Fit Supply**	Fit Supply	0	Yes		0			0			0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP11600 - Fleet Equipment	**905,756**			**905,756**		**Incomplete Scope**	**267,489**			**0**			**0**			**0**	
	BP11600.0 - General	**599,598**			**599,598**			**0**			**0**			**0**			**0**	
	Equipment	**599,598**			599,598			0			0			0			0	
	Fleet Maintenance Equipment Base	**599,598**	**Reladyne**	Reladyne	599,598	Yes	Storafe Craft	0			0			0			0	
	Sales Taxes	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
	Prequalification	**0**	**Reladyne**	Reladyne	0		Storafe Craft	0			0			0			0	
	BP11600.2 - Scope	**306,158**			**306,158**			**267,489**			**0**			**0**			**0**	
	Storage shelving	**245,266**			245,266			252,597			0			0			0	
350	STORAGE	**80,478**	**Reladyne**	Reladyne	80,478	Yes	Storafe Craft	80,950	Yes		0			0			0	
351	Tire Storage Carousel	**114,258**	**Reladyne**	Reladyne	114,258	X Sub	Storafe Craft	114,258	Yes		0			0			0	
352	Flame Cabinets	**50,530**	**Reladyne**	Reladyne	50,530	X Sub	Storafe Craft	50,530	Yes		0			0			0	
353	Pallet Racks 4ft Deep	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	6,859	Yes		0			0			0	
354	Fire Supply Storage Racks	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0	Yes		0			0			0	
355	Bunker Gear Storage Racks	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0	Yes		0			0			0	
356	Part Storage Racks	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0	Yes		0			0			0	
357	EOC Supply Storage Racks	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0	Yes		0			0			0	
358	Tool Storage Shelving	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0	Yes		0			0			0	
359	MISC	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0	Yes		0			0			0	
360	Installation	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0	Yes		0			0			0	
361	Shipping & Handling	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0	Yes		0			0			0	
	Equipment	**60,892**			60,892			14,892			0			0			0	
100	JET 8" GRINDER	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
102	JET BENCH SANDER	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
104	BAILEIGH MITTERING BAND SAW	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
106	ROTARY HEAVY DUTY TIRE CHANGER	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
107	ROTARY LIGHT DUTY TIRE CHANGER	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
108	ROTARY 3D WHEEL BALANCER :	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
110	OWNER PROVIDED 30K LIFT CONTRACTOR INSTALLED	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
112	CHALLENGER 60K 4 POST LIFT432" OVERALL LENGTH INCLUDES 2SJA 35 35K ROLLING JACKAS	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
114	OWNER PROVIDED 10K LIFT CONTRACTOR INSTALLED	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
116	ROTARY 20K TWO POST ABOVE GRD LIFT	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
122	Owner Supplied Plasma Cutter By - 240V/1PH	**0**	**Reladyne**	Reladyne	0	No	Storafe Craft	0			0			0			0	
124	Owner Supplied Welder and install by contractor	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
126	FORNEY 1710 ACETELYNE SET	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
128	SHURE HEAVY DUTY WORK BENCH	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
130	JET 8" GRINDER	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
132	JET GRINDER PEDESTAL	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
134	OWNER PROVIDED DRILL PRESS CONTR INSTALL	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
136	OWNER PROVIDED HYD PRESS CONTR.INSTALLED	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
138	BAILEIGH METAL BRAKE AND SHEAR	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
140	PORTABLE WIDE SAFETY STAIR	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
142	30x60 FLAT BED CART 2000 LB CAPACITY	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
144	EQUIPMENT INSTALLATION BE29 & BE30	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
146	SHURE 45 GALLON FLAMABLE CABINET	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
148	OIL AND COMPRESSOR ROOM	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
152	CHAMPION 10HP DUPLEX COMPRESSOR,	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
154	CHAMPION 100 CFM AIR DRYER WITH FILTER PKG	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
156	GRACO 3/8 X65 AIR REEL	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
158	GRACO AIR SHUT OFF VALVE	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
160	MILTON AIR COUPLER	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
162	INSTALL APRX 520 FT OF 32MM AIR PIPE HEADER	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
164	INSTALL APRX 320FT OF 20MM PIPE BRANCH	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
176	10HP Duplex compressor	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
176	OIL system 1 5W	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
176	OIL system 2 10W	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
176	120 LB Grease pump system	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
177	WATER REELS & REELS ACCESSORIES	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
178	Waste oil system	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
180	Waste Coolant System	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
182	Waste Fuel Tank	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
200	Freight Equipment	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	
202	NIC Signed and Engineered Drawings	**0**	**Reladyne**	Reladyne	0	Yes	Storafe Craft	0			0			0			0	

300	Car washing system, hose reels, hoses, vacuum, brushes, wands, holders, activation controls	**46,000 DS Car Wash**	DS Car Wash	46,000	Yes	Storafe Craft	0	0	0	0
901	Match Flame Cabinet with Amendment 3	**14,892 KL Estimate**	KL Estimate	14,892		KL Estimate	14,892	0	0	0

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP12300 - Manufactured Casework	**339,367**			**339,367**			**346,264**			**431,668**			**0**			**0**	
	BP12300.0 - General	**259,080**			**259,080**			**337,082**			**431,668**			**0**			**0**	
	Architectural woodwork	**259,080**			259,080			337,082			431,668			0			0	
100	Base Bid - Millwork Sub	**130,383**	**Advanced Millwork**	Advanced Millwork	130,383	Yes	Distinctive Millwork	337,082	Yes	F.L. Crane	431,668	Yes		0			0	
101	Base Bid - Countertop Sub	**102,647**	**Advanced Millwork**	Advanced Millwork	102,647	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0	Yes		0			0	
200	Sales Tax	**26,050**	**Advanced Millwork**	Advanced Millwork	26,050	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0	Yes		0			0	
300	Prequalification	**0**	**Advanced Millwork**	Advanced Millwork	0		Distinctive Millwork	0		F.L. Crane	0			0			0	
	BP12300.2 - Scope	**80,287**			**80,287**			**9,182**			**0**			**0**			**0**	
	Architectural woodwork	**80,287**			80,287			9,182			0			0			0	
100	CABINETS	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0	Yes		0			0	
101	2x4 Cabinet Base	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0	Yes		0			0	
102	Rubber Toe Kick	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0	Yes		0			0	
103	PLAM Base Cabinets	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0	Yes		0			0	
104	PLAM Upper Cabinets	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0	Yes		0			0	
105	PLAM Aprons	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0	Yes		0			0	
105	PLAM Bathroom - Removable Apron	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0	Yes		0			0	
105	PLAM - Coffee Station 1" Shelf	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0	Yes		0			0	
105	PLAM - Kithchen Banquettes	**23,082**	**Advanced Millwork**	Advanced Millwork	23,082	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0	Yes		0			0	
106	Drawer Pulls	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0	Yes		0			0	
107	Sliders/Handles/Hinges	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0	Yes		0			0	
300	FINISH CARPENTRY	**45,561**	**Advanced Millwork**	Advanced Millwork	45,561	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0	Yes		0			0	
300	Solid Wood Veneer - Lobby Ceilings	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0	Yes		0			0	
300	Solid Wood Veneer - Lobby Walls to Command Center	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0	Yes		0			0	
400	MISC	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0	Yes		0			0	
401	Solid Wood Wall Caps	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0	Yes		0			0	
402	SS Window Sills	**9,182**	**Advanced Millwork**	Advanced Millwork	9,182	Yes	Distinctive Millwork	9,182	X Sub	F.L. Crane	0	Yes		0			0	
403	Cabinet Gap Fillers	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0	Yes		0			0	
404	Hardware	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0	Yes		0			0	
405	Clean up Crew	**2,462**	**Advanced Millwork**	Advanced Millwork	2,462	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0	Yes		0			0	
405	Installation	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0	Yes		0			0	
	Countertops	**0**			0			0			0			0			0	
200	COUNTERTOPS	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0			0			0	
201	3/4" Stone Countertops	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0			0			0	
201	3/4" Stone Countertops - Waterfall Island (Kitchen/Breakroom)	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0			0			0	
202	3/4" Wall Backsplash (Kitchens/Breakrooms)	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0			0			0	
203	3/4" x 4" Stone Backsplash	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0			0			0	
204	3/4" x 4" PLAM Backsplash	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0			0			0	
205	Group Bathroom Vanity & Countertops - In Division 15 Plumbing	**0**	**Advanced Millwork**	Advanced Millwork	0	No	Distinctive Millwork	0	No	F.L. Crane	0			0			0	
206	Floating Countertop Supports	**0**	**Advanced Millwork**	Advanced Millwork	0	Yes	Distinctive Millwork	0	Yes	F.L. Crane	0			0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP12400 - Window Treatment	**12,218**			**12,218**			**17,713**			**0**			**0**			**0**	
	BP12400.0 - General	**12,218**			**12,218**			**17,713**			**0**			**0**			**0**	
	Window treatment	**12,218**			12,218			17,713			0			0			0	
100	Window Treatment Subcontractor - Base Bid	**12,218**	**Raise and Shine**	Raise and Shine	12,218	Yes	James Blinds	17,713	Yes		0			0			0	
200	Sales Tax	**0**	**Raise and Shine**	Raise and Shine	0	Yes	James Blinds	0	Yes		0			0			0	
300	Prequalification	**0**	**Raise and Shine**	Raise and Shine	0		James Blinds	0			0			0			0	
	BP12400.2 - Scope	**0**			**0**			**0**			**0**			**0**			**0**	
	Window treatment	**0**			0			0			0			0			0	
100	Manual Operated Roller Shades	**0**	**Raise and Shine**	Raise and Shine	0	Yes	James Blinds	0	Yes		0			0			0	
101	Macha Shade Single Roller 5%	**0**	**Raise and Shine**	Raise and Shine	0	Yes	James Blinds	0	Yes		0			0			0	
102	Brackets and Mounting Hardware	**0**	**Raise and Shine**	Raise and Shine	0	Yes	James Blinds	0	Yes		0			0			0	
103	Hembars	**0**	**Raise and Shine**	Raise and Shine	0	Yes	James Blinds	0	Yes		0			0			0	
104	Pre-Manudactured Metal Ceiling Pockets	**0**	**Raise and Shine**	Raise and Shine	0	Yes	James Blinds	0	Yes		0			0			0	
105	Installation	**0**	**Raise and Shine**	Raise and Shine	0	Yes	James Blinds	0	Yes		0			0			0	
106	Shipping and Handling	**0**	**Raise and Shine**	Raise and Shine	0	Yes	James Blinds	0	Yes		0			0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP12700 - Systems Furniture	**790,780**			**790,780**			**803,000**			**0**			**0**			**0**	
	BP12700.0 - General	**790,780**			**790,780**			**803,000**			**0**			**0**			**0**	
	Office furniture	**790,780**			790,780			803,000			0			0			0	
400	Furniture - Base Bid	**739,047**	**J.C. White**	J.C. White	739,047	Yes	Allowance	803,000			0			0			0	
400	Sales Tax	**51,733**	**J.C. White**	J.C. White	51,733	KLEst		0			0			0			0	
400	Prequalification	**0**	**J.C. White**	J.C. White	0			0			0			0			0	
	BP12700.2 - Scope	**0**			**0**			**0**			**0**			**0**			**0**	
	Office furniture	**0**			0			0			0			0			0	
100	LOBBY	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
101	1st FL Lobby Banquette	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
102	2nd FL Lobby Banquette	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
103	Waiting Seating	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
104	Furniture South of Elevator	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
105	2nd Floor Lobby Seating and Tables	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
105	Mens/Womens Restroom Lockers	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
106	BREAKROOMS	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
106	4x4 Sqaure Top Tables	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
106	3x3 Sqaure Top Tables	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
107	Bench Seating	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
108	Production Lounge Chairs	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
108	Production Lounge - Pool Table/Recreational Table	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
108	Communitcations Studio Furniture	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
200	OFFICES	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
201	L-Desks	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
202	Lower/Upper Cabinets	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
203	Director Office Seating	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
204	File Storage Cabinets	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
205	Conference Tables	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
206	Office/Conference Credenzas	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
206	Open Work Cubicals	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
206	Multifunction Plotter - Workroom 107	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
300	COMMAND CENTER	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
301	See Div 8 for Wall Mounted Glass Writing Surfaces - In Division 08 - Glass & Glazing	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
302	Movable Table/Desks	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
303	Foldable Rolling Chairs	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
304	Conference Tables	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
305	See Div 16 for Mobile Smart Board Carts - In Audio/Visual	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
305	IT Seating	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
305	Workroom Seating/Desks	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
500	MISC	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
501	Installation	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
502	Staging	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	
503	Shipping/Handling	**0**	**J.C. White**	J.C. White	0	Yes		0			0			0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP13120 - Pre-Engineered Structures	**726,919**			**726,919**			**0**			**0**			**0**			**0**	
	BP13120.0 - General	**726,919**			**726,919**			**0**			**0**			**0**			**0**	
	Special construction	**726,919**			726,919			0			0			0			0	
50	Fire Training Structure Base Bid	**726,919**	**Fire Training structure**	Fire Training structure	726,919	Yes		0			0			0			0	
56	Sales Taxes	**0**	**Fire Training structure**	Fire Training structure	0	Yes		0			0			0			0	
	BP13120.2 - Scope	**0**			**0**			**0**			**0**			**0**			**0**	
	Equipment	**0**			0			0			0			0			0	
	(1) NFPA Certified 3-Stack Live Fire and Confined Space USAR Training Facility Complete with (2) Class "A" Fueled Burn Rooms.	**0**	**Fire Training structure**	Fire Training structure	0	Yes		0			0			0			0	
	2 Day Product Orientation/Usage Course & Live Fire Training w/Certified Fire Instructor.	**0**	**Fire Training structure**	Fire Training structure	0	Yes		0			0			0			0	
	Bullhead Options:	**0**	**Fire Training structure**	Fire Training structure	0	Yes		0			0			0			0	
	8' x 3' x 12' Pitched Roof Ventilation Prop, Ceiling Pull Prop and active rooftop on Unit #1.	**0**	**Fire Training structure**	Fire Training structure	0	Yes		0			0			0			0	
	Void Space "Behind the Wall" Live Fire Prop.	**0**	**Fire Training structure**	Fire Training structure	0	Yes		0			0			0			0	
	Standpipe Connection & Sprinkler System	**0**	**Fire Training structure**	Fire Training structure	0	Yes		0			0			0			0	
	(4) Door Forced Entry Door Prop on Unit #2	**0**	**Fire Training structure**	Fire Training structure	0	Yes		0			0			0			0	
	Steel Panel Cutting Prop on Unit #2	**0**	**Fire Training structure**	Fire Training structure	0	Yes		0			0			0			0	
	Variable Angle Rebar Cutting Prop on Unit U2	**0**	**Fire Training structure**	Fire Training structure	0	Yes		0			0			0			0	
	Premium 40' Maze System in Unit #2	**0**	**Fire Training structure**	Fire Training structure	0	Yes		0			0			0			0	
	Active Rooftop with interior stairway & hatch on Unit #3	**0**	**Fire Training structure**	Fire Training structure	0	Yes		0			0			0			0	
	Rappelling Tower with Caged Ladder	**0**	**Fire Training structure**	Fire Training structure	0	Yes		0			0			0			0	
	8' x 20' Container with interior stairway & Hatch, (l) Personnel Door, and (2) Windows may be added on top of Unit #3.	**0**	**Fire Training structure**	Fire Training structure	0	Yes		0			0			0			0	
	Additional Requested Options:	**0**	**Fire Training structure**	Fire Training structure	0	Yes		0			0			0			0	
	Electrical & Lighting System: To consist of (3) Interior Lights, (2) Wall Receptacles/Switches (located within all container units not having live fire training), (4) Exterior Lights and (1) Exterior Mounted Load C	**0**	**Fire Training structure**	Fire Training structure	0	Yes		0			0			0			0	
	Exterior High-Rise Stair System: As provided on the Lakeland FL System	**0**	**Fire Training structure**	Fire Training structure	0	Yes		0			0			0			0	
	Delivery & Crane	**0**	**Fire Training structure**	Fire Training structure	0	Yes		0			0			0			0	
	Warranty on all workmanship and materials for 1 year fr	**0**	**Fire Training structure**	Fire Training structure	0	Yes		0			0			0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP13200 - Fuel Storage Tank & Piping	**266,000**			**266,000**			**292,500**			**0**			**0**			**0**	
	BP13200.0 - General	**266,000**			**266,000**			**292,500**			**0**			**0**			**0**	
	Storage tanks	**266,000**			266,000			292,500			0			0			0	
100	Fuel Tank Base Bid Per Quote	**266,000**	**Glasgow Equipment Service,**	Glasgow Equipment Ser	266,000	Yes	LUTZ	292,500	Yes		0			0			0	
200	Sales Tax	**0**	**Glasgow Equipment Service,**	Glasgow Equipment Ser	0	Yes	LUTZ	0	Yes		0			0			0	
400	Prequalified	**0**	**Glasgow Equipment Service,**	Glasgow Equipment Ser	0		LUTZ	0			0			0			0	
	BP13200.2 - Scope	**0**			**0**			**0**			**0**			**0**			**0**	
	Storage tanks	**0**			0			0			0			0			0	
205	2000 Gal Unleaded Fuel Steel Tank ,UL-2085	**0**	**Glasgow Equipment Service,**	Glasgow Equipment Ser	0	Yes	LUTZ	0	Yes		0			0			0	
206	Fuel Dispensers: Each with 2 Unleaded Hoses and Automatic Nozzles (one pump on each side).	**0**	**Glasgow Equipment Service,**	Glasgow Equipment Ser	0	Yes	LUTZ	0	Yes		0			0			0	
207	Dispenser Sump	**0**	**Glasgow Equipment Service,**	Glasgow Equipment Ser	0	Yes	LUTZ	0	Yes		0			0			0	
207	Ladder & Platform	**0**	**Glasgow Equipment Service,**	Glasgow Equipment Ser	0	Yes	LUTZ	0	Yes		0			0			0	
208	STP Pump Set (within fuel tank).	**0**	**Glasgow Equipment Service,**	Glasgow Equipment Ser	0	Yes	LUTZ	0	Yes		0			0			0	
210	Underground Piping: Double wall piping from STP pump set to dispenser.	**0**	**Glasgow Equipment Service,**	Glasgow Equipment Ser	0	Yes	LUTZ	0	Yes		0			0			0	
220	Emergency Power Button (location to be coordinated in field, NEC 514.11).	**0**	**Glasgow Equipment Service,**	Glasgow Equipment Ser	0	Yes	LUTZ	0	Yes		0			0			0	
222	Fire Extinguisher: Weather resistive case, mounted to column, 4' AFF.	**0**	**Glasgow Equipment Service,**	Glasgow Equipment Ser	0	Yes	LUTZ	0	Yes		0			0			0	
232	Audible Alarm for fuel tank system (mounted on bollard/pole by specialty engineer).	**0**	**Glasgow Equipment Service,**	Glasgow Equipment Ser	0	Yes	LUTZ	0	Yes		0			0			0	
234	Fuel Master 5000 Series on FM Live Software (fuel management system).	**0**	**Glasgow Equipment Service,**	Glasgow Equipment Ser	0	Yes	LUTZ	0	Yes		0			0			0	
236	NO FUEL SUPPLY INCLUDED. FUEL DELIVERY WILL BE NEEDED TO COMPLETE START UP & CHECK OUT.	**0**	**Glasgow Equipment Service,**	Glasgow Equipment Ser	0	Yes	LUTZ	0	Yes		0			0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP14200 - Elevators/Escalators/Lifts	**135,000**			**135,000**			**148,288**			**0**			**0**			**0**	
	BP14200.0 - General	**125,000**			**125,000**			**121,788**			**0**			**0**			**0**	
	Elevators	**125,000**			125,000			121,788			0			0			0	
100	Elevator - Base Bid	**125,000**	**Schindler**	Schindler	125,000	Yes	TKE	121,788	Yes		0			0			0	
200	Sales Tax	**0**	**Schindler**	Schindler	0	Yes	TKE	0			0			0			0	
300	Prequalification	**0**	**Schindler**	Schindler	0		TKE	0			0			0			0	
	BP14200.2 - Scope	**10,000**			**10,000**			**26,500**			**0**			**0**			**0**	
	Elevators	**10,000**			10,000			26,500			0			0			0	
	Elevator Temp Use	**10,000**	**Schindler**	Schindler	10,000	KLEst	TKE	10,000	KLEst		0			0			0	
100	Basis of Design - Schindler Model 3300	**0**	**Schindler**	Schindler	0	Yes	TKE	0	No		0			0			0	
102	Elevator Type - Gearless Traction - Machine Room-less	**0**	**Schindler**	Schindler	0	Yes	TKE	0	Yes		0			0			0	
104	Rated Capacity - 3500 LB'S (1630 KG)	**0**	**Schindler**	Schindler	0	Yes	TKE	5,000	Sub +		0			0			0	
106	Speed of 100 FPM included - Rated Speed - 350 FPM (Typical Basis)	**0**	**Schindler**	Schindler	0	No	TKE	8,000	Sub +		0			0			0	
108	Travel Height - Up to 150 FT	**0**	**Schindler**	Schindler	0	Yes	TKE	0			0			0			0	
110	Stops / Openings - 3	**0**	**Schindler**	Schindler	0	Yes	TKE	3,500	Sub +		0			0			0	
112	New - Cab finishes: Wall Finish: Laminate | Toronto Grey (new)	**0**	**Schindler**	Schindler	0		TKE	0			0			0			0	
114	Cab finishes: Skirting: Anodized Aluminum.	**0**	**Schindler**	Schindler	0	Yes	TKE	0	Yes		0			0			0	
116	Cab finishes: Handrail type: Three handrails, Flat Handrail / Aluminum.	**0**	**Schindler**	Schindler	0	Yes	TKE	0	Yes		0			0			0	
118	Cab finishes: Ceiling Type: Downlight Lit LED / #4 Brushed Stainless Steel.	**0**	**Schindler**	Schindler	0	Yes	TKE	0	Yes		0			0			0	
120	Cab finishes: Landing Door Finish: Brushed Stainless Steel.	**0**	**Schindler**	Schindler	0	Yes	TKE	0	Yes		0			0			0	
122	Delivery and Installation	**0**	**Schindler**	Schindler	0	Yes	TKE	0	Yes		0			0			0	
124	??? Hoistway barricade & OSHA netting	**0**	**Schindler**	Schindler	0	No	TKE	0	No		0			0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP15300 - Fire Supression	**237,470**			**237,470**			**429,190**		**Incomplete Scope**	**195,000**			**0**			**0**	
	BP15300.0 - Fire Supression - General	**237,470**			**237,470**			**429,190**			**190,000**			**0**			**0**	
	Fire protection pipe	**237,470**			237,470			429,190			190,000			0			0	
100	Base Bid per Quote - Fire Protection	**237,470**	**Sprinklermatic**	Sprinklermatic	237,470	Yes	Farmer Irwin	429,190	Yes	All Around Fire	190,000	Yes		0			0	
200	Sales Tax	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
400	Prequalified	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
	BP15300.2 - Fire Supression - Scope	**0**			**0**			**0**			**5,000**			**0**			**0**	
	Fire protection pipe	**0**			0			0			5,000			0			0	
100	1.0 GENERAL REQUIREMENTS & DESIGN:	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
105	Provide complete fire protection system design, engineering, and installation	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
110	Provide fully sprinklered building (2-story) designed to accommodate future 3rd floor	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
115	Comply with Florida Fire Prevention Code (8th Edition)	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
120	Comply with NFPA Standards (13, 14, 20, 24, 25)	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
125	Provide UL-listed and FM-approved materials and equipment	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
130	Design for all hazard classifications (Light, OH I, OH II, Extra Hazard I)	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
135	Include required densities, remote areas, and hose stream allowances	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
140	2.0 FIRE SPRINKLER SYSTEM:	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
145	Provide and install complete wet pipe sprinkler system	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
150	Provide quick response sprinkler heads (155°F unless noted otherwise)	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
155	Provide sprinkler guards where required (mechanical/hazard areas)	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
160	Coordinate sprinkler head layout with ceiling grid and lighting	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
165	Provide Schedule 10 black steel piping (mains and branch lines)	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
170	Provide grooved or threaded fittings per pipe size requirements	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
175	Provide galvanized piping in exposed/corrosive environments	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
180	Provide hangers and supports per NFPA requirements	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
185	Provide clevis hangers for 4" pipe and larger	**0**	**Sprinklermatic**	Sprinklermatic	0	No	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
190	3.0 PREACTION SYSTEM:	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
195	Provide double interlock preaction system (second floor)	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
200	Integrate preaction system with heat detection system	**0**	**Sprinklermatic**	Sprinklermatic	0	No	Farmer Irwin	0	No	All Around Fire	0	No		0			0	
205	Provide all valves, trim, panels, and controls required for operation	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
210	4.0 FIRE PUMP & WATER SUPPLY:	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
215	Provide and install electric fire pump (750 GPM @ 95 PSI, 60 HP)	**0**	**Sprinklermatic**	Sprinklermatic	0	No	Farmer Irwin	0	Yes	All Around Fire	0	No		0			0	
220	Provide jockey pump (7.5 GPM, 1.5 HP)	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
225	Provide complete pump controllers and accessories	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
230	Coordinate electrical connections with electrical contractor	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
235	5.0 STANDPIPE SYSTEM:	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
240	Provide Class I automatic standpipe system	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	No		0			0	
245	Provide standpipes at Stair #1 and Stair #2	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
250	Provide hose valves, check valves, and butterfly valves	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
255	Provide risers and manifolds per drawings	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
260	6.0 FIRE DEPARTMENT CONNECTION (FDC):	**0**	**Sprinklermatic**	Sprinklermatic	0	N/A	Farmer Irwin	0	N/A	All Around Fire	0	N/A		0			0	
265	Provide Fire Department Connection (FDC)	**0**	**Sprinklermatic**	Sprinklermatic	0	No	Farmer Irwin	0	No	All Around Fire	0	No		0			0	
270	Install FDC 18"–36" above finished grade	**0**	**Sprinklermatic**	Sprinklermatic	0	No	Farmer Irwin	0	No	All Around Fire	0	No		0			0	
275	Provide signage and identification	**0**	**Sprinklermatic**	Sprinklermatic	0	No	Farmer Irwin	0	No	All Around Fire	0	No		0			0	
280	Provide bollard protection at FDC	**0**	**Sprinklermatic**	Sprinklermatic	0	No	Farmer Irwin	0	No	All Around Fire	0	No		0			0	
285	Connect FDC to existing 8" circulating main	**0**	**Sprinklermatic**	Sprinklermatic	0	No	Farmer Irwin	0	No	All Around Fire	0	No		0			0	
290	7.0 BACKFLOW PREVENTION:	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
295	Provide Double Check Detector Assembly (DDCA)	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
305	8.0 VALVES, DEVICES & MONITORING:	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
310	Provide control valves throughout system	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	
315	Provide tamper switches on all valves	**0**	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes		0			0	

320	Provide waterflow switches	0	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes	0	0
325	Provide supervisory and alarm monitoring connections	0	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes	0	0
330	Provide central station monitoring integration	0	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	No	0	0
335	9.0 FIRESTOPPING:	0	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes	0	0
340	Firestop all penetrations through rated walls and floors	0	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes	0	0
345	Use UL-listed firestopping assemblies	0	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes	0	0
350	Maintain required fire-resistance ratings	0	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes	0	0
355	10.0 SPECIAL SUPPRESSION SYSTEMS:	0	**Sprinklermatic**	Sprinklermatic	0	N/A	Farmer Irwin	0	N/A	All Around Fire	0	N/A	0	0
360	Provide tank-based kitchen hood fire suppression system (UL 300 compliant)	0	**Sprinklermatic**	Sprinklermatic	0	No	Farmer Irwin	0	No	All Around Fire	0	No	0	0
380	11.0 FIRE ALARM SYSTEM INTEGRATION:	0	**Sprinklermatic**	Sprinklermatic	0	N/A	Farmer Irwin	0	N/A	All Around Fire	0	N/A	0	0
385	Integrate sprinkler system with fire alarm system	0	**Sprinklermatic**	Sprinklermatic	0	No	Farmer Irwin	0	No	All Around Fire	0	No	0	0
420	12.0 TESTING & COMMISSIONING:	0	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes	0	0
425	Perform hydrostatic testing of all piping	0	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes	0	0
430	Perform flushing of underground and aboveground piping	0	**Sprinklermatic**	Sprinklermatic	0	No	Farmer Irwin	0	Yes	All Around Fire	0	Yes	0	0
435	Perform acceptance testing per NFPA 13 / 13R	0	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes	0	0
440	Coordinate inspections with AHJ	0	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes	0	0
445	Provide test reports and certifications	0	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes	0	0
450	13.0 COORDINATION & CLOSEOUT:	0	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes	0	0
455	Coordinate with mechanical, electrical, plumbing, and structural trades	0	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes	0	0
460	Provide coordinated shop drawings and BIM (if required)	0	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	5,000	Yes	0	0
465	Provide as-built drawings	0	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes	0	0
470	Provide O&M manuals	0	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes	0	0
475	Provide training to Owner	0	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes	0	0
480	14.0 DRAWINGS & REFERENCES (FOR BID):	0	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes	0	0
485	Fire Protection Plans	0	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes	0	0
490	Fire Alarm Plans	0	**Sprinklermatic**	Sprinklermatic	0	No	Farmer Irwin	0	No	All Around Fire	0	Yes	0	0
495	Life Safety Plans	0	**Sprinklermatic**	Sprinklermatic	0	No	Farmer Irwin	0	No	All Around Fire	0	Yes	0	0
500	Design Criteria Sheets	0	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes	0	0
505	Details and Schedules	0	**Sprinklermatic**	Sprinklermatic	0	Yes	Farmer Irwin	0	Yes	All Around Fire	0	Yes	0	0
610	Add Alt: Fire line from point of connection at street (tapping sleeve) up to building and including DDCV.	0	**Sprinklermatic**	Sprinklermatic	0	No	Farmer Irwin	0	No	All Around Fire	0	No	0	0
615	Add Alt: Fire line from the outflow of the DDCV to inside the building.	0	**Sprinklermatic**	Sprinklermatic	0	No	Farmer Irwin	0	No	All Around Fire	0	No	0	0

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP15400 - Plumbing	**1,150,477**			**1,185,421**			**1,795,800**			**1,150,477**			**0**			**0**	
	BP15400.0 - Plumbing - General	**1,129,107**			**1,067,441**			**1,795,800**			**1,129,107**			**0**			**0**	
	Plumbing	**1,129,107**			1,067,441			1,795,800			1,129,107			0			0	
100	Plumbing Base Bid Quote	**1,096,220**	**A Better Plumbing**	Anchor Mechanical	1,036,350	Yes	Farmer Irwin	1,795,800	Yes	A Better Plumbing	1,096,220	Yes		0			0	
105	Sales Tax	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
115	Prequalified	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
	BP15400.2 - Plumbing - Scope	**21,370**			**117,980**			**0**			**21,370**			**0**			**0**	
	Plumbing	**21,370**			117,980			0			21,370			0			0	
010	Plumbing fixtures	**0**	**A Better Plumbing**	Anchor Mechanical	101,280	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
020	Allowance: Materials, installation and coordination per note #4 of P-100 for the Car Wash Station	**21,370**	**A Better Plumbing**	Anchor Mechanical	16,700	Sub +	Farmer Irwin	0	No	A Better Plumbing	21,370	Yes		0			0	
100	2.0 DOMESTIC WATER SYSTEMS:	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
105	Provide complete hot and cold domestic water distribution systems (all floors)	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
110	Install domestic water piping to all fixtures and equipment	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
115	Provide domestic water risers (hot, cold, and recirculation)	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
120	Provide domestic hot water return systems	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
125	Install booster pumps and recirculation pumps	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
130	Provide under-slab water piping systems	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
135	Provide isolation valves throughout system	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
140	Provide auxiliary valve boxes	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
145	Provide point-of-use mixing valves	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
150	3.0 WASTE & VENT SYSTEMS (DWV):	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
155	Provide complete waste and vent piping systems (all floors)	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
160	Install piping for water closets, lavatories, sinks, and showers	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
165	Provide vent systems per code requirements	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
170	Install floor drains, floor sinks, and mop sinks	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
175	Provide cleanouts (two-way, wall, and exterior)	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
180	Provide trap primer systems	**0**	**A Better Plumbing**	Anchor Mechanical	0	No	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
185	Provide condensate drain piping and drywells	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
190	Provide condensate drain boxes	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
195	4.0 INTERCEPTORS & SPECIAL DRAINAGE SYSTEMS:	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
200	Provide grease interceptor (GB-75 or approved equal)	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
205	Provide solids interceptor (SI-75 or approved equal)	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
210	Provide interceptor sizing and calculations	**0**	**A Better Plumbing**	Anchor Mechanical	0	No	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
215	Install oil separators in applicable areas	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
220	Provide oil level monitoring system	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
225	Coordinate all interceptor installations with site and civil work	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
230	5.0 PUMPS & SPECIAL EQUIPMENT:	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
235	Provide elevator sump pump systems	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
240	Provide all associated piping, controls, and discharge connections	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
245	6.0 PLUMBING FIXTURES:	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
250	Provide and install all plumbing fixtures per fixture schedule on P-601	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
255	Install water closets, lavatories, sinks, showers, and drinking fountains	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
260	Provide all fixture carriers, supports, and trim	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
265	Install fixtures in accordance with ADA and accessibility requirements	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
270	Coordinate fixture locations with architectural plans	**0**	**A Better Plumbing**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes		0			0	
275	In 11600 - Fleet Equipment - 7.0 SPECIALTY PLUMBING SYSTEMS:	**0**	**A Better Plumbing**	Anchor Mechanical	0	No	Farmer Irwin	0	Yes	A Better Plumbing	0	No		0			0	
280	Provide compressed air system including:	**0**	**A Better Plumbing**	Anchor Mechanical	0	No	Farmer Irwin	0	Yes	A Better Plumbing	0	No		0			0	
285	Air piping and distribution lines	**0**	**A Better Plumbing**	Anchor Mechanical	0	No	Farmer Irwin	0	Yes	A Better Plumbing	0	No		0			0	
290	Drip legs and valves, Pressure regulators, Quick disconnects, Filters and compressors	**0**	**A Better Plumbing**	Anchor Mechanical	0	No	Farmer Irwin	0	Yes	A Better Plumbing	0	No		0			0	
305	See Div 11 Equipment for Oil and grease tanks and connections to piping system	**0**	**A Better Plumbing**	Anchor Mechanical	0	No	Farmer Irwin	0	Yes	A Better Plumbing	0	No		0			0	
310	Provide oil reel and grease reel drop systems in maintenance areas	**0**	**A Better Plumbing**	Anchor Mechanical	0	No	Farmer Irwin	0	Yes	A Better Plumbing	0	No		0			0	
315	Coordinate all specialty systems with equipment layouts	**0**	**A Better Plumbing**	Anchor Mechanical	0	No	Farmer Irwin	0	Yes	A Better Plumbing	0	No		0			0	

320	8.0 INSTALLATION REQUIREMENTS:	0	A Better Plumbing	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes	0	0
325	Provide pipe hangers and supports (insulated and non-insulated)	0	A Better Plumbing	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes	0	0
330	Install piping systems in accordance with code and manufacturer requirements	0	A Better Plumbing	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes	0	0
335	Coordinate routing to avoid conflicts with other trades	0	A Better Plumbing	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes	0	0
340	Maintain proper slopes for drainage piping	0	A Better Plumbing	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes	0	0
345	9.0 FIRESTOPPING & PENETRATIONS:	0	A Better Plumbing	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes	0	0
350	Firestop all pipe penetrations through rated walls and floors	0	A Better Plumbing	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes	0	0
355	Provide UL-listed firestop assemblies	0	A Better Plumbing	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes	0	0
360	Maintain fire-resistance ratings for all penetrations	0	A Better Plumbing	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	A Better Plumbing	0	Yes	0	0

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP15500 - Heating Ventilating and Air Conditioning	**2,802,545**			**3,146,154**			**3,406,128**			**2,877,940**			**2,802,545**			**0**	
	BP15500.0 - HVAC - General	**2,774,615**			**3,110,600**			**3,378,198**			**2,850,010**			**2,774,615**			**0**	
	HVAC	**2,774,615**			3,110,600			3,378,198			2,850,010			2,774,615			0	
100	H.V.A.C. Base Bid	**2,693,801**	**Hill York**	Anchor Mechanical	3,020,000	Yes	Farmer Irwin	3,378,198	Yes	Southeast	2,767,000	Yes	Hill York	2,693,801	Yes			0
108	Sales Tax	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
112	Prequalification	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
	BP15500.2 - HVAC - Scope	**27,930**			**35,554**			**27,930**			**27,930**			**27,930**			**0**	
	HVAC	**27,930**			35,554			27,930			27,930			27,930			0	
102	CHILLED WATER AIR HANDLING UNIT:	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
104	Chilled Water AHU-1	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
106	Chilled Water AHU-2	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
108	Manufacturer: Trane CSAA	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
110	DUCTLESS SPLIT SYSTEM INDOOR UNIT:	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
112	AC-1 Manufacturer: Mitsubishi Electric PKA-A24KA7	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
114	DUCTLESS SPLIT SYSTEM OUTDOOR UNIT :	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
116	CU-1 Manufacturer: Mitsubishi Electric PUY-A24NHA7(-BS)	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
118	COMPUTER ROOM INDOOR AIR HANDLER UNIT :	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
120	CRV-1, 2 & 3 Manufacturer: Liebert CR035RA1A7	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
122	Air Cooled Chillers:	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
124	CH-1 & CH-2 Manufacturer: Trane CGAM052	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
126	Pumps P-1 & P-2 Manufacturer : Taco 2009D	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
127	Chilled water piping with PVC jacketed insulation	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
128	Expansion Tank: ET-1 Manufacturer Taco CA90-125	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
130	AIR/DIRT SEPARATOR SCHEDULE: Manufacturer Taco 4904AD	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
132	BUFFER TANK SCHEDULE: BT-1 Manufacturer Taco BTH0150F04-125N	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
134	VAV UNIT SCHEDULE: Manufacturer Trane	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
136	Provide DDC's/VFD's with controls for the chillers/pumps	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
138	REFRIGERANT PIING EXPOSED OUTDOORS SHALL BE INSULATED AND PROTECTED WITH ALUMINUM JACKETING	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
140	Condensate piping with p-trap to specified floor drains.	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
142	Ductwork	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
144	Duct Construction Schedule Sheet M-601	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
146	Sealing: All duct seams, joints, and connections sealed with mastic and/or approved sealant.	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
148	Firestopping to your trade	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
150	Insulation for your trade	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
152	Supply, Return, Outside , Exhaust & Transfer Air	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
153	Controls package	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
154	Exhaust fans, Grilles, registers, Diffusers	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
156	Kitchen Exhaust Hood with Fire Supression System Captive Aire supply and install	**27,930**	**Hill York**	Anchor Mechanical	35,554	N/A	Farmer Irwin	27,930	X Sub	Southeast	27,930	X Sub	Hill York	27,930	Yes			0
156	HVLS Big Ass Fans Schedule M601	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0
158	10 YEAR FACTORY MECHANICAL WARRANTY & 1 YEAR ELECTRICAL WARRANTY FOR (HVLS) FANS . per sheet M-601.	**0**	**Hill York**	Anchor Mechanical	0	No	Farmer Irwin	0	Yes	Southeast	0	No	Hill York	0	Yes			0
160	5 YEARS PARTS AND LABOR WARRANTY For CH-1 & CH-2 per sheet M-602.	**0**	**Hill York**	Anchor Mechanical	0	Yes	Farmer Irwin	0	Yes	Southeast	0	Yes	Hill York	0	Yes			0

****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP16100 - Electrical	**3,984,717**			**4,212,121**			**3,984,717**			**4,581,750**			**0**			**0**	
	BP16100.0 - Electrical General	**4,065,000**			**4,343,404**			**4,065,000**			**4,746,750**			**0**			**0**	
	Electrical	**4,065,000**			4,343,404			4,065,000			4,746,750			0			0	
100	Basic Electric	**4,065,000**	**C.Davis Electric**	Kasper Electric	4,343,404	Yes	C.Davis Electric	4,065,000	Yes	Wave Electric	4,746,750	Yes		0			0	
140	Sales Tax	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0	Yes		0			0	
144	Prequalified	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0	Yes		0			0	
	BP16100.2 - Electrical Scope	**-80,283**			**-131,283**			**-80,283**			**-165,000**			**0**			**0**	
	Electrical	**-86,215**			-137,215			-86,215			-165,000			0			0	
100	TEMP POWER	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
100	Power to Site Lighting	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
100	Power for Site Trailer	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
100	PRIMARY POWER	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
101	Furnish and Install Splice Box @ Existing FPL Transformer	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
102	Install 100A/200A Disconnects @ Existing Building	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
103	Run In Ground Primary Power From Existing Equipment to Proposed.	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
104	Run In Ground Primary Power From EOC to Fire Training	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
105	Run In Ground Primary Power From EOC to Fuel Island	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
106	Run In Ground Primary Power From EOC to Car Washing Station	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
107	Furnish and Install Site Lighting (Light Poles)	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
108	Furnish and Install North Landscape Lighting	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
109	Furnish and Install North Memorial Lighting	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
110	Furnish and Install South Covered Parking Lighting	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
111	Furnish and Install Tamper Switches at Back Flow Preventer	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
112	Bring Power to Motorized Gates	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
113	Furnish and Install Level 2 Dual EV Chargers	**27,785**	**C.Davis Electric**	Kasper Electric	27,785	Yes	C.Davis Electric	27,785	X Sub	Wave Electric	0			0			0	
114	Install 60Hz/3Ph/40A power For AC-1/2	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
115	Install 30Hz/2Ph/15A power For DR-1	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
115	Switch Gear	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
116	Above/Underground Conduit	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
118	Special Sleeves/Dedicated Pathways	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
120	Grounding/Bonding	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
200	SECONDARY POWER	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
201	Furnish and Install 3/4" Galv. Steel Conduit throughout Building	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
202	Pull All Wire to Specified Locations per Electric Plans	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
203	Furnish and Install all Single Gang Outlets	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
204	Furnish and Install all Double Gang Outlets (G/IG/EWC/WPG/CR/USB)	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
204	Furnish and Install all Quad Gang Outlets @ Mech Open Work Cubicals	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
204	Furnish and Install all Quad Gang Outlets @ Countertops	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
204	Furnish and Install all Specialty Outlets (5-20R)	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
205	Furnish and Install Floor Outless and Boxes	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
205	Furnish and Install Junction Boxes	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
206	Stub out 30Hz/1Ph Power at all VAV locations	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
207	Stub out 30Hz/3Ph Power at BP-1 Fire Pump	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
208	Provide 60Hz/3Ph Power at Kitchen Range	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
208	Install 100Hz/3Ph/80A power For The Elevator	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
209	Furnish and install EPO (Emergency Power Off) for Kitchen Hood	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
210	Furnish and Install Waterflow Signaling Bell	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
211	Furnish and Install Access Panels for Troubleshooting and Services	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
212	Cable Trays/Supportive Infrastructure	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
300	POWER DISTRIBUTION	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
301	Main Switch Board (1600A, 277/480V, 3ohm, 4W)	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
301	Distribution Panel (1LDP 800A)	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
302	Panel 1M1 - 150A	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	
303	Panel 1K1 - 250A	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0			0			0	

304	Panel 1L3 - 400A	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
305	Panel 1L2 - 225A	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
306	Panel 1L1 - 400A	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
306	Panel 1H3 - 250A	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
306	Panel 1H2 - 250A	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
306	Panel 1H1 - 400A	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
306	Panel 1LDH - 100A	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
306	Panel 1LSL - 50A	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
307	XFMR 1TM - F 45KVA	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
307	Light Control Panel - 1LCP1	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
307	Light Control Panel - 1LCP2	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
308	XFRM 1TK - C 75KVA	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
309	XFRM 1TL1 - E 225KVA	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
310	XFRM 1TLS - A 15KVA	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
311	Panel 2HL 600A	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
312	XFRM 2TL1 - A 12.5KVA	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
313	Panel 2L2 - 225A	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
314	Panel 2L1 - 400A - MLO	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
314	Panel 2L1 - 400A - MLB	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
314	In Division 15 - HVAC - 6' BAFs - Gym	**0**	**C.Davis Electric**	Kasper Electric	0	No	C.Davis Electric	0	No	Wave Electric	0		0		0
314	In Division 15 - HVAC - 6' BAF - Gym	**0**	**C.Davis Electric**	Kasper Electric	0	No	C.Davis Electric	0	No	Wave Electric	0		0		0
314	In Division 15 - HVAC - 8' BAFs - Covered Patio	**0**	**C.Davis Electric**	Kasper Electric	0	No	C.Davis Electric	0	No	Wave Electric	0		0		0
314	In Division 15 - HVAC -10' BAFs - Vehicle Bay	**0**	**C.Davis Electric**	Kasper Electric	0	No	C.Davis Electric	0	No	Wave Electric	0		0		0
314	Fire Training Fans	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
600	MISC	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
601	Install all Electrical Equipment per plans	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
601	Install all Electrical Equipment per plans	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
601	Removal of ex. Light Poles	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
602	Final Appliance Hookup	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
603	Final Mechanical Hookup	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
604	Arc Flash Study	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
604	Testing and Final Inspection	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
604	ADD: Provide 120/220v Power to oil Pump Yard w/ Disconnects	**0**	**C.Davis Electric**	Kasper Electric	0	No	C.Davis Electric	0	Yes	Wave Electric	0		0		0
604	Carried in Fire Suppression - Tamper Switches at DDCV	**0**	**C.Davis Electric**	Kasper Electric	0	No	C.Davis Electric	0	No	Wave Electric	0		0		0
605	Aluminum Feeders ilo Copper	**-165,000**	**C Davis Electric**	Kasper Electric	-165,000	X Sub	C Davis Electric	-165,000	Yes	Wave Electric	-165,000	X Sub	0		0
900	Rev 1 Adjustments	**0**	**C Davis Electric**		0		C Davis Electric	0			0		0		0
901	Chiller feeder not aluminum	**6,600**	**C Davis Electric**		0		C Davis Electric	6,600			0		0		0
902	Updated FPL design associated electrical costs	**39,500**	**C Davis Electric**		0		C Davis Electric	39,500			0		0		0
903	Updated FPL design run to property line	**4,900**	**C Davis Electric**		0		C Davis Electric	4,900			0		0		0
	Emergency generators	**5,932**			5,932			5,932			0		0		0
400	GENERATOR	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
400	Furnish and Install1250KW/ 277/480V /3Ph/ Generator	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
400	Fill and Test Tank	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
400	Top off Desiel Tank	**5,932**	**C.Davis Electric**	Kasper Electric	5,932	Yes	C.Davis Electric	5,932	X Sub	Wave Electric	0		0		0
400	Furnish and Install Manual Tranfer Switches	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
	Lighting fixtures and lamps	**0**			0			0			0		0		0
500	LIGHTING PACKAGE	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
501	4" Cylinder Pendant	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
502	6" Round Pendant	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
503	48" Ring Pendant - Gym	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
504	36" Ring Pendant - Gym	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
505	24" Ring Pendant - Gym	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
506	12" Dome Pendant Lights	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
507	Custom Leaf Shape Pendants	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
508	8" Decorative Pendant	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
509	4' Linear Ceiling Lights	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
510	Suspended LED Linear Lights - Command Room	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
511	Perimeter Slot Lighting	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
511	Power to Exterior Signage	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0
512	Lightning Protection	**0**	**C.Davis Electric**	Kasper Electric	0	Yes	C.Davis Electric	0	Yes	Wave Electric	0		0		0

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP16150 - Electrical - Alarms & Security	**422,988**		***Only w Electric contract**	**422,988**			**422,988**			**567,849**			**0**			**0**
	BP16150.0 - General	**422,988**			**422,988**			**422,988**			**747,646**			**0**			**0**
	Security	**422,988**			422,988			422,988			747,646			0			0
100	Burglar/Security LV Bid	**422,988**	**Security 101**	Kasper Electric	422,988	Yes	Security 101	422,988	Yes	Universal Cabling	747,646	Yes		0			0
101	Access Control Bid	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
102	CCTV Bid	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
200	Sales Tax	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
500	Prequalified	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	No	Universal Cabling	0	No		0			0
	BP16150.2 - Scope	**0**			**0**			**0**			**-179,797**			**0**			**0**
	Security	**0**			0			0			-179,797			0			0
300	BURGLAR ALARM SYSTEM	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	Main Intrusion Detection Control	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	Head-End Equipment	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	Head-End Mounting Hardware	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	Head-End Grounding/Bond	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	Zone Expander Panel & Zone Cards	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	Power Supplies	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	Battery Backup	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	Tamper Switches at All Exterior Panels	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	Panel Grounding	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	Passive Infrared Motion Sensors (S-1)	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	Glass Break Detectors (S-2)	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	Door/Window Contacts (S-3 / 4)	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	Key Pads	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	Alarm / Disarm Stations	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	UI Programming	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	Sirens / Alarms	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	Blue Strobe Siren Alarms	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	Horn Strobes	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	Device Backboxes	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	400/700/800 MHz Antenna	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	Exterior Wall Mounted Antenna	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	Mounting Hardware/Supports	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	Antenna Bonding to Roof	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	Antenna Installation/Alignment/Testing	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	18/4 Unshielded PVC Jacket Cable	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	22/4 Unshielded PVC Jacket Cable	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	18/2 Unshielded PVC Jacket Cable	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
300	Cable Supports	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
400	ACCESS CONTROLS	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
401	Encosure/Cabinets	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
401	Battery Backup	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
401	Network Interface	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
401	Door Control Modules	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
401	Input/Output Modules	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
401	Surge Protection	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
401	Surface Mounted Cards Readers	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
401	New Surface Mounted Cards Readers @ All Offices - per 05.29.26 Tech	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
401	Keypads	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
401	Mounting Hardware	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
401	Backboxes	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
401	Door Electric Locks	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
401	Mag Locks	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
401	Electric Transfer Hinges	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
401	Door Position Switches	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
401	New Door Position Switches @ All Offices - per 05.29.26 Tech	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
401	Site Gate Access Integration	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
401	Knock Boxes	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
401	Click2Enter System	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
401	Vehicle Entry Control Devices	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
401	Operated Sensors	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
401	ADA Push Buttons	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
500	CCTV	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
501	Interior Wall Mounted Cameras	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
501	Exterior Wall Mounted Cameras	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
501	Pole Mounted Cameras	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
501	Brackets/Arms/Supports/Adapters	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
501	Backboxes/Weatherproofing	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
501	Alignment/Testing	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
502	Cat6a UTP Copper Cabling	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
502	RJ45 Connectors	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
502	OSP Data Cabling	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
502	Testing	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
502	2 Strand Fiber Cabling	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
502	Fiber Termination	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0
502	Fiber Extension to light poles	**0**	**Security 101**	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes		0			0

502	Fiber Cabling Raceways	0	Security 101	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes	0	0
502	Patch Cords	0	Security 101	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes	0	0
502	Jumpers	0	Security 101	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes	0	0
502	Adapters	0	Security 101	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes	0	0
502	Video Managment System	0	Security 101	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes	0	0
502	DVR - Digital Video Recording	0	Security 101	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes	0	0
503	Video Management/Recorder Rack Mount in Server Room	0	Security 101	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes	0	0
504	View Application	0	Security 101	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes	0	0
505	COTS Workstations	0	Security 101	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes	0	0
506	CCTV Trainging/Testing	0	Security 101	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes	0	0
508	NVT - Network Video Recorder	0	Security 101	Kasper Electric	0	Yes	Security 101	0	Yes	Universal Cabling	0	Yes	0	0
508	Security - Customer Service Plan	0	Security 101	Kasper Electric	0	No	Security 101	0	No	Universal Cabling	-179,797	No	0	0

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP16200 - Communications - LAN/Data - 27 & 28	**303,202**			**315,530**		***Only w Electric contract**	**376,267**			**456,930**			**0**			**0**	
	BP16200.0 - General	**56,672**			**69,000**			**48,600**			**56,672**			**0**			**0**	
	BDA System	**56,672**			69,000			48,600			56,672			0			0	
100	BDA System Bid	**56,672**	**Universal Cabling**	Skylight Tech	69,000	Yes	Kasper Electric	40,900	Yes	Universal Cabling	56,672	Yes		0			0	
100	Sub Tax	**0**	**Universal Cabling**	Skylight Tech	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
600	BDA SYSTEM	**0**	**Universal Cabling**	Skylight Tech	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
600	Ecludes Public Safety Radio Enhancement - 400MHz Signals - Miami Dade ONLY	**0**	**Universal Cabling**	Skylight Tech	0	No	Kasper Electric	0	No	Universal Cabling	0	No		0			0	
600	Public Safety Radio Enhancement - 800MHz Signal	**0**	**Universal Cabling**	Skylight Tech	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
600	ERCES System for Emergency Responder Communications	**0**	**Universal Cabling**	Skylight Tech	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
600	Meet AHJ/NFPA/IFC Requirments	**0**	**Universal Cabling**	Skylight Tech	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
600	Radio Coverage Signal Analysis - Post Shell Construction	**0**	**Universal Cabling**	Skylight Tech	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
600	Site/Building Signal Verifcation	**0**	**Universal Cabling**	Skylight Tech	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
600	Head-End / Core Equipment	**0**	**Universal Cabling**	Skylight Tech	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
600	Donor Antennas	**0**	**Universal Cabling**	Skylight Tech	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
600	Coverage Antennas	**0**	**Universal Cabling**	Skylight Tech	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
600	400MHz Repeater	**0**	**Universal Cabling**	Skylight Tech	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
600	800MHz Repeater	**0**	**Universal Cabling**	Skylight Tech	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
600	Bi-Directional Amplifier	**0**	**Universal Cabling**	Skylight Tech	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
600	Distributed Antenna System (for BDA system, Non-Cell Coverage)	**0**	**Universal Cabling**	Skylight Tech	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
600	Battery Backup	**0**	**Universal Cabling**	Skylight Tech	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
600	Splitters/Taps	**0**	**Universal Cabling**	Skylight Tech	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
600	NEMA panels	**0**	**Universal Cabling**	Skylight Tech	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
600	Server Room - Equipment Racks/Cabinets	**0**	**Universal Cabling**	Skylight Tech	0	Yes	Kasper Electric	7,700	X Sub	Universal Cabling	0	Yes		0			0	
600	OS Training	**0**	**Universal Cabling**	Skylight Tech	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
600	Installation	**0**	**Universal Cabling**	Skylight Tech	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
600	Testing/Analysis	**0**	**Universal Cabling**	Skylight Tech	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
	BP16200.2 - Scope	**246,530**			**246,530**			**327,667**			**400,258**			**0**			**0**	
	Structured cabling	**246,530**			246,530			327,667			400,258			0			0	
100	Structured Cabling Bid	**232,011**	**Reliable Cable**	Reliable Cable	232,011	Yes	Kasper Electric	327,667	Yes	Universal Cabling	400,258	Yes		0			0	
160	Sales Tax	**14,519**	**Reliable Cable**	Reliable Cable	14,519	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
168	Prequalified	**0**	**Reliable Cable**	Reliable Cable	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	No		0			0	
200	STRUCTURED CABLE	**0**	**Reliable Cable**	Reliable Cable	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
201	Provide Cat6a Plenum-Rated for All Data Cabling	**0**	**Reliable Cable**	Reliable Cable	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
202	Patch Panels for Cat6a Cabling	**0**	**Reliable Cable**	Reliable Cable	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
203	Cat6a Cabling Jacks	**0**	**Reliable Cable**	Reliable Cable	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
204	Cat6a Cabling Modules	**0**	**Reliable Cable**	Reliable Cable	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
205	Fiber Optic Cabling and Terminations	**0**	**Reliable Cable**	Reliable Cable	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
206	Rack Mounted Fiber Optic Cabling Enclosures (Server Racks)	**0**	**Reliable Cable**	Reliable Cable	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
207	Fiber Optic Cabling and Terminations	**0**	**Reliable Cable**	Reliable Cable	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
209	Access Contol Cabling	**0**	**Reliable Cable**	Reliable Cable	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
210	Intrusion/Security Cabling	**0**	**Reliable Cable**	Reliable Cable	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
211	CCTV/Video Surveillance Cabling	**0**	**Reliable Cable**	Reliable Cable	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
212	Intrusion/Security Cabling	**0**	**Reliable Cable**	Reliable Cable	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
213	Specialized Coaxial Cabling for ERCES/BDA Systems	**0**	**Reliable Cable**	Reliable Cable	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
214	RG-6 Coaxial Cable for CATV Outlets	**0**	**Reliable Cable**	Reliable Cable	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
215	OSP Gel-Filed Cable for In-Slab/Slab-on-Grade Cable Runs	**0**	**Reliable Cable**	Reliable Cable	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
221	Testing/Closeout	**0**	**Reliable Cable**	Reliable Cable	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	
222	Installation	**0**	**Reliable Cable**	Reliable Cable	0	Yes	Kasper Electric	0	Yes	Universal Cabling	0	Yes		0			0	

***Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.

Item Code	Description *Not to be used as scope	Carried Cost	Carried Bidder	Bidder 1	Bid 1	Scope C	Bidder 2	Bid 2	Scope C	Bidder 3	Bid 3	Scope C	Bidder 4	Bid 4	Scope C	Bidder 5	Bid 5	Scope C
	BP16700 - Audio Visual Systems	**504,753**			**504,753**			**0**			**0**			**0**			**0**	
	Equipment	**504,753**			**504,753**			**0**			**0**			**0**			**0**	
100	A/V Systems Bid	**460,258**	**AVI-SPL**	AVI-SPL	460,258	Yes		0			0			0			0	
100	Sales Tax	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
200	A/V - SYSTEMS	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
201	Shielded AV - Low Voltage Cabling	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
201	65" Smart TV	**44,495**	**AVI-SPL**	AVI-SPL	44,495	Yes		0			0			0			0	
202	75" Smart TV	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
203	85" Smart TV	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
204	115" Smart TV	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
205	Mobile Smart Boards	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
206	Touch Screen Monitors	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
207	Mobile Stands	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
208	284" x 53.5" Frameless LED Display	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
209	Hiperwall Video Wall Systems	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
210	Absen LED KLO B 1.2 V2 Video Wall	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
211	Display Controls	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
212	Distribution Equipment	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
213	Switch/Routing Controls	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
214	Audio/Visual Control Integration	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
215	Interior Exterior Speakers	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
216	Surface Mounted/Recessed Speakers	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
217	Concealed Microphones	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
218	Table/Ceiling Microphones	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
218	Conference Cameras	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
218	Monitor/Camera/TV/Video Wall Mounting	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
219	Amplifiers	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
220	DSP/Audio Processors	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
221	Audio Mixers/Patching	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
222	Testing & Closeout	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
223	Installation	**0**	**AVI-SPL**	AVI-SPL	0	Yes		0			0			0			0	
223	Estimating Design Fee	**0**	**AVI-SPL**	AVI-SPL	0	No		0			0			0			0	

*****Leveling sheets are not to be used as nor do they represent the full and accurate scope fo the project. Please refer to the Qualifications and Assumptions, Plans, Specifications, and other contract documents.**

KL KAUFMAN LYNN CONSTRUCTION

Greenacres Municiple Operations Center

Greenacres , FL

SUMMARY OF GENERAL CONDITIONS

17 Month Duration

July 7, 2026

	Item	Line Item Cost	Category Total	Notes
I.	**Management Personnel**		$2,038,976	
	A. Salaried Payroll	$1,954,185		
	B. Scheduling	$84,790		
	C. Vehicles	$0		
	D. Parking/Mileage/Travel	$0		
II.	**Field Office Set-up and Maintenance**	$114,586	$114,586	
III.	**Administrative, Communications & IT**		$63,917	
	A. Telephones & Radios	$4,669		
	B. Software Licensing & Connectivity	$0		
	C. Office Supplies	$14,414		
	D. Office Equipment	$20,350		
	E. Postage & Shipping	$848		
	F. Drawing Reproduction	$0		
	G. Fuel, Lunches, Ceremonies	$18,169		
	H. Project Photography	$5,468		
IV.	**Survey/Field Engineering**		$0	
	A. Field Engineering Staff	$0		
	B. Survey Equipment and Materials	$0		
	C. Surveying	$0		
V.	**Field Operations Support**		$59,713	
	A. Field Labor (Cleaning/Safety)	$46,994		
	B. On Site Storage Trailer	$4,240		
	C. Contractor Equipment	$0		
	D. Hoisting	$0		
	E. Small Tools & Hardware	$8,479		
	F. Temporary Protection	$0		
	G. Jobsite Cleanup/Trash Hauling	$0		
	H. Misc. Ops Support	$0		
VI.	**Jobsite Conditions**		$0	
	A. Site Security (Fence & Guard Service)	$0		
	B. Temporary Roads, Laydown	$0		
	C. Temporary Toilets	$0		
	D. Project Signs	$0		
	E. Misc. Site Support	$0		
VII.	**Project Safety**		$144,156	
	A. Safety & Quality Control Program	$135,665		
	B. Safety Equipment & Supplies	$8,492		
	C. Ladders, Barricades and Safety Rails	$0		
VIII.	**Energy/ Environmental Controls**		$1,133	
	A. Temporary Utilities	$0		
	B. Temporary Heating and Cooling	$0		
	C. Temporary Enclosures/Partitions	$0		
	D. Temporary Fire Protection	$1,133		
IX.	**Quality Assurance / Quality Control**	$4,162	$4,162	
X.	**Warranty Period Services**	$0	$0	
	A. Punch Crew			
	B. Record Retention			
	TOTAL GENERAL CONDITIONS		**$2,426,644**	

Exhibit B

List of the approved Construction Documents

Kaufman Lynn Construction, Inc.

Printed on Mon Aug 10, 2026 at 04:06 pm EDT

Job #: 1189 Greenacres Municipal Operations Center
Greenacres
Greenacres, Florida

GREENACRES EOC - Current Drawings

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
General					
G-000	COVER	1	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
G-100	GENERAL NOTES,VICINITY MAP, & LEGEND	2	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
G-101	PROJECT SHEET INDEX	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
G-102	ISOMETRIC VIEWS	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
G-103	INTERIOR 3D VIEWS	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
G-104	INTERIOR 3D VIEWS	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
G-105	INTERIOR 3D VIEWS	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
Survey					
SURVEY 1-3	BOUNDARY & TOPOGRAPHIC SURVEY	4	07/02/2026	08/07/2026	GMP Addendum #3 (08/06/26)
SURVEY 2-3	BOUNDARY & TOPOGRAPHIC SURVEY GREENACRES EMERGENCY OPERATIONS CENTER SECTION 26, TOWNSHIP 44 SOUTH, RANGE 42 EAST PALM BEACH COUNTY, FLORIDA CAD JOB NO. DRAWN BY CHECK BY DATE 11478.00	4	07/02/2026	08/07/2026	GMP Addendum #3 (08/06/26)
SURVEY 3-3	BOUNDARY & TOPOGRAPHIC SURVEY GREENACRES EMERGENCY OPERATIONS CENTER SECTION 26, TOWNSHIP 44 SOUTH, RANGE 42 EAST PALM BEACH COUNTY, FLORIDA CHECK BY DATE	4	07/02/2026	08/07/2026	GMP Addendum #3 (08/06/26)
Civil					
C-1	PRELIMINARY CIVIL ENGINEERING PLANS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-2	GENERAL NOTES	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-3	DEMOLITION PLAN	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-4	EROSION & SEDIMENTATION CONTROL PLAN	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-5	PAVING AND GRADING PLAN	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-6	DRAINAGE PLAN	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-7	UTILITY PLAN	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-8	SIGNING, MARKING, AND DIMENSION PLAN	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-9	FIRE ACCESS PLAN	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)

Kaufman Lynn Construction, Inc.

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
C-10	SITE CROSS SECTIONS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-11	CONSTRUCTION DETAILS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-12	CONSTRUCTION DETAILS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-13	CONSTRUCTION DETAILS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-14	POTABLE WATER #1 STANDARD DETAILS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-15	POTABLE WATER #2 STANDARD DETAILS	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-16	POTABLE WATER #3 STANDARD DETAILS	3	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-17	POTABLE WATER #4 STANDARD DETAILS	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-18	POTABLE WATER #5 STANDARD DETAILS	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-19	POTABLE WATER #6 STANDARD DETAILS	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-20	WASTEWATER #1 STANDARD DETAILS	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-21	WASTEWATER #2 STANDARD DETAILS	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-22	WASTEWATER #3 STANDARD DETAILS	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-23	WASTEWATER #4 STANDARD DETAILS	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-24	WASTEWATER #5 STANDARD DETAILS	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-25	WASTEWATER #6 STANDARD DETAILS	3	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
C-26	WASTEWATER #6 STANDARD DETAILS	3	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
Landscape					
LP1	Landscape Index	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
LP2	Landscape Plan	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
LP3	Landscape Plan	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
LP4	Landscape Plan	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
LP5	Landscape Plan	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
LP6	Landscape Calculations	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
LP7	Landscape Details	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)

Kaufman Lynn Construction, Inc.

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
LP8	VUA Exhibit	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
LP9	Landscape Specifications	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
LP10	Landscape Details	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
TD1	Tree Disposition Plan	3	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
TD2	Tree Disposition Plan	3	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
TD3	Tree Disposition Plan	3	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
TD4	Tree Disposition Table and Details	3	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
Irrigation					
IR-1	Irrigation Index	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
IR-2	Irrigation Plan	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
IR-3	Irrigation Plan	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
IR-4	Irrigation Plan	2		08/07/2026	GMP Addendum #3 (08/06/26)
IR-5	Irrigation Plan	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
IR-6	Irrigation Specifications	2	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
Site					
A-100	SITE PLAN	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-101	MEMORIAL SITE PLAN	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-102	MEMORIAL ELEVATIONS	1	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-103	MEMORIAL BENCH DETAILS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-150	SITE PLAN DETAILS	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-151	CANOPY SITE PLAN DETAILS	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-152	CANOPY SITE PLAN DETAILS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-153	FIRE TRAINING, CAR WASH STAION & FUEL ISLAND	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-154	CANOPY SITE PLAN DETAILS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
Life Safety					

Kaufman Lynn Construction, Inc.

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
LS-000	LIFE SAFETY SUMMARY	2	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
LS-101	LIFE SAFETY SITE PLAN	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
LS-200	LIFE SAFETY OVERALL FLOOR PLANS	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
LS-201A	LIFE SAFETY FIRST FLOOR PARTIAL PLAN	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
LS-201B	LIFE SAFETY FIRST FLOOR PARTIAL PLAN	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
LS-202	LIFE SAFETY SECOND FLOOR PLAN	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
Architectural					
A-200	OVERALL FLOOR PLANS	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-201A	PARTIAL FLOOR PLAN	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-201A.1	DIMENSION PLAN	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-201B	PARTIAL FLOOR PLAN	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-201B.1	DIMENSION PLAN	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-202A	SECOND FLOOR PLAN	4	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-202A.1	DIMENSION PLAN	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-250	FLOOR PLAN DETAILS	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-300	OVERALL	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-301A	PARTIAL FIRST	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-301B	PARTIAL FIRST	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-302A	PARTIAL SECOND	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-350	REFLECTED CEILING PLAN	2	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-401	OVERALL ROOF PLAN	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-450	ROOF DETAILS	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-451	ROOF DETAILS	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-501	EXTERIOR ELEVATIONS	2	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-501.1	EXTERIOR COLORED ELEVATIONS	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
A-502	EXTERIOR ELEVATIONS	2	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-502.1	EXTERIOR COLORED ELEVATIONS	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-550	EXTERIOR ELEVATION DETAILS	2	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-601	BUILDING SECTIONS	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-602	BUILDING SECTIONS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-603	BUILDING SECTIONS	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-610	PARTIAL SECTIONS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-611	PARTIAL SECTION & WALL SECTIONS	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-612	WALL SECTIONS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-613	WALL SECTIONS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-614	WALL SECTIONS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-615	WALL SECTIONS	1	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-630	ENLARGED STAIR PLANS, SECTIONS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-631	ENLARGED ELEV PLANS, SECTIONS	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-632	ENLARGED STAIR PLANS, SECTIONS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-633	ENLARGED STAIR PLANS, SECTIONS	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-650	WALL AND PARTITION TYPES	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-651	WALL PENETRATION DETAILS	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-700	OVERALL FF&E PLANS	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-701A	FIRST FLOOR FF&E PLAN	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-701B	FIRST FLOOR FF&E PLAN	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-702	SECOND FLOOR FFE PLAN	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-750	EQUIPMENT DETAILS AND MOUNTING HEIGHTS	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-751	ENLARGED TOILET PLANS & ELEVATIONS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-752	ENLARGED TOILET PLANS & ELEVATIONS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)

Kaufman Lynn Construction, Inc.

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
A-753	ENLARGED TOILET PLANS & ELEVATIONS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-761	CASEWORK PLANS & ELEVATIONS - FLOOR 1	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-762	CASEWORK PLANS AND ELEVATIONS - FLOOR 1 & 2	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-763	CASEWORK DETAILS	1	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-801	DOOR, WINDOW TYPES & SCHEDULES	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-802	DOOR, WINDOW TYPES & SCHEDULES	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-850	HEAD, JAMB AND SILL DETAILS	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-851	HEAD, JAMB AND SILL DETAILS	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-900	WAYFINDING SIGNAGE	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-901A	INTERIOR SIGNAGE - PARTIAL FIRST FLOOR PLAN	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-901B	INTERIOR SIGNAGE - PARTIAL FIRST FLOOR PLAN	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-902	INTERIOR SIGNAGE - SECOND FLOOR PLAN	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-903	WAYFINDING SIGNAGE	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-904	SIGNAGE DETAILS	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-905	SIGNAGE DETAILS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
A-906	SIGNAGE DETAILS	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
Interior					
ID-101	INTERIOR FINISH SPECIFICATIONS	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
ID-102	INTERIOR FINISH SCHEDULE	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
ID-200	OVERALL FLOOR FINISH PLANS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
ID-201A	FIRST FLOOR FINISH PLAN - PARTIAL A	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
ID-201B	FIRST FLOOR FINISH PLAN - PARTIAL B	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
ID-202A	SECOND FLOOR FINISH PLAN - PARTIAL A	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
ID-701	INTERIOR FINISH ELEVATIONS	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
ID-702	INTERIOR FINISH ELEVATIONS	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)

Kaufman Lynn Construction, Inc.

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
ID-703	INTERIOR FINISH ELEVATIONS	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
ID-704	INTERIOR FINISH ELEVATIONS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
Structural					
S-001	GENERAL NOTES	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-002	DESIGN CRITERIA	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-003	CONCRETE GENERAL NOTES & SCHEDULES	0	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-004	CMU & STEEL GENERAL NOTES & SCHEDULES	0	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-005	SPECIAL INSPECTIONS PLAN	0	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-006	SPECIAL INSPECTIONS TABLES	0	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-200	OVERALL PLANS	0	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-201A	FOUNDATION PLAN -AREA A	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-201B	FOUNDATION PLAN -AREA B	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-202A	SECOND FLOOR FRAMING PLAN - AREA A	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-202B	SECOND FLOOR FRAMING PLAN - AREA B	0	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-203A	ROOF FRAMING PLAN -AREA A	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-203B	ROOF FRAMING PLAN -AREA B	0	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-204	OVERALL SITE PLAN	1	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-205	CANOPY FOUNDATION PLANS	0	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-206	DUMPSTER & FIRE TRAINING FOUNDATION PLANS	0	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-207	FOUNDATION PLAN - FIRE TRAINING BUILDING	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-300	TYPICAL FOUNDATION DETAILS	0	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-301	FOUNDATION DETAILS	1	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-302	FOUNDATION DETAILS	0	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-303	TYPICAL STEEL FOUNDATION DETAILS	0	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-310	TYPICAL SLAB-ON-GROUND DETAILS	0	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)

Kaufman Lynn Construction, Inc.

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
S-311	SLAB-ON-GROUND DETAILS	0	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-401	TYPICAL CMU DETAILS	0	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-402	TILT-UP WALL DETAILS	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-510	TYPICAL STEEL FRAMING DETAILS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-511	TYPICAL STEEL FRAMING DETAILS	0	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-512	TYPICAL STEEL FRAMING DETAILS	0	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-513	TYPICAL STEEL FRAMING DETAILS	0	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-520	TYPICAL STEEL FRAMING AT ROOF DETAILS	1	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-521	TYPICAL STEEL FRAMING AT ROOF DETAILS	0	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
S-600	BUILDING SECTIONS	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
Mechanical					
M-001	GENERAL NOTES - HVAC	1	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
M-101A	FIRST FLOOR PLAN - PARTIAL A - HVAC	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
M-101B	FIRST FLOOR PLAN - PARTIAL B - HVAC	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
M-102	SECOND FLOOR PLAN - HVAC	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
M-201	ENLARGED MECHANICAL ROOMS - HVAC	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
M-202	ENLARGED PLAN - CEP - HVAC	1	03/20/2026	08/07/2026	GMP Addendum #3 (08/06/26)
M-301	CHILLED WATER PIPING SCHEMATIC - HVAC	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
M-501	DETAILS - HVAC	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
M-502	DETAILS - HVAC	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
M-503	DETAILS - HVAC	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
M-504	DETAILS - HVAC	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
M-601	SCHEDULES - HVAC	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
M-602	SCHEDULES - HVAC	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
M-603	SCHEDULES - HVAC	1	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)

Kaufman Lynn Construction, Inc.

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
M-604	SCHEDULES - HVAC	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
M-605	SCHEDULES - HVAC	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
M-606	SCHEDULES - HVAC	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
M-607	SCHEDULES - HVAC	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
M-701	CONTROLS - HVAC	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
M-702	CONTROLS - HVAC	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
M-703	CONTROLS - HVAC	1	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
Plumbing					
P-001	GENERAL NOTES - PLUMBING	1	03/20/2026	08/07/2026	GMP Addendum #3 (08/06/26)
P-100	FOUNDATION PLAN - PLUMBING	1	03/20/2026	08/07/2026	GMP Addendum #3 (08/06/26)
P-101A	FIRST FLOOR PLAN -WASTE- PLUMBING	2	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
P-101B	FIRST FLOOR PLAN -WASTE- PLUMBING	1	03/20/2026	08/07/2026	GMP Addendum #3 (08/06/26)
P-102	SECOND FLOOR PLAN -WASTE- PLUMBING	2	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
P-201A	FIRST FLOOR PLAN - DOMESTIC -PLUMBING	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
P-201B	FIRST FLOOR PLAN - DOMESTIC - PARTIAL B - PLUMBING	2	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
P-202	SECOND FLOOR PLAN - DOMESTIC - PLUMBING	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
P-401	RISER DIAGRAMS - PLUMBING	2	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
P-402	RISER DIAGRAMS - PLUMBING	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
P-403	RISER DIGRAMS - PLUMBING	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
P-404	RISER DIAGRAM - PLUMBING	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
P-405	RISER DIAGRAMS- PLUMBING	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
P-501	DETAILS - PLUMBING	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
P-502	DETAILS - PLUMBING	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
P-503	DETAILS - PLUMBING	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
P-504	DETAILS - PLUMBING	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)

Kaufman Lynn Construction, Inc.

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
P-505	DETAILS - PLUMBING	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
P-601	SCHEDULES - PLUMBING	2	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
Fire Protection					
F-001	GENERAL NOTES - FIRE PROTECTION	1	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
F-002	DESIGN CRITERIA - FIRE PROTECTION	1	08/06/2026	08/07/2026	GMP Addendum #3 (08/06/26)
F-101A	FIRST FLOOR PLAN - PARTIAL A - FIRE PROTECTION	21	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
F-101B	FIRST FLOOR PLAN - FIRE PROTECTION	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
F-102	SECOND FLOOR PLAN - FIRE PROTECTION	2	03/20/2026	08/07/2026	GMP Addendum #3 (08/06/26)
F-501	DETAILS - FIRE PROTECTION	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
F-502	DETAILS - FIRE PROTECTION	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
F-503	DETAILS - FIRE PROTECTION	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
F-504	DETAILS - FIRE PROTECTION	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
Electrical					
E-001	SYMBOL LEGEND & GENERAL NOTES - ELECTRICAL	2	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-002	FIXTURE SHEDULE- ELECTRICAL	2	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-010	SITE PLAN - LIGHTING	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-011	SITE PLAN - PHOTOMETRICS	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-020	SITE PLAN - POWER & FIRE	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-101A	FIRST FLOOR PLAN - PARTIAL A	2	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-101B	FIRST FLOOR PLAN - PARTIAL B - LIGHTING	2	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-102	SECOND FLOOR PLAN - LIGHTING	2	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-111	FIRST FLOOR PLAN - EMERGENCY PHOTOMETRICS	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-112	SECOND FLOOR PLAN -EMERGENCY PHOTOMETRICS	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-201A	FIRST FLOOR PLAN - PATIAL A - POWER	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-201B	FIRST FLOOR PLAN - PARTIAL B - POWER	2	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)

Kaufman Lynn Construction, Inc.

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
E-202	SECOND FLOOR PLAN - POWER	2	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-210	ROOF PLAN - POWER	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-301A	FIRST FLOOR PLAN - PARTIAL A	2	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-301B	FIRST FLOOR PLAN - PARTIAL B - FIRE ALARM	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-302	SECOND FLOOR PLAN - FIRE ALARM	2	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-401	ENLARGED PLANS -POWER	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-402	ENLARGED PLANS -POWER	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-501	TYPICAL FOR MULTIPLE (TWO OR MORE) DUCTS, QUANTITY PER PLANS	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-502	DETAILS - ELECTRICAL	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-503	DETAILS - LIGHTNING PROTECTION	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-504	DETAILS - FIRE ALARM	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-505	DETAILS - LIGHTING CONTROLS	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-506	DETAILS - LIGHTING CONTROLS	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-601	ELECTRICAL RISER DIAGRAM	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-602	ELECTRICAL RISER DIAGRAM	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-603	FIRE ALARM RISER	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-701	ELECTRICAL PANEL SCHEDULES	2	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-702	ELECTRICAL PANEL SCHEDULES	3	07/31/2026	08/07/2026	GMP Addendum #3 (08/06/26)
E-703	ELECTRICAL PANEL SCHEDULES	2	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
Technology					
T-001	GENERAL NOTES - TECHNOLOGY	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
T-010	SITE PLAN - TECHNOLOGY	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
T-101A	FIRST FLOOR PLAN -PARTIAL A - TECHNOLOGY	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
T-101B	FIRST FLOOR PLAN -PARTIAL B - TECHNOLOGY	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
T-102	SECOND FLOOR PLAN - TECHNOLOGY	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)

Kaufman Lynn Construction, Inc.

Drawing No.	Drawing Title	Revision	Drawing Date	Received Date	Set
T-110	ROOF PLAN - TECHNOLOGY	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
T-201	ENLARGED PLANS - TECHNOLOGY	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
T-202	ENLARGED PLANS - TECHNOLOGY	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
T-203	ENLARGED PLANS - TECHNOLOGY	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
T-301	RISER DIAGRAM - TECHNOLOGY	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
T-302	ERCES RISER DIAGRAM - TECHNOLOGY	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
T-401	DETAILS - TECHNOLOGY	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
T-402	DETAILS - TECHNOLOGY	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
T-403	DETAILS - TECHNOLOGY	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)
T-404	DETAILS - TECHNOLOGY	1	05/29/2026	08/07/2026	GMP Addendum #3 (08/06/26)
T-405	DETAILS - TECHNOLOGY	0	02/27/2026	08/07/2026	GMP Addendum #3 (08/06/26)

Kaufman Lynn Construction, Inc.

Current Specifications

Number	Description	Revision	Issued Date	Received Date	Set
00 - Procurement and Contracting Requirements					
000110	Table of Contents	1		08/07/26	GMP - Addendum #3
01 - General Requirements					
01 10 00	Summary	1		08/07/26	GMP - Addendum #3
01 25 00	Substitution Procedures	0		08/07/26	GMP - Addendum #3
01 30 00	Administrative Requirements	2		08/07/26	GMP - Addendum #3
01 32 16	Construction Progress Schedule	1		08/07/26	GMP - Addendum #3
01 40 00	Quality Requirements	2		08/07/26	GMP - Addendum #3
01 50 00	Temporary Facilities and Controls	1		08/07/26	GMP - Addendum #3
01 60 00	Product Requirements	2		08/07/26	GMP - Addendum #3
01 61 16	VOC Content Restrictions	1		08/07/26	GMP - Addendum #3
01 70 00	Execution and Closeout Requirements	2		08/07/26	GMP - Addendum #3
01 74 19	Construction Waste Management and Disposal	1		08/07/26	GMP - Addendum #3
01 78 00	Closeout Submittals	1		08/07/26	GMP - Addendum #3
02 - Existing Conditions					
02 00 00	Geotechnical Report	0	05/29/26	06/18/26	Specs - GMP
02 41 00	Demolition	1		08/07/26	GMP - Addendum #3
02 65 00	Underground Storage Tank Removal	1		08/07/26	GMP - Addendum #3
03 - Concrete					
03 10 00	Concrete Forming and Accessories	1		08/07/26	GMP - Addendum #3
03 20 00	Concrete Reinforcing	1		08/07/26	GMP - Addendum #3
03 30 00	Cast-in-Place Concrete	1		08/07/26	GMP - Addendum #3
03 35 11	Concrete Floor Finishes	1		08/07/26	GMP - Addendum #3
03 35 33	Stamped Concrete Finishing	1		08/07/26	GMP - Addendum #3
03 47 13	Tilt-Up Concrete	1		08/07/26	GMP - Addendum #3
04 - Masonry					
04 20 00	Unit Masonry	1		08/07/26	GMP - Addendum #3
05 - Metals					
05 12 00	Structural Steel Framing	1		08/07/26	GMP - Addendum #3
05 20 00	Metal Joists	2		08/07/26	GMP - Addendum #3
05 30 00	Steel Decking	1		08/07/26	GMP - Addendum #3
05 51 33	Metal Ladders	1		08/07/26	GMP - Addendum #3
05 52 13	Pipe and Tube Railings	1		08/07/26	GMP - Addendum #3
05 58 13	Aluminum Plate Column Covers	1		08/07/26	GMP - Addendum #3
05 73 11	Decorative Metal Railing	0		08/07/26	GMP - Addendum #3
05 73 13	Decorative Metal Railings	1		08/07/26	GMP - Addendum #3
06 - Wood, Plastics, and Composites					

Kaufman Lynn Construction, Inc.

Number	Description	Revision	Issued Date	Received Date	Set
06 10 00	Rough Carpentry	1		08/07/26	GMP - Addendum #3
06 41 00	Architectural Wood Casework	1		08/07/26	GMP - Addendum #3
06 42 00	Wood Paneling	1		08/07/26	GMP - Addendum #3
07 - Thermal and Moisture Protection					
07 13 26	Under-Slab Vapor Barrier	1		08/07/26	GMP - Addendum #3
07 14 00	Fluid-Applied Waterproofing	1		08/07/26	GMP - Addendum #3
07 21 00	Thermal Insulation	1		08/07/26	GMP - Addendum #3
07 26 00	Vapor Retarders	1		08/07/26	GMP - Addendum #3
07 42 13	Metal Wall Panels	1		08/07/26	GMP - Addendum #3
07 52 00	Modified Bituminous Membrane Roofing	1		08/07/26	GMP - Addendum #3
07 62 00	Sheet Metal Flashing and Trim	1		08/07/26	GMP - Addendum #3
07 71 00	Roof Specialties	1		08/07/26	GMP - Addendum #3
07 72 00	Roof Accessories	1		08/07/26	GMP - Addendum #3
07 81 00	Applied Fire Protection	1		08/07/26	GMP - Addendum #3
07 84 00	Firestopping	1		08/07/26	GMP - Addendum #3
07 92 00	Joint Sealants	3		08/07/26	GMP - Addendum #3
07 95 13	Expansion Joint Cover Assemblies	1		08/07/26	GMP - Addendum #3
08 - Openings					
08 11 13	Hollow Metal Doors and Frames	1		08/07/26	GMP - Addendum #3
08 14 16	Flush Wood Doors	1		08/07/26	GMP - Addendum #3
08 17 00	Integrated Door Opening Assemblies	1		08/07/26	GMP - Addendum #3
08 33 23	Overhead Coiling Doors	1		08/07/26	GMP - Addendum #3
08 41 26	All-Glass Entrances and Storefronts	1		08/07/26	GMP - Addendum #3
08 43 13	Aluminum-Framed Storefronts	2		08/07/26	GMP - Addendum #3
08 44 13	Glazed Aluminum Curtain Walls	1		08/07/26	GMP - Addendum #3
08 56 59	Service and Teller Window Units	1		08/07/26	GMP - Addendum #3
08 71 13	Power Door Operators	1		08/07/26	GMP - Addendum #3
08 71 23	Commercial Door Operators - Overhead Door	1		08/07/26	GMP - Addendum #3
08 80 00	Glazing	1		08/07/26	GMP - Addendum #3
08 91 00	Louvers	1		08/07/26	GMP - Addendum #3
09 - Finishes					
09 05 61	Common Work Results for Flooring Preparation	1		08/07/26	GMP - Addendum #3
09 21 16	Gypsum Board Assemblies	1		08/07/26	GMP - Addendum #3
09 30 00	Tiling	1		08/07/26	GMP - Addendum #3
09 51 00	Acoustical Ceilings	1		08/07/26	GMP - Addendum #3
09 51 30	Suspended Metal Panel Ceilings	1		08/07/26	GMP - Addendum #3
09 54 23	Linear Metal Ceilings	1		08/07/26	GMP - Addendum #3
09 62 53	Synthetic Turf Flooring	1		08/07/26	GMP - Addendum #3
09 65 00	Resilient Flooring	1		08/07/26	GMP - Addendum #3
09 68 13	Tile Carpeting	1		08/07/26	GMP - Addendum #3
09 91 13	Exterior Painting	1		08/07/26	GMP - Addendum #3

Number	Description	Revision	Issued Date	Received Date	Set
09 91 23	Interior Painting	1		08/07/26	GMP - Addendum #3
09 97 23	Concrete and Masonry Coatings	1		08/07/26	GMP - Addendum #3
097716	Framed Decorative Panel System	2		08/07/26	GMP - Addendum #3
10 - Specialties					
10 14 00	Signage	1		08/07/26	GMP - Addendum #3
10 14 16	Plaques	1		08/07/26	GMP - Addendum #3
10 21 13	Phenolic Toilet Compartments	2		08/07/26	GMP - Addendum #3
10 22 29	Operable Glass Partition	1		08/07/26	GMP - Addendum #3
10 22 39	Folding Panel Partitions	1		08/07/26	GMP - Addendum #3
10 28 00	Toilet, Bath, and Laundry Accessories	1		08/07/26	GMP - Addendum #3
10 43 00	Emergency Aid Specialties	1		08/07/26	GMP - Addendum #3
10 44 00	Fire Protection Specialties	1		08/07/26	GMP - Addendum #3
10 71 13	Exterior Sun Control Devices	2		08/07/26	GMP - Addendum #3
10 71 13.53	Exterior Vertical Sun Control Devices	1		08/07/26	GMP - Addendum #3
10 73 00	Aluminum Shade Structures	1		08/07/26	GMP - Addendum #3
10 73 13	Awnings	1		08/07/26	GMP - Addendum #3
10 73 16	Canopies	2		08/07/26	GMP - Addendum #3
10 75 00	Flagpoles	1		08/07/26	GMP - Addendum #3
11 - Equipment					
11 11 36	Vehicle Charging Equipment	1		08/07/26	GMP - Addendum #3
11 11 70	Self-Serve Wash Bay Equipment	1		08/07/26	GMP - Addendum #3
11 12 00	Parking Control Equipment	1		08/07/26	GMP - Addendum #3
11 14 00	Pedestrian Control Equipment	1		08/07/26	GMP - Addendum #3
12 - Furnishings					
12 24 00	Window Shades	2		08/07/26	GMP - Addendum #3
12 32 00	Manufactured Wood Casework	1		08/07/26	GMP - Addendum #3
12 36 00	Countertops	1		08/07/26	GMP - Addendum #3
12 48 13	Entrance Floor Mats and Frames	1		08/07/26	GMP - Addendum #3
129313	Bicycle Racks	0	02/19/26	03/02/26	Specs 95%CD
14 - Conveying Equipment					
14 21 00	Electric Traction Elevators	1		08/07/26	GMP - Addendum #3
21 - Fire Suppression					
21 01 00	Operation and Maintenance of Fire Suppression	2		08/07/26	GMP - Addendum #3
21 05 17	SLEEVES AND SLEEVES SEALS FOR FIRE SUPPRESSION PIPING	2		08/07/26	GMP - Addendum #3
21 05 18	ESCUTCHEINS FOR FIRE SUPPRESSION PIPING	2		08/07/26	GMP - Addendum #3
21 05 23	General-Duty Valves for Water-Based Fire-Suppression Piping	2		08/07/26	GMP - Addendum #3
21 05 29	Hangers and Supports for Fire-Suppression Piping and Equipment	2		08/07/26	GMP - Addendum #3
21 05 53	Identification for Fire-Suppression Piping and Equipment	3		08/07/26	GMP - Addendum #3
21 13 13	Wet-Pipe Sprinkler Systems	2		08/07/26	GMP - Addendum #3
21 31 13	Electric-Drive, Centrifugal Fire Pumps	2		08/07/26	GMP - Addendum #3
22 - Plumbing					

Number	Description	Revision	Issued Date	Received Date	Set
22 01 00	Operation and Maintenance of Plumbing	2		08/07/26	GMP - Addendum #3
22 05 19	Meters and Gages for Plumbing Piping	0	02/19/26	03/02/26	Specs 95%CD
22 05 23	General-Duty Valves for Plumbing Piping	1		06/18/26	Specs - GMP
22 05 23.14	CHECK VALVE FOR PLUMBING PIPING	1		08/07/26	GMP - Addendum #3
22 05 23.15	GATE VALVES FOR PLUMBING PIPING	1		08/07/26	GMP - Addendum #3
22 05 29	Hangers and Supports for Plumbing Piping and Equipment	2		08/07/26	GMP - Addendum #3
22 05 53	Identification for Plumbing Piping and Equipment	1		06/18/26	Specs - GMP
22 07 16	Plumbing Equipment Insulation	2		08/07/26	GMP - Addendum #3
22 07 19	Plumbing Piping Insulation	2		08/07/26	GMP - Addendum #3
22 11 13	Facility Water Distribution Piping	2		08/07/26	GMP - Addendum #3
22 11 16	Domestic Water Piping	2		08/07/26	GMP - Addendum #3
22 11 19	Domestic Water Piping Specialties	2		08/07/26	GMP - Addendum #3
22 11 23	Domestic Water Pumps	1		08/07/26	GMP - Addendum #3
22 13 16	Sanitary Waste and Vent Piping	2		08/07/26	GMP - Addendum #3
22 13 19	Sanitary Waste Piping Specialties	1		08/07/26	GMP - Addendum #3
22 13 19.13	Sanitary Drains	2		08/07/26	GMP - Addendum #3
22 13 23	Sanitary Waste Interceptors	2		08/07/26	GMP - Addendum #3
22 14 13	Facility Storm Drainage Piping	2		08/07/26	GMP - Addendum #3
22 14 29	Sump Pumps	2		08/07/26	GMP - Addendum #3
22 33 00	Electric Domestic Water Heaters	2		08/07/26	GMP - Addendum #3
220523.12	BALL VALVES FOR PLUMBING PIPING	2		08/07/26	GMP - Addendum #3
23 - Heating, Ventilating, and Air Conditioning (HVAC)					
23 01 00	GENERAL MECHANICAL PROVISIONS	2		08/07/26	GMP - Addendum #3
23 05 00	BASIC MECHANICAL MATERIALS AND METHODS	2		08/07/26	GMP - Addendum #3
23 05 13	ELECTRIC MOTORS PREMIUM EFFICIENCY TYPE	2		08/07/26	GMP - Addendum #3
23 05 15	INSTRUCTIONS AND MAINTENANCE MANUALS	2		08/07/26	GMP - Addendum #3
23 05 16	Housekeeping Pads, Concrete	2		08/07/26	GMP - Addendum #3
23 05 18	PIPING: CONDENSATE DRAIN	2		08/07/26	GMP - Addendum #3
23 05 19	GAUGES	2		08/07/26	GMP - Addendum #3
23 05 20	Piping Systems: Flushing and Cleaning	2		08/07/26	GMP - Addendum #3
23 05 21	Thermometers	2		08/07/26	GMP - Addendum #3
23 05 22	Flow Stations Venturi Type	2		08/07/26	GMP - Addendum #3
23 05 23	Valves Cocks and Specialties HVAC Systems	2		08/07/26	GMP - Addendum #3
23 05 24	Air Control Equipment Hydronic Systems	2		08/07/26	GMP - Addendum #3
23 05 29	Hangers and Supports	2		08/07/26	GMP - Addendum #3
23 05 48	Vibration Isolation Equipment	2		08/07/26	GMP - Addendum #3
23 05 53	Identification of Piping Systems and Equipment	2		08/07/26	GMP - Addendum #3
23 05 93	Performance Verification Preliminary	2		08/07/26	GMP - Addendum #3
23 05 94	Performance Verification Final	2		08/07/26	GMP - Addendum #3
23 07 00	HVAC Insulation	2		08/07/26	GMP - Addendum #3
23 08 00	Commissioning of HVAC	2		08/07/26	GMP - Addendum #3

Number	Description	Revision	Issued Date	Received Date	Set
23 09 23	Instrumentation and Control for HVAC	2		08/07/26	GMP - Addendum #3
23 09 25	Variable Frequency Drive	2		08/07/26	GMP - Addendum #3
23 21 13	Piping Systems: HVAC Water	2		08/07/26	GMP - Addendum #3
23 21 25	Pumps Horizontal Base Mounted End Suction	2		08/07/26	GMP - Addendum #3
23 23 13	Refrigerant Piping Valves	2		08/07/26	GMP - Addendum #3
23 25 00	HVAC Water Treatment System: Chilled Water and Condenser Water	2		08/07/26	GMP - Addendum #3
23 31 00	Ductwork	2		08/07/26	GMP - Addendum #3
23 33 00	Duct System Accessories	2		08/07/26	GMP - Addendum #3
23 36 16	Terminal Units VAV Single Inlet Electrical Coil	2		08/07/26	GMP - Addendum #3
23 37 13	Air Distribution Devices	2		08/07/26	GMP - Addendum #3
23 37 25	Louvers	2		08/07/26	GMP - Addendum #3
23 43 24	Air Purification System	2		08/07/26	GMP - Addendum #3
23 64 17	Chillers: Air Cooled Packaged Rotary Screw	2		08/07/26	GMP - Addendum #3
23 73 13	Air Handling Units, Central Station, Modular	2		08/07/26	GMP - Addendum #3
23 81 23	Computer-Room Air-Conditioners	2		08/07/26	GMP - Addendum #3
23 81 26	Condensing Units Air Cooled Hermetic	2		08/07/26	GMP - Addendum #3
23 81 31	Ductless Split System Air Conditioning Units	2		08/07/26	GMP - Addendum #3
26 - Electrical					
26 00 10	Supplmental Requirements for Electrical	2		08/07/26	GMP - Addendum #3
26 01 00	Operation and Maintenance of Electrical Systems	2		08/07/26	GMP - Addendum #3
26 05 19	Low-Voltage Electrical Power Conductors and Cables	2		08/07/26	GMP - Addendum #3
26 05 26	Grounding and Bonding for Electrical Systems	2		08/07/26	GMP - Addendum #3
26 05 29	Hangers and Supports for Electrical Systems	2		08/07/26	GMP - Addendum #3
26 05 33	Raceway and Boxes for Electrical Systems	2		08/07/26	GMP - Addendum #3
26 05 43	Underground Ducts and Raceways for Electrical Systems	2		08/07/26	GMP - Addendum #3
26 05 44	Sleeves and Sleeve Seals for Electrical Raceways and Cabling	2		08/07/26	GMP - Addendum #3
26 05 53	Identification for Electrical Systems	2		08/07/26	GMP - Addendum #3
26 05 73.16	COORDINATION STUDIES	1		08/07/26	GMP - Addendum #3
26 08 00	Commissioning of Electrical Systems	2		08/07/26	GMP - Addendum #3
26 09 23	Lighting Control Devices	2		08/07/26	GMP - Addendum #3
26 22 13	Low-Voltage Distribution Transformers	2		08/07/26	GMP - Addendum #3
26 24 13	Switchboards	2		08/07/26	GMP - Addendum #3
26 24 16	Panelboards	2		08/07/26	GMP - Addendum #3
26 27 13	Electricity Metering	2		08/07/26	GMP - Addendum #3
26 27 26	Wiring Devices	2		08/07/26	GMP - Addendum #3
26 28 13	Fuses	2		08/07/26	GMP - Addendum #3
26 28 16	Enclosed Switches and Circuit Breakers	2		08/07/26	GMP - Addendum #3
26 32 13	Diesel Emergency Engine Generators	2		08/07/26	GMP - Addendum #3
26 36 00	Transfer Switches	2		08/07/26	GMP - Addendum #3
26 41 13	Lightning Protection for Structures	2		08/07/26	GMP - Addendum #3
26 43 13	Surge Protective Devices for Low-Voltage Electrical Power Circuits	2		08/07/26	GMP - Addendum #3

Number	Description	Revision	Issued Date	Received Date	Set
26 51 00	Interior Lighting	2		08/07/26	GMP - Addendum #3
26 56 00	Exterior Lighting	2		08/07/26	GMP - Addendum #3
27 - Communications					
27 00 10	Supplemental Requirements for Communication	2		08/07/26	GMP - Addendum #3
27 05 26	Grounding and Bonding for Communications Systems	2		08/07/26	GMP - Addendum #3
27 05 28	Pathways for Communications Systems	2		08/07/26	GMP - Addendum #3
27 05 29	Hangers and Supports for Communications Systems	2		08/07/26	GMP - Addendum #3
27 05 36	Cable Trays for Communications Systems	2		08/07/26	GMP - Addendum #3
27 05 44	Sleeves and Sleeve Seals for Communications Pathways and Cabling	2		08/07/26	GMP - Addendum #3
27 05 53	Identification for Communications Systems	2		08/07/26	GMP - Addendum #3
27 11 00	Communications Equipment Room Fittings	2		08/07/26	GMP - Addendum #3
27 11 16	Communications Cabinets, Racks, Frames, and Enclosures	2		08/07/26	GMP - Addendum #3
27 13 13	Communications Copper Backbone Cabling	2		08/07/26	GMP - Addendum #3
27 13 23	Communications Optical Fiber Backbone Cabling	2		08/07/26	GMP - Addendum #3
27 15 13	Communications Copper Horizontal Cabling	2		08/07/26	GMP - Addendum #3
27 15 23	Communications Optical Fiber Horizontal Cabling	2		08/07/26	GMP - Addendum #3
27 41 00	Audio-Video Systems	2		08/07/26	GMP - Addendum #3
27 53 19	Distributed Antenna System (DAS)	2		08/07/26	GMP - Addendum #3
28 - Electronic Safety and Security					
28 00 00	Electronic Safety and Security Systems	3		08/07/26	GMP - Addendum #3
28 05 00	Common Work Results for Electronic Safety and Security	3		08/07/26	GMP - Addendum #3
28 05 13	Conductors and Cables for Electronic Safety and Security	3		08/07/26	GMP - Addendum #3
28 08 00	Commissioning of Electronic Safety and Security	3		08/07/26	GMP - Addendum #3
28 13 00	Access Control	3		08/07/26	GMP - Addendum #3
28 16 00	Intrusion Detection	3		08/07/26	GMP - Addendum #3
28 23 00	Video Surveillance	3		08/07/26	GMP - Addendum #3
28 46 21.11	Addressable Fire Alarm Systems	3		08/07/26	GMP - Addendum #3

Exhibit C

Qualifications and Assumptions

Greenacres MOC
City of Greenacres
GMP 8/11/26

Contractor's Assumptions and Qualifications

GENERAL

This Assumptions and Qualifications document serves to expand and/or clarify the Agreement/Contract Documents and the basis of the GMP.

DOCUMENTS:

1. This GMP Proposal is based on the referenced Exhibits and Documents as follows:
    a. GMP Cost Summary
    b. Allowances – In this document
    c. Assumptions and Qualifications – This document
    d. Document Log
    f. Construction Schedule

SCHEDULE, DURATIONS & TIME:

1. The schedule is based on work being performed during normal business hours (7:00 AM to 5:00 PM) Monday through Friday.

INSURANCES & BONDING:

1. This proposal includes either individual subcontractor bonds or a subcontractor default insurance program at the discretion of Kaufman Lynn Construction.

PAYMENTS, DEPOSITS & RETAINAGE:

a. Deposit percentages listed below shall apply to the material value only. No single deposit for any trade shall exceed $50,000. Deposits shall only be payable after product submittal/shop drawings approval unless the contract terms of a Subcontractor dictate otherwise or cause the schedule to be otherwise delayed
b. Elevator – Payment terms for elevator scope as described below.
    i. 50% of the final sales price will be due and payable within 30 days from receipt of a fully executed subcontract agreement. This initial payment will be

applied to pre-production, engineering, initial submittals, project management, and raw material procurement. Receipt of this payment is required prior to ordering the manufacturing of any materials.

ii. 30% of total sales price, including any modification s by scope changes, shall be due and payable when the material has been received at Schindler's warehouse hub and ready for delivery to the customer. Receipt of this payment is required prior to delivery and mobilization of labor.

iii. 20% will be invoiced upon commencement of on-site installation.

iv. Retention shall be 5%.

c. Fire Training – Progress Payments for offsite production included in Subcontractor's Schedule of Values.
d. Fitness Equipment – 50% Deposit ahead of material release.
e. Furniture – 50% Deposit 20 weeks before installation
f. Lockers & Storage Cabinets
g. Millwork, Cabinets, & Counter (ST-1, ST-2, & ST-3) – 50% Deposit on stone 3 months prior to install date.
h. Structured Cabling & Data – 10% Deposit for cable material release.
i. Appliances – 25% deposit for materials at contract execution.
j. Laundry Equipment - 25% deposit for materials at contract execution.

Design-Build Qualifications and Design Development. Due to the timing and status of the design, the Design-Builder has included certain qualifications, assumptions, and allowances as the basis of the Contract Sum and schedule. The Owner's acknowledgment or acceptance of any such qualification, assumption, or allowance is intended solely to establish the contractual basis of pricing and scope and shall not constitute approval of the adequacy of the Design-Builder's design or transfer any design responsibility to the Owner. The Design-Builder remains responsible for determining the final requirements necessary for code compliance, proper operation and performance, compliance with the Authority Having Jurisdiction, manufacturer requirements and recommendations, and a complete and functional installation. If further design development determines that any qualified or assumed item must be modified, resized, upgraded, or otherwise revised to satisfy these requirements, such revision shall remain the Design-Builder's responsibility and shall not constitute a basis for additional compensation, except where the revision results from an Owner-directed change in scope or performance requirements.

Contractor includes project specific Quality Control and safety program, per DB SOP's, the plans and reports of which shall be shared in a timely manner by DB with Owner

PERMITTING, SPECIAL INSPECTIONS, TESTING, CAPACITY FEES & IMPACT FEES:

1. Regarding temporary and permanent power, temporary/construction power will be the responsibility of Contractor DB in its entirety. Regarding permanent power and consumption: DB will coordinate with Owner and FPL to provide permanent FPL services to the project ("hot"

transformers) prior to the date indicated in the construction schedule. DB will be responsible for installation of the secondary building power feeds and receipt of the temp-for-test inspections. Owner shall be responsible for all costs from FPL for any primary power feeds up to and including the transformer and transformer pads. Upon completion of the temp-for-test inspections, DB has included 8 business days in the construction schedule for receipt and install of the permanent meters from FPL/Owner. Once the permanent meter(s) have been installed by FPL for the project, which cost and installation is an Owner responsibility, Contractor will no longer be responsible to pay for consumption.

SITE:

1. Industry standard 6' temporary construction screened chain link fencing with a gate and a combination lock will be used to secure the site. Two (x2) AI surveillance tower-mounted cameras will be utilized for security. In consultation with the City, KL has included nine months of surveillance services, to commence on a date mutually agreed upon by the parties

CONTRACTOR EXCLUSIONS/INCLUSIONS:

The following items are excluded by Contractor, and shall be provided by the Owner:

1. Contractor excludes Occupancy Permit fees, Impact fees, Permanent, and Utility Fees, FPL, Assessments.
2. Contractor excludes FPL transformers, Primary Conduits material (install included), wire, and Deposits.
3. Contractor excludes Main Service Water Meters, Fees and Deposits
4. Contractor excludes Cable TV/Phone equipment and cable or phone wire from service point to communication room(s).
5. Contractor excludes deposits for permanent electric at Meters.
6. Contractor excludes removal, relocations, and main line installations to building point, including fiber optics, gas (including meter), ~~power~~, phone, cable, etc. These shall be provided by the appropriate service provider.
7. All permanent power bills from Temp-for-test through the end of the project will be paid by the City of Greenacres.
8. Contractor is only responsible for the debris generated by construction activities
9. Contractor excludes Fire Alarm Monitoring Service, Elevator Service agreement, Gas service agreement and any other additional service agreement Costs which could be required for Certificate of Occupancy.
10. Contractor excludes cost relating to Radon Mitigation either passive or active.
11. Mockups per specifications are included
12. Contractor excludes any special labor rates that may be required by project location, funding, municipality governance, etc. such as Davis Bacon Act.

Allowances:

1. Turf: Turf allowance outside the gym is being carried at $15,300 ($15/SF)

DIVISION 02 - SITE WORK
EARTHWORK AND UTILITIES

Contractor Excludes:

1. Video inspection of existing sanitary mains, prior to and upon completion of work.
2. Any/all Removal of regulated contaminated material, if required.
3. Permits, protection, removal, abatement or removal of any asbestos or regulated hazardous materials.
4. Meters.

LANDSCAPING

1. Although the Contract Drawings indicate the relocation of multiple existing hardwood trees, the Owner has elected to dispose of 27 of the indicated trees in lieu of relocation. The Contractor shall furnish and install replacement trees per the contract documents.

Contractor Excludes the guaranteed survivability of relocated trees.

DIVISION 05 - METALS

Contractor Excludes:
1. Attic Stock for Alucobond Metal Panels.

DIVISION 07-THERMAL AND MOISTURE PROTECTION

ROOFING

1. Scuppers, emergency scuppers will be Stainless Steel custom manufactured as a cost saving alternative.

Doors & Hardware
1. Metal Door assembly shall have a minimum of 1 year warranty

DIVISION 11

Fleet maintenance Equipment

Contractor Excludes:
1. Any responsibility for the condition or operability of the existing equipment or owner provided equipment. If any existing equipment is found to be inoperable or requires repairs during relocation

or installation, such repairs shall be performed only upon authorization and will be billed as an additional cost on a time-and-materials basis.

DIVISION 12

Furnishings
Contractor Includes

1. GMP includes cost to procure and install the furnishings notated in JC White Quote (Order) number 134861 dated 8/7/2026 which proposal is incorporated herein by reference

DIVISION 13 – Pre-Engineered Structures

1. The fire training structure is a sole-source specialty item that is typically procured directly by the Owner. At Greenacres' request, Kaufman Lynn has agreed to include the procurement and installation of the fire training structure within its scope of work. Notwithstanding the foregoing, to the extent that the procurement, delivery, or installation of this item extends beyond the durations allocated in the Project Schedule, any resulting delay shall not be attributable to Kaufman Lynn and shall entitle Kaufman Lynn to an equitable extension of the Contract Time.
2. Fire Training structure included as follows: Design builder shall furnish and install fire training structure notated in Fire Training Structures, LLC Quote #: 5699-6 dated 6/30/2026

Fuel System

1. Excludes fuel filling of the fuel system tank

DIVISION 16 – ELECTRICAL

1. Electrical Feeder and Subfeeder Conductors. Notwithstanding conductor materials indicated on the current Drawings, the Design-Builder's Contract Sum is based upon providing aluminum conductors for all feeders and subfeeders rated 100 amperes and below, except that copper conductors are included for the chiller and fire pump. This clarification establishes the basis of pricing and is not intended to transfer any design, code, or performance responsibility to the Owner. The Design-Builder remains responsible for final conductor selection, sizing, ampacity, terminations, compatibility, installation, and compliance with all applicable codes, the requirements of the Authority Having Jurisdiction, equipment manufacturer requirements, and the requirements necessary for a complete and properly functioning system. If aluminum conductors are not permitted or are otherwise unsuitable for a particular application based upon the foregoing requirements, the Design-Builder shall provide the appropriate compliant conductor material and sizing without additional cost to the Owner, except to the extent such change results from an Owner-directed change in scope occurring after execution of this Amendment.

Burglar Alarm / CCTV / Access Control
Contractor Excludes

1. Excludes any monthly fees for system training, customer support, disposable parts replacement, emergency service requests unless noted otherwise.

Audio Visual Systems


Contractor Includes low voltage work outlined in AVI SPL's proposal numbers 480701-10 and 516619-2, both dated 7/1/2026 which proposal is incorporated herein by reference

END OF CONTRACTOR CLARIFICATIONS

Exhibit D

Construction Schedule

#	Activity ID	Activity Name	Original Duration	Start	Finish
1	**Greenacres Municipal Operations Center 04Aug2026**		506	23-Mar-26 A	15-Mar-28
2	**Owner Preconstruction :**		174	23-Mar-26 A	13-Sep-26
3	01-VALU-0001	VE'd GMP Prepared / Submitted to Owner	58	23-Mar-26 A	19-May-26 A
4	014-PERM-0003	Permitting - Building Dept Plan Review	49	23-Mar-26 A	11-Sep-26
5	010-VEGM-0301	VE'd GMP City Review / Approval	0	05-Aug-26*	05-Aug-26
6	010-KLAU-2	City Council Approval	0	17-Aug-26*	
7	010-KLAU-0002	KL Authorizes Early Buy-out (Cal Days)	0	13-Sep-26	
8	DOC	Date of Commencement	0	13-Sep-26	
9	**Milestones :**		624	13-May-26 A	15-Mar-28
10	**Owner Milestones**		624	13-May-26 A	15-Mar-28
11	FCO-Cont10	Land Permit / Clearing & Grubbing Permit	0		13-May-26 A
12	NTP	NTP - Owner (Cal Days)	0	12-Sep-26*	
13	SCO-Cont	Contract Substantial Comp-REQ	0		14-Feb-28
14	FCO-Cont	Contract Final Comp-REQ	0		15-Mar-28*
15	**Project Actual Current Tracking (ACT)**		551	12-Sep-26	15-Mar-28
16	NTP-TCO-001	Notice to Proceed to Achievement of Temporary Certificate of Occupancy	491	12-Sep-26	15-Jan-28
17	NTP-SCO-020	Notice to Proceed to Achievement of Substantial Completion	521	12-Sep-26	14-Feb-28
18	NTP-FCO-010	Notice to Proceed to Achievement of Final Completion	551	12-Sep-26	15-Mar-28
19	TCO	Temp Cert of Occupancy (Cal Days)	0		15-Jan-28
20	SCO-Act	ACT Substantial Comp (Cal Days)	0		14-Feb-28
21	FCO-Act	ACT Final Comp (Cal Days)	0		15-Mar-28
22	**Project Milestones**		521	12-Sep-26	14-Feb-28
23	**Building**		521	12-Sep-26	14-Feb-28
24	MS-STAR-282	Permit Bldg	0	12-Sep-26	
25	MS-STAR-292	Mobilization	0	13-Sep-26	
26	MS-STAR-0005	Start Foundations - Bldg	0	07-Dec-26	
27	Ms-STAR-0282	Start Tilt Wall Erection - Bldg	0	11-May-27	
28	Ms-TOPO-0283	Top Out - Bldg	0		21-May-27
29	Ms-WATE-0289	Water Meter Conveyance - Bldg	0		21-May-27
30	Ms-DRYR-0285	Dry-in Roof - Bldg	0		17-Jun-27
31	Ms-EXTE-0284	Exterior Envelope Dry-in - Bldg	0		09-Jul-27
32	MS-STAR-302	MEP Rough In Completion - Bldg	0		13-Aug-27
33	Ms-TEMP-0286	Temp for Test Insp Passed - Bldg	0		23-Aug-27
34	Ms-PERM-297	Generator Commissioning - Bldg	0	31-Aug-27	
35	Ms-PERM-0287	Permanent Power to Bldg - Bldg	0		14-Oct-27
36	Ms-HVAC-0288	HVAC start-up - Bldg	0		19-Oct-27
37	Ms-PERM-287	Chiller Commissioning - Bldg	0	20-Oct-27	
38	Ms-PERM-317	Elevator Start Up & State Approval - Bldg	0	28-Oct-27	
39	Ms-PERM-307	Training Commencement - Bldg	0	31-Oct-27	
40	Ms-HVAC-288	TCO - Bldg	0		14-Jan-28
41	Ms-ACTS-0376	ACT Substantial Comp (Cal Days) - Bldg	0		14-Feb-28
42	**Procurement :**		245	13-Sep-26	27-Aug-27
43	**Award Subcontracts**		10	14-Sep-26	25-Sep-26
44	211-SPRI-0008	Fire Sprinkler - Subcontract Award	10	14-Sep-26	25-Sep-26
45	08-SUBC-0009	Hollow Metal Frames / Doors - Subcontract Award	10	14-Sep-26	25-Sep-26
46	093-FLOO-0010	Flooring / Tile - Subcontract Award	10	14-Sep-26	25-Sep-26

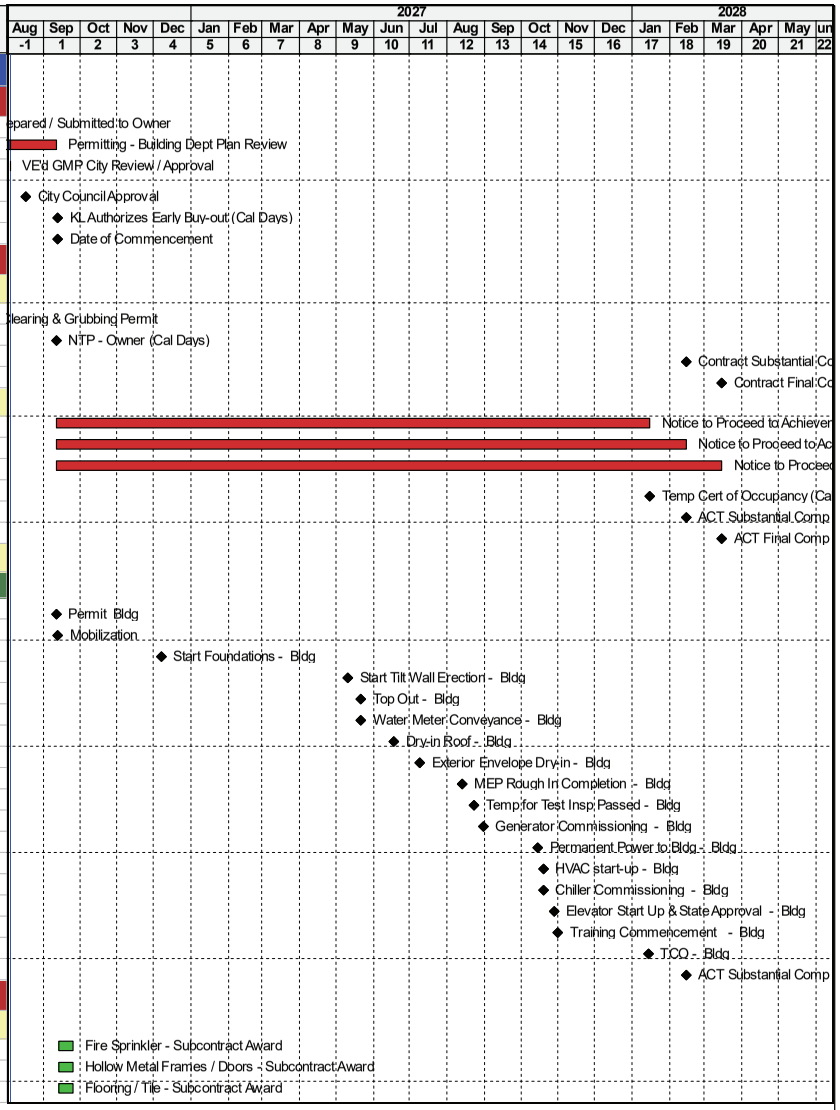


Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26
Page 1 of 30
2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
47	08-SUBC-0011	Windows / Storefronts / Glazing - Subcontract Award	10	14-Sep-26	25-Sep-26
48	06-SUBC-0012	Finish Carp / Wood Doors & Hdwr - Subcontract Award	10	14-Sep-26	25-Sep-26
49	32-LAND-0013	Landscape & Irrigation	10	14-Sep-26	25-Sep-26
50	09-SUBC-0014	Acoustical Ceilings - Subcontract Award	10	14-Sep-26	25-Sep-26
51	10-SUBC-0015	Div 10 - Subcontract Award	10	14-Sep-26	25-Sep-26
52	10-SUBC-0016	Signage - Subcontract Award	10	14-Sep-26	25-Sep-26
53	07-SUBC-0290	Roofing - Subcontract Award	10	14-Sep-26	25-Sep-26
54	051-STEE-0291	Structural Steel / Joists - Subcontract Award	10	14-Sep-26	25-Sep-26
55	02-SUBC-0292	Surveying - Subcontract Award	5	14-Sep-26	18-Sep-26
56	26-SUBC-0293	Electrical - Subcontract Award	10	14-Sep-26	25-Sep-26
57	01-SUBC-0294	Conc / Tilt-up / Masonry - Subcontract Award	5	14-Sep-26	18-Sep-26
58	23-SUBC-0295	HVAC - Subcontract Award	10	14-Sep-26	25-Sep-26
59	09-SUBC-0296	Painting - Subcontract Award	10	14-Sep-26	25-Sep-26
60	09-SUBC-0297	Drywall & Metal Framing - Subcontract Award	10	14-Sep-26	25-Sep-26
61	22-SUBC-0298	Plumbing - Subcontract Award	10	14-Sep-26	25-Sep-26
62	32-SUBC-0299	Civil / Site / Paving - Subcontract Award	10	14-Sep-26	25-Sep-26
63	06-SUBC-0300	Millwork / Countertops - Subcontract Award	10	14-Sep-26	25-Sep-26
64	071-WATE-0388	Waterproofing - Subcontract Award	10	14-Sep-26	25-Sep-26
65	010-FENC-0440	Fencing / Gates - Subcontract Award	10	14-Sep-26	25-Sep-26
66	010-FITN-0470	Fitness Equipment - Subcontract Award	10	14-Sep-26	25-Sep-26
67	14-SUBC-1090	Automative Lfits - Subcontract Award	10	14-Sep-26	25-Sep-26
68	211-SPRI-1110	Fire Training Complex - Subcontract Award	10	14-Sep-26	25-Sep-26
69	**Prep & Submit Submittal Packages**		50	14-Sep-26	20-Nov-26
70	013-ELEV-0384	Elevator - Submittal Package	10	14-Sep-26	25-Sep-26
71	03-TUDE-0010	Tilt-Up Panel Delegated Engineer — Submit Signed/Sealed Fabrication & Erection Drawings	9	18-Sep-26	01-Oct-26
72	01-SUBM-0018	Tilt-Up Concrete - Submittal Package	20	21-Sep-26	16-Oct-26
73	03-SUBM-0019	Concrete & Masonry - Submittal Package	10	21-Sep-26	02-Oct-26
74	013-PREC-0380	Precast Stairs - Submittal Package	10	23-Sep-26	06-Oct-26
75	051-STEE-0017	Structural Steel (Anchor Bolts & Embeds) - Submittal Package	15	28-Sep-26	16-Oct-26
76	09-SUBM-0020	Drywall - Submittal Package	10	28-Sep-26	09-Oct-26
77	32-SUBM-0021	Paving - Submittal Package	10	28-Sep-26	09-Oct-26
78	09-SUBM-0022	Lt Ga Metal Framing - Submittal Package	10	28-Sep-26	09-Oct-26
79	01-SUBM-0023	Site Structures - Submittal Package	20	28-Sep-26	23-Oct-26
80	093-FLOO-0024	Flooring / Tile - Submittal Package	20	28-Sep-26	23-Oct-26
81	07-SUBM-0025	Roofing & LWIC - Submittal Package	20	28-Sep-26	23-Oct-26
82	07-SUBM-0026	Waterproofing - Submittal Package	10	28-Sep-26	09-Oct-26
83	26-SUBM-0027	Electrical (Panels/Disconects) - Submittal Package	20	28-Sep-26	23-Oct-26
84	07-SUBM-0028	Wall Insulation - Submittal Package	10	28-Sep-26	09-Oct-26
85	23-SUBM-0029	HVAC AHUs - Submittal Package	20	28-Sep-26	23-Oct-26
86	09-SUBM-0030	Painting - Submittal Package	20	28-Sep-26	23-Oct-26
87	22-SUBM-0031	Plumbing - Submittal Package	20	28-Sep-26	23-Oct-26
88	08-SUBM-0032	H.M.Frames / Drs - Submittal Package	10	28-Sep-26	09-Oct-26
89	08-SUBM-0033	Doors & Hdwr - Submittal Package	20	28-Sep-26	23-Oct-26
90	06-WORK-0034	Countertops	20	28-Sep-26	23-Oct-26
91	06-SUBM-0035	Millwork - Submittal Package	20	28-Sep-26	23-Oct-26
92	211-SPRI-0036	Fire Sprinkler - Submittal Package	20	28-Sep-26	23-Oct-26
93	01-SUBM-0037	Wall & Corner Guards - Submittal Package	2	28-Sep-26	29-Sep-26
94	09-SUBM-0038	Acoustical Ceilings - Submittal Package	10	28-Sep-26	09-Oct-26

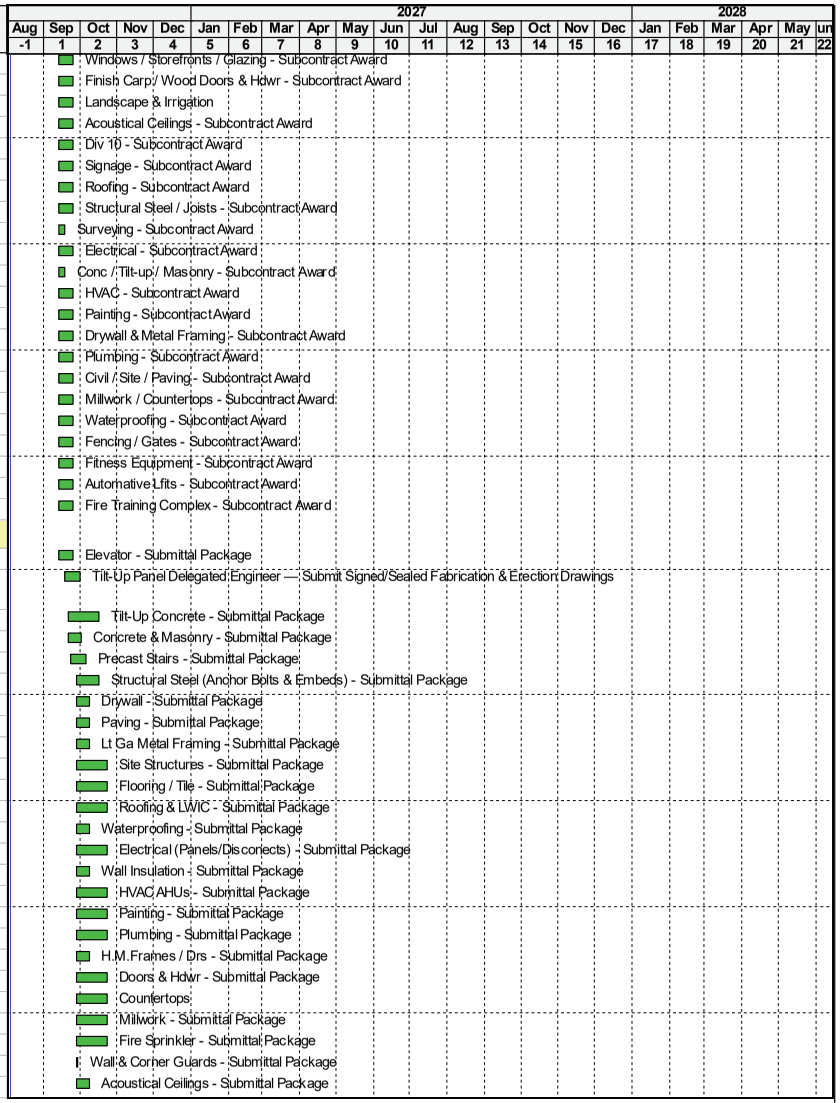

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
95	22-SUBM-0039	Toilet Acc - Submittal Package	10	28-Sep-26	09-Oct-26
96	21-SUBM-0040	FIre Ext Cabinets - FECs - Submittal Package	10	28-Sep-26	09-Oct-26
97	08-SUBM-0041	Windows / Storefronts / Glazing - Submittal Package	20	28-Sep-26	23-Oct-26
98	32-SUBM-0042	Irrigation - Submittal Package	20	28-Sep-26	23-Oct-26
99	10-SUBM-0043	Signage - Submittal Package	20	28-Sep-26	23-Oct-26
100	01-SUBM-0389	Roll-up Doors - Submittal Package	10	28-Sep-26	09-Oct-26
101	013-HVAC-0410	HVAC Duct - Submittal Package	20	28-Sep-26	23-Oct-26
102	23-SUBM-0410	HVAC Duct - Submittal Package	20	28-Sep-26	23-Oct-26
103	23-SUBM-0411	HVAC CU's & AHU/CU - Submittal Package	20	28-Sep-26	23-Oct-26
104	236-HVAC-0413	HVAC Chiller Pumps - Submittal Package	20	28-Sep-26	23-Oct-26
105	262-ELEC-0420	Electrical Switchgear - Submittal Package	10	28-Sep-26	09-Oct-26
106	26-SUBM-0421	Electrical Em Generator - Submittal Package	20	28-Sep-26	23-Oct-26
107	263-ELEC-0424	Electrical Em Generator (Missile Impact) - Submittal Package	20	28-Sep-26	23-Oct-26
108	265-ELEC-0425	Electrical (Lighting) - Submittal Package	20	28-Sep-26	23-Oct-26
109	262-ELEC-0426	Electrical F/A NES Panel - Submittal Package	20	28-Sep-26	23-Oct-26
110	051-STEE-0432	Structural Steel (Misc Metals) - Submittal Package	30	28-Sep-26	06-Nov-26
111	051-STEE-0433	Structural Steel (Joist & Deck) - Submittal Package	10	28-Sep-26	09-Oct-26
112	013-SITE-0459	Site Utilities (Pipe, Valves etc) - Submittal Package	20	28-Sep-26	23-Oct-26
113	010-FITN-384	Fitness Equipment -- Submittal Package	10	28-Sep-26	09-Oct-26
114	26-SUBM-428	Electrical BDA - Submittal Package	10	28-Sep-26	09-Oct-26
115	14-ALIFT-384	Automotive Lifts - Submittal Package	10	28-Sep-26	09-Oct-26
116	211-SPRI-1120	Fire Training Complex- Submittal Package	10	28-Sep-26	09-Oct-26
117	01-SUBM-0380	Precast Stairs - Submittal Package	10	07-Oct-26	20-Oct-26
118	26-SUBM-0426	Electrical F/A NES Panel - Submittal Package	10	12-Oct-26	23-Oct-26
119	013-WOOD-0393	Wood Doors - Submittal Package	10	26-Oct-26	06-Nov-26
120	01-SUBM-0459	Site Utilities (Pipe, Valves etc) - Submittal Package	20	26-Oct-26	20-Nov-26
121	06-SUBM-0393	Wood Doors - Submittal Package	10	09-Nov-26	20-Nov-26
122	**A/E Review & Approve Submittal Packages**		50	28-Sep-26	07-Dec-26
123	23-SUBM-0408	HVAC Chiller Pumps - Submittal Package A/E R&A	15	28-Sep-26	16-Oct-26
124	01-SUBM-0438	Fencing / Gate(s) - Submittal Package A/E R&A	10	28-Sep-26	09-Oct-26
125	14-ELEC-430	Elevator - Submittal Package A/E R&A	20	28-Sep-26	23-Oct-26
126	01-SUBM-0064	Wall & Corner Guards - Submittal Package A/E R&A	10	30-Sep-26	13-Oct-26
127	03-TUAE-0010	Tilt-Up Panel Delegated Engineer Drawings — SER Review & Approval	10	01-Oct-26	15-Oct-26
128	03-SUBM-0044	Concrete & Masonry - Submittal Package A/E R&A	10	12-Oct-26	23-Oct-26
129	32-SUBM-0045	Paving - Submittal Package A/E R&A	10	12-Oct-26	23-Oct-26
130	07-SUBM-0048	Waterproofing - Submittal Package A/E R&A	10	12-Oct-26	23-Oct-26
131	09-SUBM-0053	Drywall - Submittal Package A/E R&A	10	12-Oct-26	23-Oct-26
132	09-SUBM-0054	Lt Ga Metal Framing - Submittal Package A/E R&A	10	12-Oct-26	23-Oct-26
133	08-SUBM-0057	H.M.Frames / Drs - Submittal Package A/E R&A	10	12-Oct-26	23-Oct-26
134	07-SUBM-0062	Wall Insulation - Submittal Package A/E R&A	10	12-Oct-26	23-Oct-26
135	22-SUBM-0063	Toilet Acc - Submittal Package A/E R&A	10	12-Oct-26	23-Oct-26
136	09-SUBM-0065	Acoustical Ceilings - Submittal Package A/E R&A	13	12-Oct-26	28-Oct-26
137	21-SUBM-0066	FIre Ext Cabinets - FECs- Submittal Package A/E R&A	10	12-Oct-26	23-Oct-26
138	01-SUBM-0390	Roll-up Doors - Submittal Package A/E R&A	10	12-Oct-26	23-Oct-26
139	051-STEE-0435	Structural Steel (Joist & Deck) - Submittal Package A/E R&A	10	12-Oct-26	23-Oct-26
140	013-FENC-0438	Fencing / Gate(s) - Submittal Package A/E R&A	10	12-Oct-26	23-Oct-26
141	10-FITN-411	Fitness Equipment- Submittal Package A/E R&A	15	12-Oct-26	30-Oct-26
142	14-ALIFT-440	Automotive Lifts - Submittal Package A/E R&A	20	12-Oct-26	06-Nov-26
143	211-SPRI-1130	Fire Training Complex - Submittal Package A/E R&A	10	12-Oct-26	23-Oct-26

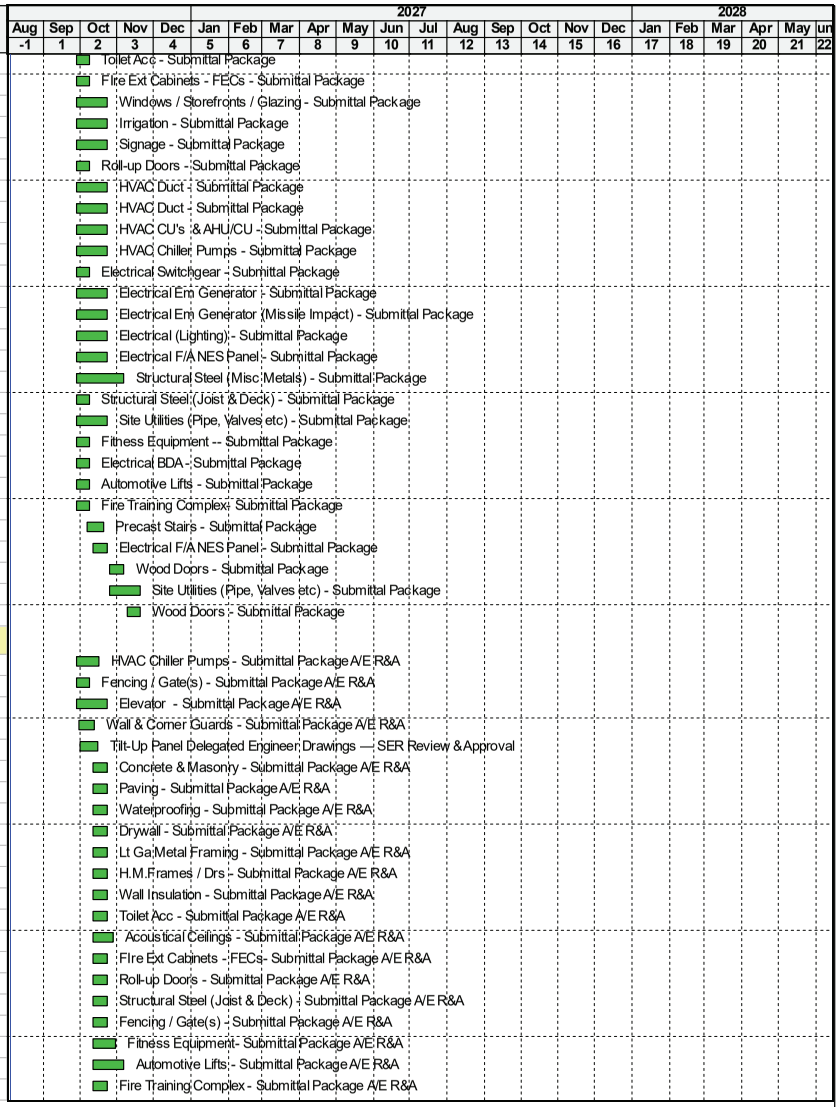

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
144	01-SUBM-0049	Tilt-Up Concrete - Submittal Package A/E R&A	10	19-Oct-26	30-Oct-26
145	051-STEE-0051	Structural Steel (Anchor Bolts & Embeds) - Submittal Package A/E R&A (*Only Embeds Pending)	10	19-Oct-26	30-Oct-26
146	236-HVAC-0404	HVAC Chillers - Submittal Package A/E R&A	15	19-Oct-26	06-Nov-26
147	093-FLOO-0046	Flooring / Tile - Submittal Package A/E R&A	20	26-Oct-26	20-Nov-26
148	07-SUBM-0047	Roofing & LWIC - Submittal Package A/E R&A	20	26-Oct-26	20-Nov-26
149	26-ELEC-0050	Electrical (Panels/Disconects) - Submittal Package A/E R&A	10	26-Oct-26	06-Nov-26
150	09-SUBM-0052	Painting - Submittal Package A/E R&A	20	26-Oct-26	20-Nov-26
151	22-SUBM-0055	Plumbing - Submittal Package A/E R&A	20	26-Oct-26	20-Nov-26
152	01-SUBM-0056	Site Structures - Submittal Package A/E R&A	10	26-Oct-26	06-Nov-26
153	08-SUBM-0058	Doors & Hdwr - Submittal Package A/E R&A (*Only Level E Doors Pending)	20	26-Oct-26	20-Nov-26
154	23-SUBM-0059	HVAC AHUs - Submittal Package A/E R&A	15	26-Oct-26	13-Nov-26
155	06-SUBM-0060	Countertops - Submittal Package A/E R&A	20	26-Oct-26	20-Nov-26
156	06-SUBM-0061	Millwork - Submittal Package A/E R&A	20	26-Oct-26	20-Nov-26
157	10-SUBM-0067	Signage - Submittal Package A/E R&A	20	26-Oct-26	20-Nov-26
158	08-SUBM-0068	Windows / Storefronts / Glazing - Submittal Package A/E R&A	10	26-Oct-26	06-Nov-26
159	32-LAND-0069	Landscape & Irrigation	30	26-Oct-26	07-Dec-26
160	211-SPRI-0070	Fire Sprinkler - Submittal Package A/E R&A	15	26-Oct-26	13-Nov-26
161	013-HVAC-0405	HVAC Duct - Submittal Package A/E R&A	15	26-Oct-26	13-Nov-26
162	23-SUBM-0405	HVAC Duct - Submittal Package A/E R&A	15	26-Oct-26	13-Nov-26
163	23-SUBM-0406	HVAC CU's & AHU/CU - Submittal Package A/E R&A	15	26-Oct-26	13-Nov-26
164	236-HVAC-0408	HVAC Chiller Pumps - Submittal Package A/E R&A	15	26-Oct-26	13-Nov-26
165	263-ELEC-0428	Electrical Em Generator - Submittal Package A/E R&A	10	26-Oct-26	06-Nov-26
166	265-ELEC-0430	Electrical (Lighting) - Submittal Package A/E R&A	20	26-Oct-26	20-Nov-26
167	262-ELEC-0431	Electrical F/A NES Panel - Submittal Package A/E R&A	20	26-Oct-26	20-Nov-26
168	051-STEE-0434	Structural Steel (Misc Metals) - Submittal Package A/E R&A	15	09-Nov-26	30-Nov-26
169	**Fabricate & Deliver (c/d)**		349	13-Sep-26	27-Aug-27
170	01-WORK-0097	Site Furnishings - F&D	20	13-Sep-26	02-Oct-26
171	01-WORK-0382	Precast Stairs - F&D	10	13-Sep-26	22-Sep-26
172	08-FNSH-0096	Finish Hardware - F&D	35	26-Sep-26	30-Oct-26
173	26-WORK-0081	Electrical Switchgear - F&D - 36wks	252	10-Oct-26	18-Jun-27
174	27-ELEC-708	Electrical BDA - F&D	50	10-Oct-26	28-Nov-26
175	01-WORK-0089	Wall & Corner Guards - F&D	35	14-Oct-26	17-Nov-26
176	010-PREC-0382	Precast Stairs - F&D	10	21-Oct-26	30-Oct-26
177	03-WORK-0072	Concrete & Masonry Materials - F&D	10	24-Oct-26	02-Nov-26
178	07-WORK-0075	Waterproofing Materials - F&D	5	24-Oct-26	28-Oct-26
179	01-WORK-0077	Exterior Metal Cladding System - F&D	25	24-Oct-26	17-Nov-26
180	09-WORK-0078	Drywall Materials - F&D	10	24-Oct-26	02-Nov-26
181	09-WORK-0079	Light-Gage Metal Framing - F&D	10	24-Oct-26	02-Nov-26
182	22-WORK-0095	Toilet Acc / Compartments - F&D	10	24-Oct-26	02-Nov-26
183	104-EXTI-0100	Fire Extinguishers & Cabinets - F&D	10	24-Oct-26	02-Nov-26
184	07-WORK-0103	Wall Insulation Materials - F&D	30	24-Oct-26	22-Nov-26
185	01-WORK-0107	Fencing / Gate(s) - F&D	56	24-Oct-26	18-Dec-26
186	14-ELEV-0386	Elevator - F&D	140	24-Oct-26	12-Mar-27
187	08-WORK-0391	Roll-up Doors - F&D	5	24-Oct-26	28-Oct-26
188	051-STEE-0437	Structural Steel (Joist & Deck) - F&D	40	24-Oct-26	02-Dec-26
189	21-ELEC-718	Electrical Fire Alarm Panel /NAC Panels - F&D - 6 wks	50	24-Oct-26	12-Dec-26
190	211-SPRI-1140	Fire Training Complex - F&D - (8 Months)	240	24-Oct-26	20-Jun-27
191	09-WORK-0099	Acoustical Ceilings - F&D	10	29-Oct-26	07-Nov-26

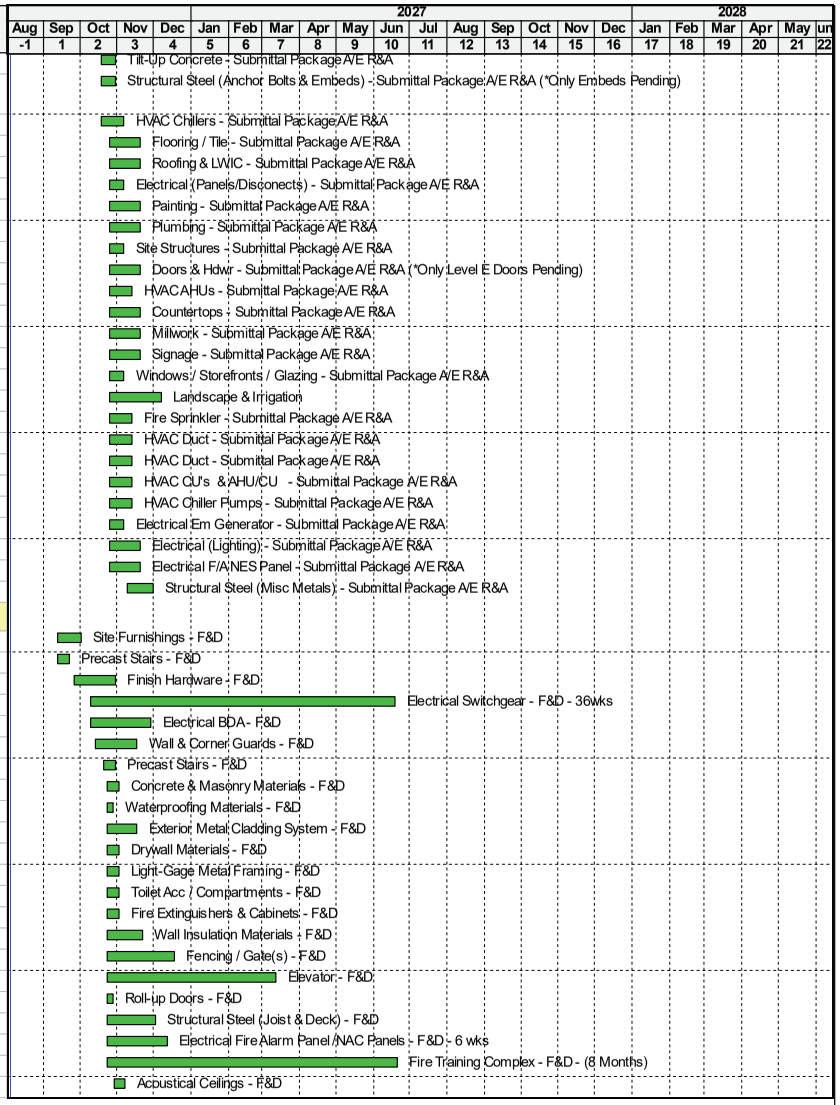

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
192	03-WORK-0076	Tilt-Up Concrete Materials - F&D	7	31-Oct-26	06-Nov-26
193	051-STEE-0087	Structural Steel (Anchor Bolts & Embeds) - F&D	10	31-Oct-26	09-Nov-26
194	10-FITN-382	Fitness Equipment - F&D	90	31-Oct-26	28-Jan-27
195	26-WORK-0071	Electrical Em Generator - F&D - 38 Wks	266	07-Nov-26	30-Jul-27
196	26-WORK-0073	Electrical Equip (Panels/Disconects) - F&D - 12wks	84	07-Nov-26	29-Jan-27
197	01-WORK-0080	Site Structures - F&D	20	07-Nov-26	26-Nov-26
198	23-WORK-0093	HVAC Chillers - F&D - 20 Wks	140	07-Nov-26	26-Mar-27
199	08-WORK-0101	Window / Storefront Glazing - F&D	45	07-Nov-26	21-Dec-26
200	26-WORK-382	Generator ATS - F&D - 42 wks	294	07-Nov-26	27-Aug-27
201	26-WORK-392	Electrical Transformers - F&D - 12wks	84	07-Nov-26	29-Jan-27
202	14-ALift-386	Automative Lifts - F&D	95	07-Nov-26	09-Feb-27
203	23-WORK-0090	HVAC Duct - F&D	40	14-Nov-26	23-Dec-26
204	23-WORK-0094	HVAC AHUs - F&D	175	14-Nov-26	07-May-27
205	211-SPRI-0105	Fire Sprinkler Equip - F&D	20	14-Nov-26	03-Dec-26
206	237-HVAC-0414	HVAC AHU & CU's Splits - F&D	110	14-Nov-26	03-Mar-27
207	233-HVAC-0415	HVAC VAV's - F&D	75	14-Nov-26	27-Jan-27
208	236-HVAC-0419	HVAC Chiller Pumps - F&D	100	14-Nov-26	21-Feb-27
209	09-WORK-0082	Ceramic Tile / Carpet Tile / Vinyl Flooring & Trim - F&D	20	21-Nov-26	10-Dec-26
210	07-WORK-0083	Roofing Insulation - F&D	15	21-Nov-26	05-Dec-26
211	08-WORK-0084	Hollow Metal Frames - F&D	30	21-Nov-26	20-Dec-26
212	09-WORK-0085	Accent Tile - F&D	20	21-Nov-26	10-Dec-26
213	07-WORK-0086	Roofing & LWIC Materials - F&D	20	21-Nov-26	10-Dec-26
214	08-WORK-0088	Hollow Metal Doors - F&D	50	21-Nov-26	09-Jan-27
215	09-WORK-0091	Painting Materials - F&D	20	21-Nov-26	10-Dec-26
216	22-WORK-0092	Plumbing Fixtures & Equip - F&D	20	21-Nov-26	10-Dec-26
217	06-WORK-0098	Millwork Materials - F&D	20	21-Nov-26	10-Dec-26
218	10-WORK-0104	Signage Materials - F&D	20	21-Nov-26	10-Dec-26
219	06-WORK-0106	Countertops - F&D	15	21-Nov-26	05-Dec-26
220	081-WOOD-0395	Wood Doors / Frames- F&D	90	21-Nov-26	18-Feb-27
221	265-ELEC-0396	Electrical Equip (Lighting) - F&D - 12wks	84	21-Nov-26	12-Feb-27
222	262-ELEC-0423	Electrical F/A NES Panel - F&D	150	21-Nov-26	19-Apr-27
223	010-SITE-0461	Site Utilities (Pipe, Valves etc) - F&D	20	21-Nov-26	10-Dec-26
224	051-STEE-0436	Structural Steel (Misc Metals) - F&D	20	01-Dec-26	20-Dec-26
225	32-LAND-0102	Landscape & Irrigation Materials - F&D	20	08-Dec-26	27-Dec-26
226	32-WORK-0074	Paving Materials - F&D	10	25-Jan-27	03-Feb-27
227	**Sitework :**		312	15-Jun-26 A	21-Sep-27
228	**Site Clearing**		58	14-Sep-26	03-Dec-26
229	01-MOBL-0109	Mobilize Site -	2	14-Sep-26	15-Sep-26
230	02-DEMO-0110	Site Demolition	10	14-Sep-26	25-Sep-26
231	010-CALL-0377	Call Sunshine -	2	14-Sep-26	15-Sep-26
232	010-SITE-0458	Site Clearing	10	16-Sep-26	29-Sep-26
233	02-DEMO-110	Tree Removal / Site Disposal	10	16-Sep-26	29-Sep-26
234	02-WORK-0108	Survey Boundary	2	21-Sep-26	22-Sep-26
235	010-CALL-377	Site Logistics - Fencing , Boundaries , Entrance	10	30-Sep-26	13-Oct-26
236	31-GRAD-0111	Site Grading / Fill	10	14-Oct-26	27-Oct-26
237	01-WORK-0112	Building Pad	8	23-Nov-26	03-Dec-26
238	**Utilities**		176	28-Sep-26	04-Jun-27
239	**New Concrete Parking**		24	28-Sep-26	29-Oct-26

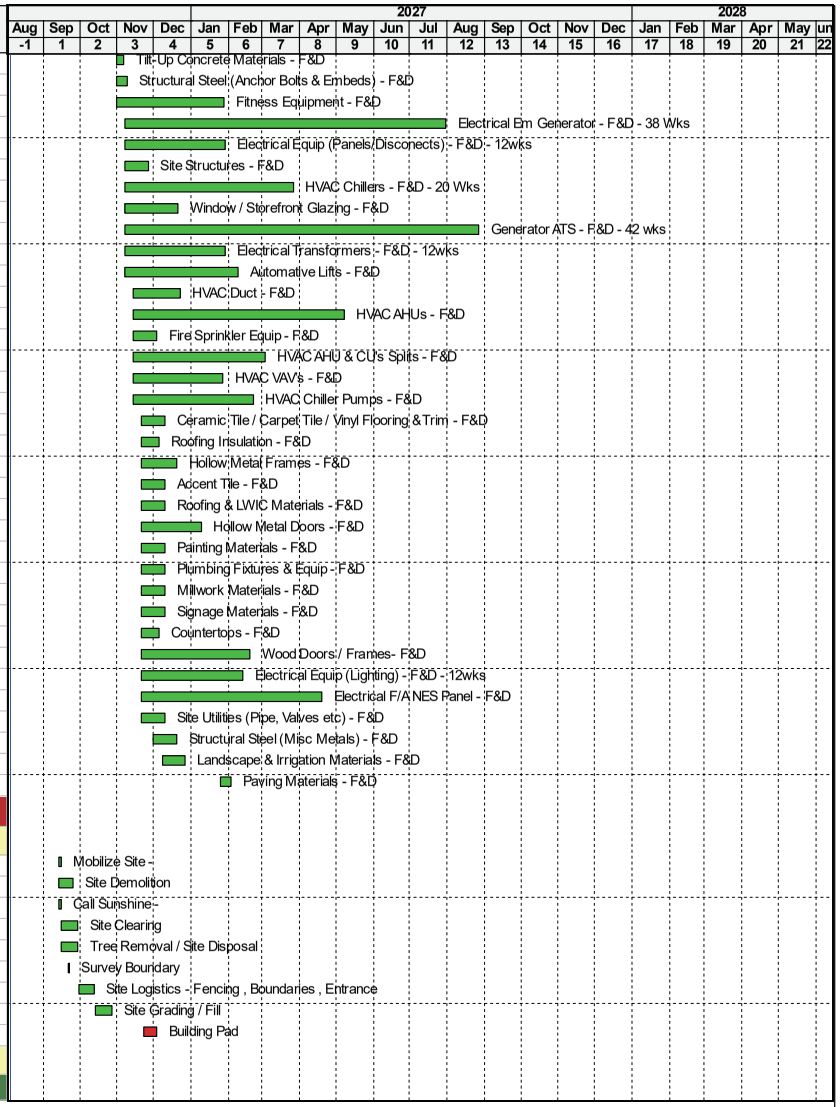

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
240	31-CONP-0101	S-13 to 14 HDPE 15"	5	28-Sep-26	02-Oct-26
241	31-CONP-101	Fill & Compaction New Concrete Paving Area	7	05-Oct-26	13-Oct-26
242	31-CONP-111	Curbs and Drainage	5	14-Oct-26	20-Oct-26
243	31-CONP-121	1st Lift of Parking Area	7	21-Oct-26	29-Oct-26
244	**South Sanitary Sewer System**		64	12-Jan-27	09-Apr-27
245	22-WORK-0355	Sanitary Sewer Laterals - South Sewer	2	12-Jan-27	13-Jan-27
246	22-WORK-0114	Sanitary Sewer - South Sewer	5	26-Mar-27	01-Apr-27
247	22-WORK-0354	Sanitary Sewer - South Sewer	2	02-Apr-27	05-Apr-27
248	333-MOTS-0353	MOT Sanitary Sewer Tie-in - South Sewer	2	06-Apr-27	07-Apr-27
249	333-SANI-0354	Sanitary Sewer - South Sewer	2	08-Apr-27	09-Apr-27
250	**Sanitary Sewer System**		6	14-Jan-27	21-Jan-27
251	**North Sanitary Sewer System**		6	14-Jan-27	21-Jan-27
252	22-WORK-0358	Sanitary Sewer - North Sewer	2	14-Jan-27	15-Jan-27
253	333-MOTS-0357	MOT Sanitary Sewer Tie-in - North Sewer	2	18-Jan-27	19-Jan-27
254	333-SANI-0358	Sanitary Sewer - North Sewer	2	20-Jan-27	21-Jan-27
255	**Drainage Sewer System**		33	04-Dec-26	22-Jan-27
256	**North Drainage Sewer System**		24	04-Dec-26	11-Jan-27
257	010-DRYD-0515	S-1 Connect to Dry Detention	4	04-Dec-26	09-Dec-26
258	010-S1XX-0516	S-1 to S-2	4	10-Dec-26	15-Dec-26
259	010-S2XX-0517	S-2 to S-3 / S-2 to S-4	4	16-Dec-26	21-Dec-26
260	010-S4XX-0518	S-4 to S-6 / S-4 to S-5	4	22-Dec-26	29-Dec-26
261	010-RWLN-0519	RWL North East Elevations	4	30-Dec-26	05-Jan-27
262	010-LAKE-0520	Connect S-6 to Existing Lake	4	06-Jan-27	11-Jan-27
263	**South Drainage Sewer System**		20	11-Dec-26	12-Jan-27
264	01-WORK-0115	S-10 to S-9	4	11-Dec-26	16-Dec-26
265	010-11XX-0323	S-8 to S-11	4	17-Dec-26	22-Dec-26
266	010-S7XX-0324	S-8 to S7	4	23-Dec-26	30-Dec-26
267	010-RWLE-0325	RWL System (East Building)	4	31-Dec-26	06-Jan-27
268	010-11LA-0378	S-11 to Lake	4	07-Jan-27	12-Jan-27
269	**West Drainage Sewer System**		8	13-Jan-27	22-Jan-27
270	010-RWLW-0513	RWL West Elevations	4	13-Jan-27	18-Jan-27
271	010-STOM-0514	Connect to Existing Stom Structure	4	19-Jan-27	22-Jan-27
272	**Dom / Fire Water System**		12	22-Jan-27	08-Feb-27
273	**Dom / Fire Water System**		12	22-Jan-27	08-Feb-27
274	01-WORK-0113	MOT DW Set-up - D/F Water	2	22-Jan-27	25-Jan-27
275	010-HYDR-0326	Fire Hydrant Relocate / FDC Install - D/F Water	2	26-Jan-27	27-Jan-27
276	221-MAIN-0327	Fire Main Tap to Backflow - D/F Water	2	28-Jan-27	29-Jan-27
277	221-DOME-0328	Domestic Main Tap to Backflow - D/F Water	2	01-Feb-27	02-Feb-27
278	010-WATE-0334	Fire Water Flush / Pressure Test - D/F Water	2	01-Feb-27	02-Feb-27
279	328-IRRI-0329	Irrigation Main Tap to Backflow - D/F Water	2	03-Feb-27	04-Feb-27
280	221-MAIN-0330	Fire Main Backflow Install - D/F Water	2	03-Feb-27	04-Feb-27
281	221-DOME-0333	Domestic Water Flush / Pressure Test - D/F Water	2	03-Feb-27	04-Feb-27
282	221-DOME-0331	Domestic Main Backflow Install - D/F Water	2	05-Feb-27	08-Feb-27
283	328-IRRI-0332	Irrigation Main Backflow Install - D/F Water	2	05-Feb-27	08-Feb-27
284	**North Dom / Fire Water System**		0		
285	**Utilities Certifications / Easements / Conveyances**		102	13-Jan-27	04-Jun-27
286	**Power Service / Data / Comm - Easements / Conveyances**		10	21-May-27	04-Jun-27

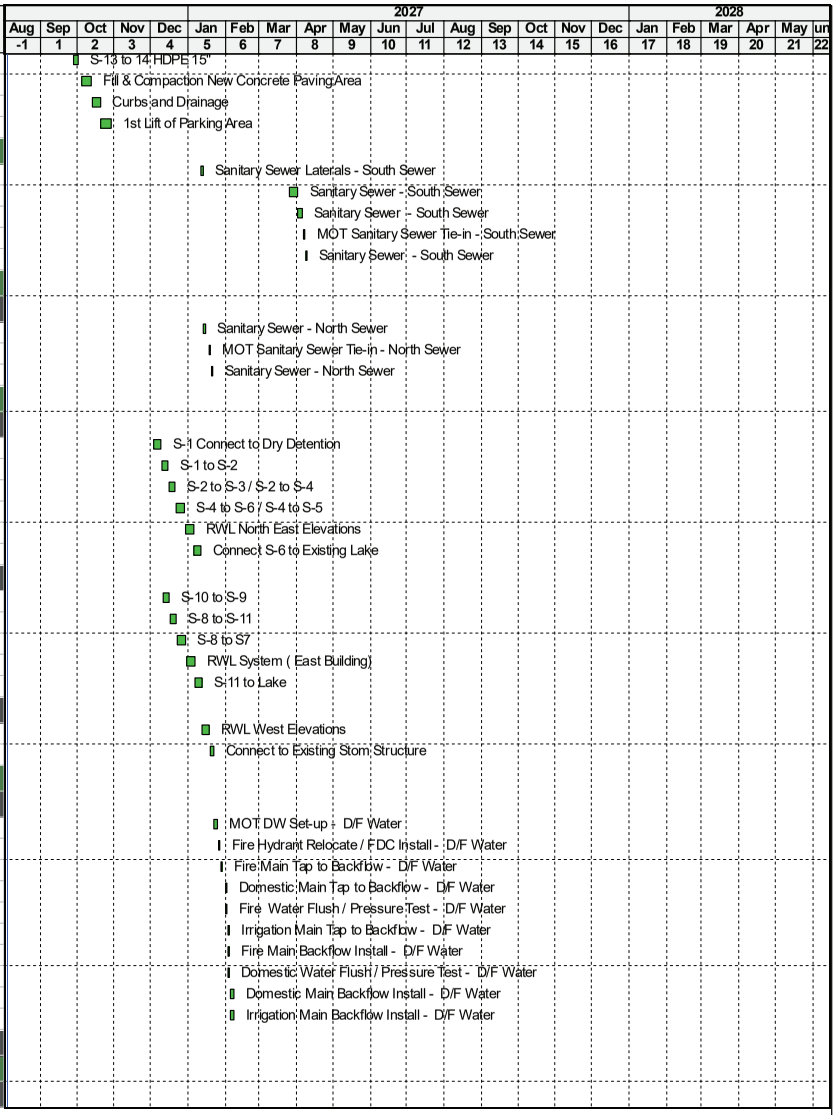

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
287	101-ASBU-0371	Asbuilts Signed / Sealed FPL Primary u/g Rgh-in - Utl's C/C	5	21-May-27	27-May-27
288	10-WORK-0371	Asbuilts Signed / Sealed FPL Primary u/g Rgh-in - Utl's C/C	5	21-May-27	27-May-27
289	010-EORA-0373	EOR Asbuilts FPL Primary Easement / Approval - Utl's C/C	5	28-May-27	04-Jun-27
290	01-APPR-0373	EOR Asbuilts FPL Primary Easement / Approval - Utl's C/C	5	28-May-27	04-Jun-27
291	**Drainage System - Cert's / Easements / Conveyances**		70	13-Jan-27	20-Apr-27
292	221-DRAI-0365	Drainage System Asbuilts - Utl's C/C	5	13-Jan-27	19-Jan-27
293	22-WORK-0365	Drainage System Asbuilts - Utl's C/C	5	20-Jan-27	26-Jan-27
294	22-WORK-0369	Drainage System Asbuilts to PW / Easement Conveyance - Utl's C/C	5	20-Jan-27	26-Jan-27
295	221-DRAI-0368	Drainage System Asbuilts County Approval / Approval - Utl's C/C	30	27-Jan-27	09-Mar-27
296	01-APPR-0368	Drainage System Asbuilts County Approval / Approval - Utl's C/C	30	10-Mar-27	20-Apr-27
297	014-SITE-0478	Site Permit TCO	3	10-Mar-27	12-Mar-27
298	**Water & Sanitary Cert's / Easements / Conveyances**		78	03-Feb-27	21-May-27
299	**Water & Sanitary Cert's / Easements / Conveyances**		78	03-Feb-27	21-May-27
300	331-WATE-0361	Water main tie-in - Utl's C/C	2	03-Feb-27	04-Feb-27
301	010-SAMP-0362	Sample points Install - Utl's C/C	2	09-Feb-27	10-Feb-27
302	014-BACT-0363	Bac-T's Testing / Report - Utl's C/C	5	11-Feb-27	17-Feb-27
303	010-DOMW-0364	Dom Water System Health Dept / Approval - Utl's C/C No Health dep Approval Req.	10	18-Feb-27	03-Mar-27
304	017-SANI-0360	Sanitary / Water as-builts Signed / Sealed / Submit to EOR - Utl's C/C	5	12-Apr-27	16-Apr-27
305	017-SANI-0367	Sanitary / Water as-builts EOR Review / Approval - Utl's C/C	5	19-Apr-27	23-Apr-27
306	017-SANI-0375	Sanitary / Water as-builts Easement Conveyance - Utl's C/C	5	26-Apr-27	30-Apr-27
307	262-WATE-0403	Water Conveyance / Meter DW Set - Utl's C/C	15	03-May-27	21-May-27
308	**Power Service**		295	15-Jun-26 A	26-Aug-27
309	101-FPLD-1097	Discussion / Discovery / FPL Estimate & Design	30	15-Jun-26 A	05-Aug-26
310	101-DESI-1109	Demo of Existing Power Line Poles	10	10-Aug-26*	21-Aug-26
311	101-FPLD-1117	FPL New EOC Transformer Design	20	14-Sep-26	09-Oct-26
312	101-FPLD-1127	Easement & Relocation Existing Transformer & Power Lines	50	14-Sep-26	20-Nov-26
313	101-DESI-1099	Design Approval & relase of Material	90	12-Oct-26	18-Feb-27
314	014-PERM-1098	Permit for Power	60	19-Feb-27	13-May-27
315	01-WORK-0116	FPL Primary u/g Rgh-in - FPL	5	14-May-27	20-May-27
316	27-WORK-0117	Comm / Data u/g Rgh-in - FPL	5	14-May-27	20-May-27
317	01-WORK-0118	FPL Secondary u/g Rgh-in - FPL	4	21-May-27	26-May-27
318	01-INSP-0119	FPL u/g Rgh-in Inspection - FPL	5	27-May-27	03-Jun-27
319	01-WORK-0120	FPL Pad - FPL	5	04-Jun-27	10-Jun-27
320	01-WORK-0121	FPL Easement Asbuilt/ Record- FPL	10	11-Jun-27	24-Jun-27
321	01-WORK-0122	FPL Tx Set- FPL	5	25-Jun-27	01-Jul-27
322	26-WORK-0123	FPL Primary Wire Pull /Terminate - FPL	5	17-Aug-27	23-Aug-27
323	260-FPLM-0124	FPL Set Meter / Energize - FPL	3	24-Aug-27	26-Aug-27
324	**South Power Service / Data / Comm**		0		
325	**North Power Service / Data / Comm**		0		
326	**Paving & Sidewalks**		127	19-Oct-26	19-Apr-27
327	010-SUBG-0336	Subgrade Prep -	10	19-Oct-26	30-Oct-26
328	328-IRRI-0335	Irrigation Sleeves across Road -	5	02-Nov-26	06-Nov-26
329	230-LIME-0337	Limerock Base / Fine Grade -	10	09-Nov-26	20-Nov-26
330	**Asphalt & Sidewalks Parking lot**		74	31-Dec-26	14-Apr-27
331	32-IRRI-0125	Irrigation Sleeves across Road -	4	31-Dec-26	06-Jan-27
332	32-WORK-0126	'F' Curbs -	5	28-Jan-27	03-Feb-27
333	32-WORK-0127	Asphalt First Lift -	8	04-Feb-27	15-Feb-27
334	32-WORK-0128	"D" Curbs -	5	16-Feb-27	22-Feb-27

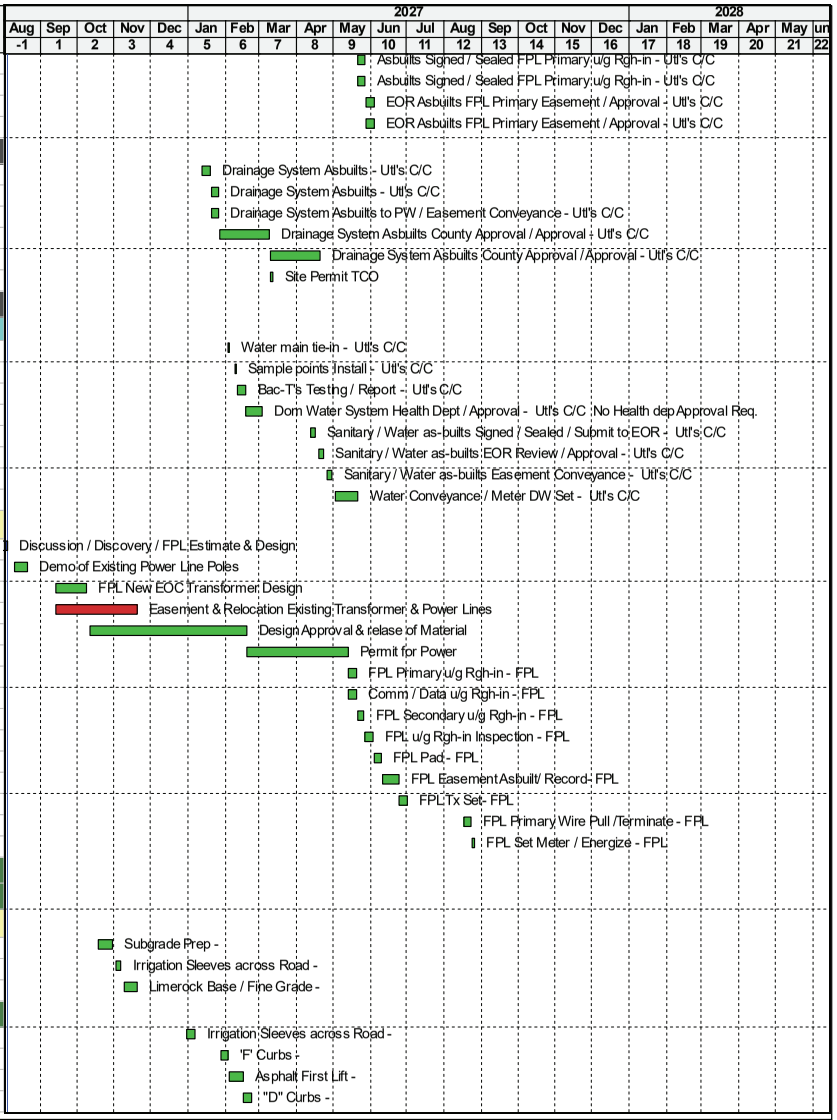


Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26
Page 7 of 30
2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
335	32-WORK-0129	Sidewalk -	8	23-Feb-27	04-Mar-27
336	01-WORK-0130	Fencing / Gates -	8	02-Mar-27	11-Mar-27
337	32-WORK-0131	Asphalt Final Lift -	5	01-Apr-27	07-Apr-27
338	101-STRI-0307	Stripping / Signage -	5	08-Apr-27	14-Apr-27
339	**Boat Ramp**		40	23-Nov-26	21-Jan-27
340	323-TURB-0512	Install Turbidity Curtains & Silt Fence	2	23-Nov-26	24-Nov-26
341	010-COFF-0590	Install Cofferdam/Water Diversion	5	25-Nov-26	02-Dec-26
342	010-DEWA-0591	Dewatering & Muck Out	3	03-Dec-26	07-Dec-26
343	312-EXCA-0592	Excavation & Grade Ramp Prism	5	08-Dec-26	14-Dec-26
344	044-COMP-0593	Place & Compact Stone Bedding	3	15-Dec-26	17-Dec-26
345	032-FORM-0594	Install Forms & Rebar (Upper/Dry)	4	18-Dec-26	23-Dec-26
346	010-FINI-0595	Pour & Finish Concrete	2	28-Dec-26	29-Dec-26
347	010-CONC-0596	Concrete Curing Period	7	30-Dec-26	08-Jan-27
348	010-RIPR-0597	Install Rip-Rap Scour Protection	4	11-Jan-27	14-Jan-27
349	010-BOAR-0598	Install Boarding Dock/Piles	4	11-Jan-27	14-Jan-27
350	010-REMO-0599	Remove Cofferdam & Restoration	3	15-Jan-27	19-Jan-27
351	014-INSP-0600	Final Inspection	2	20-Jan-27	21-Jan-27
352	**Concrete Quad North**		50	04-Feb-27	14-Apr-27
353	321-CURB-0338	'F' Curbs -	5	04-Feb-27	10-Feb-27
354	32-WORK-0338	'F' Curbs -	5	11-Feb-27	17-Feb-27
355	321-SIDE-0340	Sidewalk -	8	18-Feb-27	01-Mar-27
356	031-FORM-0642	Form	1	02-Mar-27	02-Mar-27
357	032-REBA-0643	Rebar	1	03-Mar-27	03-Mar-27
358	014-INSP-0644	Inspection	1	04-Mar-27	04-Mar-27
359	010-POUR-0645	Pour	1	05-Mar-27	05-Mar-27
360	010-FENC-0341	Fencing / Gates -	8	09-Mar-27	18-Mar-27
361	101-STRI-0342	Stripping / Signage -	5	08-Apr-27	14-Apr-27
362	**Concrete Quad South**		35	18-Feb-27	07-Apr-27
363	321-CURB-0646	'F' Curbs -	5	18-Feb-27	24-Feb-27
364	321-CURB-0647	"D" Curbs -	5	25-Feb-27	03-Mar-27
365	321-SIDE-0648	Sidewalk -	8	04-Mar-27	15-Mar-27
366	031-FORM-0651	Form	1	16-Mar-27	16-Mar-27
367	032-REBA-0652	Rebar	1	17-Mar-27	17-Mar-27
368	014-INSP-0653	Inspection	1	18-Mar-27	18-Mar-27
369	010-POUR-0654	Pour	1	19-Mar-27	19-Mar-27
370	010-FENC-0649	Fencing / Gates -	8	22-Mar-27	31-Mar-27
371	101-STRI-0650	Stripping / Signage -	5	01-Apr-27	07-Apr-27
372	**Concrete Quad West**		48	11-Feb-27	19-Apr-27
373	321-CURB-0655	'F' Curbs -	5	11-Feb-27	17-Feb-27
374	321-CURB-0656	"D" Curbs -	5	18-Feb-27	24-Feb-27
375	321-SIDE-0657	Sidewalk -	8	25-Feb-27	08-Mar-27
376	031-FORM-0660	Form	1	09-Mar-27	09-Mar-27
377	032-REBA-0661	Rebar	1	10-Mar-27	10-Mar-27
378	014-INSP-0662	Inspection	1	11-Mar-27	11-Mar-27
379	010-POUR-0663	Pour	1	12-Mar-27	12-Mar-27
380	010-FENC-0658	Fencing / Gates -	8	01-Apr-27	12-Apr-27
381	101-STRI-0659	Stripping / Signage -	5	13-Apr-27	19-Apr-27
382	**Landscape**		65	07-Jan-27	07-Apr-27

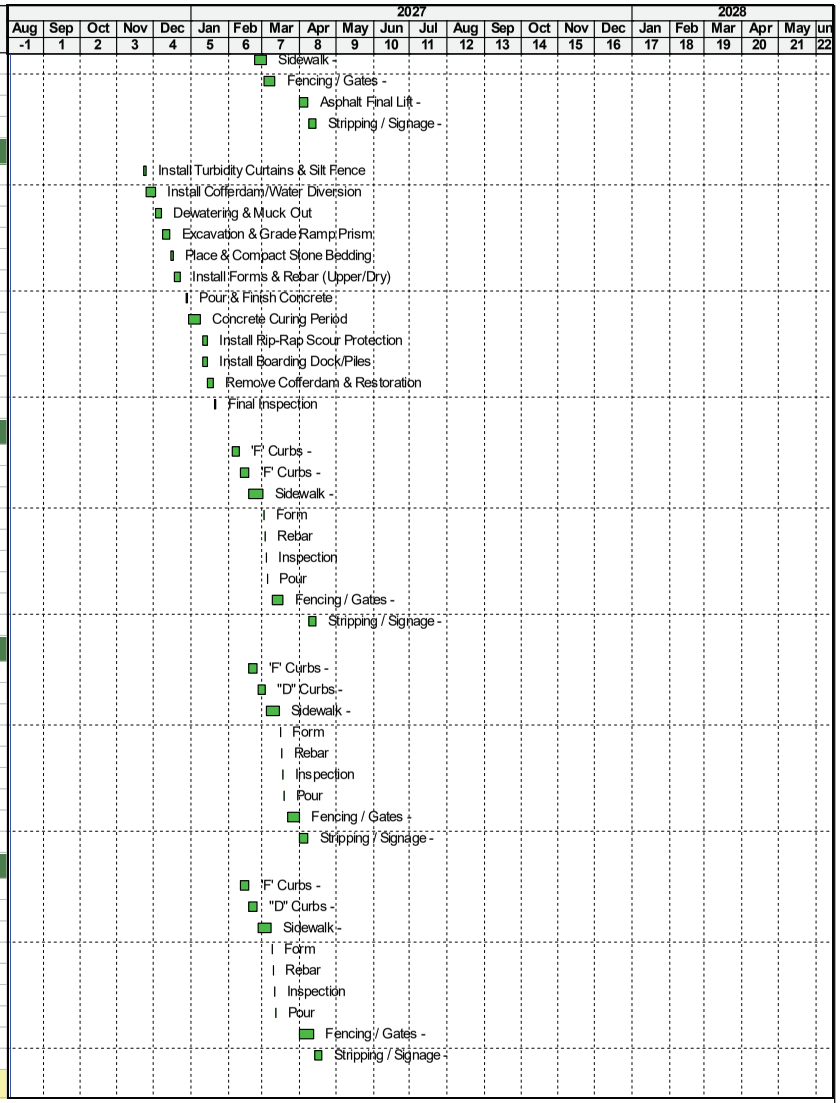

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
383	**Landscape South**		60	07-Jan-27	31-Mar-27
384	32-FNSH-0137	Irrigation Lines - South Site Finishes	7	07-Jan-27	15-Jan-27
385	01-FNSH-0138	Final Grade & Topsoil - South Site Finishes	5	05-Mar-27	11-Mar-27
386	32-FNSH-0140	Landscaping - South Site Finishes	16	10-Mar-27	31-Mar-27
387	01-FNSH-0139	Large Trees - South Site Finishes	14	12-Mar-27	31-Mar-27
388	**Landscape North**		58	18-Jan-27	07-Apr-27
389	328-IRRI-0348	Irrigation Lines - North Site Finishes	7	18-Jan-27	26-Jan-27
390	010-GRAD-0349	Final Grade & Topsoil - North Site Finishes	5	12-Mar-27	18-Mar-27
391	329-LAND-0351	Landscaping - North Site Finishes	16	17-Mar-27	07-Apr-27
392	010-LARG-0350	Large Trees - North Site Finishes	14	19-Mar-27	07-Apr-27
393	**Site Finishes**		23	01-Apr-27	03-May-27
394	**South Site Finishes**		18	01-Apr-27	26-Apr-27
395	01-FNSH-0132	Trash Bins - South Site Finishes	2	01-Apr-27	02-Apr-27
396	01-FNSH-0133	Recycling Bins - South Site Finishes	2	05-Apr-27	06-Apr-27
397	01-FNSH-0134	Picnic Tables - South Site Finishes	2	07-Apr-27	08-Apr-27
398	12-FNSH-0135	Benches - South Site Finishes	2	09-Apr-27	12-Apr-27
399	10-FNSH-0136	Bike Rack - South Site Finishes	2	13-Apr-27	14-Apr-27
400	01-FNSH-0141	KL Site Punch - South Site Finishes	8	15-Apr-27	26-Apr-27
401	**North Site Finishes**		18	08-Apr-27	03-May-27
402	010-TRAS-0343	Trash Bins - North Site Finishes	2	08-Apr-27	09-Apr-27
403	010-RECY-0344	Recycling Bins - North Site Finishes	2	12-Apr-27	13-Apr-27
404	010-PICN-0345	Picnic Tables - North Site Finishes	2	14-Apr-27	15-Apr-27
405	125-BENC-0346	Benches - North Site Finishes	2	16-Apr-27	19-Apr-27
406	105-BIKE-0347	Bike Rack - North Site Finishes	2	20-Apr-27	21-Apr-27
407	010-KLSI-0352	KL Site Punch - North Site Finishes	8	22-Apr-27	03-May-27
408	**North Memorial Garden**		34	07-Jan-27	23-Feb-27
409	010-SITE-0617	Site Survey & Layout Stakes	2	07-Jan-27	08-Jan-27
410	328-TREN-0618	Trenching for Irrigation Mains	5	11-Jan-27	15-Jan-27
411	230-EXCA-0620	Excavate & Pour Sculpture Base	3	11-Jan-27	13-Jan-27
412	260-ELEC-0619	Electrical Conduit & Pole Bases	5	18-Jan-27	22-Jan-27
413	312-PATH-0621	Path Sub-grade Prep & Compaction	3	25-Jan-27	27-Jan-27
414	010-MEMO-0623	Install Memorial Sculpture	3	25-Jan-27	27-Jan-27
415	230-PATH-0622	Install Path Edging & Base Rock	3	28-Jan-27	01-Feb-27
416	321-PAVI-0624	Paving / Final Path Surface	3	02-Feb-27	04-Feb-27
417	224-LIGH-0625	Erect Light Poles & Fixtures	2	02-Feb-27	03-Feb-27
418	328-IRRI-0626	Install Irrigation Laterals & Heads	3	05-Feb-27	09-Feb-27
419	010-SOIL-0627	Soil Prep & Planting (Trees/Shrubs)	5	10-Feb-27	16-Feb-27
420	312-GRAD-0628	Final Grading & Sod/Turf	3	17-Feb-27	19-Feb-27
421	017-TEST-0629	System Testing & Final Punchlist	2	22-Feb-27	23-Feb-27
422	**External Structures**		186	30-Dec-26	21-Sep-27
423	**Car Wash**		38	19-Jan-27	11-Mar-27
424	010-SITE-0480	Site Layout & Staking	2	19-Jan-27	20-Jan-27
425	312-EXCA-0601	Excavation & Grading	4	21-Jan-27	26-Jan-27
426	221-UNDE-0602	Underground Wet Utilities (Drainage)	5	27-Jan-27	02-Feb-27
427	010-OILW-0603	Oil/Water Separator Installation	3	29-Jan-27	02-Feb-27
428	010-PLUM-0604	Plumbing Rough-In (Water Lines)	3	03-Feb-27	05-Feb-27
429	260-UNDE-0605	Underground Electrical Conduits	2	08-Feb-27	09-Feb-27
430	032-FORM-0606	Formwork & Rebar Placement	3	10-Feb-27	12-Feb-27

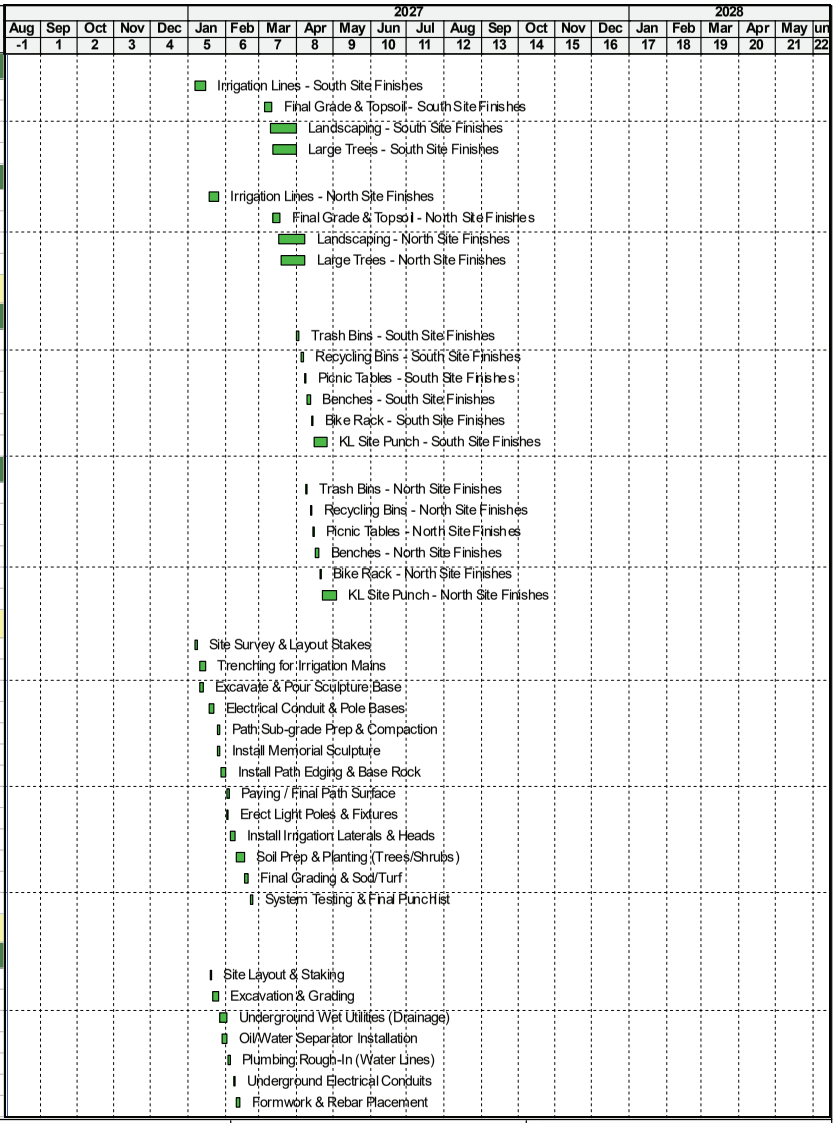

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
431	050-ANCH-0607	Anchor Bolt Setting & Survey	1	15-Feb-27	15-Feb-27
432	033-SLAB-0608	Pour Slab-on-Grade	1	16-Feb-27	16-Feb-27
433	010-CONC-0609	Concrete Curing Period	7	17-Feb-27	25-Feb-27
434	051-STEE-0610	Erect Steel Canopy Columns	2	26-Feb-27	01-Mar-27
435	051-ROOF-0611	Install Roof Trusses & Purlins	3	02-Mar-27	04-Mar-27
436	262-ROOF-0612	Install Metal Roofing Panels	3	05-Mar-27	09-Mar-27
437	263-PLUM-0614	Final Plumbing Hookups (Hoses/Nozzles)	2	08-Mar-27	09-Mar-27
438	265-LIGH-0613	Install Lighting & Sensors	2	10-Mar-27	11-Mar-27
439	101-LINE-0615	Line Striping & Signage	1	10-Mar-27	10-Mar-27
440	014-INSP-0616	Final Inspections & Testing	1	11-Mar-27	11-Mar-27
441	**Fuel Stand**		186	30-Dec-26	21-Sep-27
442	**Foundation**		13	30-Dec-26	18-Jan-27
443	225-PRES-0568	Pre-Slab Fuel Piping Installation	3	30-Dec-26	04-Jan-27
444	033-GENC-0569	Gen Room Concrete Slab & Foundation	5	05-Jan-27	11-Jan-27
445	050-ANCH-0570	Anchor Bolt/Embed Installation	1	12-Jan-27	12-Jan-27
446	225-FUEL-0571	Fuel Tank Pad/Base Construction	4	13-Jan-27	18-Jan-27
447	**Rough**		163	12-Jan-27	30-Aug-27
448	042-CONS-0572	Wall Construction (Block/Frame)	15	12-Jan-27	01-Feb-27
449	225-FUEL-0574	Fuel Piping Installation & Testing (Above Ground)	4	19-Jan-27	22-Jan-27
450	010-ROOF-0573	Roofing & Weatherproofing	5	02-Feb-27	08-Feb-27
451	010-EXHA-0575	Exhaust System Installation (Muffler & Piping)	5	09-Feb-27	15-Feb-27
452	260-POWE-0577	Power Cabling Pull (Main Feeder)	7	09-Feb-27	17-Feb-27
453	010-CONT-0578	Control Wiring & Interlocks	5	09-Feb-27	15-Feb-27
454	263-AUTO-0576	Automatic Transfer Switch (ATS) Mounting	1	30-Aug-27	30-Aug-27
455	**Finishes**		12	09-Feb-27	24-Feb-27
456	099-COAT-0579	Wall Coatings/Paint	4	09-Feb-27	12-Feb-27
457	225-CONN-0583	Final Connections (Fuel, Cooling)	2	09-Feb-27	10-Feb-27
458	096-FINI-0580	Floor Finishes (Sealing/Epoxy)	4	15-Feb-27	18-Feb-27
459	089-LOUV-0582	Louver/Ventilation Installation	3	16-Feb-27	18-Feb-27
460	081-DOOR-0581	Door Installation (Acoustic rated)	4	19-Feb-27	24-Feb-27
461	010-ELEC-0584	Final Electrical Dress-out & Labeling	2	19-Feb-27	22-Feb-27
462	**Inspections / Commissioning**		15	31-Aug-27	21-Sep-27
463	010-CHEC-0585	System Checkouts & Pre-Functional Tests	3	31-Aug-27	02-Sep-27
464	014-STAR-0586	Startup & Functional Testing (Wet Run)	2	03-Sep-27	07-Sep-27
465	014-INTE-0587	Integrated Systems Testing (IST)/Blackout Test	2	08-Sep-27	09-Sep-27
466	014-AHJI-0588	Final AHJ Inspection & Sign-off	3	10-Sep-27	14-Sep-27
467	017-TURN-0589	Turnover Documentation & Closeout	5	15-Sep-27	21-Sep-27
468	**Cover Parking**		51	17-Feb-27	28-Apr-27
469	**Foundations**		28	17-Feb-27	26-Mar-27
470	010-LAYO-0489	Layout & Survey Control	2	17-Feb-27	18-Feb-27
471	010-EART-0490	Earthwork & Rough Grade	5	19-Feb-27	25-Feb-27
472	221-UNDE-0491	Install Underground Utilities/Drainage	8	23-Feb-27	04-Mar-27
473	033-EXCA-0492	Excavate & Form Column Footings	5	05-Mar-27	11-Mar-27
474	033-REBA-0493	Install Rebar & Embeds (Footings)	4	12-Mar-27	17-Mar-27
475	033-CURE-0494	Pour & Cure Concrete Footings	7	18-Mar-27	26-Mar-27
476	**Canopy Structure & Deck**		21	29-Mar-27	26-Apr-27
477	010-MATE-0495	Material Delivery: Canopy Steel	1	29-Mar-27	29-Mar-27
478	015-STEE-0496	Mobilize Steel Erection Crew & Crane	2	30-Mar-27	31-Mar-27

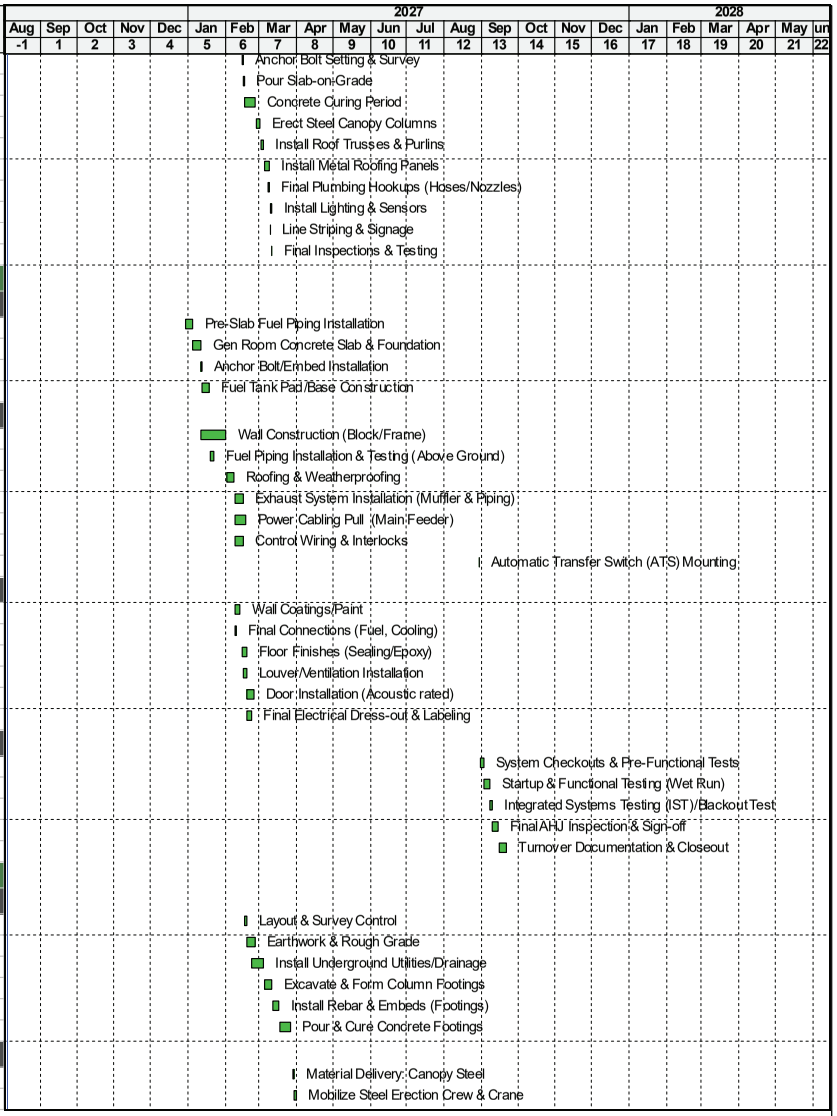

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
479	010-CANO-0497	Erect Canopy Columns & Main Beams	7	01-Apr-27	09-Apr-27
480	010-SECO-0498	Install Secondary Framing (Purlins, Bracing)	5	06-Apr-27	12-Apr-27
481	010-CANO-0499	Install Canopy Decking/Roofing	10	13-Apr-27	26-Apr-27
482	010-GUTT-0500	Install Gutters & Downspouts	3	20-Apr-27	22-Apr-27
483	**Utilities & Finishes**		39	05-Mar-27	28-Apr-27
484	321-PREP-0502	Prepare & Pour Paving Sub-Base (Aggregate)	4	05-Mar-27	10-Mar-27
485	321-ASPH-0503	Pour Asphalt/Concrete Paving	5	11-Mar-27	17-Mar-27
486	101-STRI-0504	Striping, Signage & Bollard Installation	3	18-Mar-27	22-Mar-27
487	265-LIGH-0501	Install Lighting Fixtures & Power Drops	4	13-Apr-27	16-Apr-27
488	024-CLEA-0505	Final Clean-Up & Demobilization	2	27-Apr-27	28-Apr-27
489	014-INSP-0506	Final Inspection & Project Turnover	0		28-Apr-27
490	**Training Canopy**		30	29-Apr-27	10-Jun-27
491	010-LAYO-0630	Layout & Staking	1	29-Apr-27	29-Apr-27
492	312-EXCA-0631	Excavation	1	30-Apr-27	30-Apr-27
493	050-REIN-0632	Reinforcement & Anchor Bolts	2	03-May-27	04-May-27
494	033-CONC-0633	Pour Concrete Footings	1	05-May-27	05-May-27
495	010-CONC-0634	Concrete Curing (7-Day)	7	06-May-27	14-May-27
496	010-ALUM-0635	Erect Aluminum Columns	3	17-May-27	19-May-27
497	010-SUPP-0636	Install Support Beams	3	20-May-27	24-May-27
498	010-PURL-0637	Install Purlins & Bracing	2	25-May-27	26-May-27
499	262-ROOF-0638	Install Roof Panels	5	27-May-27	03-Jun-27
500	010-GUTT-0639	Gutters & Downspouts	2	04-Jun-27	07-Jun-27
501	071-CAUL-0640	Caulking & Waterproofing	2	08-Jun-27	09-Jun-27
502	017-INSP-0641	Final Inspection/Punchlist	1	10-Jun-27	10-Jun-27
503	**FireTraining Complex**		165	26-Feb-27	09-Aug-27
504	211-SPRI-1150	Fire Training Complex -- Misc Structures	10	26-Feb-27	07-Mar-27
505	211-SPRI-1160	Fire Training Complex -- Run Utilities / Water & Power / Perimter Fencing	15	08-Mar-27	22-Mar-27
506	211-SPRI-1170	Fire Training Complex -- Complex Erection	20	21-Jun-27	10-Jul-27
507	211-SPRI-1180	Fire Training Complex -- County Inspection Approval / Released for Use	30	11-Jul-27	09-Aug-27
508	**Building Construction :**		342	05-Oct-26	07-Feb-28
509	**Building**		342	05-Oct-26	07-Feb-28
510	**Building Structure**		228	05-Oct-26	25-Aug-27
511	**Elevator Foundations**		16	07-Dec-26	30-Dec-26
512	14-WORK-0142	Layout / Batterboards - Elevator Fnd - Bldg	4	07-Dec-26	10-Dec-26
513	14-EXCV-0143	Elevator Pit - Excavate - Elevator Fnd - Bldg	3	11-Dec-26	15-Dec-26
514	14-WORK-0144	Elevator Pit - Foundation FRP - Elevator Fnd - Bldg	3	16-Dec-26	18-Dec-26
515	14-WORK-0145	Elevator Pit -Walls FRP- Elevator Fnd - Bldg	3	21-Dec-26	23-Dec-26
516	07-WORK-0146	Waterproof Elevator Pit Walls - Elevator Fnd - Bldg	2	28-Dec-26	29-Dec-26
517	31-WORK-0147	Backfill / Compaction Elevator Pit Walls - Elevator Fnd - Bldg	2	29-Dec-26	30-Dec-26
518	**Foundations To SOG**		98	04-Dec-26	22-Apr-27
519	22-RGIN-0149	Plumbing U/G Rough - Foundation - Bldg	8	04-Dec-26	15-Dec-26
520	01-RGIN-0151	Elect U/G Rough - Foundation - Bldg	8	10-Dec-26	21-Dec-26
521	312-SOGF-0397	SOG Fill / Compact — 4" Slab Area A — Foundation	5	22-Dec-26	30-Dec-26
522	03-EXCV-0148	Isolated Footings C - F - Excavate & Rebar - Foundation - Bldg	2	31-Dec-26	04-Jan-27
523	01-GEOS-0148	Geotechnical Engineer Verify Bearing Capacity Prior to Footing Pour (S-003 / Req'd)	2	04-Jan-27	06-Jan-27
524	033-CONT-0463	Continous Footings A - F - Excavate & Rebar - Foundation - Bldg	1	05-Jan-27	05-Jan-27
525	033-ISOL-0462	Isolated Footings C - F - Inspect & Pour - Foundation - Bldg	3	07-Jan-27	11-Jan-27
526	03-EXCV-0463	Continous Footings A - F - Excavate & Rebar - Foundation - Bldg	3	12-Jan-27	14-Jan-27

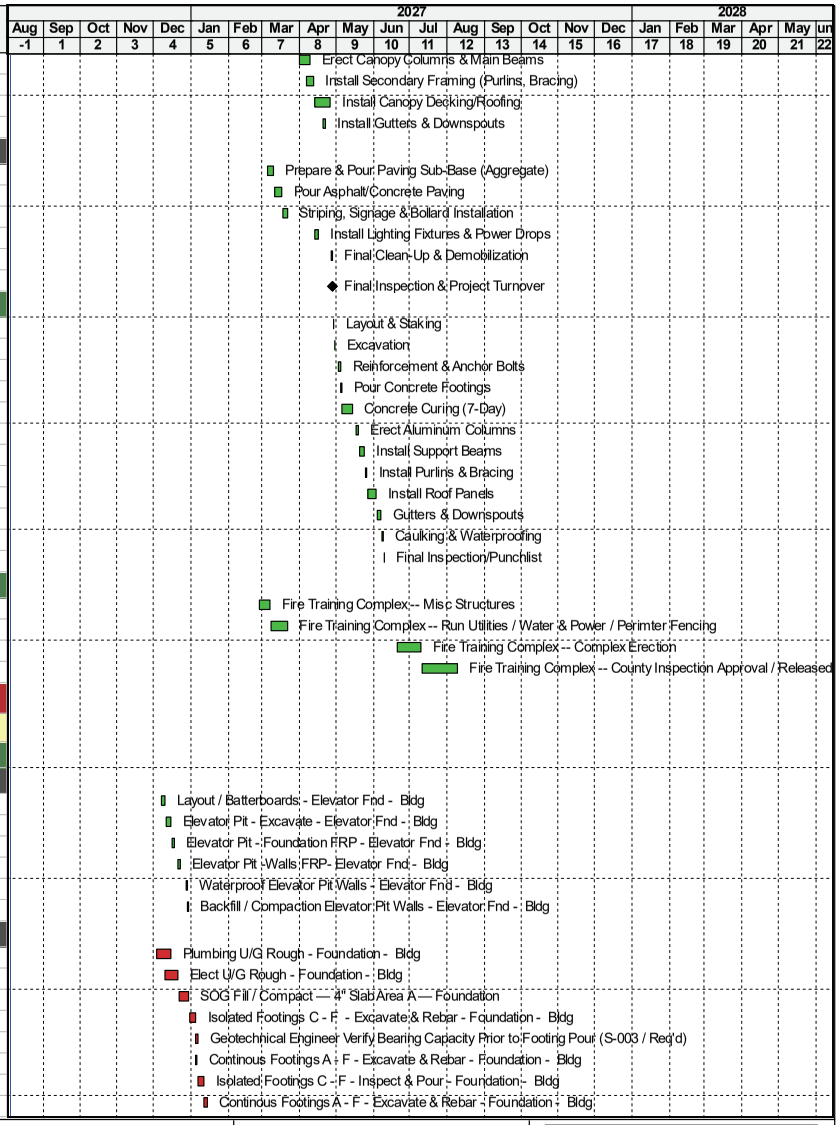

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
527	033-ISOL-0481	Isolated Footings G - J - Excavate & Rebar - Foundation - Bldg	1	12-Jan-27	12-Jan-27
528	033-ISOL-0482	Isolated Footings G - J - Inspect & Pour - Foundation - Bldg	1	13-Jan-27	13-Jan-27
529	033-CONT-0483	Continous Footings F - J - Excavate & Rebar - Foundation - Bldg	3	15-Jan-27	19-Jan-27
530	03-EXCV-0484	Continous Footings J - M - Excavate & Rebar - Foundation - Bldg	3	20-Jan-27	22-Jan-27
531	033-CONT-0484	Continous Footings J - M - Excavate & Rebar - Foundation - Bldg	3	25-Jan-27	27-Jan-27
532	03-EXCV-0483	Continous Footings F - J - Excavate & Rebar - Foundation - Bldg	3	28-Jan-27	01-Feb-27
533	03-EXCV-0485	Continous Footings M - O - Excavate & Rebar - Foundation - Bldg	1	28-Jan-27	28-Jan-27
534	03-INST-0486	Continous Footings F - J - Inspect & Pour - Foundation - Bldg	3	02-Feb-27	04-Feb-27
535	03-WORK-0150	Form SOG — Area A (4" NWC / WWR 6x6-W1.4xW1.4)	5	05-Feb-27	11-Feb-27
536	03-INST-0152	SOG Prep / Inspect / Pour / Cut — Area A — 3,000 PSI	5	12-Feb-27	18-Feb-27
537	010-ELEC-0309	Electrical Deep U/G Rough - Foundation - Bldg	5	19-Feb-27	25-Feb-27
538	**SOG - Maintenance Base / Fire Storage**		75	11-Dec-26	30-Mar-27
539	07-WORK-0267	Layout/ Batter Boards - Foundation - Bldg	2	11-Dec-26	14-Dec-26
540	312-SOGF-0399	SOG Fill / Compact — 12" Structural Slab — Maint Base / Fire Storage	3	31-Dec-26	05-Jan-27
541	03-WORK-0270	Form SOG — Maint Base / Fire Storage (12" Structural NWC)	5	06-Jan-27	12-Jan-27
542	01-RGIN-0269	Elect Deep U/G Rough - Foundation - Bldg	5	26-Feb-27	04-Mar-27
543	03-EXCV-0268	Foundations - Excavate, Forms & Rebar - Foundation - Bldg	8	05-Mar-27	16-Mar-27
544	010-FOUN-0468	Foundations - Inspect & Pour - Foundation - Bldg	2	05-Mar-27	08-Mar-27
545	22-RGIN-0271	Plumbing U/G Rough - Foundation - Bldg	5	17-Mar-27	23-Mar-27
546	010-ELEC-0398	Elect U/G Rough - Foundation - Bldg	5	22-Mar-27	26-Mar-27
547	03-INST-0272	SOG Prep / Inspect / Pour / Cut — Maint Base — 3,000 PSI	5	24-Mar-27	30-Mar-27
548	03-INST-0468	Foundations - Inspect & Pour - Foundation - Bldg	2	29-Mar-27	30-Mar-27
549	**SOG - Generator Room**		91	15-Dec-26	22-Apr-27
550	07-WORK-0273	Layout/ Batter Boards - Foundation - Bldg	2	15-Dec-26	16-Dec-26
551	312-SOGF-0401	SOG Fill / Compact — 6" Slab — Generator Room	3	06-Jan-27	08-Jan-27
552	01-RGIN-0275	Elect Deep U/G Rough - Foundation - Bldg	5	05-Mar-27	11-Mar-27
553	03-EXCV-0274	Foundations - Excavate, Forms & Rebar - Foundation - Bldg	8	17-Mar-27	26-Mar-27
554	03-SOG-0160C	SOG Prep / Inspect / Pour — Structural Slab (12" NWC / #5@12" EW T&B / 3,000 PSI)	5	30-Mar-27	06-Apr-27
555	03-WORK-0276	Form SOG — Generator Room (6" NWC / WWR 6x6-W2.9xW2.9)	5	31-Mar-27	06-Apr-27
556	22-RGIN-0277	Plumbing U/G Rough - Foundation - Bldg	5	31-Mar-27	06-Apr-27
557	010-ELEC-0400	Elect U/G Rough - Foundation - Bldg	5	02-Apr-27	08-Apr-27
558	03-CURE-SOG-C	SOG Concrete Cure — Structural Slab (7 Days Min — Generator / Lift Pit Areas)	7	06-Apr-27	15-Apr-27
559	03-INST-0278	SOG Prep / Inspect / Pour / Cut — Generator Room — 3,000 PSI	5	09-Apr-27	15-Apr-27
560	03-HKPD-0165	Form / Pour / Cure Housekeeping Pads — Generator (14" Isolated) & Chiller (6") — 3,000 PSI	5	15-Apr-27	22-Apr-27
561	**Emergency Generators**		28	12-Mar-27	20-Apr-27
562	26-WORK-0303	Deep Electrical U/G Rgh-in -EOC-EG	5	12-Mar-27	18-Mar-27
563	01-WORK-0304	Cont Footers FRP -EOC-EG	3	19-Mar-27	23-Mar-27
564	26-WORK-0305	Electrical U/G Rgh-in -EOC-EG	2	24-Mar-27	25-Mar-27
565	010-PLUM-0443	Plumbing U/G Rgh-in -EOC-EG	2	24-Mar-27	25-Mar-27
566	03-INST-0306	H/K Pads Form / Inspect / Pour -EOC-EG	3	26-Mar-27	30-Mar-27
567	031-SOGF-0318	SOG Form / Inspect / Pour -EOC-EG	3	16-Apr-27	20-Apr-27
568	**Tilt Panel Construction**		152	05-Oct-26	10-May-27
569	01-WORK-0153	Prepare for Casting Beds - Bldg	5	05-Oct-26	09-Oct-26
570	010-FINI-0154	Pour & Finish Casting Beds - Bldg	5	12-Oct-26	16-Oct-26
571	26-WORK-0155	Form & Prep Tilt-Up Panels — Bldg	35	05-Feb-27	25-Mar-27
572	26-INST-0156	Inspect & Pour Tilt-Up Panels — 3,000 PSI Min (ACI 318/ACI 551) — Delegated Engineer	35	16-Feb-27	05-Apr-27
573	26-WORK-0157	Tilt-Up Panel Cure — 3,000 PSI Min Required Prior to Erection	34	25-Feb-27	13-Apr-27
574	262-TILT-0158	Erect Tilt-Up Panels (TW7.25/TW8.0/TW9.25) — Delegated Engineer Required	46	08-Mar-27	10-May-27

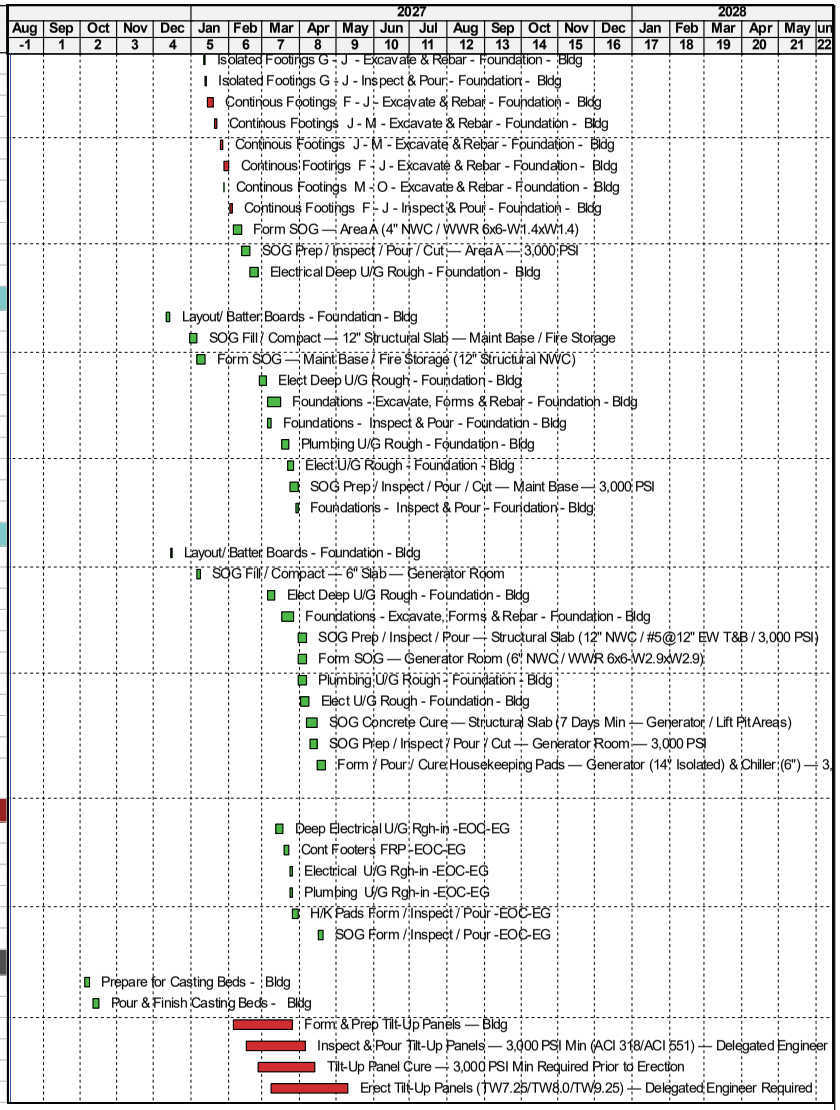

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
575		**1st to 2nd Floor**	51	11-May-27	22-Jul-27
576	051-STEE-1086	Erect Steel Cols/Beams/Joists — Elevator Shaft Roof	2	11-May-27	12-May-27
577	05-INST-0159	Erect Structural Steel Beams — Area A (W21X44/W24X55 typ.)	5	13-May-27	19-May-27
578	05-INSP-0161	Structural Steel Beams Inspection — Area A	2	20-May-27	21-May-27
579	053-DECK-0160	Install Composite Steel Deck — 2nd Floor Area A (CPS 2.0VLI20 / 2" deck)	5	27-May-27	03-Jun-27
580	053-DECK-0162	Metal Decking Inspection — 2nd Floor Area A	2	04-Jun-27	07-Jun-27
581	26-WORK-0163	Electrical Slab L/O & Rgh-in - Bldg	5	08-Jun-27	14-Jun-27
582	03-INST-0164	Install Slab Rebar / WWR 6x6-W1.4xW1.4 — 2nd Floor Area A	5	08-Jun-27	14-Jun-27
583	010-INST-0472	Install MEP Hangers @ Steel Beams — 2nd Floor Area A	3	15-Jun-27	17-Jun-27
584	03-INST-0165	Pour & Inspect 2nd Floor Topping Slab — Area A — 4,000 PSI / 6.5" Total	2	18-Jun-27	21-Jun-27
585	03-INST-486	2nd Floor Slab Concrete Cure Bldg	7	22-Jun-27	30-Jun-27
586	033-PLUM-0455	Plumbing Slab L/O & Rgh-in - Bldg	5	01-Jul-27	08-Jul-27
587	033-MECH-0456	Mechanical Slab L/O & Rgh-in - Bldg	5	09-Jul-27	15-Jul-27
588	033-SPKL-0457	Fire Spklr Slab L/O & Rgh-in - Bldg	5	16-Jul-27	22-Jul-27
589		**2nd Floor to Roof**	0		
590		**Roof**	75	10-May-27	25-Aug-27
591	051-JOIS-0201	Erect Open Web Steel Joists — 2nd Floor Area B (18K3 / 30K10 @ 4'-0" OC max)	5	10-May-27	17-May-27
592	051-STUD-1088	Install Headed Shear Studs on Composite Beams — Roof Area A (3/4" dia.)	2	12-May-27	14-May-27
593	053-DECK-1088	Install Composite Steel Deck — Roof Area A (CPS 3.0VLI20 / 3" deck)	5	17-May-27	21-May-27
594	051-BRDG-0201	Install Joist Bridging & Bracing — 2nd Floor Area B (SJI Spec / Special Inspection)	3	17-May-27	20-May-27
595	053-DECK-0201	Install Non-Composite Roof Deck — Area B (SD 1.5B20 / 1.5" Type B 20ga Galv Vented)	5	20-May-27	27-May-27
596	051-STUD-0160	Install Headed Shear Studs on Composite Beams — 2nd Floor Area A (3/4" dia.)	3	21-May-27	26-May-27
597	051-JOIS-0301	Erect Open Web Steel Joists — Roof Area B (60DLH16 Long Span)	5	21-May-27	28-May-27
598	053-DECK-1090	Metal Decking Inspection — Roof Area A	1	24-May-27	24-May-27
599	010-ELEC-1092	Electrical Roof L/O & Rgh-in - Roof - Bldg	5	25-May-27	01-Jun-27
600	010-PLUM-1095	Plumbing Roof L/O & Rgh-in - Roof - Bldg	5	25-May-27	01-Jun-27
601	053-INSP-0201	Steel Deck Inspection — Area B (Non-Composite / No Concrete)	1	27-May-27	28-May-27
602	051-BRDG-0301	Install Joist Bridging & Bracing — Roof Area B (SJI Spec / Special Inspection)	3	28-May-27	03-Jun-27
603	010-ROOF-1094	Pour & Inspect Roof Topping Slab — Area A — 4,000 PSI / 7.5" Total	5	02-Jun-27	08-Jun-27
604	053-DECK-0301	Install Non-Composite Roof Deck — Roof Area B (SD 1.5B20 / 1.5" Type B 20ga Galv)	5	03-Jun-27	10-Jun-27
605	03-CURE-1094	Roof Topping Slab Concrete Cure — 7 Days Min — Area A — 4,000 PSI	7	08-Jun-27	17-Jun-27
606	053-INSP-0301	Steel Deck Inspection — Roof Area B (Non-Composite / No Concrete Pour)	1	10-Jun-27	11-Jun-27
607	07-INST-0173	Roof Insulation Install — Area A (after concrete cure)	5	18-Jun-27	24-Jun-27
608	03-CURE-0165	2nd Floor Topping Slab Concrete Cure — 7 Days Min — Area A — 4,000 PSI	7	21-Jun-27	30-Jun-27
609	01-WORK-0167	Stairs 1st to 2nd Flr - 2nd to 3rd - Bldg	8	23-Jul-27	03-Aug-27
610	01-WORK-0171	Stairs 2nd Flr to Roof - 2nd to 3rd - Bldg	8	04-Aug-27	13-Aug-27
611	010-STAI-1087	Stairs 1st to 2nd Flr - Roof - Bldg	8	04-Aug-27	13-Aug-27
612	010-STAI-1091	Stairs 2nd Flr to Roof - Roof - Bldg	8	16-Aug-27	25-Aug-27
613		**Emergency Generator / Installation**	92	21-Apr-27	30-Aug-27
614	271-PREP-0319	Prep & Patch Panels -EOC-EG	3	21-Apr-27	23-Apr-27
615	26-WORK-0321	Em Generator Fuel Line Tie-in -EOC-EG	2	26-Apr-27	27-Apr-27
616	099-PRIM-0320	Prime & Paint (5d cure lag) -EOC-EG	2	03-May-27	04-May-27
617	263-EMGE-0313	Em Generator Install -EOC-EG	5	02-Aug-27	06-Aug-27
618	26-INST-0313	Em Generator Tank Install -EOC-EG	5	09-Aug-27	13-Aug-27
619	260-ELEC-0315	Elec Panels / Conduit / Wire -EOC-EG	3	16-Aug-27	18-Aug-27
620	263-EMGE-0321	Em Generator Fuel Line Tie-in -EOC-EG	2	16-Aug-27	17-Aug-27
621	263-TRAN-0316	Transfer Switch / Conduit / Wire -EOC-EG	3	19-Aug-27	23-Aug-27
622	263-EMGE-0317	Em Generator System Start-up -EOC-EG	5	24-Aug-27	30-Aug-27
623		**Chiller Plant**	70	23-Jul-27	01-Nov-27

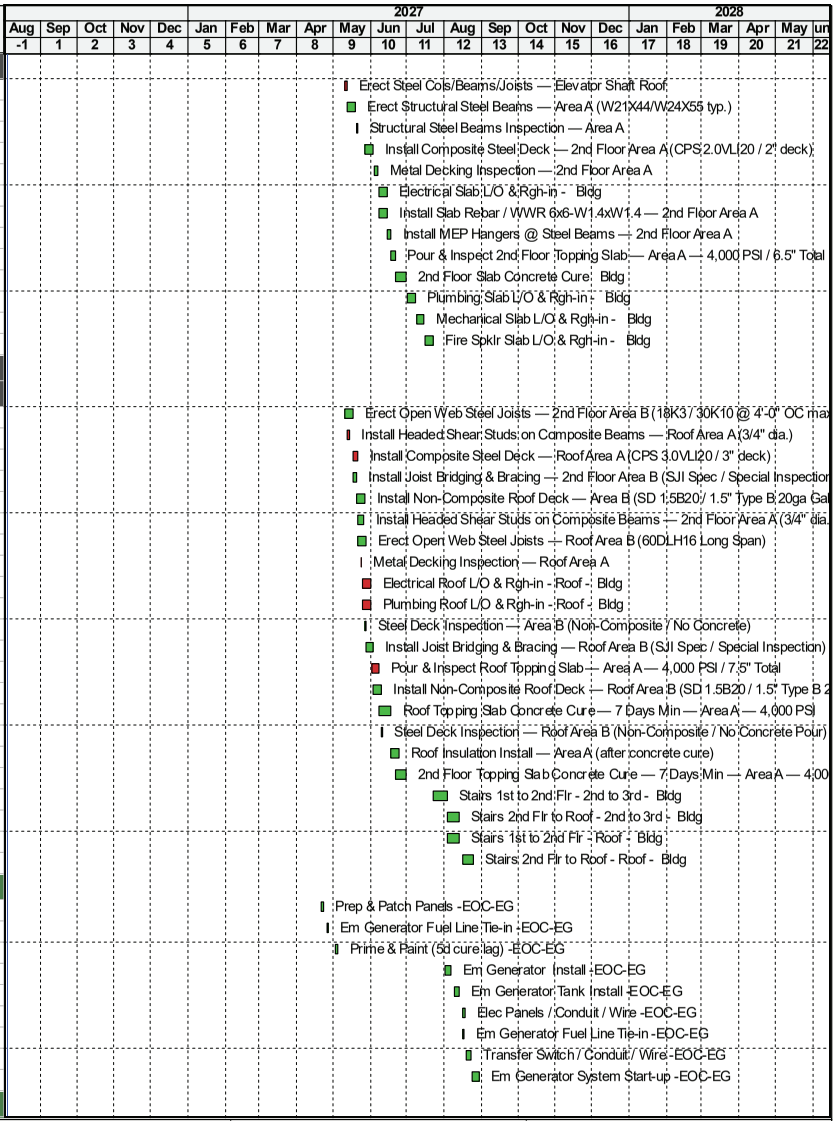

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
624	23-WORK-0175	UG Piping - Chiller Plant	8	23-Jul-27	03-Aug-27
625	23-WORK-0176	U/G Elect- Chiller Plant	5	04-Aug-27	10-Aug-27
626	23-WORK-0177	Housekeeping Pad - Chiller Plant	3	11-Aug-27	13-Aug-27
627	23-WORK-0178	SOG - Chiller Plant	3	16-Aug-27	18-Aug-27
628	236-STAN-0312	Equipment Stands Install / Inspect - Chiller Plant	3	16-Aug-27	18-Aug-27
629	23-INST-0179	Air-Cooled Chillers Install - Chiller Plant (TEMP)	8	19-Aug-27	30-Aug-27
630	23-INST-0180	CW Pumps Install - Chiller Plant	5	19-Aug-27	25-Aug-27
631	236-CUCH-0416	CU's Install - Chiller Plant	2	19-Aug-27	20-Aug-27
632	014-CUTI-0417	CU's Tie-in / Inspection - Chiller Plant	4	23-Aug-27	26-Aug-27
633	23-INSP-0181	CWP Tie-in / Inspection - Chiller Plant	5	31-Aug-27	07-Sep-27
634	07-INSP-0182	CWP Insulation / Inspection - Chiller Plant	5	08-Sep-27	14-Sep-27
635	230-CHIL-0310	Chiller System Controls -Chiller Yard	8	08-Sep-27	17-Sep-27
636	236-ELEC-0311	Electrical Chiller System Tie-in / Inspect -Chiller Yard	8	08-Sep-27	17-Sep-27
637	236-PLUM-0441	Plumbing Chiller System Tie-in / Inspect -Chiller Yard	8	08-Sep-27	17-Sep-27
638	236-MECH-0442	Mechanical Chiller System Tie-in / Inspect -Chiller Yard	8	08-Sep-27	17-Sep-27
639	23-WORK-0183	CW Pumps Start-up - Chiller Plant	3	15-Oct-27	19-Oct-27
640	236-CHIL-0184	Flush System - Chiller Plant	4	20-Oct-27	25-Oct-27
641	236-CUPU-0418	CU's Pumps Start-up - Chiller Plant	2	20-Oct-27	21-Oct-27
642	23-WORK-0185	Chilled Water System Start-up - Chiller Plant	5	26-Oct-27	01-Nov-27
643	**Final connection**		10	26-Aug-27	09-Sep-27
644	236-PERM-0473	Set Permanent Chiller	2	26-Aug-27	27-Aug-27
645	010-CWPT-0474	CWP Tie-in	2	30-Aug-27	31-Aug-27
646	010-CUTI-0475	CU Tie-in	2	01-Sep-27	02-Sep-27
647	010-ELEC-0476	Electrical Tie-in	2	03-Sep-27	07-Sep-27
648	010-PLUM-0477	Plumbing Tie-in	2	08-Sep-27	09-Sep-27
649	**Exterior Envelope**		54	02-Jun-27	17-Aug-27
650	07-WORK-0186	Waterproof Window Openings - Ext Envelope - Bldg	7	02-Jun-27	10-Jun-27
651	262-CAUL-0471	Caulk Tiltwall Panels - Ext Envelope - Bldg	15	09-Jun-27	29-Jun-27
652	08-WORK-0187	Window / Caulking - Ext Envelope - Bldg	20	11-Jun-27	09-Jul-27
653	08-WORK-0188	Exterior H.M. Doors & Frames - Ext Envelope - Bldg	5	11-Jun-27	17-Jun-27
654	08-INST-0189	Roll-up Doors Install - Ext Envelope - Bldg	8	11-Jun-27	22-Jun-27
655	01-WORK-0194	Dry-in Roof - Ext Envelope - Bldg	5	11-Jun-27	17-Jun-27
656	01-FNSH-0195	Finish Roof System - Ext Envelope - Bldg	8	18-Jun-27	29-Jun-27
657	09-FNSH-0193	Finish Paint Exterior - Ext Envelope - Bldg	10	29-Jun-27	13-Jul-27
658	09-WORK-0190	Prime Paint Exterior - Ext Envelope - Bldg	8	30-Jun-27	12-Jul-27
659	08-INST-0191	Storefront Install - Ext Envelope - Bldg	8	30-Jun-27	12-Jul-27
660	01-WORK-0192	Stair Rails - Ext Envelope - Bldg	8	13-Jul-27	22-Jul-27
661	010-BALC-0465	Balcony Rails - Ext Envelope - Bldg	8	23-Jul-27	03-Aug-27
662	01-PNCH-0196	KL Punch - Ext Envelope - Bldg	10	04-Aug-27	17-Aug-27
663	**Interior Build-out**		150	16-Jun-27	18-Jan-28
664	**1st Floor Build-out :**		130	16-Jun-27	17-Dec-27
665	**Office Space -101 thru 112**		116	18-Jun-27	03-Dec-27
666	**Rough-ins**		40	18-Jun-27	13-Aug-27
667	010-LAYO-0906	Layout Framing / MEP O/H - Office Space 101-112 - Bldg	2	18-Jun-27	21-Jun-27
668	010-HVAC-0907	HVAC O/H Rgh-in	6	22-Jun-27	29-Jun-27
669	010-ELEC-0908	Elec O/H Rgh-in	4	30-Jun-27	06-Jul-27
670	010-PLUM-0909	Plumbing O/H Rgh-in	3	07-Jul-27	09-Jul-27
671	010-SPKL-0910	Fire Spklr O/H Rgh-in	3	12-Jul-27	14-Jul-27
672	010-FRAM-0911	Frame Walls	5	15-Jul-27	21-Jul-27

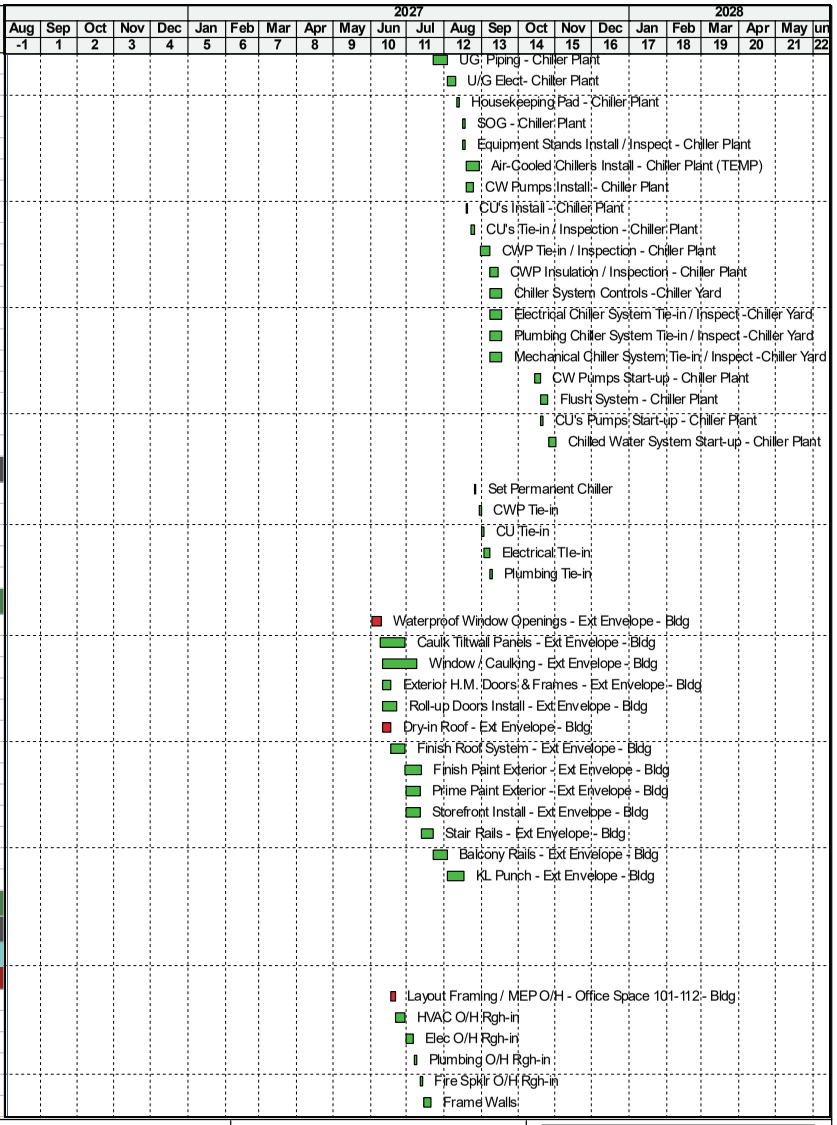

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
673	081-DOOR-0912	Door Frames	2	22-Jul-27	23-Jul-27
674	014-CMUI-0913	CMU Insulate / Furring & Inspection	2	26-Jul-27	27-Jul-27
675	014-HVAC-0914	HVAC Rgh-in Inspection	3	28-Jul-27	30-Jul-27
676	014-SPKL-0915	Fire Spklr Rgh-in Inspection	3	02-Aug-27	04-Aug-27
677	010-ELEC-0916	Elec Wall Rgh-in	3	05-Aug-27	09-Aug-27
678	014-ELEC-0917	Elec Rgh-in Inspection	3	10-Aug-27	12-Aug-27
679	014-FRAM-0918	Wall Framing Inspection	1	13-Aug-27	13-Aug-27
680	**Finishes**		76	16-Aug-27	03-Dec-27
681	092-DRYW-0664	Hang Drywall / Inspect	4	16-Aug-27	19-Aug-27
682	092-FINI-0665	Finish Drywall Walls	5	20-Aug-27	26-Aug-27
683	081-DOOR-0666	Doors / Trim	2	27-Aug-27	30-Aug-27
684	099-PRIM-0667	Prime Paint	2	31-Aug-27	01-Sep-27
685	010-ACTG-0668	ACT Grid	4	02-Sep-27	08-Sep-27
686	010-MECH-0920	Mechanical Trim-out	3	02-Sep-27	07-Sep-27
687	010-ELEC-0921	Electrical Trim-out	3	08-Sep-27	10-Sep-27
688	224-MEPF-0671	MEPF Grid Fixtures	4	09-Sep-27	14-Sep-27
689	211-SPRI-0922	Fire Sprinkler Trim-out	3	13-Sep-27	15-Sep-27
690	010-PLUM-0923	Plumbing Trim-out	3	16-Sep-27	20-Sep-27
691	010-HVAC-0669	HVAC Start-up — Office Space 101-112 L1 — Bldg	1	20-Oct-27	20-Oct-27
692	010-FLOO-0670	Flooring	4	21-Oct-27	26-Oct-27
693	014-MECH-0924	Mechanical Final Inspection	3	21-Oct-27	25-Oct-27
694	014-ELEC-0925	Electrical Final Inspection	3	26-Oct-27	28-Oct-27
695	099-FINI-0672	Finish Paint	2	27-Oct-27	28-Oct-27
696	010-ACTT-0673	ACT Tiles	3	29-Oct-27	02-Nov-27
697	014-SPRI-0926	Fire Sprinkler Final Inspection	3	29-Oct-27	02-Nov-27
698	014-PLUM-0927	Plumbing Final Inspection	3	29-Oct-27	02-Nov-27
699	085-WIND-0674	Window Shades	2	03-Nov-27	04-Nov-27
700	101-SIGN-0675	Signage	1	05-Nov-27	05-Nov-27
701	064-KITC-0677	Kitchen Cabinets/Sinks.	3	08-Nov-27	10-Nov-27
702	010-APPL-0678	Appliances	1	12-Nov-27	12-Nov-27
703	010-CLEA-0679	Final Cleaning	2	15-Nov-27	16-Nov-27
704	010-OFFI-0676	Office Furniture (KL) 1st Floor	12	17-Nov-27	03-Dec-27
705	010-KLPU-0680	KL Punch-out *	5	17-Nov-27	23-Nov-27
706	**Lobby / Corridors**		122	16-Jun-27	09-Dec-27
707	**Rough-ins**		44	16-Jun-27	17-Aug-27
708	010-LAYO-0755	Layout Framing / MEP O/H - Lobby / Corridors - Bldg	2	16-Jun-27	18-Jun-27
709	010-HVAC-0756	HVAC O/H Rgh-in	6	18-Jun-27	25-Jun-27
710	010-ELEC-0757	Elec O/H Rgh-in	4	28-Jun-27	01-Jul-27
711	010-PLUM-0758	Plumbing O/H Rgh-in	3	02-Jul-27	07-Jul-27
712	010-SPKL-0759	Fire Spklr O/H Rgh-in	4	08-Jul-27	13-Jul-27
713	010-FRAM-0760	Frame Walls	5	14-Jul-27	20-Jul-27
714	081-DOOR-0761	Door Frames	3	21-Jul-27	23-Jul-27
715	014-CMUI-0762	CMU Insulate / Furring & Inspection	3	26-Jul-27	28-Jul-27
716	014-HVAC-0763	HVAC Rgh-in Inspection	3	29-Jul-27	02-Aug-27
717	014-SPKL-0764	Fire Spklr Rgh-in Inspection	3	03-Aug-27	05-Aug-27
718	010-ELEC-0765	Elec Wall Rgh-in	3	06-Aug-27	10-Aug-27
719	014-ELEC-0766	Elec Rgh-in Inspection	3	11-Aug-27	13-Aug-27
720	014-FRAM-0767	Wall Framing Inspection	2	16-Aug-27	17-Aug-27
721	**Finishes**		76	20-Aug-27	09-Dec-27

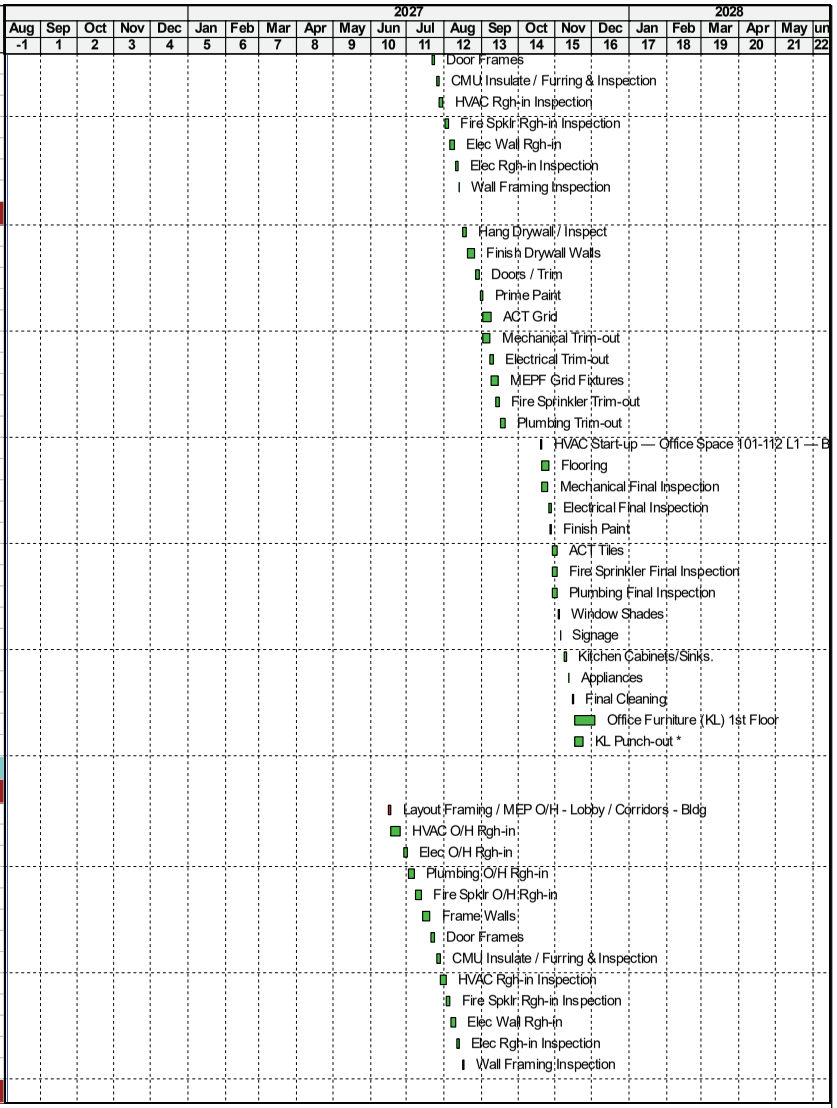

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
722	092-DRYW-0740	Hang Drywall / Inspect	3	20-Aug-27	24-Aug-27
723	092-FINI-0741	Finish Drywall Walls	4	25-Aug-27	30-Aug-27
724	099-PRIM-0743	Prime Paint	2	31-Aug-27	01-Sep-27
725	010-ACTG-0744	ACT Grid	3	02-Sep-27	07-Sep-27
726	010-MECH-0928	Mechanical Trim-out	3	02-Sep-27	07-Sep-27
727	224-MEPF-0747	MEPF Grid Fixtures	3	08-Sep-27	10-Sep-27
728	010-ELEC-0929	Electrical Trim-out	3	08-Sep-27	10-Sep-27
729	211-SPRI-0930	Fire Sprinkler Trim-out	3	13-Sep-27	15-Sep-27
730	010-PLUM-0931	Plumbing Trim-out	3	16-Sep-27	20-Sep-27
731	010-HVAC-0745	HVAC Start-up — Lobby / Corridors L1 — Bldg	1	21-Oct-27	21-Oct-27
732	010-FLOO-0746	Flooring	4	22-Oct-27	27-Oct-27
733	014-MECH-0932	Mechanical Final Inspection	3	22-Oct-27	26-Oct-27
734	014-ELEC-0933	Electrical Final Inspection	3	27-Oct-27	29-Oct-27
735	081-DOOR-0742	Doors / Trim	3	28-Oct-27	01-Nov-27
736	014-SPRI-0934	Fire Sprinkler Final Inspection	3	01-Nov-27	03-Nov-27
737	099-FINI-0748	Finish Paint	2	02-Nov-27	03-Nov-27
738	010-ACTT-0749	ACT Tiles	3	04-Nov-27	08-Nov-27
739	014-PLUM-0935	Plumbing Final Inspection	3	04-Nov-27	08-Nov-27
740	085-WIND-0750	Windows Shades	3	09-Nov-27	12-Nov-27
741	101-SIGN-0751	Signage	1	15-Nov-27	15-Nov-27
742	010-CLEA-0753	Final Cleaning	3	15-Nov-27	17-Nov-27
743	010-OFFI-0752	Office Furniture	10	18-Nov-27	02-Dec-27
744	010-KLPU-0754	KL Punch-out	5	03-Dec-27	09-Dec-27
745	**Fitness Rooms - GYM -126**		111	18-Jun-27	26-Nov-27
746	**Rough-ins**		40	18-Jun-27	13-Aug-27
747	010-LAYO-0819	Layout Framing / MEP O/H - Fitness Rooms GYM 126 - Bldg	2	18-Jun-27	21-Jun-27
748	010-HVAC-0820	HVAC O/H Rgh-in	6	22-Jun-27	29-Jun-27
749	010-ELEC-0821	Elec O/H Rgh-in	4	30-Jun-27	06-Jul-27
750	010-PLUM-0822	Plumbing O/H Rgh-in	3	07-Jul-27	09-Jul-27
751	010-SPKL-0823	Fire Spklr O/H Rgh-in	4	12-Jul-27	15-Jul-27
752	010-FRAM-0824	Frame Walls	4	16-Jul-27	21-Jul-27
753	081-DOOR-0825	Door Frames	2	22-Jul-27	23-Jul-27
754	014-CMUI-0826	CMU Insulate / Furring & Inspection	2	26-Jul-27	27-Jul-27
755	014-HVAC-0827	HVAC Rgh-in Inspection	3	28-Jul-27	30-Jul-27
756	014-SPKL-0828	Fire Spklr Rgh-in Inspection	3	02-Aug-27	04-Aug-27
757	010-ELEC-0829	Elec Wall Rgh-in	3	05-Aug-27	09-Aug-27
758	014-ELEC-0830	Elec Rgh-in Inspection	3	10-Aug-27	12-Aug-27
759	014-FRAM-0831	Wall Framing Inspection	1	13-Aug-27	13-Aug-27
760	**Finishes**		71	16-Aug-27	26-Nov-27
761	085-INTE-0800	Interior Windows	3	16-Aug-27	18-Aug-27
762	084-INTE-0801	Interior storefront Doors	2	19-Aug-27	20-Aug-27
763	092-DRYW-0802	Hang Drywall / Inspect	3	25-Aug-27	27-Aug-27
764	092-FINI-0803	Finish Drywall Walls	3	30-Aug-27	01-Sep-27
765	099-PRIM-0805	Prime Paint	2	02-Sep-27	03-Sep-27
766	010-ACTG-0806	ACT Grid	3	07-Sep-27	09-Sep-27
767	010-MECH-0936	Mechanical Trim-out	3	07-Sep-27	09-Sep-27
768	224-MEPF-0809	MEPF Grid Fixtures	3	10-Sep-27	14-Sep-27
769	010-ELEC-0937	Electrical Trim-out	3	10-Sep-27	14-Sep-27
770	211-SPRI-0938	Fire Sprinkler Trim-out	3	15-Sep-27	17-Sep-27

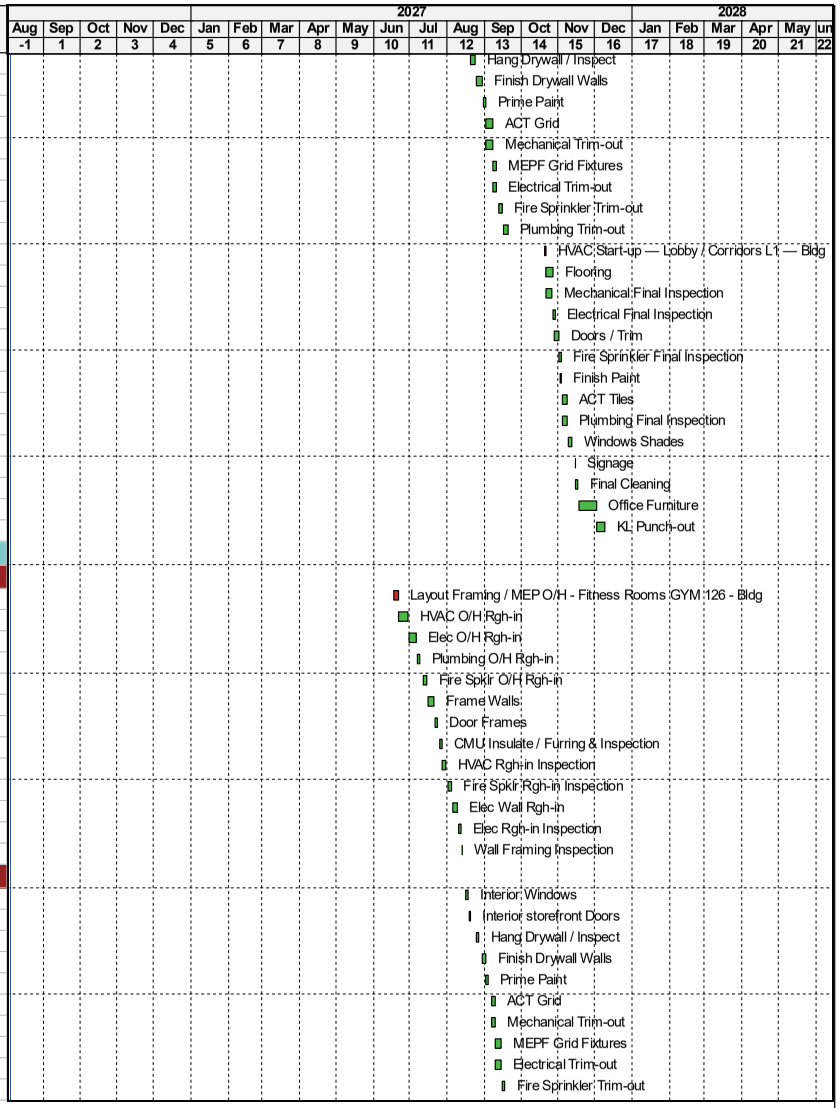

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
771	010-PLUM-0939	Plumbing Trim-out	3	20-Sep-27	22-Sep-27
772	010-HVAC-0807	HVAC Start-up — Fitness Room / GYM 126 L1 — Bldg	1	22-Oct-27	22-Oct-27
773	010-FLOO-0808	Flooring	4	25-Oct-27	28-Oct-27
774	014-MECH-0940	Mechanical Final Inspection	3	25-Oct-27	27-Oct-27
775	014-ELEC-0941	Electrical Final Inspection	3	28-Oct-27	01-Nov-27
776	081-DOOR-0804	Doors / Trim	2	29-Oct-27	01-Nov-27
777	099-FINI-0810	Finish Paint	2	02-Nov-27	03-Nov-27
778	014-SPRI-0942	Fire Sprinkler Final Inspection	3	02-Nov-27	04-Nov-27
779	010-ACTT-0811	ACT Tiles	2	04-Nov-27	05-Nov-27
780	010-MIRR-0812	Install Wall Mirrors	1	08-Nov-27	08-Nov-27
781	101-SIGN-0813	Signage	1	09-Nov-27	09-Nov-27
782	014-PLUM-0943	Plumbing Final Inspection	3	09-Nov-27	12-Nov-27
783	010-OFFI-0814	Fitness Equipment	2	10-Nov-27	12-Nov-27
784	064-KITC-0815	Cabinets/Sinks.	2	15-Nov-27	16-Nov-27
785	010-CLEA-0817	Final Cleaning	2	17-Nov-27	18-Nov-27
786	010-KLPU-0818	KL Punch-out	5	19-Nov-27	26-Nov-27
787	**Break Room / Kitchen 125A 125**		120	22-Jun-27	13-Dec-27
788	**Rough-ins**		38	22-Jun-27	13-Aug-27
789	010-LAYO-0788	Layout Framing / MEP O/H - Break Room / Kitchen 125A - Bldg	2	22-Jun-27	23-Jun-27
790	010-HVAC-0789	HVAC O/H Rgh-in	6	24-Jun-27	01-Jul-27
791	010-ELEC-0790	Elec O/H Rgh-in	4	02-Jul-27	08-Jul-27
792	010-PLUM-0791	Plumbing O/H Rgh-in	3	09-Jul-27	13-Jul-27
793	010-SPKL-0792	Fire Spklr O/H Rgh-in	4	14-Jul-27	19-Jul-27
794	010-FRAM-0793	Frame Walls	4	20-Jul-27	23-Jul-27
795	081-DOOR-0794	Door Frames	2	26-Jul-27	27-Jul-27
796	014-HVAC-0795	HVAC Rgh-in Inspection	3	28-Jul-27	30-Jul-27
797	014-SPKL-0796	Fire Spklr Rgh-in Inspection	3	02-Aug-27	04-Aug-27
798	010-ELEC-0797	Elec Wall Rgh-in	3	05-Aug-27	09-Aug-27
799	014-ELEC-0798	Elec Rgh-in Inspection	3	10-Aug-27	12-Aug-27
800	014-FRAM-0799	Wall Framing Inspection	1	13-Aug-27	13-Aug-27
801	**Finishes**		82	16-Aug-27	13-Dec-27
802	085-INTE-0768	Interior Windows	2	16-Aug-27	17-Aug-27
803	084-INTE-0769	Interior storefront Doors	2	18-Aug-27	19-Aug-27
804	092-DRYW-0770	Hang Drywall / Inspect	2	30-Aug-27	31-Aug-27
805	092-FINI-0771	Finish Drywall Walls	3	01-Sep-27	03-Sep-27
806	099-PRIM-0773	Prime Paint	2	07-Sep-27	08-Sep-27
807	010-ACTG-0774	ACT Grid	2	09-Sep-27	10-Sep-27
808	010-MECH-0944	Mechanical Trim-out	3	09-Sep-27	13-Sep-27
809	010-MEPF-0777	MEPF Trim-Out	3	13-Sep-27	15-Sep-27
810	010-ELEC-0945	Electrical Trim-out	3	14-Sep-27	16-Sep-27
811	224-MEPF-0778	MEPF Grid Fixtures	3	16-Sep-27	20-Sep-27
812	211-SPRI-0946	Fire Sprinkler Trim-out	3	17-Sep-27	21-Sep-27
813	010-PLUM-0947	Plumbing Trim-out	3	22-Sep-27	24-Sep-27
814	010-HVAC-0775	HVAC Start-up — Break Room / Kitchen 125AL1 — Bldg	1	25-Oct-27	25-Oct-27
815	010-FLOO-0776	Flooring	2	26-Oct-27	27-Oct-27
816	014-MECH-0948	Mechanical Final Inspection	3	26-Oct-27	28-Oct-27
817	081-DOOR-0772	Doors / Trim	2	28-Oct-27	29-Oct-27
818	105-FOLD-0779	Folding/mechanical wall/w track	5	28-Oct-27	03-Nov-27
819	014-ELEC-0949	Electrical Final Inspection	3	29-Oct-27	02-Nov-27

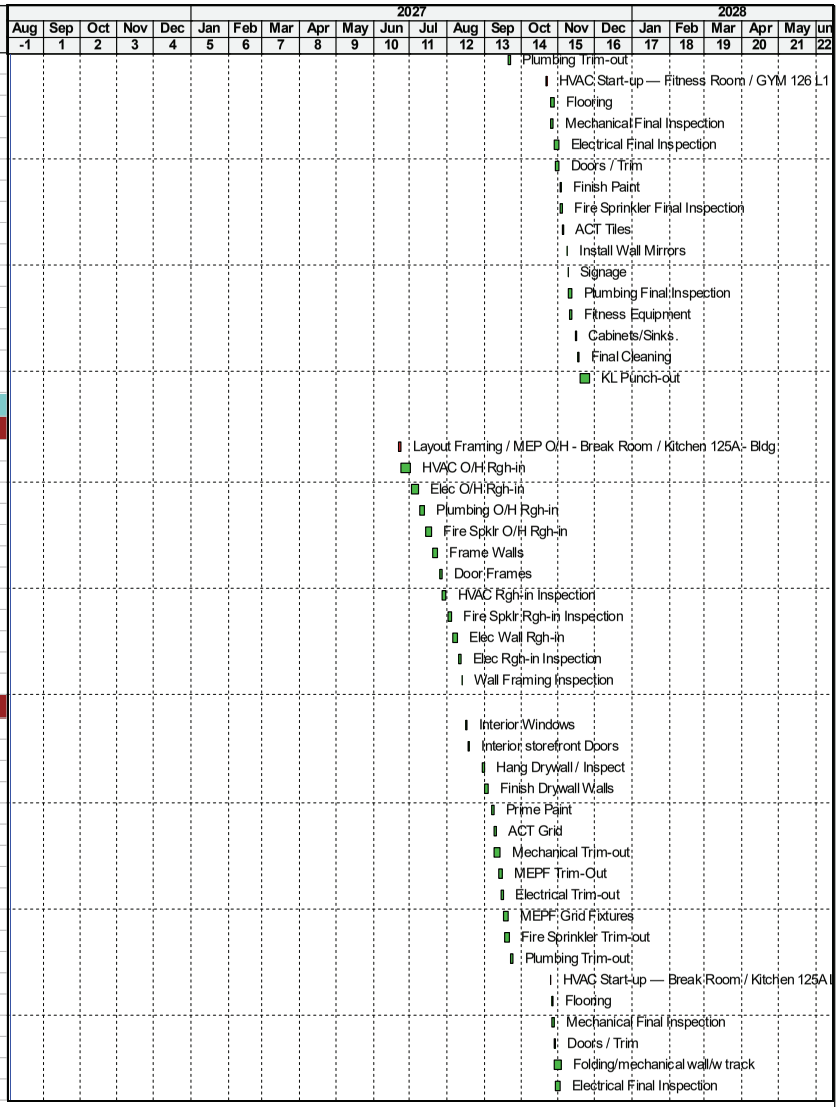

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
820	014-SPRI-0950	Fire Sprinkler Final Inspection	3	03-Nov-27	05-Nov-27
821	099-FINI-0780	Finish Paint	2	04-Nov-27	05-Nov-27
822	010-ACTT-0781	ACT Tiles	2	08-Nov-27	09-Nov-27
823	101-SIGN-0782	Signage	1	10-Nov-27	10-Nov-27
824	010-OFFI-0783	Office Furniture	10	12-Nov-27	26-Nov-27
825	014-PLUM-0951	Plumbing Final Inspection	3	15-Nov-27	17-Nov-27
826	064-KITC-0784	Kitchen Cabinets/Sinks.	3	29-Nov-27	01-Dec-27
827	010-APPL-0785	Appliances	1	02-Dec-27	02-Dec-27
828	010-CLEA-0786	Final Cleaning	2	03-Dec-27	06-Dec-27
829	010-KLPU-0787	KL Punch-out	5	07-Dec-27	13-Dec-27
830	**Restrooms 127/128**		114	24-Jun-27	07-Dec-27
831	**Rough-ins**		39	24-Jun-27	18-Aug-27
832	010-LAYO-0844	Layout Framing / MEP O/H - Restrooms 127/128 - Bldg	2	24-Jun-27	25-Jun-27
833	010-HVAC-0845	HVAC O/H Rgh-in	6	28-Jun-27	06-Jul-27
834	010-ELEC-0846	Elec O/H Rgh-in	4	07-Jul-27	12-Jul-27
835	010-PLUM-0847	Plumbing O/H Rgh-in	3	13-Jul-27	15-Jul-27
836	010-SPKL-0848	Fire Spklr O/H Rgh-in	4	16-Jul-27	21-Jul-27
837	010-FRAM-0849	Frame Walls	5	22-Jul-27	28-Jul-27
838	081-DOOR-0850	Door Frames	2	29-Jul-27	30-Jul-27
839	014-HVAC-0851	HVAC Rgh-in Inspection	3	02-Aug-27	04-Aug-27
840	014-SPKL-0852	Fire Spklr Rgh-in Inspection	3	05-Aug-27	09-Aug-27
841	010-ELEC-0853	Elec Wall Rgh-in	3	10-Aug-27	12-Aug-27
842	014-ELEC-0854	Elec Rgh-in Inspection	3	13-Aug-27	17-Aug-27
843	014-FRAM-0855	Wall Framing Inspection	1	18-Aug-27	18-Aug-27
844	**Finishes**		66	01-Sep-27	07-Dec-27
845	092-DRYW-0832	Hang Drywall / Inspect	4	01-Sep-27	07-Sep-27
846	092-FINI-0833	Finish Drywall Walls/Ceilings	3	08-Sep-27	10-Sep-27
847	081-DOOR-0834	Doors / Trim	2	13-Sep-27	14-Sep-27
848	099-PRIM-0835	Prime Paint	2	15-Sep-27	16-Sep-27
849	010-MECH-0952	Mechanical Trim-out	3	17-Sep-27	21-Sep-27
850	010-ELEC-0953	Electrical Trim-out	3	22-Sep-27	24-Sep-27
851	211-SPRI-0954	Fire Sprinkler Trim-out	3	27-Sep-27	29-Sep-27
852	010-PLUM-0955	Plumbing Trim-out	3	30-Sep-27	04-Oct-27
853	093-FLOO-0836	Flooring (Floor and Wall Tiles)	5	26-Oct-27	01-Nov-27
854	010-MEPF-0837	MEPF Trim-Out	4	02-Nov-27	05-Nov-27
855	010-HVAC-0838	HVAC Start-up — Restrooms 127/128 L1 — Bldg	3	08-Nov-27	10-Nov-27
856	099-FINI-0839	Finish Paint	2	12-Nov-27	15-Nov-27
857	014-MECH-0956	Mechanical Final Inspection	3	12-Nov-27	16-Nov-27
858	010-BATH-0840	Install bathroom accessories/partitons	5	16-Nov-27	22-Nov-27
859	014-ELEC-0957	Electrical Final Inspection	3	17-Nov-27	19-Nov-27
860	014-SPRI-0958	Fire Sprinkler Final Inspection	3	22-Nov-27	24-Nov-27
861	101-SIGN-0841	Signage	1	23-Nov-27	23-Nov-27
862	010-CLEA-0842	Final Cleaning	2	24-Nov-27	26-Nov-27
863	014-PLUM-0959	Plumbing Final Inspection	3	26-Nov-27	30-Nov-27
864	010-KLPU-0843	KL Punch-out	5	01-Dec-27	07-Dec-27
865	**Fire Supply Room 120**		115	28-Jun-27	10-Dec-27
866	**Rough-ins**		40	28-Jun-27	23-Aug-27
867	010-LAYO-0893	Layout Framing / MEP O/H - Fire Supply Room 120 - Bldg	2	28-Jun-27	29-Jun-27
868	010-HVAC-0894	HVAC O/H Rgh-in	6	30-Jun-27	08-Jul-27

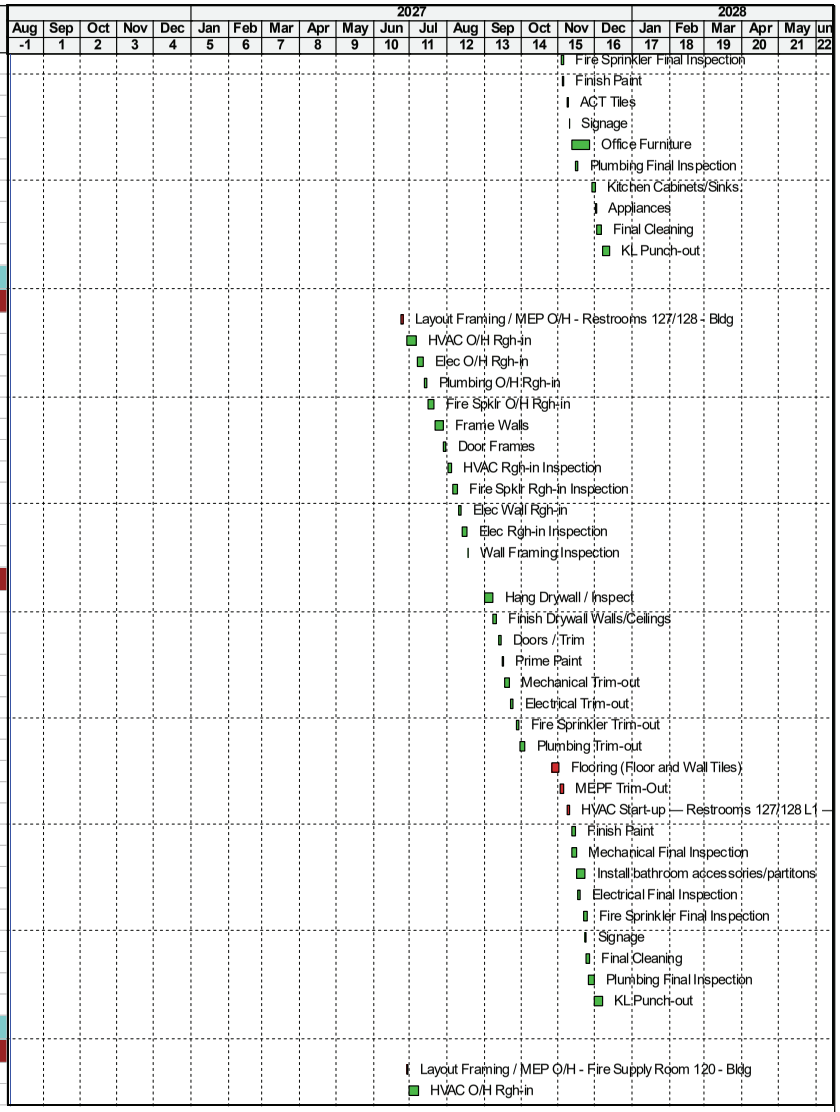

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
869	010-ELEC-0895	Elec O/H Rgh-in	4	09-Jul-27	14-Jul-27
870	010-PLUM-0896	Plumbing O/H Rgh-in	3	15-Jul-27	19-Jul-27
871	010-SPKL-0897	Fire Spklr O/H Rgh-in	4	20-Jul-27	23-Jul-27
872	010-FRAM-0898	Frame Walls	3	26-Jul-27	28-Jul-27
873	081-DOOR-0899	Door Frames	2	29-Jul-27	30-Jul-27
874	014-CMUI-0900	CMU Insulate / Furring & Inspection	3	02-Aug-27	04-Aug-27
875	014-HVAC-0901	HVAC Rgh-in Inspection	3	05-Aug-27	09-Aug-27
876	014-SPKL-0902	Fire Spklr Rgh-in Inspection	3	10-Aug-27	12-Aug-27
877	010-ELEC-0903	Elec Wall Rgh-in	3	13-Aug-27	17-Aug-27
878	014-ELEC-0904	Elec Rgh-in Inspection	3	18-Aug-27	20-Aug-27
879	014-FRAM-0905	Wall Framing Inspection	1	23-Aug-27	23-Aug-27
880	**Finishes**		65	08-Sep-27	10-Dec-27
881	092-DRYW-0880	Hang Drywall / Inspect	4	08-Sep-27	13-Sep-27
882	092-FINI-0881	Finish Drywall Walls	3	14-Sep-27	16-Sep-27
883	081-DOOR-0882	Doors / Trim	2	17-Sep-27	20-Sep-27
884	099-PRIM-0883	Prime Paint	2	21-Sep-27	22-Sep-27
885	099-PAIN-0884	Final Paint Exposed Ceiling/Deck	2	23-Sep-27	24-Sep-27
886	010-MECH-0960	Mechanical Trim-out	3	23-Sep-27	27-Sep-27
887	262-ACOU-0885	Acoustical wall panels	3	27-Sep-27	29-Sep-27
888	010-ELEC-0961	Electrical Trim-out	3	28-Sep-27	30-Sep-27
889	010-MEPF-0887	MEPF Trim-Out	3	30-Sep-27	04-Oct-27
890	211-SPRI-0962	Fire Sprinkler Trim-out	3	01-Oct-27	05-Oct-27
891	010-PLUM-0963	Plumbing Trim-out	3	06-Oct-27	08-Oct-27
892	010-HVAC-0886	HVAC Start-up — Fire Supply Room 120 L1 — Bldg	3	08-Nov-27	10-Nov-27
893	010-FLOO-0888	Flooring (Gym Flooring)	5	12-Nov-27	18-Nov-27
894	014-MECH-0964	Mechanical Final Inspection	3	12-Nov-27	16-Nov-27
895	014-ELEC-0965	Electrical Final Inspection	3	17-Nov-27	19-Nov-27
896	099-FINI-0889	Finish Paint	2	19-Nov-27	22-Nov-27
897	014-SPRI-0966	Fire Sprinkler Final Inspection	3	22-Nov-27	24-Nov-27
898	101-SIGN-0890	Signage	1	23-Nov-27	23-Nov-27
899	010-CLEA-0891	Final Cleaning	3	24-Nov-27	29-Nov-27
900	014-PLUM-0967	Plumbing Final Inspection	3	01-Dec-27	03-Dec-27
901	010-KLPU-0892	KL Punch-out	5	06-Dec-27	10-Dec-27
902	**Electrical Room :190**		53	30-Jun-27	14-Sep-27
903	010-LAYO-0699	Layout Framing / MEP O/H - Electrical Room 190 - Bldg	2	30-Jun-27	01-Jul-27
904	010-HOUS-0700	Housekeeping Pads	2	02-Jul-27	06-Jul-27
905	010-MEPF-0701	MEPF o/h and wall Rgh-in	4	07-Jul-27	12-Jul-27
906	061-FRAM-0702	Frame walls (Backing for Equipment)	3	13-Jul-27	15-Jul-27
907	081-DOOR-0703	Door Frames	2	16-Jul-27	19-Jul-27
908	014-CMUI-0704	CMU Insulate / Furring & Inspection	3	20-Jul-27	22-Jul-27
909	092-FINI-0705	Hang and Finish Drywall walls	3	23-Jul-27	27-Jul-27
910	099-PRIM-0706	Prime Paint/1st Coat	1	28-Jul-27	28-Jul-27
911	010-PPXX-0707	P & P	3	29-Jul-27	02-Aug-27
912	262-ELEC-0708	Install Elec Panels / S-Gear	15	03-Aug-27	23-Aug-27
913	260-ELEC-0710	Electrical Wire Pull / Terminate	3	05-Aug-27	09-Aug-27
914	260-SECO-0711	Secondary Wire Pull / Terminate	3	10-Aug-27	12-Aug-27
915	014-TEMP-0712	Temp For Testing Inspection	2	13-Aug-27	16-Aug-27
916	081-DOOR-0709	Doors/Trim	2	24-Aug-27	25-Aug-27
917	010-ELEC-0714	Electrical System Start-up	2	24-Aug-27	25-Aug-27

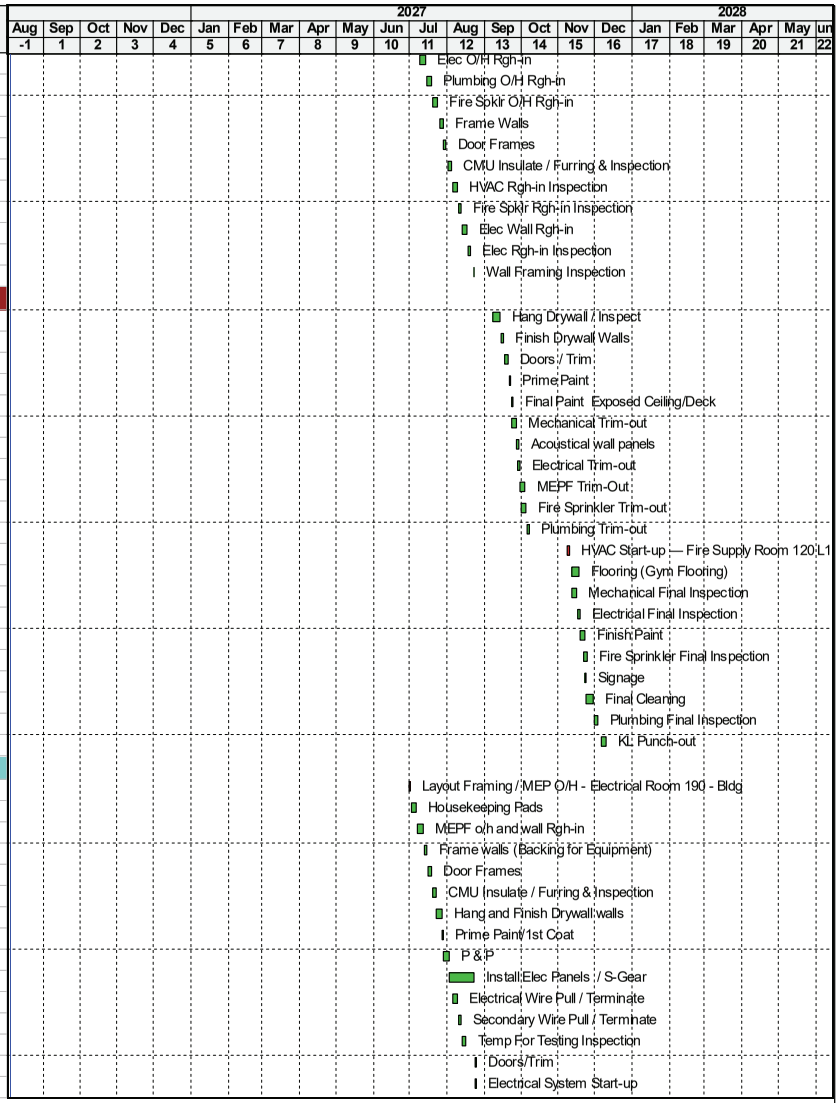

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
918	010-MEPF-0715	MEPF Trim Out	3	26-Aug-27	30-Aug-27
919	010-SEAL-0716	Seal Concrete Floor	1	31-Aug-27	31-Aug-27
920	099-PAIN-0717	Final Paint	2	01-Sep-27	02-Sep-27
921	101-SIGN-0718	Signage	1	03-Sep-27	03-Sep-27
922	010-CLEA-0719	Final Cleaning	1	07-Sep-27	07-Sep-27
923	010-KLPU-0720	KL Punch Out	5	08-Sep-27	14-Sep-27
924	**Mechanical Rooms:180**		47	02-Jul-27	08-Sep-27
925	010-LAYO-0721	Layout Framing / MEP O/H - Mechanical Room 180 - Bldg	2	02-Jul-27	06-Jul-27
926	010-HOUS-0722	Housekeeping Pads	2	07-Jul-27	08-Jul-27
927	010-MEPF-0723	MEPF O/H and Wall Rgh-in	4	09-Jul-27	14-Jul-27
928	061-FRAM-0724	Frame walls (Backing for Equipment)	2	15-Jul-27	16-Jul-27
929	081-DOOR-0725	Door Frames	1	19-Jul-27	19-Jul-27
930	014-CMUI-0726	CMU Insulate / Furring & Inspection	2	20-Jul-27	21-Jul-27
931	092-FINI-0727	Finish Drywall walls	2	22-Jul-27	23-Jul-27
932	099-PRIM-0728	Prime Paint/1st Coat	2	26-Jul-27	27-Jul-27
933	237-AHUE-0729	AHU Equip Install	5	28-Jul-27	03-Aug-27
934	230-AHUC-0730	AHU System Controls	5	04-Aug-27	10-Aug-27
935	237-AHUM-0731	AHU MEP Tie-ins	3	11-Aug-27	13-Aug-27
936	237-AHUS-0732	AHU Syst Start-up	2	16-Aug-27	17-Aug-27
937	081-DOOR-0733	Door/Trim	2	18-Aug-27	19-Aug-27
938	010-MEPF-0734	MEPF Trim Out	3	20-Aug-27	24-Aug-27
939	010-SEAL-0735	Seal Concrete Floor	1	25-Aug-27	25-Aug-27
940	099-PAIN-0736	Final Paint	2	26-Aug-27	27-Aug-27
941	101-SIGN-0737	Signage	1	30-Aug-27	30-Aug-27
942	010-CLEA-0738	Final Cleaning	1	31-Aug-27	31-Aug-27
943	010-KLPU-0739	KL Punch Out	5	01-Sep-27	08-Sep-27
944	**Elevator Build Out 1-02**		64	23-Jul-27	21-Oct-27
945	Elev-1-02-1000	Sill angle and hoist beam installation	2	23-Jul-27	26-Jul-27
946	Elev-1-02-1010	Guide rail bracket embedments / anchorage	2	27-Jul-27	28-Jul-27
947	Elev-1-02-1020	Electrical conduit and pull boxes rough-in	3	29-Jul-27	02-Aug-27
948	Elev-1-02-1030	Main power feed and disconnect installation	2	03-Aug-27	04-Aug-27
949	Elev-1-02-1040	Ventilation rough-in for machine room or shaft	1	05-Aug-27	05-Aug-27
950	Elev-1-02-1050	Temporary hoisting equipment setup	1	06-Aug-27	06-Aug-27
951	**Elevator - Rough In**		0		
952	**Elevator - Equipment Installation**		12	29-Jul-27	13-Aug-27
953	Elev-1-02-1060	Guide Rail Installation & Alignment	3	29-Jul-27	02-Aug-27
954	Elev-1-02-1080	Car Sling & Platform Assembly	3	03-Aug-27	05-Aug-27
955	Elev-1-02-1110	Counterweight Assembly (if traction)	2	03-Aug-27	04-Aug-27
956	Elev-1-02-1090	Cab Enclosure Installation	2	06-Aug-27	09-Aug-27
957	Elev-1-02-1070	Hydraulic Cylinder / Piston Install	2	09-Aug-27	10-Aug-27
958	Elev-1-02-1100	Door Operator & Hall Door Frame Install	3	10-Aug-27	12-Aug-27
959	Elev-1-02-1120	Rope / Cable or Hydraulic Line Install	2	11-Aug-27	12-Aug-27
960	Elev-1-02-1130	Buffer Installation in Pit	1	11-Aug-27	11-Aug-27
961	Elev-1-02-1140	Governor & Safety Gear Installation	1	13-Aug-27	13-Aug-27
962	**Elevator - Electrical Controls**		9	16-Aug-27	26-Aug-27
963	Elev-1-02-1150	Machine / Controller Installation	2	16-Aug-27	17-Aug-27
964	Elev-1-02-1160	Wiring: Motor, Controller & Selector	3	18-Aug-27	20-Aug-27
965	Elev-1-02-1170	Car Op. Panel & Hall Call Buttons	2	23-Aug-27	24-Aug-27
966	Elev-1-02-1190	Safety Circuit Wiring	2	23-Aug-27	24-Aug-27

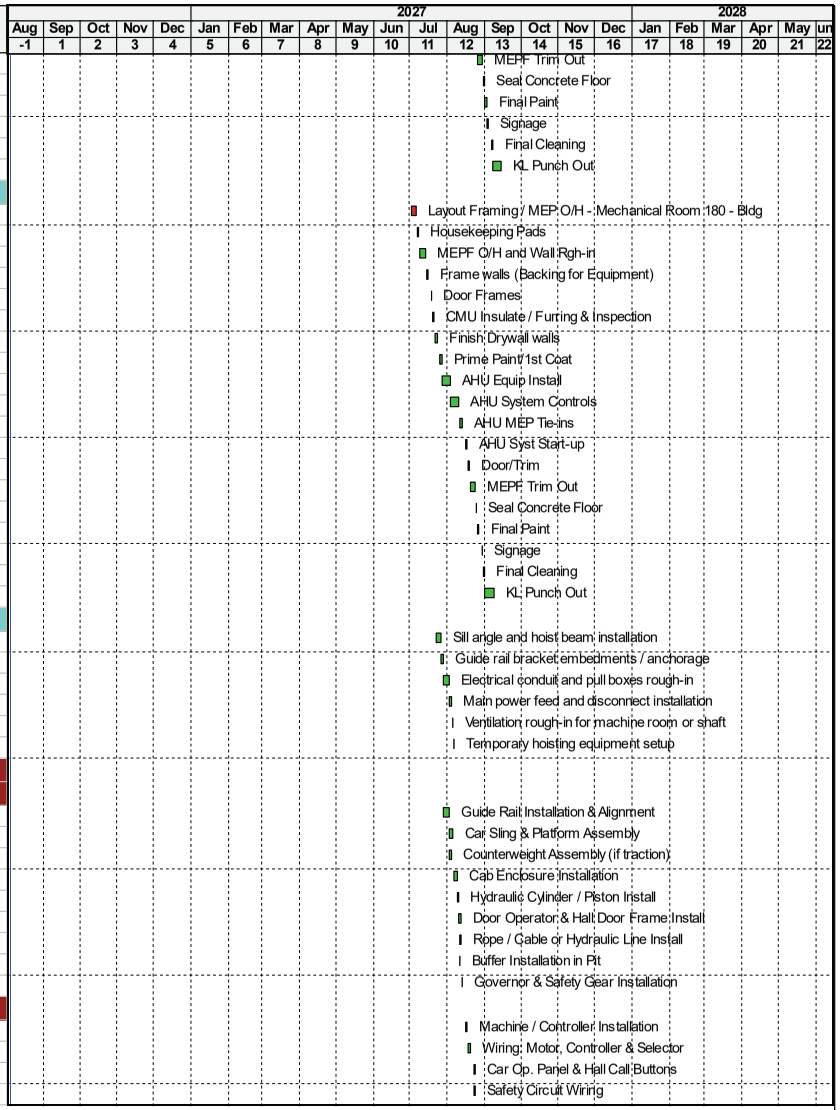

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
967	Elev-1-02-1180	Position Indicators & Displays	1	25-Aug-27	25-Aug-27
968	Elev-1-02-1200	Emergency Lighting & Phone Install	1	25-Aug-27	25-Aug-27
969	Elev-1-02-1210	Fire Service & Access Control Integration	2	25-Aug-27	26-Aug-27
970	**Elevator - Finishes**		9	13-Aug-27	25-Aug-27
971	Elev-1-02-1250	Door Sill & Threshold Finishing	1	13-Aug-27	13-Aug-27
972	Elev-1-02-1260	Hoistway Door Frames & Entrance Trim	2	16-Aug-27	17-Aug-27
973	Elev-1-02-1270	Machine Room Finishing & Security	1	18-Aug-27	18-Aug-27
974	Elev-1-02-1220	Cab Interior Finishes (Panels, Rails, Mirrors)	2	23-Aug-27	24-Aug-27
975	Elev-1-02-1240	Cab Floor Covering Installation	1	25-Aug-27	25-Aug-27
976	**Testing and Commissioning**		8	12-Oct-27	21-Oct-27
977	Elev-1-02-1280	Load Testing & Performance Testing	2	12-Oct-27	13-Oct-27
978	Elev-1-02-1290	Safety Device Testing (Governor, Buffers, Gates)	1	14-Oct-27	14-Oct-27
979	Elev-1-02-1300	Door Timing & Force Adjustments	1	15-Oct-27	15-Oct-27
980	Elev-1-02-1310	Level Accuracy & Ride Quality Tuning	1	18-Oct-27	18-Oct-27
981	Elev-1-02-1320	AHJ Final Inspection & Witness Test	2	19-Oct-27	20-Oct-27
982	Elev-1-02-1330	State Inspector - Certificate of Occupancy / Operating Permit	1	21-Oct-27	21-Oct-27
983	**MDF / AV / IT 113A**		60	07-Jul-27	29-Sep-27
984	010-LAYO-0681	Layout Framing / MEP O/H - MDF / AV / IT 113A- Bldg	1	07-Jul-27	07-Jul-27
985	010-MEPF-0682	MEPF O/H and Wall Rgh	3	08-Jul-27	12-Jul-27
986	061-FRAM-0683	Frame walls (Backing for Equipment)	3	13-Jul-27	15-Jul-27
987	014-CMUI-0684	CMU Insulate / Furring & Inspection	2	16-Jul-27	19-Jul-27
988	092-FINI-0685	Hang and Finish Drywall walls	5	20-Jul-27	26-Jul-27
989	099-PRIM-0686	Prime Paint/1st Coat	2	27-Jul-27	28-Jul-27
990	010-ACTG-0687	ACT GRID	4	29-Jul-27	03-Aug-27
991	010-MEPF-0688	MEPF Trim Out	3	04-Aug-27	06-Aug-27
992	224-MEPF-0689	MEPF Grid Fixtures	3	09-Aug-27	11-Aug-27
993	010-FLOO-0690	Flooring- Concrete sealer/IT pads	2	12-Aug-27	13-Aug-27
994	283-FACP-0691	FACP Equipment Boards	5	16-Aug-27	20-Aug-27
995	260-FACP-0692	FACP Equip / Wire	5	23-Aug-27	27-Aug-27
996	014-FACP-0693	FACP Equip Inspection	5	30-Aug-27	03-Sep-27
997	283-FACP-0694	FACP System Start-up	5	07-Sep-27	13-Sep-27
998	010-ACTT-0695	ACT Tiles	2	14-Sep-27	15-Sep-27
999	099-PAIN-0696	Final Paint	2	16-Sep-27	17-Sep-27
1000	101-SIGN-0697	Signage	1	20-Sep-27	20-Sep-27
1001	010-CLEA-0698	Final Cleaning	2	21-Sep-27	22-Sep-27
1002	010-KLPU-0919	KL Punch	5	23-Sep-27	29-Sep-27
1003	**Back of House 181/193/191 (Chiller/Gen)**		111	08-Jul-27	15-Dec-27
1004	**Rough-ins**		39	08-Jul-27	31-Aug-27
1005	010-LAYO-0867	Layout Framing / MEP O/H - Back of House 181/193/191 - Bldg	2	08-Jul-27	09-Jul-27
1006	010-HVAC-0868	HVAC O/H Rgh-in	6	12-Jul-27	19-Jul-27
1007	010-ELEC-0869	Elec O/H Rgh-in	4	20-Jul-27	23-Jul-27
1008	010-PLUM-0870	Plumbing O/H Rgh-in	3	26-Jul-27	28-Jul-27
1009	010-SPKL-0871	Fire Spklr O/H Rgh-in	4	29-Jul-27	03-Aug-27
1010	010-FRAM-0872	Frame Walls	3	04-Aug-27	06-Aug-27
1011	081-DOOR-0873	Door Frames	2	09-Aug-27	10-Aug-27
1012	014-CMUI-0874	CMU Insulate / Furring & Inspection	2	11-Aug-27	12-Aug-27
1013	014-HVAC-0875	HVAC Rgh-in Inspection	3	13-Aug-27	17-Aug-27
1014	014-SPKL-0876	Fire Spklr Rgh-in Inspection	3	18-Aug-27	20-Aug-27
1015	010-ELEC-0877	Elec Wall Rgh-in	3	23-Aug-27	25-Aug-27

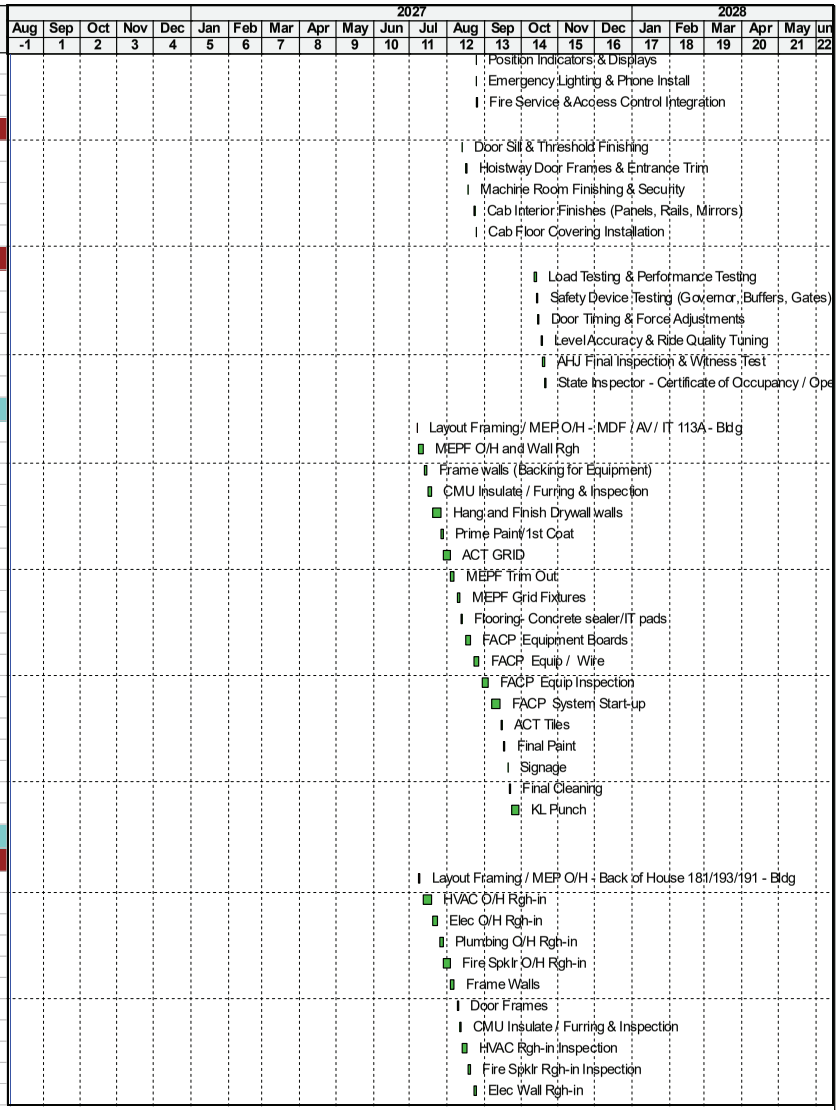

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
1016	014-ELEC-0878	Elec Rgh-in Inspection	3	26-Aug-27	30-Aug-27
1017	014-FRAM-0879	Wall Framing Inspection	1	31-Aug-27	31-Aug-27
1018	**Finishes**		64	14-Sep-27	15-Dec-27
1019	092-DRYW-0856	Hang Drywall / Inspect	4	14-Sep-27	17-Sep-27
1020	092-FINI-0857	Finish Drywall Walls	3	20-Sep-27	22-Sep-27
1021	081-DOOR-0858	Doors / Trim	3	23-Sep-27	27-Sep-27
1022	099-PRIM-0859	Prime Paint	2	28-Sep-27	29-Sep-27
1023	010-ROOF-0860	Install roof hatch (135)	3	30-Sep-27	04-Oct-27
1024	010-MECH-0968	Mechanical Trim-out	3	30-Sep-27	04-Oct-27
1025	010-FLOO-0861	Flooring (Concrete Sealer)	4	05-Oct-27	08-Oct-27
1026	010-ELEC-0969	Electrical Trim-out	3	05-Oct-27	07-Oct-27
1027	211-SPRI-0970	Fire Sprinkler Trim-out	3	08-Oct-27	13-Oct-27
1028	010-PLUM-0971	Plumbing Trim-out	3	14-Oct-27	18-Oct-27
1029	010-HVAC-0862	HVAC Start-up — Back of House 181/191/193 L1 — Bldg	3	08-Nov-27	10-Nov-27
1030	099-FINI-0863	Finish Paint	4	12-Nov-27	17-Nov-27
1031	014-MECH-0972	Mechanical Final Inspection	3	12-Nov-27	16-Nov-27
1032	014-ELEC-0973	Electrical Final Inspection	3	17-Nov-27	19-Nov-27
1033	101-SIGN-0864	Signage	1	18-Nov-27	18-Nov-27
1034	010-CLEA-0865	Final Cleaning	3	19-Nov-27	23-Nov-27
1035	014-SPRI-0974	Fire Sprinkler Final Inspection	3	22-Nov-27	24-Nov-27
1036	014-PLUM-0975	Plumbing Final Inspection	3	06-Dec-27	08-Dec-27
1037	010-KLPU-0866	KL Punch-out	5	09-Dec-27	15-Dec-27
1038	**Maintenance Bays 113 A/B/C/D**		111	12-Jul-27	17-Dec-27
1039	**Rough-ins**		36	12-Jul-27	30-Aug-27
1040	010-LAYO-0976	Layout Framing / MEP O/H - Maint Bay L1 - Bldg	3	12-Jul-27	14-Jul-27
1041	010-HVAC-0977	HVAC O/H Rgh-in - Maint Bay L1 - Bldg	10	15-Jul-27	28-Jul-27
1042	010-ELEC-0978	Elec O/H Rgh-in - Maint Bay L1 - Bldg	8	15-Jul-27	26-Jul-27
1043	010-PLUM-0979	Plumbing O/H Rgh-in - Maint Bay L1 - Bldg	8	15-Jul-27	26-Jul-27
1044	010-SPKL-0980	Fire Spklr O/H Rgh-in - Maint Bay L1 - Bldg	7	15-Jul-27	23-Jul-27
1045	010-FRAM-0981	Frame Walls - Maint Bay L1 - Bldg	8	15-Jul-27	26-Jul-27
1046	010-ELEC-0990	Electrical Ceiling Rgh-in - Maint Bay L1 - Bldg	8	15-Jul-27	26-Jul-27
1047	010-MECH-0995	Mechanical Ceiling Rgh-in - Maint Bay L1 - Bldg	8	15-Jul-27	26-Jul-27
1048	010-SPKL-0996	Fire Spklr Ceiling Rgh-in - Maint Bay L1 - Bldg	8	15-Jul-27	26-Jul-27
1049	014-SPKL-0982	Fire Spklr Rgh-in Inspection - Maint Bay L1 - Bldg	2	26-Jul-27	27-Jul-27
1050	010-ELEC-0984	Elec Wall Rgh-in - Maint Bay L1 - Bldg	8	27-Jul-27	05-Aug-27
1051	010-PLUM-0985	Plumbing Wall Rgh-in - Maint Bay L1 - Bldg	8	27-Jul-27	05-Aug-27
1052	014-ELEC-0991	Electrical Ceiling Inspection - Maint Bay L1 - Bldg	2	27-Jul-27	28-Jul-27
1053	014-MECH-0993	Mechanical Ceiling Inspection - Maint Bay L1 - Bldg	2	27-Jul-27	28-Jul-27
1054	014-SPKL-0994	Fire Spklr Ceiling Inspection - Maint Bay L1 - Bldg	2	27-Jul-27	28-Jul-27
1055	014-HVAC-0983	HVAC Rgh-in Inspection - Maint Bay L1 - Bldg	2	29-Jul-27	30-Jul-27
1056	014-ELEC-0986	Elec Rgh-in Inspection - Maint Bay L1 - Bldg	2	06-Aug-27	09-Aug-27
1057	014-PLUM-0987	Plumbing Rgh-in Inspection - Maint Bay L1 - Bldg	2	06-Aug-27	09-Aug-27
1058	014-FRAM-0988	Wall Framing Inspection - Maint Bay L1 - Bldg	2	10-Aug-27	11-Aug-27
1059	092-DRYW-0997	Hang Drywall Rippers - Maint Bay L1 - Bldg	3	12-Aug-27	16-Aug-27
1060	010-FRAM-0989	Frame Ceilings - Maint Bay L1 - Bldg	8	17-Aug-27	26-Aug-27
1061	014-FRAM-0992	Ceiling Framing Inspection - Maint Bay L1 - Bldg	2	27-Aug-27	30-Aug-27
1062	**Finishes**		88	12-Aug-27	17-Dec-27
1063	092-DRYW-0998	Hang Drywall / Inspect- Maint Bay L1 - Bldg	10	12-Aug-27	25-Aug-27
1064	092-FINI-0999	Finish Drywall Walls - Maint Bay L1 - Bldg	12	26-Aug-27	13-Sep-27

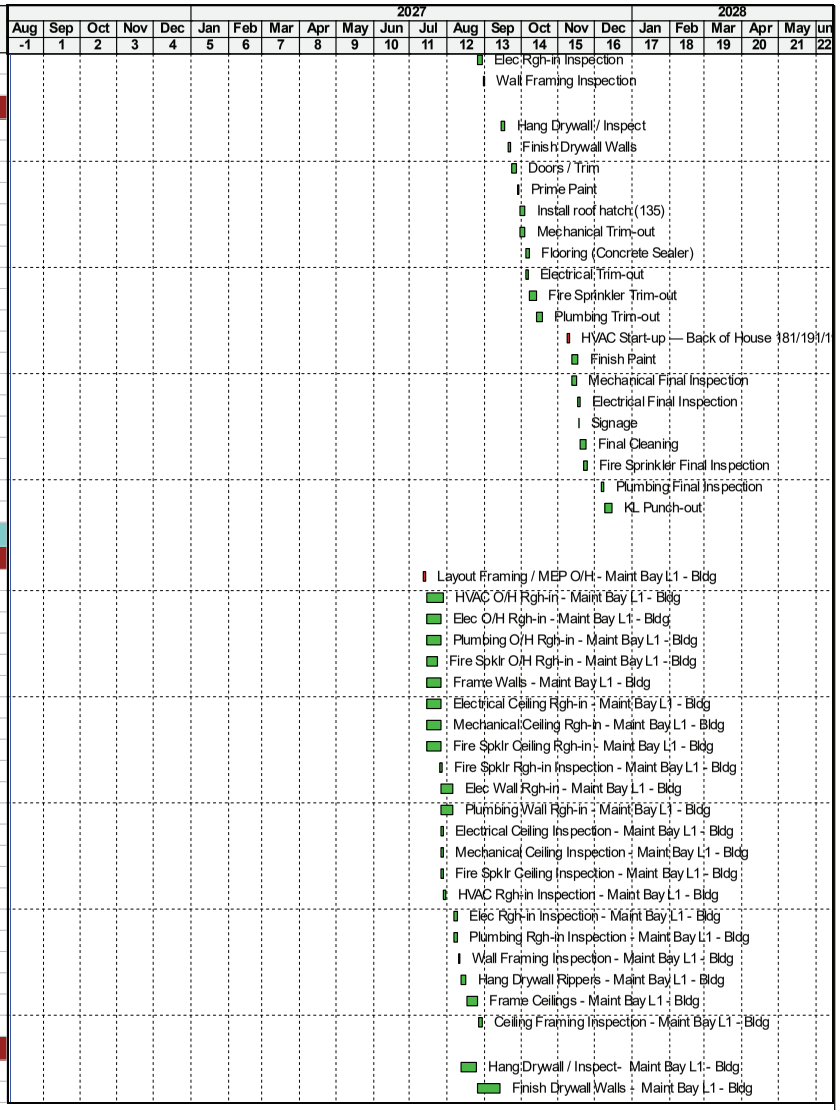

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
1065	092-DRYW-1001	Hang Drywall Ceilings / Inspect- Maint Bay L1 - Bldg	7	31-Aug-27	09-Sep-27
1066	09-FNSH-0999	Finish Drywall Walls - Maint Bay L1 - Bldg	12	10-Sep-27	27-Sep-27
1067	081-DOOR-1000	Doors / Trim - Maint Bay L1 - Bldg	5	14-Sep-27	20-Sep-27
1068	010-BATH-1003	Bathroom Tile - Maint Bay L1 - Bldg	8	28-Sep-27	07-Oct-27
1069	099-PRIM-1004	Prime Paint- Maint Bay L1 - Bldg	5	28-Sep-27	04-Oct-27
1070	010-ACTG-1007	ACT Grid - Maint Bay L1 - Bldg	5	05-Oct-27	12-Oct-27
1071	064-MILL-1010	Millwork - Maint Bay L1 - Bldg	8	05-Oct-27	15-Oct-27
1072	064-COUN-1021	Countertops - Maint Bay L1 - Bldg	8	05-Oct-27	15-Oct-27
1073	224-ELEC-1006	Electrical Grid Fixtures - Maint Bay L1 - Bldg	8	13-Oct-27	22-Oct-27
1074	010-MECH-1018	Mechanical Trim-Out - Maint Bay L1 - Bldg	8	13-Oct-27	22-Oct-27
1075	224-MECH-1020	Mechanical Grid Fixtures - Maint Bay L1 - Bldg	8	13-Oct-27	22-Oct-27
1076	099-FINI-1005	Finish Paint- Maint Bay L1 - Bldg	10	18-Oct-27	29-Oct-27
1077	224-PLUM-1008	Plumbing Fixtures - Maint Bay L1 - Bldg	5	18-Oct-27	22-Oct-27
1078	010-ELEC-1012	Electrical Trim-Out - Maint Bay L1 - Bldg	8	25-Oct-27	03-Nov-27
1079	010-MIRR-1014	Mirrors - Maint Bay L1 - Bldg	8	01-Nov-27	10-Nov-27
1080	010-DIV1-1015	Div 10 - Maint Bay L1 - Bldg	8	01-Nov-27	10-Nov-27
1081	010-HVAC-1009	HVAC Start-up - Maint Bay L1 - Bldg	3	12-Nov-27	16-Nov-27
1082	010-ACTT-1011	ACT Tiles - Maint Bay L1 - Bldg	8	17-Nov-27	29-Nov-27
1083	010-FLOO-1013	Flooring / Install Lift Equipment- Maint Bay L1 - Bldg	12	17-Nov-27	03-Dec-27
1084	010-SPKL-1019	Fire Spklr Trim-Out - Maint Bay L1 - Bldg	8	30-Nov-27	09-Dec-27
1085	010-KLPU-1016	KL Punch-out- Maint Bay L1 - Bldg	10	06-Dec-27	17-Dec-27
1086	010-CLEA-1017	Final Cleaning - Maint Bay L1 - Bldg	5	13-Dec-27	17-Dec-27
1087	**2nd Floor Build-out**		138	02-Jul-27	18-Jan-28
1088	**General Area**		119	20-Jul-27	10-Jan-28
1089	**Restrooms-215/216**		119	20-Jul-27	10-Jan-28
1090	**Rough-ins**		38	20-Jul-27	10-Sep-27
1091	010-LAYO-1034	Layout Framing / MEP O/H	2	20-Jul-27	21-Jul-27
1092	010-HVAC-1035	HVAC O/H Rgh-in	4	22-Jul-27	27-Jul-27
1093	010-ELEC-1036	Elec O/H Rgh-in	4	28-Jul-27	02-Aug-27
1094	010-PLUM-1037	Plumbing O/H Rgh-in	3	03-Aug-27	05-Aug-27
1095	010-SPKL-1038	Fire Spklr O/H Rgh-in	5	06-Aug-27	12-Aug-27
1096	010-FRAM-1039	Frame Walls	5	13-Aug-27	19-Aug-27
1097	081-DOOR-1040	Door Frames	2	20-Aug-27	23-Aug-27
1098	014-HVAC-1041	HVAC Rgh-in Inspection	3	24-Aug-27	26-Aug-27
1099	014-SPKL-1042	Fire Spklr Rgh-in Inspection	3	27-Aug-27	31-Aug-27
1100	010-ELEC-1043	Elec Wall Rgh-in	3	01-Sep-27	03-Sep-27
1101	014-ELEC-1044	Elec Rgh-in Inspection	3	07-Sep-27	09-Sep-27
1102	014-FRAM-1045	Wall Framing Inspection	1	10-Sep-27	10-Sep-27
1103	**Finishes**		81	13-Sep-27	10-Jan-28
1104	092-DRYW-1022	Hang Drywall / Inspect	4	13-Sep-27	16-Sep-27
1105	092-FINI-1023	Finish Drywall Walls/Ceilings	3	17-Sep-27	21-Sep-27
1106	081-DOOR-1024	Doors / Trim	2	22-Sep-27	23-Sep-27
1107	099-PRIM-1025	Prime Paint	2	24-Sep-27	27-Sep-27
1108	010-MECH-1046	Mechanical Trim-out	3	28-Sep-27	30-Sep-27
1109	010-ELEC-1047	Electrical Trim-out	3	01-Oct-27	05-Oct-27
1110	211-SPRI-1048	Fire Sprinkler Trim-out	3	06-Oct-27	08-Oct-27
1111	010-PLUM-1049	Plumbing Trim-out	3	12-Oct-27	14-Oct-27
1112	093-FLOO-1026	Flooring (Floor and Wall Tiles)	5	23-Nov-27	30-Nov-27
1113	010-MEPF-1027	MEPF Trim-Out	3	01-Dec-27	03-Dec-27

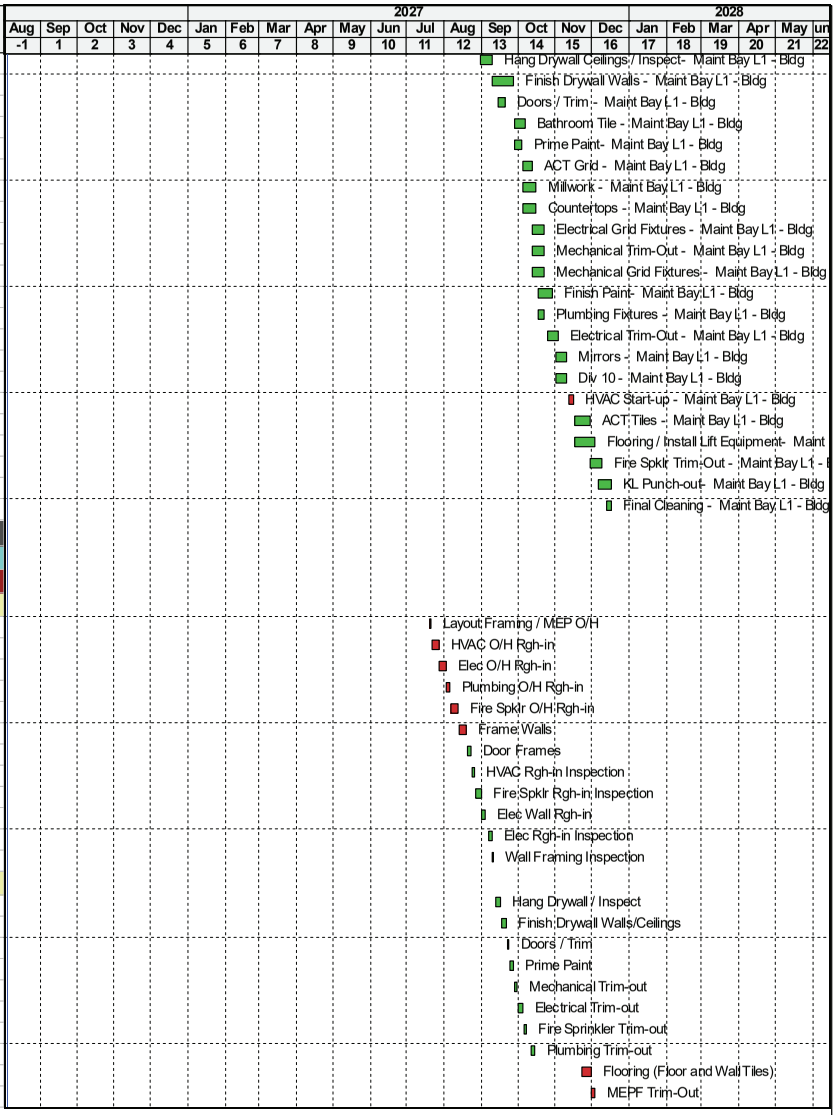

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
1114	010-HVAC-1028	HVAC Start-up — Locker / Shower Zone A — Maint Bay L1 — Bldg	5	06-Dec-27	10-Dec-27
1115	099-FINI-1029	Finish Paint	2	13-Dec-27	14-Dec-27
1116	014-MECH-1050	Mechanical Final Inspection	3	13-Dec-27	15-Dec-27
1117	010-BATH-1030	Install bathroom accessories/partitons	5	15-Dec-27	21-Dec-27
1118	014-ELEC-1051	Electrical Final Inspection	3	16-Dec-27	20-Dec-27
1119	014-SPRI-1052	Fire Sprinkler Final Inspection	3	21-Dec-27	23-Dec-27
1120	101-SIGN-1031	Signage	1	22-Dec-27	22-Dec-27
1121	010-CLEA-1032	Final Cleaning	2	23-Dec-27	27-Dec-27
1122	014-PLUM-1053	Plumbing Final Inspection	5	27-Dec-27	03-Jan-28
1123	010-KLPU-1033	KL Punch-out	5	04-Jan-28	10-Jan-28
1124	**Restrooms - 242/243**		81	20-Aug-27	16-Dec-27
1125	**Rough-ins**		39	20-Aug-27	15-Oct-27
1126	010-LAYO-1066	Layout Framing / MEP O/H	2	20-Aug-27	23-Aug-27
1127	010-HVAC-1067	HVAC O/H Rgh-in	4	24-Aug-27	27-Aug-27
1128	010-ELEC-1068	Elec O/H Rgh-in	3	30-Aug-27	01-Sep-27
1129	010-PLUM-1069	Plumbing O/H Rgh-in	3	02-Sep-27	07-Sep-27
1130	010-SPKL-1070	Fire Spklr O/H Rgh-in	4	08-Sep-27	13-Sep-27
1131	010-FRAM-1071	Frame Walls	5	14-Sep-27	20-Sep-27
1132	081-DOOR-1072	Door Frames	2	21-Sep-27	22-Sep-27
1133	014-HVAC-1073	HVAC Rgh-in Inspection	3	23-Sep-27	27-Sep-27
1134	014-SPKL-1074	Fire Spklr Rgh-in Inspection	3	28-Sep-27	30-Sep-27
1135	010-ELEC-1075	Elec Wall Rgh-in	4	01-Oct-27	06-Oct-27
1136	014-ELEC-1076	Elec Rgh-in Inspection	4	07-Oct-27	13-Oct-27
1137	014-FRAM-1077	Wall Framing Inspection	2	14-Oct-27	15-Oct-27
1138	**Finishes**		42	18-Oct-27	16-Dec-27
1139	092-DRYW-1054	Hang Drywall / Inspect	4	18-Oct-27	21-Oct-27
1140	092-FINI-1055	Finish Drywall Walls/Ceilings	3	22-Oct-27	26-Oct-27
1141	081-DOOR-1056	Doors / Trim	4	27-Oct-27	01-Nov-27
1142	099-PRIM-1057	Prime Paint	2	02-Nov-27	03-Nov-27
1143	093-FLOO-1058	Flooring (Floor and Wall Tiles)	4	04-Nov-27	09-Nov-27
1144	010-MECH-1078	Mechanical Trim-out	3	04-Nov-27	08-Nov-27
1145	010-ELEC-1079	Electrical Trim-out	3	09-Nov-27	12-Nov-27
1146	010-MEPF-1059	MEPF Trim-Out	3	10-Nov-27	15-Nov-27
1147	211-SPRI-1080	Fire Sprinkler Trim-out	3	15-Nov-27	17-Nov-27
1148	010-HVAC-1060	HVAC Start-up — Locker / Shower Zone B — Maint Bay L1 — Bldg	2	16-Nov-27	17-Nov-27
1149	099-FINI-1061	Finish Paint	2	18-Nov-27	19-Nov-27
1150	010-PLUM-1081	Plumbing Trim-out	3	18-Nov-27	22-Nov-27
1151	010-BATH-1062	Install bathroom accessories/partitons	5	22-Nov-27	29-Nov-27
1152	014-MECH-1082	Mechanical Final Inspection	3	23-Nov-27	26-Nov-27
1153	014-ELEC-1083	Electrical Final Inspection	3	29-Nov-27	01-Dec-27
1154	101-SIGN-1063	Signage	1	30-Nov-27	30-Nov-27
1155	010-CLEA-1064	Final Cleaning	2	01-Dec-27	02-Dec-27
1156	014-SPRI-1084	Fire Sprinkler Final Inspection	3	02-Dec-27	06-Dec-27
1157	014-PLUM-1085	Plumbing Final Inspection	3	07-Dec-27	09-Dec-27
1158	010-KLPU-1065	KL Punch-out	5	10-Dec-27	16-Dec-27
1159	**Restrooms /Shower -223 / 220A**		84	20-Aug-27	21-Dec-27
1160	**Rough-ins**		39	20-Aug-27	15-Oct-27
1161	010-LAYO-1086	Layout Framing / MEP O/H	2	20-Aug-27	23-Aug-27
1162	010-HVAC-1107	HVAC O/H Rgh-in	6	24-Aug-27	31-Aug-27

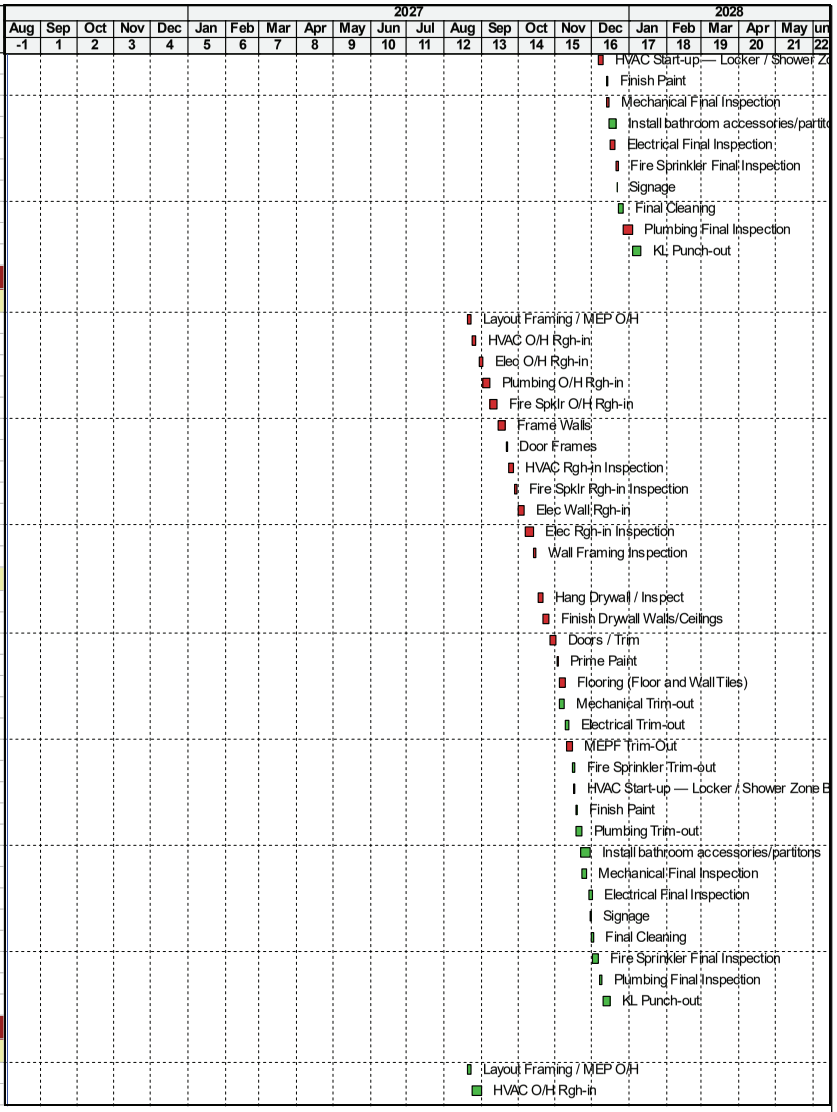

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
1163	010-ELEC-1132	Elec O/H Rgh-in	4	01-Sep-27	07-Sep-27
1164	010-PLUM-1125	Plumbing O/H Rgh-in	3	08-Sep-27	10-Sep-27
1165	010-SPKL-1090	Fire Spklr O/H Rgh-in	4	13-Sep-27	16-Sep-27
1166	010-FRAM-1091	Frame Walls	5	17-Sep-27	23-Sep-27
1167	081-DOOR-1112	Door Frames	2	24-Sep-27	27-Sep-27
1168	014-HVAC-1093	HVAC Rgh-in Inspection	3	28-Sep-27	30-Sep-27
1169	014-SPKL-1094	Fire Spklr Rgh-in Inspection	3	01-Oct-27	05-Oct-27
1170	010-ELEC-1142	Elec Wall Rgh-in	3	06-Oct-27	08-Oct-27
1171	014-ELEC-1113	Elec Rgh-in Inspection	3	12-Oct-27	14-Oct-27
1172	014-FRAM-1097	Wall Framing Inspection	1	15-Oct-27	15-Oct-27
1173	Finishes		45	18-Oct-27	21-Dec-27
1174	092-DRYW-1074	Hang Drywall / Inspect	4	18-Oct-27	21-Oct-27
1175	092-FINI-1075	Finish Drywall Walls/Ceilings	3	22-Oct-27	26-Oct-27
1176	010-BATH-1082	Install Shower Stalls	5	27-Oct-27	02-Nov-27
1177	081-DOOR-1102	Doors / Trim	2	03-Nov-27	04-Nov-27
1178	010-CLEA-1084	Final Cleaning	2	03-Nov-27	04-Nov-27
1179	099-PRIM-1077	Prime Paint	2	05-Nov-27	08-Nov-27
1180	093-FLOO-1078	Flooring (Floor and Wall Tiles)	5	09-Nov-27	16-Nov-27
1181	010-MECH-1098	Mechanical Trim-out	3	09-Nov-27	12-Nov-27
1182	010-ELEC-1152	Electrical Trim-out	3	15-Nov-27	17-Nov-27
1183	010-MEPF-1079	MEPF Trim-Out	3	17-Nov-27	19-Nov-27
1184	211-SPRI-1100	Fire Sprinkler Trim-out	3	18-Nov-27	22-Nov-27
1185	010-PLUM-1135	Plumbing Trim-out	3	18-Nov-27	22-Nov-27
1186	010-HVAC-1097	HVAC Start-up — Locker / Shower Zone D — Maint Bay L1 — Bldg	2	22-Nov-27	23-Nov-27
1187	099-FINI-1081	Finish Paint	2	24-Nov-27	26-Nov-27
1188	014-MECH-1102	Mechanical Final Inspection	3	29-Nov-27	01-Dec-27
1189	014-ELEC-1123	Electrical Final Inspection	3	02-Dec-27	06-Dec-27
1190	014-SPRI-1104	Fire Sprinkler Final Inspection	3	07-Dec-27	09-Dec-27
1191	014-PLUM-1105	Plumbing Final Inspection	3	10-Dec-27	14-Dec-27
1192	010-KLPU-1085	KL Punch-out /Signage	5	15-Dec-27	21-Dec-27
1193	Restrooms-224/225/226		84	22-Jul-27	19-Nov-27
1194	Rough-ins		39	22-Jul-27	15-Sep-27
1195	010-LAYO-1076	Layout Framing / MEP O/H	2	22-Jul-27	23-Jul-27
1196	010-HVAC-1087	HVAC O/H Rgh-in	6	26-Jul-27	02-Aug-27
1197	010-ELEC-1102	Elec O/H Rgh-in	4	03-Aug-27	06-Aug-27
1198	010-PLUM-1105	Plumbing O/H Rgh-in	3	09-Aug-27	11-Aug-27
1199	010-SPKL-1080	Fire Spklr O/H Rgh-in	4	12-Aug-27	17-Aug-27
1200	010-FRAM-1081	Frame Walls	5	18-Aug-27	24-Aug-27
1201	081-DOOR-1092	Door Frames	2	25-Aug-27	26-Aug-27
1202	014-HVAC-1083	HVAC Rgh-in Inspection	3	27-Aug-27	31-Aug-27
1203	014-SPKL-1084	Fire Spklr Rgh-in Inspection	3	01-Sep-27	03-Sep-27
1204	010-ELEC-1112	Elec Wall Rgh-in	3	07-Sep-27	09-Sep-27
1205	014-ELEC-1093	Elec Rgh-in Inspection	3	10-Sep-27	14-Sep-27
1206	014-FRAM-1087	Wall Framing Inspection	1	15-Sep-27	15-Sep-27
1207	Finishes		45	16-Sep-27	19-Nov-27
1208	092-DRYW-1064	Hang Drywall / Inspect	4	16-Sep-27	21-Sep-27
1209	092-FINI-1065	Finish Drywall Walls/Ceilings	3	22-Sep-27	24-Sep-27
1210	010-BATH-1072	Install Shower Stalls	5	27-Sep-27	01-Oct-27
1211	081-DOOR-1082	Doors / Trim	2	04-Oct-27	05-Oct-27

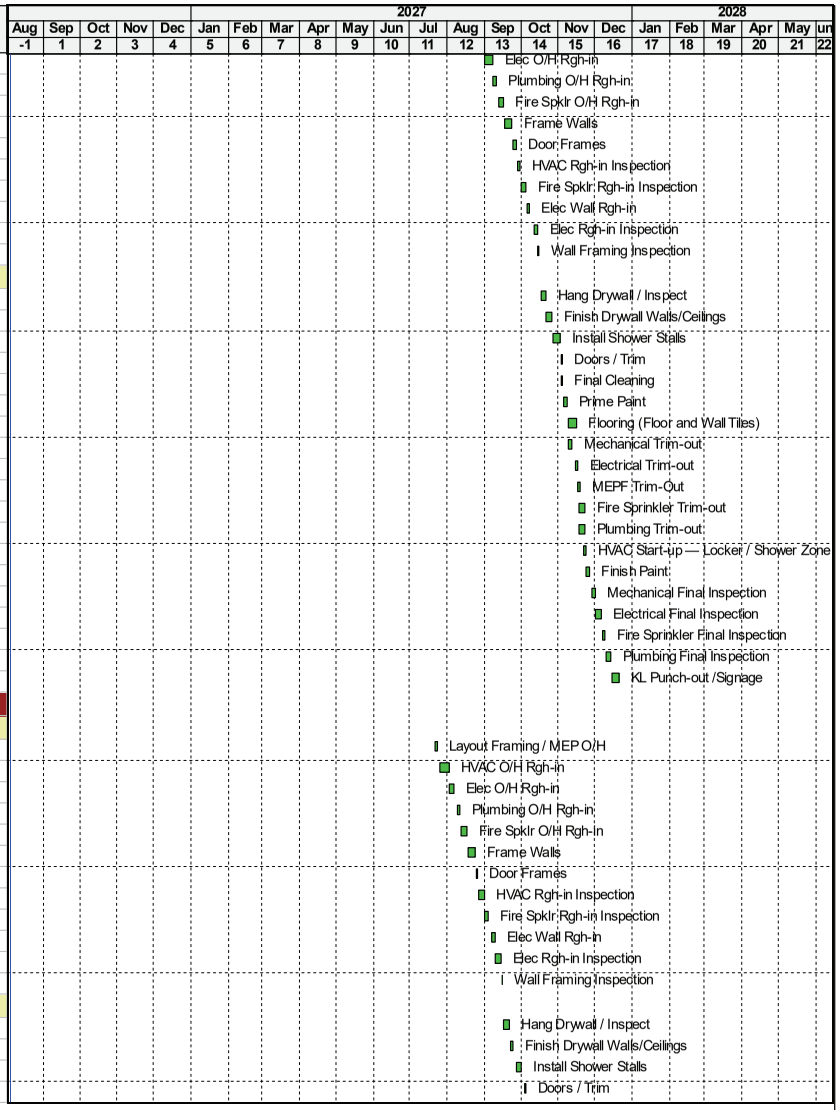

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
1212	010-CLEA-1074	Final Cleaning	2	04-Oct-27	05-Oct-27
1213	099-PRIM-1067	Prime Paint	2	06-Oct-27	07-Oct-27
1214	093-FLOO-1068	Flooring (Floor and Wall Tiles)	5	08-Oct-27	15-Oct-27
1215	010-MECH-1088	Mechanical Trim-out	3	08-Oct-27	13-Oct-27
1216	010-ELEC-1122	Electrical Trim-out	3	14-Oct-27	18-Oct-27
1217	010-MEPF-1069	MEPF Trim-Out	3	18-Oct-27	20-Oct-27
1218	211-SPRI-1090	Fire Sprinkler Trim-out	3	19-Oct-27	21-Oct-27
1219	010-PLUM-1115	Plumbing Trim-out	3	19-Oct-27	21-Oct-27
1220	010-HVAC-1077	HVAC Start-up — Locker / Shower Zone C — Maint Bay L1 — Bldg	2	21-Oct-27	22-Oct-27
1221	099-FINI-1071	Finish Paint	2	25-Oct-27	26-Oct-27
1222	014-MECH-1092	Mechanical Final Inspection	3	27-Oct-27	29-Oct-27
1223	014-ELEC-1103	Electrical Final Inspection	3	01-Nov-27	03-Nov-27
1224	014-SPRI-1094	Fire Sprinkler Final Inspection	3	04-Nov-27	08-Nov-27
1225	014-PLUM-1095	Plumbing Final Inspection	3	09-Nov-27	12-Nov-27
1226	010-KLPU-1075	KL Punch-out /Signage	5	15-Nov-27	19-Nov-27
1227	**Office Perimeter North - 227-238**		110	15-Jul-27	21-Dec-27
1228	**Rough-ins**		29	15-Jul-27	24-Aug-27
1229	09-WORK-0213	Layout Framing / MEP O/H - Office Area L2 - Bldg	3	15-Jul-27	19-Jul-27
1230	23-WORK-0214	HVAC O/H Rgh-in - Office Area L2 - Bldg	10	20-Jul-27	02-Aug-27
1231	01-WORK-0215	Elec O/H Rgh-in - Office Area L2 - Bldg	8	20-Jul-27	29-Jul-27
1232	22-WORK-0216	Plumbing O/H Rgh-in - Office Area L2 - Bldg	8	20-Jul-27	29-Jul-27
1233	010-SPKL-0217	Fire Spklr O/H Rgh-in - Office Area L2 - Bldg	7	20-Jul-27	28-Jul-27
1234	08-WORK-0218	Frame Walls - Office Area L2 - Bldg	5	20-Jul-27	26-Jul-27
1235	26-WORK-0230	Electrical Ceiling Rgh-in - Office Area L2 - Bldg	8	20-Jul-27	29-Jul-27
1236	010-MECH-0449	Mechanical Ceiling Rgh-in - Office Area L2 - Bldg	8	20-Jul-27	29-Jul-27
1237	010-SPKL-0450	Fire Spklr Ceiling Rgh-in - Office Area L2 - Bldg	8	20-Jul-27	29-Jul-27
1238	01-WORK-0221	Elec Wall Rgh-in - Office Area L2 - Bldg	5	27-Jul-27	02-Aug-27
1239	22-WORK-0222	Plumbing Wall Rgh-in - Office Area L2 - Bldg	5	27-Jul-27	02-Aug-27
1240	014-SPKL-0219	Fire Spklr Rgh-in Inspection - Office Area L2 - Bldg	2	29-Jul-27	30-Jul-27
1241	26-INSP-0231	Electrical Ceiling Inspection - Office Area L2 - Bldg	2	30-Jul-27	02-Aug-27
1242	014-MECH-0447	Mechanical Ceiling Inspection - Office Area L2 - Bldg	2	30-Jul-27	02-Aug-27
1243	014-SPKL-0448	Fire Spklr Ceiling Inspection - Office Area L2 - Bldg	2	30-Jul-27	02-Aug-27
1244	23-INSP-0220	HVAC Rgh-in Inspection - Office Area L2 - Bldg	2	03-Aug-27	04-Aug-27
1245	01-INSP-0223	Elec Rgh-in Inspection - Office Area L2 - Bldg	2	03-Aug-27	04-Aug-27
1246	22-INSP-0224	Plumbing Rgh-in Inspection - Office Area L2 - Bldg	2	03-Aug-27	04-Aug-27
1247	09-INSP-0225	Wall Framing Inspection - Office Area L2 - Bldg	2	05-Aug-27	06-Aug-27
1248	07-INSP-0226	Insulation / Inspection - Office Area L2 - Bldg	4	09-Aug-27	12-Aug-27
1249	092-DRYW-0466	Hang Drywall Rippers - Office Area L2 - Bldg	5	09-Aug-27	13-Aug-27
1250	08-WORK-0229	Frame Ceilings - Office Area L2 - Bldg	5	16-Aug-27	20-Aug-27
1251	09-INSP-0233	Ceiling Framing Inspection - Office Area L2 - Bldg	2	23-Aug-27	24-Aug-27
1252	**Finishes**		81	25-Aug-27	21-Dec-27
1253	092-DRYW-0227	Hang Drywall / Inspect- Office Area L2 - Bldg	10	25-Aug-27	08-Sep-27
1254	092-DRYW-0234	Hang Drywall Ceilings / Inspect- Office Area L2 - Bldg	5	25-Aug-27	31-Aug-27
1255	09-FNSH-0235	Finish Drywall Ceilings - Office Area L2 - Bldg	7	01-Sep-27	10-Sep-27
1256	09-FNSH-0228	Finish Drywall Walls - Office Area L2 - Bldg	12	09-Sep-27	24-Sep-27
1257	09-WORK-0236	Bathroom Tile - Office Area L2 - Bldg	8	13-Sep-27	22-Sep-27
1258	09-WORK-0237	Prime Paint- Office Area L2 - Bldg	5	13-Sep-27	17-Sep-27
1259	01-WORK-0240	ACT Grid - Office Area L2 - Bldg	5	20-Sep-27	24-Sep-27
1260	06-WORK-0243	Millwork - Office Area L2 - Bldg	8	20-Sep-27	29-Sep-27

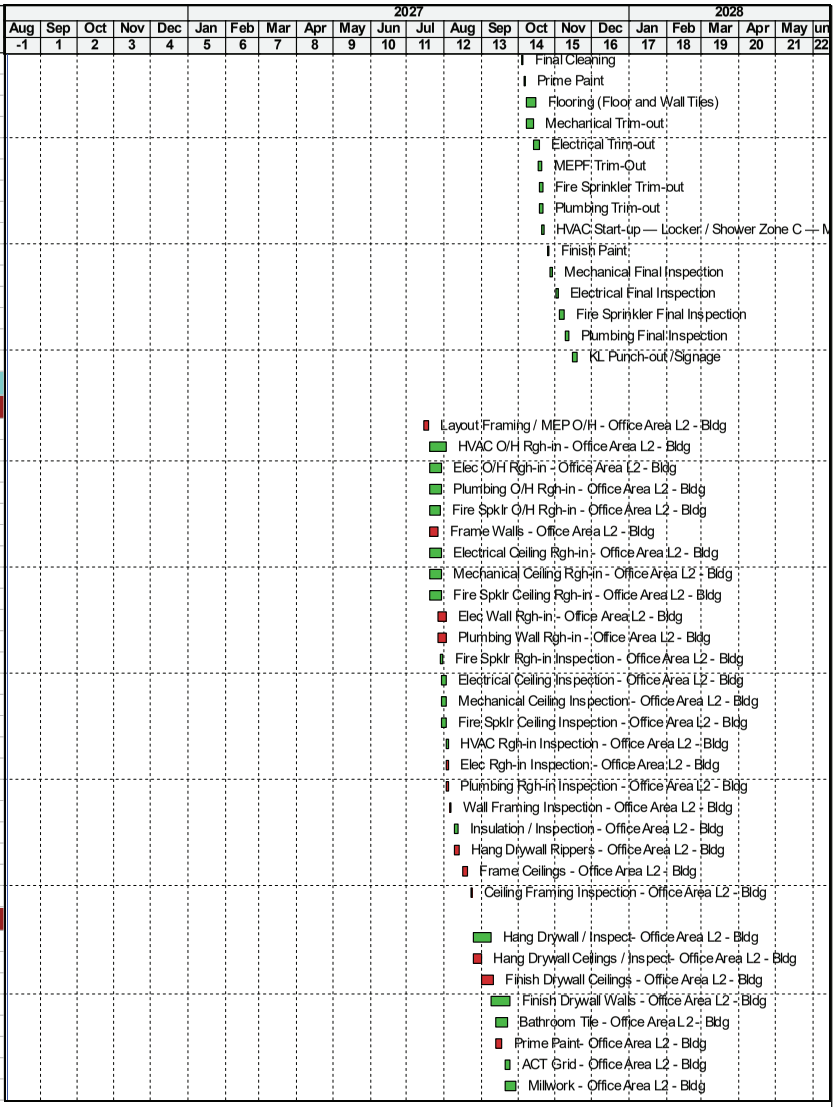

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
1261	064-COUN-0467	Countertops - Office Area L2 - Bldg	8	20-Sep-27	29-Sep-27
1262	08-WORK-0232	Doors / Trim - Office Area L2 - Bldg	5	27-Sep-27	01-Oct-27
1263	26-WORK-0239	Electrical Grid Fixtures - Office Area L2 - Bldg	8	27-Sep-27	06-Oct-27
1264	010-MECH-0444	Mechanical Trim-Out - Office Area L2 - Bldg	8	27-Sep-27	06-Oct-27
1265	224-MECH-0446	Mechanical Grid Fixtures - Office Area L2 - Bldg	8	27-Sep-27	06-Oct-27
1266	09-FNSH-0238	Finish Paint- Office Area L2 - Bldg	10	30-Sep-27	14-Oct-27
1267	22-WORK-0241	Plumbing Fixtures - Office Area L2 - Bldg	5	30-Sep-27	06-Oct-27
1268	26-TRIM-0245	Electrical Trim-Out - Office Area L2 - Bldg	8	07-Oct-27	19-Oct-27
1269	01-WORK-0247	Mirrors - Office Area L2 - Bldg	8	15-Oct-27	26-Oct-27
1270	10-WORK-0248	Div 10 - Office Area L2 - Bldg	8	15-Oct-27	26-Oct-27
1271	23-WORK-0242	HVAC Start-up - Office Area L2 - Bldg	3	17-Nov-27	19-Nov-27
1272	09-WORK-0244	ACT Tiles - Office Area L2 - Bldg	8	22-Nov-27	02-Dec-27
1273	09-WORK-0246	Flooring - Office Area L2 - Bldg	10	23-Nov-27	07-Dec-27
1274	010-SPKL-0445	Fire Spklr Trim-Out - Office Area L2 - Bldg	8	03-Dec-27	14-Dec-27
1275	010-OFFI-814	Office Furniture (KL) 2nd Floor	12	06-Dec-27	21-Dec-27
1276	01-PNCH-0249	KL Punch-out- Office Area L2 - Bldg	10	08-Dec-27	21-Dec-27
1277	01-WORK-0250	Final Cleaning - Office Area L2 - Bldg	5	15-Dec-27	21-Dec-27
1278	**Office Perimeter-East /South -201 - 219**		104	27-Jul-27	23-Dec-27
1279	**Rough-ins**		36	27-Jul-27	15-Sep-27
1280	09-WORK-246	Layout Framing / MEP O/H - Office Area L2 - Bldg	3	27-Jul-27	29-Jul-27
1281	23-WORK-242	HVAC O/H Rgh-in - Office Area L2 - Bldg	10	30-Jul-27	12-Aug-27
1282	01-WORK-382	Elec O/H Rgh-in - Office Area L2 - Bldg	8	30-Jul-27	10-Aug-27
1283	22-WORK-369	Plumbing O/H Rgh-in - Office Area L2 - Bldg	8	30-Jul-27	10-Aug-27
1284	010-SPKL-1100	Fire Spklr O/H Rgh-in - Office Area L2 - Bldg	7	30-Jul-27	09-Aug-27
1285	08-WORK-391	Frame Walls - Office Area L2 - Bldg	8	30-Jul-27	10-Aug-27
1286	26-WORK-402	Electrical Ceiling Rgh-in - Office Area L2 - Bldg	8	30-Jul-27	10-Aug-27
1287	010-MECH-1118	Mechanical Ceiling Rgh-in - Office Area L2 - Bldg	8	30-Jul-27	10-Aug-27
1288	010-SPKL-1120	Fire Spklr Ceiling Rgh-in - Office Area L2 - Bldg	8	30-Jul-27	10-Aug-27
1289	014-SPKL-1104	Fire Spklr Rgh-in Inspection - Office Area L2 - Bldg	2	10-Aug-27	11-Aug-27
1290	01-WORK-392	Elec Wall Rgh-in - Office Area L2 - Bldg	7	11-Aug-27	19-Aug-27
1291	22-WORK-379	Plumbing Wall Rgh-in - Office Area L2 - Bldg	8	11-Aug-27	20-Aug-27
1292	26-INSP-257	Electrical Ceiling Inspection - Office Area L2 - Bldg	2	11-Aug-27	12-Aug-27
1293	014-MECH-1112	Mechanical Ceiling Inspection - Office Area L2 - Bldg	2	11-Aug-27	12-Aug-27
1294	014-SPKL-1114	Fire Spklr Ceiling Inspection - Office Area L2 - Bldg	2	11-Aug-27	12-Aug-27
1295	23-INSP-254	HVAC Rgh-in Inspection - Office Area L2 - Bldg	2	13-Aug-27	16-Aug-27
1296	01-INSP-261	Elec Rgh-in Inspection - Office Area L2 - Bldg	2	20-Aug-27	23-Aug-27
1297	22-INSP-256	Plumbing Rgh-in Inspection - Office Area L2 - Bldg	2	23-Aug-27	24-Aug-27
1298	09-INSP-233	Wall Framing Inspection - Office Area L2 - Bldg	2	25-Aug-27	26-Aug-27
1299	07-INSP-226	Insulation / Inspection - Office Area L2 - Bldg	4	27-Aug-27	01-Sep-27
1300	092-DRYW-1104	Hang Drywall Rippers - Office Area L2 - Bldg	3	27-Aug-27	31-Aug-27
1301	08-WORK-401	Frame Ceilings - Office Area L2 - Bldg	8	01-Sep-27	13-Sep-27
1302	09-INSP-243	Ceiling Framing Inspection - Office Area L2 - Bldg	2	14-Sep-27	15-Sep-27
1303	**Finishes**		68	16-Sep-27	23-Dec-27
1304	092-DRYW-1084	Hang Drywall / Inspect- Office Area L2 - Bldg	10	16-Sep-27	29-Sep-27
1305	092-DRYW-1094	Hang Drywall Ceilings / Inspect- Office Area L2 - Bldg	7	16-Sep-27	24-Sep-27
1306	09-FNSH-1009	Finish Drywall Ceilings - Office Area L2 - Bldg	8	27-Sep-27	06-Oct-27
1307	09-FNSH-999	Finish Drywall Walls - Office Area L2 - Bldg	12	30-Sep-27	18-Oct-27
1308	09-WORK-256	Bathroom Tile - Office Area L2 - Bldg	8	07-Oct-27	19-Oct-27
1309	09-WORK-266	Prime Paint- Office Area L2 - Bldg	5	07-Oct-27	14-Oct-27

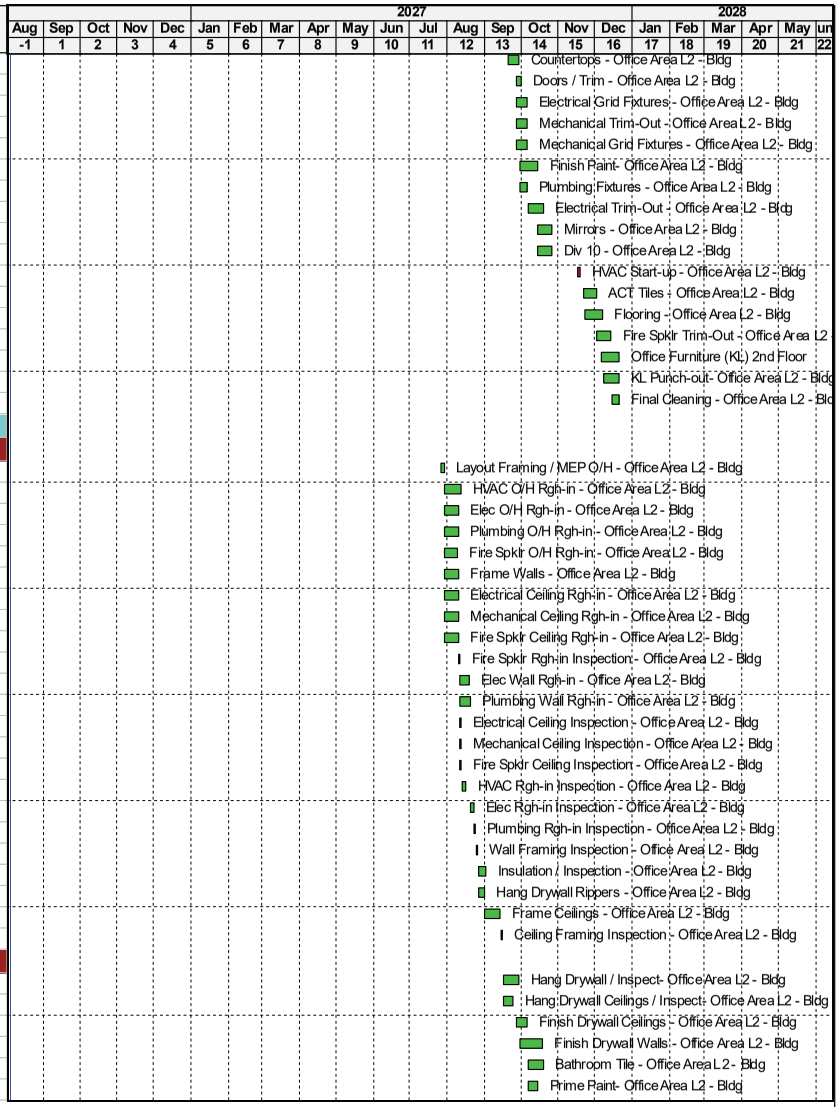

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
1310	01-WORK-402	ACT Grid - Office Area L2 - Bldg	5	15-Oct-27	21-Oct-27
1311	06-WORK-243	Millwork - Office Area L2 - Bldg	8	15-Oct-27	26-Oct-27
1312	064-COUN-1031	Countertops - Office Area L2 - Bldg	8	15-Oct-27	26-Oct-27
1313	08-WORK-411	Doors / Trim - Office Area L2 - Bldg	5	19-Oct-27	25-Oct-27
1314	26-WORK-412	Electrical Grid Fixtures - Office Area L2 - Bldg	8	22-Oct-27	02-Nov-27
1315	010-MECH-1108	Mechanical Trim-Out - Office Area L2 - Bldg	8	22-Oct-27	02-Nov-27
1316	224-MECH-1030	Mechanical Grid Fixtures - Office Area L2 - Bldg	8	22-Oct-27	02-Nov-27
1317	09-FNSH-1019	Finish Paint- Office Area L2 - Bldg	10	27-Oct-27	09-Nov-27
1318	22-WORK-389	Plumbing Fixtures - Office Area L2 - Bldg	5	27-Oct-27	02-Nov-27
1319	23-WORK-252	HVAC Start-up - Office Area L2 - Bldg	5	03-Nov-27	09-Nov-27
1320	26-TRIM-245	Electrical Trim-Out - Office Area L2 - Bldg	8	03-Nov-27	15-Nov-27
1321	09-WORK-276	ACT Tiles - Office Area L2 - Bldg	8	10-Nov-27	22-Nov-27
1322	01-WORK-412	Mirrors - Office Area L2 - Bldg	8	10-Nov-27	22-Nov-27
1323	10-WORK-371	Div 10 - Office Area L2 - Bldg	8	10-Nov-27	22-Nov-27
1324	09-WORK-286	Flooring - Office Area L2 - Bldg	12	23-Nov-27	09-Dec-27
1325	010-SPKL-1110	Fire Spklr Trim-Out - Office Area L2 - Bldg	8	23-Nov-27	03-Dec-27
1326	01-PNCH-264	KL Punch-out- Office Area L2 - Bldg	10	10-Dec-27	23-Dec-27
1327	01-WORK-422	Final Cleaning - Office Area L2 - Bldg	5	17-Dec-27	23-Dec-27
1328	**Comand Center 240 240D/240C**		127	15-Jul-27	18-Jan-28
1329	**Rough-ins**		50	15-Jul-27	23-Sep-27
1330	010-LAYO-0521	Layout Framing / MEP O/H - Command Center 240 L2 - Bldg	3	15-Jul-27	19-Jul-27
1331	010-HVAC-0522	HVAC O/H Rgh-in - Command Center 240 L2 - Bldg	10	20-Jul-27	02-Aug-27
1332	010-PLUM-0524	Plumbing O/H Rgh-in - Command Center 240 L2 - Bldg	8	20-Jul-27	29-Jul-27
1333	010-SPKL-0525	Fire Spklr O/H Rgh-in - Command Center 240 L2 - Bldg	7	20-Jul-27	28-Jul-27
1334	010-FRAM-0526	Frame Walls - Command Center 240 L2 - Bldg	5	20-Jul-27	26-Jul-27
1335	010-ELEC-0536	Electrical Ceiling Rgh-in - Command Center 240 L2 - Bldg	8	20-Jul-27	29-Jul-27
1336	010-MECH-0540	Mechanical Ceiling Rgh-in - Command Center 240 L2 - Bldg	8	20-Jul-27	29-Jul-27
1337	010-SPKL-0541	Fire Spklr Ceiling Rgh-in - Command Center 240 L2 - Bldg	8	20-Jul-27	29-Jul-27
1338	010-PLUM-0530	Plumbing Wall Rgh-in - Command Center 240 L2 - Bldg	8	27-Jul-27	05-Aug-27
1339	014-SPKL-0527	Fire Spklr Rgh-in Inspection - Command Center 240 L2 - Bldg	2	29-Jul-27	30-Jul-27
1340	014-ELEC-0537	Electrical Ceiling Inspection - Command Center 240 L2 - Bldg	2	30-Jul-27	02-Aug-27
1341	014-MECH-0538	Mechanical Ceiling Inspection - Command Center 240 L2 - Bldg	2	30-Jul-27	02-Aug-27
1342	014-SPKL-0539	Fire Spklr Ceiling Inspection - Command Center 240 L2 - Bldg	2	02-Aug-27	03-Aug-27
1343	014-HVAC-0528	HVAC Rgh-in Inspection - Command Center 240 L2 - Bldg	2	03-Aug-27	04-Aug-27
1344	010-ELEC-0529	Elec Wall Rgh-in - Command Center 240 L2 - Bldg	7	03-Aug-27	11-Aug-27
1345	010-ELEC-0523	Elec O/H Rgh-in - Command Center 240 L2 - Bldg	5	05-Aug-27	11-Aug-27
1346	014-PLUM-0532	Plumbing Rgh-in Inspection - Command Center 240 L2 - Bldg	2	06-Aug-27	09-Aug-27
1347	014-ELEC-0531	Elec Rgh-in Inspection - Command Center 240 L2 - Bldg	4	12-Aug-27	17-Aug-27
1348	014-FRAM-0533	Wall Framing Inspection - Command Center 240 L2 - Bldg	4	18-Aug-27	23-Aug-27
1349	014-INSU-0534	Insulation / Inspection - Command Center 240 L2 - Bldg	6	24-Aug-27	31-Aug-27
1350	092-DRYW-0542	Hang Drywall Rippers - Command Center 240 L2 - Bldg	5	01-Sep-27	08-Sep-27
1351	010-FRAM-0535	Frame Ceilings - Command Center 240 L2 - Bldg	7	09-Sep-27	17-Sep-27
1352	014-FRAM-0546	Ceiling Framing Inspection - Command Center 240 L2 - Bldg	4	20-Sep-27	23-Sep-27
1353	**Finishes**		77	24-Sep-27	18-Jan-28
1354	092-DRYW-0543	Hang Drywall / Inspect- Command Center 240 L2 - Bldg	10	24-Sep-27	07-Oct-27
1355	092-DRYW-0547	Hang Drywall Ceilings / Inspect- Command Center 240 L2 - Bldg	5	24-Sep-27	30-Sep-27
1356	092-FINI-0548	Finish Drywall Ceilings - Command Center 240 L2 - Bldg	7	01-Oct-27	12-Oct-27
1357	092-FINI-0544	Finish Drywall Walls - Command Center 240 L2 - Bldg	12	08-Oct-27	26-Oct-27
1358	010-BATH-0549	Bathroom Tile - Command Center 240 L2 - Bldg	8	13-Oct-27	22-Oct-27

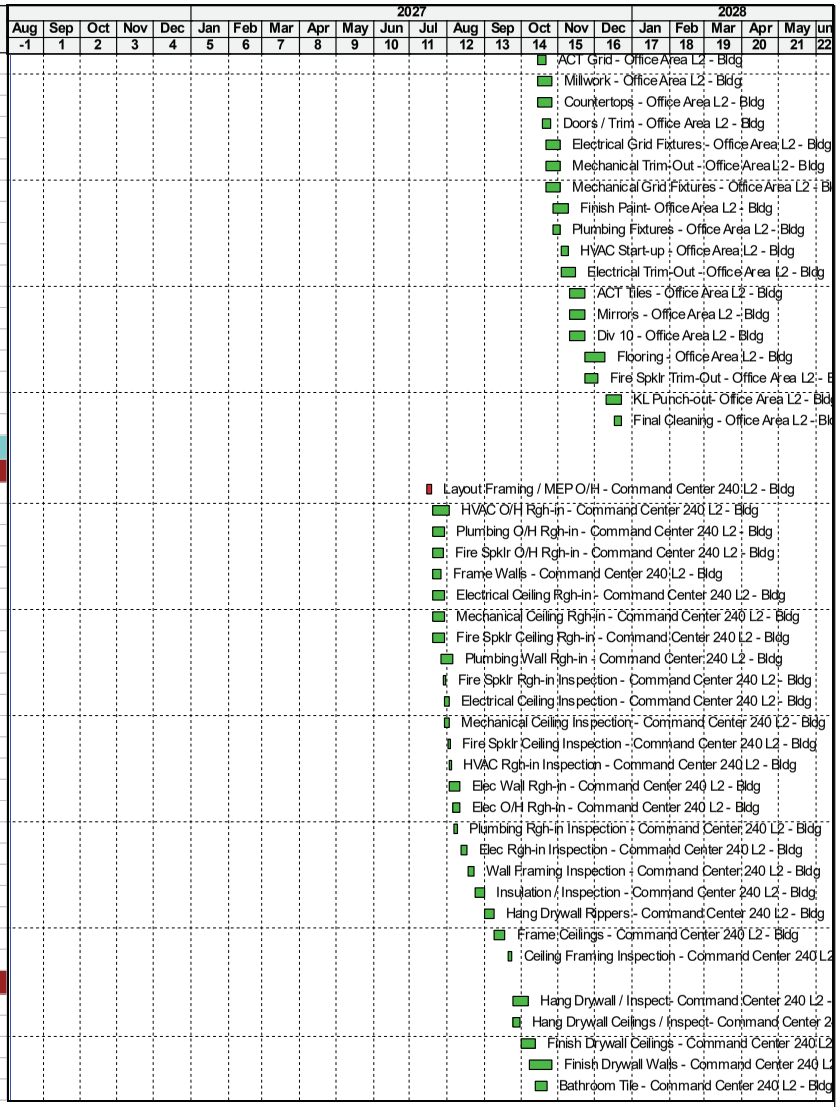

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
1359	099-PRIM-0550	Prime Paint- Command Center 240 L2 - Bldg	5	13-Oct-27	19-Oct-27
1360	010-ACTG-0553	ACT Grid - Command Center 240 L2 - Bldg	5	20-Oct-27	26-Oct-27
1361	064-MILL-0556	Millwork - Command Center 240 L2 - Bldg	8	20-Oct-27	29-Oct-27
1362	064-COUN-0567	Countertops - Command Center 240 L2 - Bldg	8	20-Oct-27	29-Oct-27
1363	081-DOOR-0545	Doors / Trim - Command Center 240 L2 - Bldg	5	27-Oct-27	02-Nov-27
1364	224-ELEC-0552	Electrical Grid Fixtures - Command Center 240 L2 - Bldg	7	27-Oct-27	04-Nov-27
1365	010-MECH-0564	Mechanical Trim-Out - Command Center 240 L2 - Bldg	8	27-Oct-27	05-Nov-27
1366	224-MECH-0566	Mechanical Grid Fixtures - Command Center 240 L2 - Bldg	8	27-Oct-27	05-Nov-27
1367	224-PLUM-0554	Plumbing Fixtures - Command Center 240 L2 - Bldg	5	01-Nov-27	05-Nov-27
1368	099-FINI-0551	Finish Paint- Command Center 240 L2 - Bldg	10	03-Nov-27	17-Nov-27
1369	010-ELEC-0558	Electrical Trim-Out - Command Center 240 L2 - Bldg	5	05-Nov-27	12-Nov-27
1370	010-HVAC-0555	HVAC Start-up - Command Center 240 L2 - Bldg	3	18-Nov-27	22-Nov-27
1371	010-MIRR-0560	Mirrors - Command Center 240 L2 - Bldg	8	18-Nov-27	30-Nov-27
1372	010-DIV1-0561	Div 10 - Command Center 240 L2 - Bldg	8	18-Nov-27	30-Nov-27
1373	010-ACTT-0557	ACT Tiles - Command Center 240 L2 - Bldg	8	23-Nov-27	03-Dec-27
1374	010-FLOO-0559	Flooring - Command Center 240 L2 - Bldg	12	23-Nov-27	09-Dec-27
1375	010-DIV1-1025	Command Center AV - Bldg	20	23-Nov-27	21-Dec-27
1376	010-SPKL-0565	Fire Spklr Trim-Out - Command Center 240 L2 - Bldg	8	06-Dec-27	15-Dec-27
1377	010-KLPU-0562	KL Punch-out- Command Center 240 L2 - Bldg	10	27-Dec-27	10-Jan-28
1378	010-CLEA-0563	Final Cleaning - Command Center 240 L2 - Bldg	5	04-Jan-28	10-Jan-28
1379	010-DIV1-1035	Command Center Furniture - Bldg	5	11-Jan-28	18-Jan-28
1380	**Server-229**		51	10-Aug-27	20-Oct-27
1381	27-BDAT-0713	BDA equipment install/Testing	10	10-Aug-27	23-Aug-27
1382	27-WORK-0197	Data/Comm Equipment Boards - Elec Rm L2 - Bldg	3	20-Sep-27	22-Sep-27
1383	26-WORK-0198	Elec Panels/ Wire Pull - Elec Rm L2 - Bldg	5	20-Sep-27	24-Sep-27
1384	26-WORK-0199	Data/Comm Equip/ Wire - Elec Rm L2 - Bldg	3	23-Sep-27	27-Sep-27
1385	26-WORK-0202	Secondary Wire Pull/Terminate - Elec Rm L2 - Bldg	3	27-Sep-27	29-Sep-27
1386	21-FIRE-713	Fire Panel Install Wiring /Terminations	7	27-Sep-27	05-Oct-27
1387	27-INSP-0200	Data/Comm Equip Inspect - Elec Rm L2 - Bldg	2	28-Sep-27	29-Sep-27
1388	26-WORK-0201	Meter/ Wire Pull - Elec Rm L2 - Bldg	5	30-Sep-27	06-Oct-27
1389	01-INSP-0203	Temp For Testing Inspection - Elec Rm L2 - Bldg	2	07-Oct-27	08-Oct-27
1390	26-WORK-0204	Electrical System Start-up - Elec Rm L2 - Bldg	3	12-Oct-27	14-Oct-27
1391	27-WORK-0205	Data/Comm System Start-up - Elec Rm L2 - Bldg	4	15-Oct-27	20-Oct-27
1392	**Rough-ins**		0		
1393	**Finishes**		0		
1394	**Electrical Room - 290**		33	02-Jul-27	18-Aug-27
1395	26-WORK-422	Install conduit sleeves and penetrations through walls/floor	5	02-Jul-27	09-Jul-27
1396	26-WORK-452	Install isolated ground (IG) receptacles throughout room	3	12-Jul-27	14-Jul-27
1397	26-WORK-442	Terminate all panel circuit connections	5	15-Jul-27	21-Jul-27
1398	21-FIRE-723	Pull Power Circuits to Panels - Elec Room 290	5	15-Jul-27	21-Jul-27
1399	01-INSP-271	Install Electrical Panel Directories and Labels - Elec Room 290	2	22-Jul-27	23-Jul-27
1400	26-WORK-462	Test continuity and megger all circuits	5	26-Jul-27	30-Jul-27
1401	27-BDAT-713	Rough-in Conduit Runs to Panel Locations - Elec Room 290	5	26-Jul-27	30-Jul-27
1402	26-WORK-432	Install electrical panels and distribution equipment	3	02-Aug-27	04-Aug-27
1403	27-INSP-200	Install Grounding Bar and Bond All Equipment - Elec Room 290	2	05-Aug-27	06-Aug-27
1404	27-WORK-215	Energize and Test Panels - Elec Room 290	4	09-Aug-27	12-Aug-27
1405	27-WORK-225	KL Punch List and Closeout - Elec Room 290	4	13-Aug-27	18-Aug-27
1406	**Rough-ins**		0		
1407	**Finishes**		0		

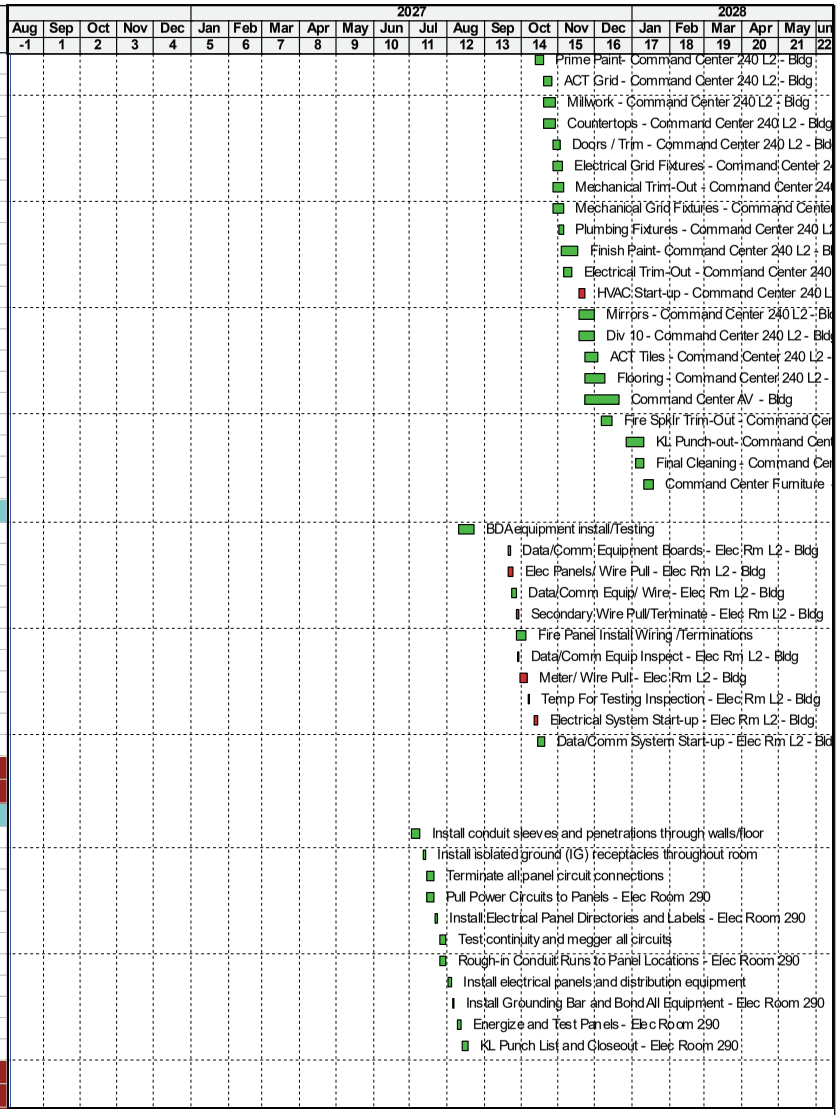

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

#	Activity ID	Activity Name	Original Duration	Start	Finish
1408		**Mechanical Rooms - 280**	74	27-Jul-27	08-Nov-27
1409	26-WORK-0207	Electrical Rgh-in - Mech Rm L2 - Bldg	3	27-Jul-27	29-Jul-27
1410	23-WORK-0208	HVAC Units / Duct- Mech Rm L2 - Bldg	15	27-Jul-27	16-Aug-27
1411	26-WORK-0210	Elec Panels/Equip- Mech Rm L2 - Bldg	10	17-Aug-27	30-Aug-27
1412	010-HVAC-0451	HVAC - Plumbing Tie-ins - Mech Rm L2 - Bldg	5	17-Aug-27	23-Aug-27
1413	230-HVAC-0452	HVAC - Mechanical & Controls Tie-ins - Mech Rm L2 - Bldg	5	17-Aug-27	23-Aug-27
1414	26-WORK-0211	Elec Wire Pull / Terminate - Mech Rm L2 - Bldg	5	20-Aug-27	26-Aug-27
1415	26-WORK-0209	HVAC - Electrical & Controls Tie-ins - Mech Rm L2 - Bldg	5	27-Aug-27	02-Sep-27
1416	09-WORK-0206	Prime & Paint- Mech Rm L2 - Bldg	3	27-Sep-27	29-Sep-27
1417	23-WORK-0212	HVAC System Start-up - Mech Rm L2 - Bldg	5	02-Nov-27	08-Nov-27
1418		**Rough-ins**	0		
1419		**Finishes**	0		
1420		**Final Inspections & Closeout**	209	08-Apr-27	07-Feb-28
1421	328-LAND-0379	Landscape / Irrigation Final Inspection - FI- Bldg	3	08-Apr-27	12-Apr-27
1422	014-CIVI-0308	Civil Final Inspection - FI- Bldg	3	11-Jun-27	15-Jun-27
1423	01-INSP-0252	Roof Final Inspection - FI - Bldg	5	30-Jun-27	07-Jul-27
1424	014-INSP-0251	Structural Final Inspection - FI- Bldg	3	21-Oct-27	25-Oct-27
1425	14-INSP-0255	Elevator Final Inspection - FI- Bldg	4	21-Oct-27	26-Oct-27
1426	01-INSP-0258	F/A Final Inspection - FI- Bldg	3	22-Oct-27	26-Oct-27
1427	26-INSP-0257	Electrical Final Inspection - FI - Bldg	3	25-Oct-27	27-Oct-27
1428	010-FIBL-0402	Test & Balance - FI- Bldg	7	22-Nov-27	01-Dec-27
1429	23-INSP-0254	Mechanical Final Inspection - FI- Bldg	3	02-Dec-27	06-Dec-27
1430	014-SPRK-0253	Fire Sprklr Final Inspection - FI- Bldg	3	15-Dec-27	17-Dec-27
1431	014-DEPT-0259	Fire Dept/ Life Safety Final Inspection - FI - Bldg	3	20-Dec-27	22-Dec-27
1432	22-INSP-0256	Plumbing Final Inspection - FI- Bldg	5	04-Jan-28	10-Jan-28
1433	01-PNCH-0260	KL Punch Final - FI- Bldg	5	11-Jan-28	18-Jan-28
1434	01-INSP-0261	Building Final Inspection - FI- Bldg	4	11-Jan-28	14-Jan-28
1435	01-WORK-0262	TCO - FI- Bldg	0		14-Jan-28
1436	01-CLSO-0266	Closeout Doc's - FI - Bldg	15	18-Jan-28	07-Feb-28
1437	010-OWNE-0479	Owner/Arch Final Punch WALK - FI- Bldg	4	18-Jan-28	21-Jan-28
1438	01-WORK-0263	Final Clean - FI- Bldg	10	19-Jan-28	01-Feb-28
1439	01-PNCH-0264	Owner/Arch Final Punch - FI- Bldg	10	24-Jan-28	04-Feb-28
1440	01-WORK-0265	SCO - FI- Bldg	0		04-Feb-28

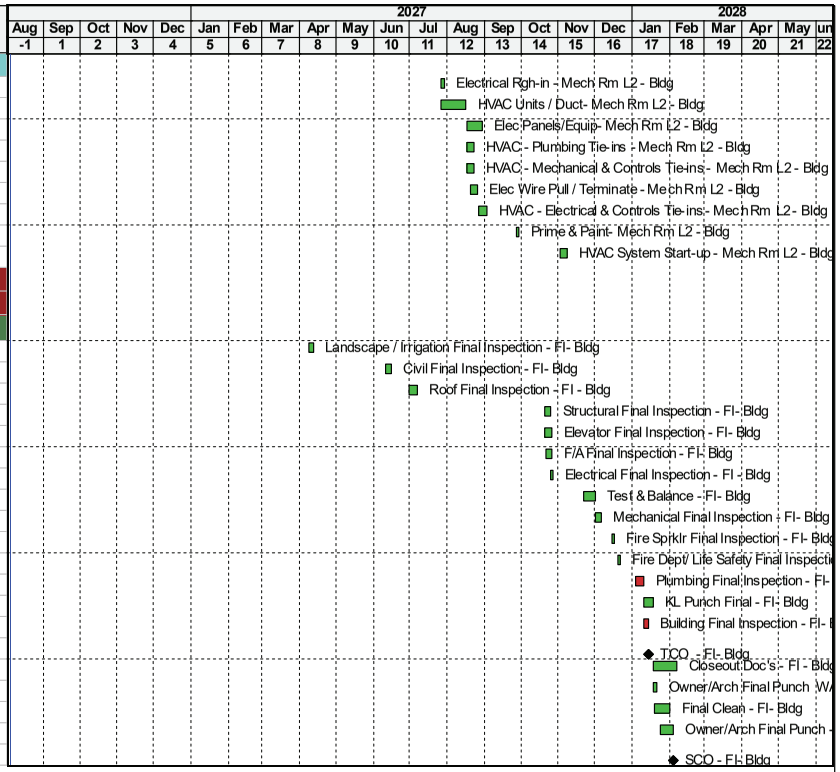

Remaining Level of Effort
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Greenacres Municipal Operations Center 04Aug2026

Data Date: 04-Aug-26
Run Date: 07-Aug-26

2.PB-EOC- OwnerGAPrelim 8

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

Exhibit E

Design-Builder's Allowances List

Turf Outside Fitness Center: Turf allowance outside the gym is carried at $15,300 ($15/SF)

Exhibit F

Commissioning Plan

Commissioning Plan

City of Greenacres
Municipal Operations Center
5770 Melaleuca Lane
Greenacres, FL 33463

August 6, 2026

Prepared for: City of Greenacres, Fl

DRAFT

CMTA
A LEGENCE Company

Performed by: CMTA
Project #2025-0113.00

DRAFT

Summary

The *Commissioning Plan* is developed in draft form for the specific project during the design phase and is updated during construction. The plan provides direction for commissioning tasks during construction. The plan focuses on providing support for the specifications and forms for the application of the commissioning process.

Table of Contents

1.0 Overview 1
1.1 Abbreviations 1
1.2 Purpose of the Commissioning Plan 2
1.3 Commissioning Scope 2
1.4 Commissioning Flow Chart 3
1.5 Commissioned Systems 4
1.6 Appendix A – Pre-Commissioning Checklist 5
1.7 Appendix B – Functional Performance Tests 5
2.0 General Building Information 6
3.0 Construction / Cx Team Data 7
4.0 Roles and Responsibilities 8
4.1 Commissioning Team 9
4.2 Responsibilities 9
5.0 Commissioning Process 11
5.1 LEED Requirements 11
5.2 Miscellaneous Management Protocols 12
5.3 Submittals and Documentations 12
5.4 Special Submittals, Notifications and Clarifications 12
5.5 Pre-functional Tests 13
5.6 Start-up 13
5.7 TAB Plan 14
5.8 Controls Check Out Plan 14
5.9 Development of Functional Test and Verification Procedures 14
5.9.1 Overview 14
5.9.2 Scope of Testing 15
5.9.3 Development Process 15
5.10 Execution of Functional Testing Procedures 15
5.10.1 Overview and Process 15
5.10.2 Deficiencies and Retesting 15
5.11 Operating and Maintenance Manuals 16
5.12 Training of Owner's Personnel 16
5.12.1 Overall Plan 16
5.13 Warranty Period 16
5.14 Final Commissioning Report 17
5.15 Schedule 18

DRAFT

1. OVERVIEW

1.1 Abbreviations

The following are common abbreviations and definitions used in this document.

A/E	Design architects/engineers
CxP	Commissioning provider
CC	Controls contractor
CM	Construction manager
Cx	Commissioning
Cx Plan	Commissioning Plan document
EC	Electrical contractor
FT	Functional performance test
GC	General contractor
MC	Mechanical contractor
PM	Owner's project manager
PC	Pre-functional checklist
Subs	Subcontractors to general
TAB	Test and balance contractor

Trade Representative: Person who competently represents the workforce engaged by the contractor for the individual trade named. This person shall be completely familiar with the work performed for this contract at all levels of detail of his trade and with coordination with other trades.

Participate: Attend commissioning events, provide technical expertise or knowledge, equipment, measurements, and observations needed or requested by the Commissioning provider or owner. Provide follow-up analysis, equipment data, design data, or other trade or professional service needed in response to commissioning events.

Verify: To positively determine that the measured or observed quantity satisfies all required criteria. Simply performing the test, measurement or observation does not constitute "verification". The test result must also pass all contract criteria. Tests which fail must be repeated at no additional cost to the owner after repairs or adjustments are made, until full verification is achieved.

DRAFT

1.2 Purpose of the Commissioning Plan

The purpose of the construction phase commissioning plan is:

> To provide direction for team members participating in the commissioning process during construction, particularly providing resolution for issues and providing details that cannot be, or were not, fully developed during design, such as scheduling, participation of various parties of this project, actual lines of reporting and approvals, coordination, etc.

This plan does not provide a detailed explanation of the required testing procedures. The detailed testing requirements and procedures are found in specification sections 230800.

1.3 Commissioning Scope

Commissioning is a systematic process of achieving, verifying, and documenting that the performance of the facility and its various systems meets the design intent and functional and operational needs of the owner and occupants. This includes the specific training of the facility personnel involved in the operation and maintenance of the building's equipment and facilities. There are numerous checks for each stage of the building commissioning process which ensure that set procedures are followed. This approach to constructing a building, along with the necessary training of facility personnel, serves as a thorough quality assurance program for building construction, and the building construction industry.

Commissioning during the construction of this project is intended to achieve the following specific objectives:


- Ensure that the equipment and systems being commissioned are installed properly and receive adequate operational checkout by installing contractors.
- Verify and document proper performance of equipment and systems.
- Ensure that O&M documentation is complete.
- Ensure that the owner's operating personnel are adequately trained.

DRAFT

1.4 Commissioning Flow Chart—For Fundamental Commissioning Requirements

The following chart illustrates the overall status of the commissioning process for the project.

Gray - Not included in scope.

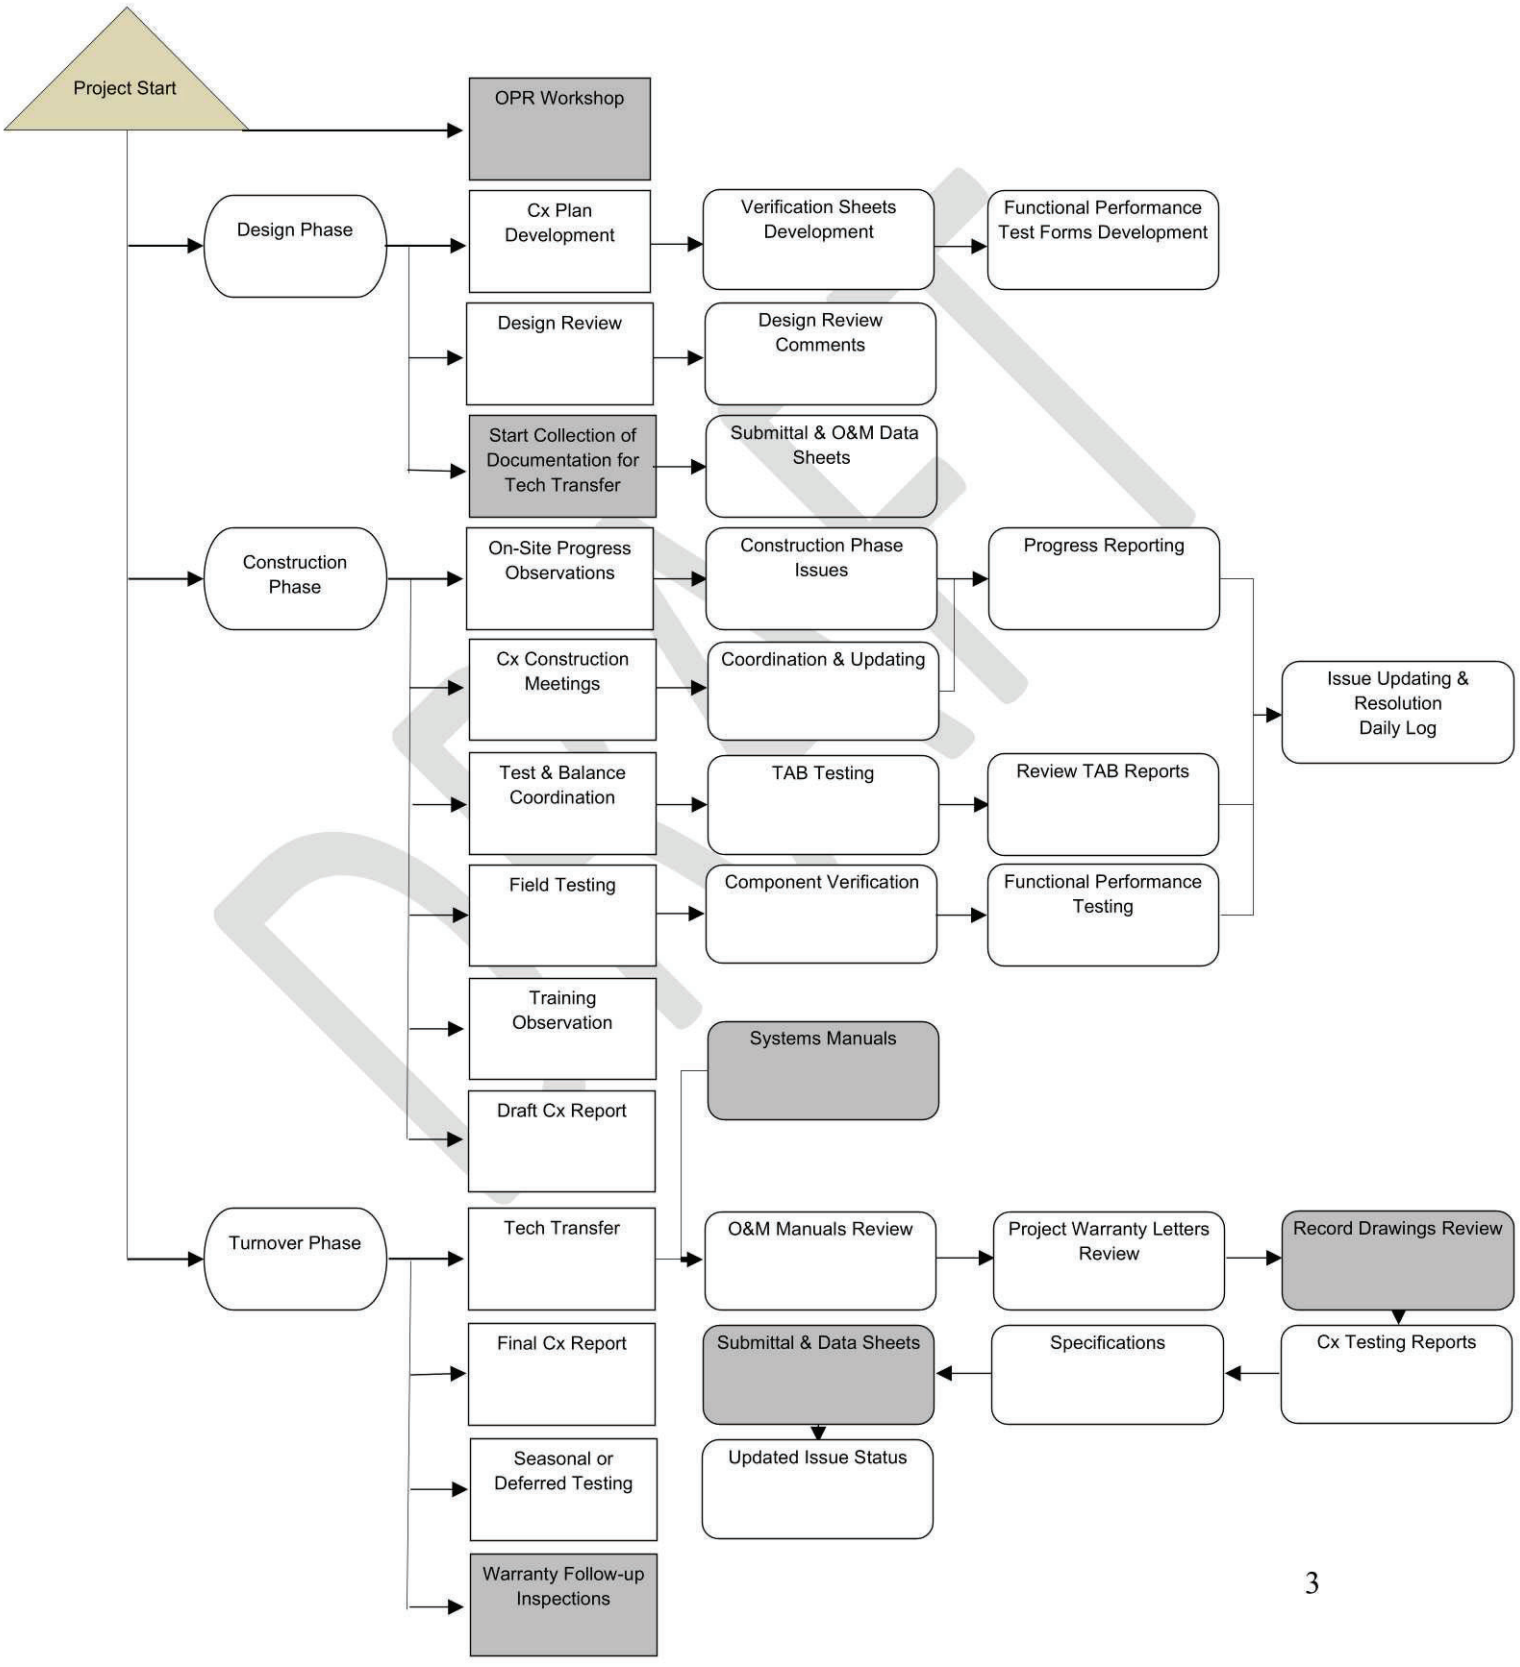

1.5 Commissioned Systems

The following systems are being commissioned for this project. All general references to equipment in this document refer only to equipment that is to be commissioned.

HVAC System (and all integral equipment controls)

- Air cooled chillers
- CHW Pumps
- AHU's
- VAV's
- CHW fan coil units
- Computer room AHU's
- Exhaust Fans / Kitchen Hood Fans
- Variable Frequency Drives
- Ductless Split Systems
- Testing, adjusting, and balancing.
- Facility management and control system (controlled devices, control loops, and system integration)

Electrical and Lighting Systems

- Panelboards
- Exterior Lighting
- Interior Lighting
- Generator

Plumbing Systems

- Plumbing Fixtures
- Water Heaters

DRAFT

1.6 Appendix A – Pre-Commissioning Checklists

Air cooled chillers
CHW pumps
Buffer Tank
AHU's
CHW fan coil units
Ductless Split Systems
Variable Frequency Drives
VAV Terminal Units
Exhaust Fans
Ductwork
Automatic Controls
Plumbing Fixtures
Elec. Water Heaters
Panelboards
Interior Lighting
Exterior Lighting
Generator

1.7 Appendix B – Functional Performance Tests

Air cooled chillers
CHW pumps
AHU's
CHW Fan coil units
Computer room AHU's
Ductless Split Systems
VAV Terminal Units
Exhaust Fans
Test & Balance Verification
Plumbing Fixtures
Water Heaters
Panelboards
Interior Lighting
Exterior Lighting
Generator

DRAFT

1.8 General Building Information

Project: City of Greenacres Municipal Operations Center

Location: 5770 Melaleuca Lane
Greenacres, Florida 33463

Square Footage: Approx. 43,000 sq. ft.

Buildings: 2-story municipal operations center.

Project Schedule:

Design Complete: February 2026

Construction Complete: Spring 2028

Project Budget: Approx. $30 m

Description: New construction of the municipal operations center, including chillers, CHW pumps, AHU's, fan coil units, VAV's, ductless split system, exhaust fans, and building automation control system.

DRAFT

3.0 Construction/Cx Team Data (primary parties)

Team Member	Company & Contact Names	Office, Cell, Email
Owner City of Greenacres		O: C: Email:
Architect Song & Associates 1545 Centrepark Drive North West Palm Beach, FL 33401		O: (561) 655-2423 C: Email:
Commissioning Provider CMTA 600 S. Orlando Ave. Maitland, FL 32751	Art Munns, CxA	O: (407) 332-5110 C: (407) 808-9782 Email: william.munns@cmta.com
Electrical Designer/Eng. CMTA 600 S. Orlando Ave. Maitland, FL 32751	Sudharma Wijegunawardan, PE	O: (561) 688-6575 C: (561) 723-0129 Email: Sudharma Wijegunawardan@cmta.com
Mechanical Designer/Eng. CMTA 600 S. Orlando Ave. Maitland, FL 32751	Jason Smith, PE	O: (407) 332-5110 C: (407) 701-0703 Email: jason.smith@cmta.com
General Contractor		O: C: Email:
Mechanical Contractor		O: C: Email:
Electrical Contractor		O: C: Email:
Plumbing Contractor		O: C: Email:
TAB Contractor		O: C: Email:
Controls Contractor		O: C: Email:

DRAFT

4.0 Roles and Responsibilities

The CxP was hired by the owner directly. In general, the CxP coordinates the commissioning activities and reports to the program manager and owner. The CxP's responsibilities, along with all other contractors' commissioning responsibilities, are detailed in the specifications. The specifications will take precedence over this Cx plan. All members work together to fulfill their contracted responsibilities and meet the objectives of the contract documents. For coordination purposes, the commissioning scope involving all parties is outlined here.

1. Document systems design intent (A/E)

2. Inspect and confirm that equipment and systems have been properly installed in accordance with the contract documents and manufacturer's written installation instructions (CxP and contractor).

3. Inspect and confirm that equipment has been placed into operation with manufacturer's oversight and approval and in accordance with contract requirements. (CxP and contractor).

4. Identify, document, and report all deficiencies of the work versus contract specifications and performance requirements, for tracking and correction (CxP and contractor).

5. Monitor and enforce accessibility of all work areas and pieces of equipment. (contractor).

6. Assemble contractor as-built drawings (contractor).

7. Assemble operation, installation and maintenance instructions and submittal data (contractor).

8. Inspect and confirm the performance of each piece of equipment and each system (CxP and contractor), as described in the contract.

9. Validate the test and balance report. (Contractor, CxP)

10. Train owners' personnel in the proper operation of each piece of equipment and each system (contractor, CxP and A/E).

11. Document warranties start and end dates (contractor).

12. Prepare final commissioning report. (CxP)

DRAFT

4.1 Commissioning Team

The commissioning team will consist of all members needed to execute the approved commissioning program. Minimum membership shall include:

1. Commissioning Provider (CxP)
2. Owner's Mechanical Engineer
3. Owner's Maintenance Representative
4. Contractor's Trade Representative
5. Mechanical Trade Representative
6. TAB Contractor
7. BAS Contractor
8. Engineer of Record

The contractor's personnel shall be made available to execute all aspects of the commissioning program until the owner accepts results.

4.2 Responsibilities

Owner:

1. Assign engineering and maintenance personnel and schedule them to participate in the various meetings, training sessions and inspections.

Commissioning Provider:

1. Review all commissioning requirements and intent of the contract documents and all related testing, verification, and quality control procedures.

2. Coordinate the pre-commissioning and final commissioning schedules and activities.

3. Make periodic visits to the site, as necessary to witness equipment and system installations.

4. Schedule a pre-commissioning coordination meeting at some convenient location and at a time suitable to the contractor and engineers of record. In attendance are the respective representatives of the GC, CM, CxP, PM, A/E and the mechanical, controls, and TAB subs. This pre-commissioning meeting will be for reviewing the complete commissioning program, the flow of documents, establishing tentative schedules for maintenance orientation and inspections, O&M submittals, training sessions, job completion, system start-up and testing. At the meeting, commissioning parties are introduced, the commissioning process is reviewed, and management and reporting lines are determined. The Cx plan is reviewed, and process questions are addressed. Also covered is the general list of each party's responsibilities.

5. Attending selected planning and job-site meetings to remain informed on construction progress and to update parties involved in commissioning. The CM and GC provide the CxP with information regarding substitutions, change orders and any supplemental instructions that may affect commissioning equipment, systems, or the commissioning schedule. Later during construction, the CxP, through the PM, as required, will schedule necessary meetings between various commissioning team parties.

6. Schedule HVAC systems training for maintenance personnel prior to final commissioning of the above systems.

7. Receive and review operation and maintenance (O&M) manuals as submitted by the contractor and approved by the engineer of record.

8. Schedule the owner training sessions.

9. Upon receipt of the approved test and balance report, plan and schedule the test and balance report validation with the TAB contractor.

10. Upon receipt of notification from the contractor that the systems have been started, and that the systems and equipment are functioning as designed and specified, schedule the functional performance tests. These demonstrations will be conducted by the contractor and the controls trade representatives and witnessed by the CxP and other appropriate parties.

11. Prepare the final commissioning report and submit it to the owner. Schedule final review with owner. Present all documentation and turn over signed acceptance of the system by the owner and CxP to the contractor.

Engineer of record:

1. Prepare basis of design and system description documentation.

2. Verify adequate maintenance accessibility for each piece of equipment in actual installation. Periodic inspections are part of the engineer of record's construction administration duties.

3. Attend and participate in maintenance training sessions.

4. Review and approve all shop drawings.

5. Receive and review O&M Manuals as submitted by the contractor. Insert sections on system description.

6. Issue field reports noting deficiencies requiring correction to the CxP.

Contractor:

1. Ensure full cooperation in the commissioning program.

2. Ensure cooperation and participation of specialty sub-trade representatives, as required.

3. Ensure participation of major equipment manufacturers and their representatives, as required.

4. Prepare operation, maintenance and installation manual submission, training sessions, equipment operation and job completion verification for use by CxP.

5. Conduct training sessions and conduct maintenance orientation and inspection sessions.

6. Update contractor as-built drawings and review with CxP.

7. Gather O&M data on all equipment and assemble it in binders. Submit to engineer of record prior to the distribution completion stage.

8. Conduct and schedule representatives to participate in the training sessions as scheduled by CxP.

9. Provide written certification that the work has been completed in accordance with the plans and specifications and that they are functioning as designed. Submit completed pre-functional checklist forms to CxP prior to the final verification.

10. At the completion of the controls and energy management systems start- up and adjustment work, demonstrate to CxP the performance of the facilities management and control systems.

11. Demonstrate the performance of each piece of equipment to the CxP. Schedule the contractor representatives that apply to demonstrate the performance of the equipment and systems.

12. Provide personnel and equipment as required to validate the TAB work.

13. Turn over set of contractor as-built drawings to CxP for review prior to incorporation into the record drawings.

5.0 Commissioning Process

This section details the commissioning process by commissioning tasks or activity.

5.1 LEED Requirements (NOT REQUIRED)

For this project, "LEED for new construction" addressed building Cx in 1 place, **EA prerequisite 1**. The scope of services for Cx should be based on the owner's project requirements. The following table outlines the team members primarily responsible for performing each Cx requirement.

Table 5-1 LEED related Cx team members' responsibilities

Task	Responsibilities
Designate Cx Authority (CxP)	Architect
Document Owner's Project Requirements (OPR)	Architect, CxP
Develop the Basis of Design	Design Team
Incorporate Cx requirements into construction documents	CxP, Design Team
Conduct Cx design review to mid-construction documents	CxP
Develop and implement a Cx plan	CxP
Review contractor submittals applicable to systems being submitted	N/A
Verify the installation and performance of commissioned systems	CxP
Develop a systems manual for the commissioned systems	N/A
Verify that the requirements for training are completed	Project team, CxP
Complete a summary Cx report	CxP
Review building operations within 10 months after substantial completion	N/A

5.2 Miscellaneous Management Protocols

The following protocols will be used on this project.

Issue	Protocol
For requests for information (RFI) or formal documentation requests:	The CxP goes first to the PM and the GC.
For minor or verbal information and clarification:	The CxP goes directly to the informed party.
For notifying contractors of deficiencies:	The CxP documents deficiencies through the PM, but may discuss deficiency issues with contractors prior to notifying the PM.
For scheduling functional tests or training:	The CxP works with the PM and GC to develop schedules.
For scheduling commissioning meetings:	The CxP selects the date and schedules through the GC.
For making a request for significant changes:	The CxP has no authority to issue change orders.
For making small changes in specified sequences of operations:	The CxP may make small sequences of operations changes to improve efficiency or control or to correct deficiencies, through the responsible contractor, but shall review the change with the A/E, document the change and provide all changes of specified sequences to the PM and A/E.
Subcontractors disagreeing with requests or interpretations by the CxP shall:	Try and resolve with the CxP first. Then work through GC who will work with CxP directly or through the PM to resolve the situation.

5.3 Submittals and Documentation

The CxP provides all subs responsible for commissioned equipment with commissioning documentation requirements for their respective equipment and systems. This data request typically coincides with the normal A/E submittal process. At minimum, this equipment data includes installation and start-up procedures, approved shop drawings, O&M data, performance data and control drawings.

5.4 Special Submittals, Notifications and Clarifications

The subs, GC or A/E notify the CxP of any new design intent or operating parameter changes, added control strategies and sequences of operation, or other change order that may affect commissioned systems. The controls contractor provides the CxP a full points list with details requested by the CxP. Thirty (30) days prior to performing any required tests, cleaning, or

flushing the subs provide the CxP full details of the procedures. As the phases of the TAB are completed, the draft TAB report is provided to the CxP with full explanations of approach, methods, results, data table legends, etc. The final TAB report is provided to the CxP upon completion. These submittals to the CxP do not constitute compliance for submittals for the O&M manuals. The CxP may request additional design narrative from the A/E and from the controls contractor depending on how complete the documentation was which was provided with the bid documents. The CxP may submit written RFIs to contractors through the PM, or address them directly for clarifications, as needed.

5.5 Pre-functional Checklists

The word pre-functional refers to before functional testing. Pre-functional checklists (PC) are important to ensure that the equipment and systems are hooked up and operational and that functional performance testing may proceed without unnecessary delays. Each piece of equipment receives full pre-functional checkout by the contractor. No sampling strategies are used. In general, pre-functional testing for a given system must be successfully completed prior to formal functional performance testing of equipment or sub-systems of the given system.

Pre-functional checklists are primarily static inspections and procedures to prepare the equipment or system for initial operation (e.g., oil levels checked, fan belt tension, labels affixed, gauges in place, sensor calibration, etc.). However, some pre-functional checklist items entail simple testing of the function of a component, a piece of equipment or system (such as measuring the voltage imbalance on a three-phase pump motor of a chiller system). Pre-functional checklists augment and are combined with the manufacturer's start-up checklist.

Contractors typically already perform some, if not all, of the pre-functional checklist items the commissioning provider will recommend. However, few contractors document in writing the execution of these checklist items. This project requires that the procedures be documented in writing by the installation technician. The CxP does not witness all the pre-functional checklist verification, except for testing larger or more critical pieces of equipment and some spot-checking.

5.6 Start-up

The CxP assists the commissioning team members responsible for start-up in developing detailed start-up plans for all equipment. All start-up plans are to be approved by the CxP.

Four weeks prior to start-up, the subs and vendors schedule start-up and initial checkout with the PM, GC and CxP. The start-up and initial checkout are directed and executed by the sub or vendor. The CxP, and PM, if necessary, observe, at minimum, the procedures for each piece of primary equipment, unless there are multiple units, when a sampling strategy is used. For components of equipment, (e.g., VAV boxes), the CxP observes a sampling of the pre-functional and start-up procedures.

To document the process of start-up and checkout, the site technician performing the line-item task initials and dates each paragraph of procedures in the "start-up plan" and checks off items on the pre-functional and manufacturer field checkout sheets, as they are completed. Only individuals having direct knowledge of a line item being completed shall check or initial the forms.

The subs and vendors execute the checklists and tests and submit a signed copy of the completed start-up and pre-functional tests and checklists to the CxP. The CxP may review pre-functional checklists in progress, as necessary.

The subs clearly list any outstanding items of the initial start-up and pre-functional procedures that were not completed successfully at the bottom of the procedures form or on an attached sheet. The procedures form and deficiencies are provided to the CxP within two days of test completion. The CxP works with the subs and vendors to correct and retest deficiencies or uncompleted items, involving the PM and others, as necessary. The installing subs or vendors correct all areas that are deficient or incomplete according to the checklists and tests.

5.7 TAB Plan

The TAB contractor submits the outline of the TAB plan and approach to the CxP and the controls contractor eight weeks prior to starting the TAB. Included in the approach is an explanation of the intended use of the building control system. The CxP reviews the plan and approach for understanding and coordination issues and may comment but does not approve changes. The controls contractor reviews the feasibility of using the building control system for assistance in the TAB work. The TAB submits weekly written reports of discrepancies, contract interpretation requests and lists of completed tests to the CxP and PM. This facilitates quicker resolution of problems and will result in a more complete TAB before functional testing begins. TAB work will not begin until the control system has been pre-functionally tested and selective functional tests have been performed and approved by the CxP.

5.8 Controls Check Out Plan

The controls contractor develops and submits a written step-by-step plan to the CxP, which describes the process they intend to follow in checking out the control system and the forms on which they will document the process. The controls contractor will also meet with the TAB contractor prior to the start of TAB and review the TAB plan to determine the capabilities of the control system for use in TAB. The controls contractor will provide the TAB with any necessary unique instruments for setting terminal unit boxes and instruct TAB in their use (hand-held control system interface for use around the building during TAB, etc.). The controls contractor should also provide a technician qualified to operate the controls to assist the TAB contractor in performing TAB.
All CxP required pre-functional checklists, calibrations, start-up and selected functional tests of the system to be completed and approved by the CxP prior to TAB. The controls contractor shall execute the tests and trend logs assigned to them and remain on site for assistance for mechanical system functional tests.

5.9 Development of Functional Test and Verification Procedures

5.9.1 Overview

Functional testing is the dynamic testing of systems (rather than just components) under full operation (e.g., the chiller pump is tested interactively with the chiller functions to see if the pump ramps up and down to maintain the differential pressure set point). Systems are tested under various modes, such as during low cooling or heating loads, high loads, component failures, unoccupied, varying outside air temperatures, fire alarm, power failure, etc. The systems are run through all the control system's sequences of operation and components are verified to be responding as the sequences state. The Commissioning provider develops the functional test procedures in a sequential written form, coordinates and documents the actual testing, which is usually performed by the installing contractor or vendor.

5.9.2 Scope of Testing

A detailed description of the functional and pre-functional testing procedures and process will be developed for this project by the CxP for each piece of commissioned equipment.

5.9.3 Development Process

Before test procedures are written, the CxP obtains all requested documentation and a current list of change orders affecting equipment or systems, including an updated points list, control sequences and set points. The CxP develops specific test procedures to verify proper operation of each piece of equipment and system. The CxP obtains clarification, as needed, from contractors and the A/E regarding sequences and operation to develop these tests. Prior to execution, the CxP provides a copy of the primary equipment tests to the installing sub (via the GC) who reviews the tests for feasibility, safety, warranty, and equipment protection. Blank copies of the procedures are input into the O&M manuals for later use by operations staff.

Functional testing and verification may be achieved by manual testing (persons manipulate the equipment and observe performance) or by monitoring the performance and analyzing the results using the control system's trend log capabilities or by stand- alone data loggers. The CxP uses judgment where needed to determine which method is most appropriate.

5.10 Execution of Functional Testing Procedures

5.10.1 Overview and Process

The CxP schedules functional tests through the PM, GC and affected subs. For any given system, prior to performing functional testing, the CxP waits until the pre-functional checklist has been submitted with the necessary signatures, confirming that the system is ready for functional testing. The CxP oversees, witnesses, and documents the functional testing of all equipment and systems according to the specifications and the Cx plan. The subs execute the tests. The control system is tested before it is used to verify the performance of other components or systems. The air balancing and water balancing is completed before functional testing of air-related or water-related equipment or systems. Testing proceeds from components to subsystems to systems and finally to interlocks and connections between systems.

5.10.2 Deficiencies and Re-testing

The CxP documents the results of the test. Corrections of minor deficiencies identified are made during the tests at the discretion of the CxP. The CxP records the results of the test on the procedure or test form. Deficiencies or non-conformance issues are noted and reported to the PM on the *Commissioning Corrective Action Report* (Daily Log). Subs correct deficiencies, notify the CxP and return the form documenting correction. The CxP schedules retesting through the PM. Decisions regarding deficiencies and corrections are made at as low a level as possible, preferably between CxP or PM and the sub. For areas in dispute, final authority, besides the owner's, resides with the A/E. The CxP recommends acceptance of each test to the PM. The PM gives final approval on each test.

5.11 Operating and Maintenance Manuals

The CxP reviews the O&M manuals and documentation for systems that were commissioned to verify compliance with the specifications. The CxP recommends approval and acceptance of these sections of the O&M manuals to the PM. The CxP also reviews each equipment warranty and verifies that all requirements to keep the warranty valid are clearly stated.

Initial preparation shall be the responsibility of the HVAC and electrical trade representative as per contract bid document.

5.12 Training of Owner's Personnel

The owner's maintenance personnel shall be given comprehensive training in understanding the systems and the operation and maintenance of each major piece of equipment. The CxP, in cooperation with the contractor, schedules the training, which shall start with classroom sessions followed by hands-on training on each piece of equipment. Hands on training shall include start-up, operation in all modes possible, shutdown and any emergency procedures.

The contractor or their representative shall conduct and record all sessions and shall add to each session any special information relating to the details of installation of the equipment as it might impact on the operation and maintenance.

5.12.1 Overall Plan

After reviewing the specifications, and after interviewing facility staff, if necessary, the owner and CxP fill out a table listing all the equipment for which training or orientation will be provided listing, among other things, the type and number of trainees, rigor of training desired by the owner, the primary responsible subcontractor, the trainer's company, and columns for tracking training agendas. The Commissioning provider provides this form to the contractor for reference.

The contractor will prepare a training agenda describing the subjects covered, duration of each subject and the methods that will be used in the training, along with the name and qualifications of the trainer(s) for submission to the owner and CxP. The owner and CxP review the agenda; make comments; approve the training subject to the comments; and submit back to the contractor. The contractor provides the approved agenda to the trainer to use during the training. The trainer provides a copy of the agenda to each trainee.

5.13 Warranty Period

During the warranty period, seasonal testing and other deferred testing required is completed according to the specifications. The CxP coordinates this activity. Tests are executed, and deficiencies corrected by the appropriate subs, witnessed by facilities staff and the CxP. Any final adjustments to the O&M manuals and record drawings due to the testing are made. In addition, the CxP will return to the project approximately 10 months into the 12-month warranty period. During this visit(s) the CxP will review with facility staff the current building operation and the condition of outstanding issues related to the original and seasonal commissioning. The CxP will also interview facility staff and identify problems or concerns they have with operating the building as originally intended.
The CxP will make suggestions for improvements and for recording these changes in the O&M

manuals. The CxP will identify areas that may come under warranty or under the original construction contract. The CxP will also assist facility staff in developing reports and documents and requests for services to remedy outstanding problems.

5.14 Final Commissioning Report

A final summary report by the CxP will be provided to the PM. The report shall include an executive summary, list of participants and roles, brief building description, overview of commissioning and testing scope and a general description of testing and verification methods. For each piece of commissioned equipment, the report should contain the disposition of the Commissioning provider regarding the adequacy of the equipment, documentation and training meeting the contract documents. All outstanding non-compliance items shall be specifically listed. Each non-compliance issue shall be referenced to the specific functional test, inspection, trend log, etc. where the deficiency is documented. The functional performance and efficiency section for each piece of equipment shall include a brief description of the verification method used (manual testing, BAS trend logs, data loggers, etc.) and include observations and conclusions from the testing.
The final commissioning report shall be submitted. The report shall contain as a minimum the following information:

- Cover sheet with the following information:
- Date
- Project and address
- Architect
- Engineer
- General contractor
- SCA (name, address, e-mail & phone number)
- Final updated commissioning plan
- Name, address, phone, e-mail for commissioning team members
- Completed copies of all commissioning forms
- Copies of Cx related RFI's, meeting minutes, contractor certification, reports, and code authority inspections.
- Copies of inspection and construction observation reports
- Copy of equipment and system certification forms with listing of equipment and systems commissioned.
- Copies of completed component test forms.

DRAFT

Exhibit G

Staff

Greenacres Municiple Operations Center

STATED RATES

POSITION	HOURLY RATE
Project Executive	$ 246.04
Sr. Superintendent	$ 202.37
Project Manager 1	$ 140.11
Sr Accountant	$ 112.92
Asst. Superintendent	$ 99.62
Project Engineer 1	$ 91.22
Admin Asst.	$ -

Exhibit H

Form of Change Order

PCPCO #002

Kaufman Lynn Construction, Inc.
3185 S. Congress Avenue
Delray Beach, Florida 33445
Phone: 561-361-6700
Fax: 561-361-6979

Greenacres
Greenacres, Florida

DRAFT

EXAMPLE CO FOR AMENDMENT

TO:	The City of Greenacres 5800 Melaleuca Lane Greenacres Florida, 33463	**FROM:**	Kaufman Lynn Construction, Inc. 3185 S. Congress Avenue Delray Beach Florida, 33445
PCO NUMBER/REVISION:	002 / 0	**CONTRACT:**	1189-01 - Precon GMP
STATUS:	Draft	**CREATED BY:**	Nathan Coker **(Kaufman Lynn Construction, Inc.)**
SCHEDULE IMPACT:		**DATE CREATED:**	7/30 /2026
		TOTAL AMOUNT:	$40,300.23

POTENTIAL CHANGE ORDER TITLE: EXAMPLE CO FOR AMENDMENT

CHANGE REASON: Adverse Weather

POTENTIAL CHANGE ORDER DESCRIPTION: *(The Contract Is Changed As Follows)*

Example description for Amendment

ATTACHMENTS:

KL- Greenacres Pruning #01623 REVISED.pdf

#	SubJob	Cost Code	Description	Type	Amount
1	1189Z Greenacres EOC Preconstruction	02-060 - Tree Removal	Root Pruning	Subcontractor	$ 36,590.00
				Subtotal:	$36,590.00
				Builders Risk: 1.00% Applies to All Line Items	$ 366.00
				KL Insurance: 1.45% Applies to All Line Items	$ 530.56
				Subcontractor Default Insurance: 1.58% Applies to All Line Items	$ 578.12
				Payment & Performance Bond: 1.11% Applies to All Line Items	$ 406.15
				Overhead & Profit: 5.00% Applies to All Line Items	$ 1,829.50
				Grand Total:	**$40,300.23**

Example only. Final numbers to be recalculated without Builders Risk

BY SIGNING BELOW, OWNER AUTHORIZES CONTRACTOR TO PROCEED AND AGREES TO ALL TERMS INCLUDING PAYMENT AS DESCRIBED IN THIS POTENTIAL CHANGE ORDER.

The City of Greenacres
5800 Melaleuca Lane
Greenacres Florida 33463

Kaufman Lynn Construction, Inc.
3185 S. Congress Avenue
Delray Beach Florida 33445

SIGNATURE	DATE	SIGNATURE	DATE	SIGNATURE	DATE

Composite Exhibit I

Miscellaneous Forms

Material Delivery Tracking Log

SAMPLE PROJECT

Late submittal based on Update Thru Date = LS C
Critical Item =
Number of Critical Items = 29

Update Thru: 08/06/2026

Update Thru: 08/06/2026

			SUBMITTALS - IN			SUMMITTALS- OUT					FABRICATION					CONSTRUCTION							
		Subcontractor / Supplier	Anticipated Receipt of Sub Shops	Shop Drwgs Required From Sub	Actual Shop Drwgs Submitted	Review Period (Cal Days)	Anticipated Approval of Shop Drwgs	Req'd Approval of Shop Drwgs	Submittal Status	Actual Approval of Shop Drwgs	Fab Lead Time (Cal Days)	Anticipated Release for Fab	Req'd Release for Fab	Actual Release for Fab	Shop Visit/ Testing/ Notes	Estimated Delivery Date to Jobsite	Req'd on Jobsite	Actual Date on Jobsite	Equipment Delivery Float (Days)	Manufacturer	Manufacturer POC	Manufacturer POC Phone	Comments
		Bought = X					08/06/2026										C = Critical item						
020000 Sitework / Utilities																							
Pavers (Pedestrian)		Crossroad		NONE			NONE	NONE			56	NONE	NONE			NONE			NONE				
Pavers (Vehicular)		Crossroad		NONE			NONE	NONE			40	NONE	NONE			NONE			NONE				
Storage Vault		Redland		NONE			NONE	NONE			30	NONE	NONE			NONE			NONE				
Sanitary Manhole Structures		Redland		NONE			NONE	NONE			21	NONE	NONE			NONE			NONE				
Storm Structures		Redland		NONE			NONE	NONE			21	NONE	NONE			NONE			NONE				
Lift Station		Redland		NONE			NONE	NONE				NONE	NONE			NONE			NONE				
FDC and Fire Hydrants		Redland		NONE			NONE	NONE				NONE	NONE			NONE			NONE				
Precast Site Wall				NONE			NONE	NONE				NONE	NONE			NONE			NONE				
Site Furnishing (Bike Racks)				NONE			NONE	NONE				NONE	NONE			NONE			NONE				
Traffic Rated Bollards		Coastal		NONE			NONE	NONE				NONE	NONE			NONE			NONE				
Irrigation Pump				12/19/2026			NONE	12/19/2026			42	NONE	12/21/2026			NONE	02/01/2027		NONE				
Boulders				NONE			NONE	NONE				NONE	NONE			NONE			NONE				
Vehicular Gates				NONE			NONE	NONE				NONE	NONE			NONE			NONE				
040000 Masonry																							
Stone Veneer		Florida Stone	12/09/2025	06/24/2026	12/12/2025	14	12/26/2025	07/08/2026	APP	12/30/2025	42	12/28/2025	07/10/2026			07/13/2026	08/21/2026		39	L&W Supply	Scott Thibodeau	954-275-8785	
050000 Metals																							
Balcony Railings		Coastal		NONE			NONE	NONE				NONE	NONE			NONE			NONE				
Stair #2 & Railings	LS	Coastal		01/24/2026			NONE	01/24/2026			**70**	NONE	04/06/2026			NONE	04/06/2026		-122				
Main Entry Canopies		Coastal		12/13/2026	04/24/2026		04/24/2026	12/13/2026				NONE	12/15/2026			NONE	12/15/2026		NONE				
Wrap Around Canopy	LS	Coastal		12/13/2026			NONE	12/13/2026				NONE	12/15/2026			NONE	12/15/2026		NONE				
Elevator Metals (Divider Mesh and Sump Pit Cover)	LS	Coastal		01/11/2027			NONE	01/11/2027				NONE	01/13/2027			NONE	01/13/2027		NONE				
Roof Access Ladders		Coastal		NONE	01/30/2025	14	02/13/2025	NONE				NONE	NONE			NONE		01/26/2026	ON SITE				
Bahama Shutters	C	Coastal		06/14/2026	04/24/2026		04/24/2026	06/14/2026				NONE	06/16/2026			NONE	06/16/2026		-51				
Lift Station Fence		Coastal		NONE			NONE	NONE				NONE	NONE			NONE			NONE				
Dumpster Gate	LS	Coastal		02/23/2027			NONE	02/23/2027				NONE	02/25/2027			NONE	02/25/2027		NONE				
Hoist, safety and Separator Beam		Coastal		NONE			NONE	NONE				NONE	NONE			NONE			NONE				
060000 Woods & Plastics																							
Casework/Millwork (General 1st Level)	LS			10/05/2026			NONE	10/05/2026				NONE	10/07/2026			NONE	10/07/2026		NONE				
Stone/Quartz Backsplash	LS			09/21/2026			NONE	09/21/2026				NONE	09/23/2026			NONE	09/23/2026		NONE				
Casework/Millwork (General 2nd Level)	LS			10/05/2026			NONE	10/05/2026				NONE	10/07/2026			NONE	10/07/2026		NONE				
Stone/Quartz Backsplash	LS			09/21/2026			NONE	09/21/2026				NONE	09/23/2026			NONE	09/23/2026		NONE				
Wood Railings				NONE			NONE	NONE				NONE	NONE			NONE			NONE				
Wood Pavilion				NONE			NONE	NONE				NONE	NONE			NONE			NONE				
				NONE			NONE	NONE				NONE	NONE			NONE			NONE				
				NONE			NONE	NONE				NONE	NONE			NONE			NONE				
07300 Roofing																							
Metal Roof Panels		Wolverine		08/29/2026	01/07/2026		01/07/2026	08/29/2026			**21**	NONE	08/31/2026			NONE	09/21/2026		NONE	Englert	Toni Delphino	305-776-2686	
Roofing Material (Misc.)	C	Wolverine		06/27/2026	01/07/2026		01/07/2026	06/27/2026			21	NONE	06/29/2026			NONE	07/20/2026		-17				
Roof Flashing	C	Wolverine		06/14/2026	01/07/2026		01/07/2026	06/14/2026			21	NONE	06/16/2026			NONE	07/07/2026		-30				
TPO Material (Low and High Roof)		Wolverine		NONE	01/07/2026		01/07/2026	NONE			14	NONE	NONE			NONE			NONE	Carlisle	Anthony	717-462-5021	
Gutters	LS	Wolverine		06/14/2026			NONE	06/14/2026			21	NONE	06/16/2026			NONE	07/07/2026		-30	Englert	Toni Delphino	305-776-2686	
Downspouts	LS	Wolverine		06/14/2026			NONE	06/14/2026			21	NONE	06/16/2026			NONE	07/07/2026		-30	Englert	Toni Delphino	305-776-2686	
Roof Hatches		Wolverine		05/19/2026	01/07/2026		01/07/2026	05/19/2026			7	NONE	05/21/2026			NONE	05/28/2026		-70				
Weather Vane		Wolverine		06/13/2026			NONE	06/13/2026				NONE	06/15/2026			NONE	06/15/2026		-52				
Asphalt Shingles for Wood Pavilion		Wolverine		02/02/2027	01/07/2026		01/07/2026	02/02/2027				NONE	02/04/2027			NONE	02/04/2027		NONE				
LWIC		Wolverine		05/02/2026	01/07/2026		01/07/2026	05/02/2026	APP	01/22/2026	0	NONE	05/04/2026			05/27/2026	05/04/2026		-94	Madrid 9-12	Orlando	954-391-0609	
Sheathing		Wolverine		05/23/2026	01/07/2026		01/07/2026	05/23/2026			21	NONE	05/25/2026			NONE	06/15/2026		-52				
Coping Cap	C	Wolverine		05/05/2026	01/07/2026		01/07/2026	05/05/2026			21	NONE	05/07/2026			NONE	05/28/2026		-70				
080000 Doors & Glass																							
Glass Railing	LS	Ready Window	01/30/2026	02/14/2026		14	02/13/2026	02/28/2026			70	02/15/2026	03/02/2026			04/26/2026	05/11/2026		-87				
Storefront Entry Doors & Glass	C	Ready Window	01/30/2026	02/14/2026	02/03/2026	14	02/17/2026	02/28/2026			70	02/19/2026	03/02/2026			04/30/2026	05/11/2026		-87				
Punch Window		Ready Window	01/30/2026	02/14/2026	02/03/2026	14	02/17/2026	02/28/2026			**70**	02/19/2026	03/02/2026			06/12/2026	05/11/2026		-87				
Spandrel Glass	LS	Ready Window	01/30/2026	02/14/2026		14	02/13/2026	02/28/2026			**70**	02/19/2026	03/02/2026			04/26/2026	05/11/2026		-87				
Door 225 (Switchable Glass)	LS	Ready Window	01/30/2026	02/14/2026		14	02/13/2026	02/28/2026			**70**	02/19/2026	03/02/2026			04/26/2026	05/11/2026		-87				
Break Metal	LS	Ready Window	01/30/2026	NONE		14	02/13/2026	NONE			**14**	02/19/2026	NONE			03/01/2026			NONE				
Door Lite	LS	Ready Window	01/30/2026	NONE		14	02/13/2026	NONE			10	02/19/2026	NONE			02/25/2026			NONE				
Bullet-Resistant Glass	LS	Ready Window	01/30/2026	01/17/2026		14	02/13/2026	01/31/2026			98	02/19/2026	02/02/2026			05/24/2026	05/11/2026		-87				
Interior Storefront Glass	LS	Ready Window	01/30/2026	02/28/2026		14	02/13/2026	03/14/2026			**56**	02/19/2026	03/16/2026			04/12/2026	05/11/2026		-87				
Hollow Metal Frames & Doors (Interior)		Lotspeich		NONE		14	NONE	NONE			8-10 weeks	NONE	NONE			NONE			NONE				
Flush Wood Doors		Lotspeich		NONE		14	NONE	NONE			8-10 weeks	NONE	NONE			NONE			NONE				
Door Hardware		Lotspeich		NONE		14	NONE	NONE				NONE	NONE			NONE			NONE				
Hollow Metal Frames & Doors (Exterior)	LS	Lotspeich		09/15/2026		14	NONE	09/29/2026				NONE	10/01/2026			NONE	10/01/2026		NONE				
090000 Finishes																							
SW Paint	LS			09/12/2026			NONE	09/12/2026				NONE	09/14/2026			NONE	09/14/2026		NONE				
LVT		McDermott		NONE			NONE	NONE				NONE	NONE			NONE			NONE				
PT-1	LS			08/24/2026			NONE	08/24/2026				NONE	08/26/2026			NONE	08/26/2026		NONE				
PT-2	LS			08/24/2026			NONE	08/24/2026				NONE	08/26/2026			NONE	08/26/2026		NONE				
Static Dissipative Tile		McDermott		NONE			NONE	NONE				NONE	NONE			NONE			NONE				
Terrazo		Bay to Bay		NONE			NONE	NONE				NONE	NONE			NONE			NONE				
Epoxy		Bay to Bay		NONE			NONE	NONE				NONE	NONE			NONE			NONE				
Drywall	LS			08/29/2026			NONE	08/29/2026				NONE	08/31/2026			NONE	08/31/2026		NONE				
Bullet Ressistant Drywall		Dorado		NONE			NONE	NONE				NONE	NONE			NONE			NONE				
Stucco	LS	Dorado		10/12/2026			NONE	10/12/2026				NONE	10/14/2026			NONE	10/14/2026		NONE				
Ext. Framing	LS	Dorado		08/09/2026			NONE	08/09/2026				NONE	08/11/2026			NONE	08/11/2026		NONE				
Ext. Framing Plywood	LS	Dorado		08/09/2026			NONE	08/09/2026				NONE	08/11/2026			NONE	08/11/2026		NONE				
ACT	LS	Lotspeich		08/01/2026			NONE	08/01/2026				NONE	08/03/2026			NONE	08/03/2026		-3				
Metal Wood Ceiling		LOtspeich		NONE			NONE	NONE				NONE	NONE			NONE			NONE				
Crash Bumper in Chambers		Lotspeich		NONE			NONE	NONE				NONE	NONE			NONE			NONE				

Material Delivery Tracking Log

Update Thru: 08/06/2026

Update Thru: 08/06/2026

Davie Town Hall

Late submittal based on Update Thru Date = / Critical Item =	LS	C	Subcontractor / Supplier	SUBMITTALS - IN: Anticipated Receipt of Sub Shops	SUBMITTALS - IN: Shop Drwgs Required From Sub	SUBMITTALS - IN: Actual Shop Drwgs Submitted	SUMMITTALS- OUT: Review Period (Cal Days)	SUMMITTALS- OUT: Anticipated Approval of Shop Drwgs	SUMMITTALS- OUT: Req'd Approval of Shop Drwgs	SUMMITTALS- OUT: Submittal Status	SUMMITTALS- OUT: Actual Approval of Shop Drwgs	FABRICATION: Fab Lead Time (Cal Days)	FABRICATION: Anticipated Release for Fab	FABRICATION: Req'd Release for Fab	FABRICATION: Actual Release for Fab	FABRICATION: Shop Visit/ Testing/ Notes	CONSTRUCTION: Estimated Delivery Date to Jobsite	CONSTRUCTION: Req'd on Jobsite	CONSTRUCTION: Actual Date on Jobsite	CONSTRUCTION: Equipment Delivery Float (Days)	CONSTRUCTION: Manufacturer	CONSTRUCTION: Manufacturer POC	CONSTRUCTION: Manufacturer POC Phone	Comments
Number of Critical Items = 29			Bought = X					08/06/2026										C = Critical item						
CPT-1	LS		McDermott		09/21/2026			NONE	09/21/2026				NONE	09/23/2026			NONE	09/23/2026		NONE				
CPT-2	LS		McDermott		09/21/2026			NONE	09/21/2026				NONE	09/23/2026			NONE	09/23/2026		NONE				
Baseboard	LS		McDermott		09/21/2026			NONE	09/21/2026				NONE	09/23/2026			NONE	09/23/2026		NONE				
100000 Specialties																								
Fixed Seating (Council and One Stop Lobby)	LS		Steve Ward		08/16/2026		14	NONE	08/30/2026				NONE	09/01/2026			12/07/2026	09/01/2026		-97				
14200 Elevators																								
Elevator Cab #1	LS		TKE		06/06/2026			NONE	06/06/2026			112	NONE	06/08/2026	05/08/2026		09/28/2026	09/28/2026		53				
Elevator Cab #2	LS		TKE		06/06/2026			NONE	06/06/2026			**112**	NONE	06/08/2026	05/08/2026		09/28/2026	09/28/2026		53				
Elevator Cab #3	LS		TKE		06/06/2026			NONE	06/06/2026			112	NONE	06/08/2026	05/08/2026		09/28/2026	09/28/2026		53				
Elevator Cab #4			TKE		06/06/2026			NONE	06/06/2026			112	NONE	06/08/2026	05/08/2026		09/28/2026	09/28/2026		53				
210000 Wet Sprinkler Pipe Fire Protection																								
Jockey Pump			Polaris		09/02/2026	12/18/2025	14	01/01/2026	09/16/2026	ANN	01/06/2026	84	NONE	09/18/2026			NONE	12/11/2026		NONE	GPM United	Michael Barber	561-627-1178	
Jockey Pump Controller			Polaris		09/07/2026	12/18/2025	14	01/01/2026	09/21/2026	ANN	01/06/2026	84	NONE	09/23/2026			NONE	12/16/2026		NONE	GPM United	Michael Barber	561-627-1178	
Fire Pump			Polaris		08/30/2026	12/18/2025	14	01/01/2026	09/13/2026	ANN	01/06/2026	84	NONE	09/15/2026			NONE	12/08/2026		NONE	GPM United	Michael Barber	561-627-1178	
Fire Pump Controller			Polaris		09/02/2026	12/18/2025	14	01/01/2026	09/16/2026	ANN	01/06/2026	84	NONE	09/18/2026			NONE	12/11/2026		NONE	GPM United	Michael Barber	561-627-1178	
220000 Plumbing																								
Elevator Sump Pump			WB		NONE	10/17/2025	14	10/31/2025	NONE	ANN	10/30/2025	28	NONE	NONE			NONE		05/01/2026	ON SITE	Stancor		203-268-7513	
Booster Pump			WB		08/29/2026	09/24/2025	14	10/08/2025	09/12/2026	ANN	10/06/2025	98	NONE	09/14/2026			NONE	12/21/2026		NONE	VC Systems		954-888-8150	
Tankless Water Heater			WB		09/01/2026	10/07/2025	14	10/21/2025	09/15/2026	ANN	10/13/2025	28	NONE	09/17/2026			NONE	10/15/2026	05/01/2026	ON SITE	Chronomite		626-937-4270	
Water Heater			WB		08/04/2026	10/07/2025	14	10/21/2025	08/18/2026	ANN	10/13/2025	56	NONE	08/20/2026			NONE	10/15/2026	05/01/2026	ON SITE	Lochinvar		615-889-8900	
Toilets			WB		08/04/2026	10/27/2025	14	11/10/2025	08/18/2026	ANN	11/04/2025	56	NONE	08/20/2026			NONE	10/15/2026		NONE	American Standard		800-442-1902	
Lavatories			WB		08/04/2026	10/07/2025	14	10/21/2025	08/18/2026	ANN	10/13/2025	56	NONE	08/20/2026			NONE	10/15/2026		NONE	American Standard		800-442-1902	
Faucets			WB		08/04/2026	10/15/2025	14	10/29/2025	08/18/2026	ANN	10/22/2025	56	NONE	08/20/2026			NONE	10/15/2026		NONE	American Standard		800-442-1902	
Urinals			WB		08/04/2026	10/07/2025	14	10/21/2025	08/18/2026	ANN	10/13/2025	56	NONE	08/20/2026			NONE	10/15/2026		NONE	American Standard		800-442-1902	
Sinks			WB		08/04/2026	10/07/2025	14	10/21/2025	08/18/2026	ANN	10/13/2025	56	NONE	08/20/2026			NONE	10/15/2026		NONE	American Standard		800-442-1902	
Sink Faucet			WB		08/04/2026	10/27/2025	14	11/10/2025	08/18/2026	ANN	11/04/2025	56	NONE	08/20/2026			NONE	10/15/2026		NONE	Sloan		800-982-5839	
Mop Sink			WB		08/04/2026	10/07/2025	14	10/21/2025	08/18/2026	ANN	10/13/2025	56	NONE	08/20/2026			NONE	10/15/2026		NONE	Mustee		216-267-3100	
Mop Sink Faucet			WB		08/04/2026	10/15/2025	14	10/29/2025	08/18/2026	ANN	10/22/2025	56	NONE	08/20/2026			NONE	10/15/2026		NONE	T and S		800-476-4103	
Water Fountain			WB		08/04/2026	10/27/2025	14	11/10/2025	08/18/2026	ANN	11/04/2025	56	NONE	08/20/2026			NONE	10/15/2026		NONE	Elkay		800-260-6640	
Hot Water Recirculating Pump			WB		NONE	10/07/2025	14	10/21/2025	NONE	ANN	10/13/2025	56	NONE	NONE			NONE			NONE	Taco		401-942-8000	
Roof Drain			WB		02/22/2026	10/15/2025	14	10/29/2025	03/08/2026	ANN	10/22/2025	21	NONE	03/10/2026			NONE	03/31/2026	05/01/2026	ON SITE	Josam		800-356-6726	
Overflow Drain			WB		02/22/2026	10/07/2025	14	10/21/2025	03/08/2026	ANN	10/13/2025	21	NONE	03/10/2026			NONE	03/31/2026	05/01/2026	ON SITE	Josam		800-356-6726	
Floor Drains			WB		02/22/2026	10/07/2025	14	10/21/2025	03/08/2026	ANN	10/13/2025	21	NONE	03/10/2026			NONE	03/31/2026	05/01/2026	ON SITE	Sioux Chief		800-821-3944	
Wall Cleanout	C		WB		02/22/2026	10/27/2025	14	11/10/2025	03/08/2026	ANN	11/04/2025	21	NONE	03/10/2026			NONE	03/31/2026		-128	Sioux Chief		800-821-3944	
Floor Cleanout			WB		02/22/2026	10/07/2025	14	10/21/2025	03/08/2026	ANN	10/13/2025	21	NONE	03/10/2026			NONE	03/31/2026		-128	Sioux Chief		800-821-3944	
Wall Hydrant			WB		02/22/2026	10/15/2025	14	10/29/2025	03/08/2026	ANN	10/22/2025	21	NONE	03/10/2026			NONE	03/31/2026		-128	Zurn		855-663-9876	
230000 Mechanical																								
Chiller	C		SMC	12/05/2025	01/07/2026	06/25/2025	14	07/09/2025	01/21/2026	Approved	07/09/2025	**112**	07/11/2025	01/23/2026	10/26/2025		05/15/2026	05/15/2026		-83	Trane			
Chiller pumps	C		SMC	06/17/2025	01/07/2026	06/17/2025	14	07/01/2025	01/21/2026	APP	06/26/2025	**112**	07/03/2025	01/23/2026	10/26/2025		05/15/2026	05/15/2026		-83	Trane			
Expansion Tanks			SMC	04/11/2025	01/07/2026	04/11/2025	14	04/25/2025	01/21/2026	APP	04/15/2025	**112**	04/27/2025	01/23/2026	10/26/2025		02/15/2026	05/15/2026	05/22/2026	ON SITE				
LVL1 AHU			SMC	01/25/2025	01/21/2026	06/17/2025	14	07/01/2025	02/04/2026	APP	06/26/2025	98	07/03/2025	02/06/2026	10/26/2025		05/15/2026	05/15/2026		-83	Trane			
LVL2 AHU			SMC	01/25/2025	01/21/2026	06/17/2025	14	07/01/2025	02/04/2026	APP	06/26/2025	98	07/03/2025	02/06/2026	10/26/2025		05/15/2026	05/15/2026		-83	Trane			
LVL 3 AHU			SMC	01/25/2025	01/21/2026	06/17/2025	14	07/01/2025	02/04/2026	APP	06/26/2025	98	07/03/2025	02/06/2026	10/26/2025		05/15/2026	05/15/2026		-83	Trane			
LVL 4 AHU			SMC	01/25/2025	01/21/2026	06/17/2025	14	07/01/2025	02/04/2026	APP	06/26/2025	98	07/03/2025	02/06/2026	10/26/2025		05/15/2026	05/15/2026		-83	Trane			
LVL 1 VAV			SMC	01/25/2025	01/18/2026	10/29/2025	14	11/12/2025	02/01/2026	AAN	11/06/2025	56	11/14/2025	02/03/2026	10/24/2025			03/31/2026	03/31/2026	ON SITE	Trane			
LVL 2 VAV			SMC	01/25/2025	01/18/2026	10/29/2025	14	11/12/2025	02/01/2026	ANN	11/06/2025	56	11/14/2025	02/03/2026	10/24/2025			03/31/2026	03/31/2026	ON SITE	Trane			
LVL3 VAV			SMC	01/25/2025	01/18/2026	10/29/2025	14	11/12/2025	02/01/2026	ANN	11/06/2025	56	11/14/2025	02/03/2026	10/24/2025			03/31/2026	03/31/2026	ON SITE	Trane			
LVL 4VAV			SMC	01/25/2025	01/18/2026	10/29/2025	14	11/12/2025	02/01/2026	ANN	11/06/2025	56	11/14/2025	02/03/2026	10/24/2025			03/31/2026	03/31/2026	ON SITE	Trane			
Roof Stands			SMC		05/19/2026			NONE	05/19/2026				NONE	05/21/2026				05/21/2026	03/31/2026	ON SITE				
260000 Electrical																								
Electrical Panels & Gear			C. Davis		09/16/2026	07/22/2025	14	08/05/2025	09/30/2026	APP	07/30/2025		NONE	10/02/2026			NONE	10/02/2026	05/01/2026	ON SITE				
Lighting Control Panels	C		C. Davis		07/15/2026	07/18/2025	14	08/01/2025	07/29/2026	APP	07/28/2025		NONE	07/31/2026			NONE	07/31/2026		-6				
Site Light Poles			C. Davis		09/08/2026	09/15/2025	14	09/29/2025	09/22/2026	APP	09/24/2025		NONE	09/24/2026			06/01/2026	09/24/2026		115				
Light Fixtures			C. Davis		09/21/2026	09/15/2025	14	09/29/2025	10/05/2026	APP	09/24/2025		NONE	10/07/2026			NONE	10/07/2026		NONE				
BDA			C. Davis		09/13/2026	12/18/2025	14	01/01/2026	09/27/2026	ANN	12/30/2025		NONE	09/29/2026			NONE	09/29/2026		NONE				
Generator			C. Davis		09/05/2026	06/26/2025	14	07/10/2025	09/19/2026	APP	06/26/2025		NONE	09/21/2026			07/30/2026	09/21/2026		53				
ATS			C. Davis		NONE	06/25/2025	14	07/09/2025	NONE	APP	06/25/2025		NONE	NONE			07/30/2026			NONE				
Fire Alarm (FCP)	C		C. Davis		06/06/2026	07/25/2025	14	08/08/2025	06/20/2026	APP	08/04/2025		NONE	06/22/2026			NONE	06/22/2026		-45				
Cameras					NONE			NONE	NONE				NONE	NONE			NONE			NONE				

SAMPLE PROJECT

Kaufman Lynn Construction, Inc.
3185 S. Congress Avenue
Delray Beach, Florida 33445
P: 561-361-6700
F: 561-361-6979

Project: 1178 - Davie Town Hall Design & Const
6591 Orange Drive
Davie, Florida 33314

Daily Log: Wednesday 7/1/2026

Daily Log Completed
The Daily Log was completed by John Hughes on Tue, Aug 4, 2026 at 08:54 AM EDT.

WEATHER REPORT

Temperature			Precipitation Since			Humidity				Windspeed		
Low	High	Avg	Midnight	2 Days Ago	3 Days Ago	Low	Avg	High	Dew	Avg	Max	Gust
80°F	90°F	84°F	0.06 in.	0.06 in.	0.06 in.	59%	75%	91%	75°F	5.1 mph	11 mph	21 mph

DAILY SNAPSHOT

06:00 AM	09:00 AM	12:00 PM	03:00 PM	06:00 PM	09:00 PM
Clear 81°F	**Partly Cloudy** 85°F	**Partly Cloudy** 90°F	**Partly Cloudy** 90°F	**Rain** 84°F	**Partly Cloudy** 84°F

OBSERVED WEATHER CONDITIONS

No.	Time Observed	Weather Delay	Sky	Temp	Average	Precipitation	Wind	Ground/Sea	Calamity
1	08:20:00 AM	No							
	Comments:								

MANPOWER

53 Workers | 444.0 Total Hours

No.	Contact/Company	Trade	Workers	# Hours	Total Hours	Location
1	Southeast Mechanical	HVAC	5	8.0	40.0	Tilt Wall Panels
	Comments: Pipe fitters -5, first floor install CHE mains, lay out, prefab and install mechanical pipe. Insulator Subcontractor-2, third floor install duct insulation. Sheet metal subcontractor-10, ductwork installation, second and third floor.					
2	K & Z Ductwork, Inc.	HVAC	11	8.0	88.0	
	Comments: Lvl 4 return main ductwork installation continued. Lvl 3 low pressure duct (vav) install continued.					
3	Wolverine Roofing, LLC	Roofing	10	10.0	100.0	Tilt Wall Panels
	Comments: Loaded main roof. 1 man finishing 4th floor balcony roof 7 men installing pvc on main roof					
4	C. Davis Electric Co., Inc.	Electrical	13	8.0	104.0	Tilt Wall Panels
	Comments: Worked-2-men on level four core drilling.and worked-3-men on level two mounting cable tray and -1-man hanging pipe rack.and worked on level three -1-man hanging pipe rack .and worked-6-men in wall rough at level three.					

No.	Contact/Company	Trade	Workers	# Hours	Total Hours	Location
5	Dorado Drywall & Stucco, LLC		14	8.0	112.0	
	Comments: -Lvl 2 framing -Lvl 3 framing and drywall rippers -Cleaning					
			53		**444.0**	

Manpower Attachments:


3. Wolverine Roofing, LLC




1782929442333.552002_tempImage.jpeg



1782929442270.985107_tempImage.jpeg

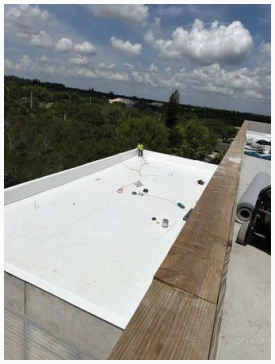

1782929440831.966797_tempImage.jpeg

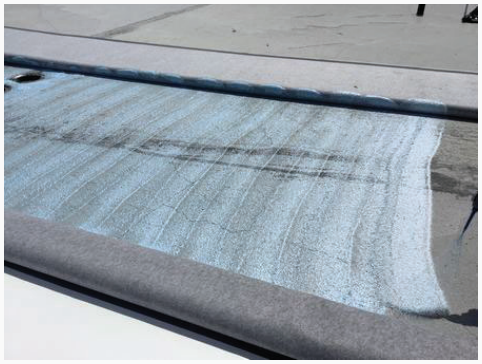

1782929442380.692871_tempImage.jpeg

NOTES


No.	Issue?	Location	Comments
1	No		Sreel Fab- rotunda steel and decking
2	No		South east mech- prepping chilled water piping
3	No		Woodland+ prep slab on grade east - excavate for CMU entrance doors east
4	No		Wright brothers- start in wall rough level 2 bathrooms and level 3
5	No		C Davis- in wall rough level 3 - slab on grade east add underground
6	No		Wolverine roofing- start level 5 west - detail level 4 south and level 5 east

Notes Attachments:

1.



06C2021B-137A-4D28-A0B1-BEA03ADA2853.jpeg

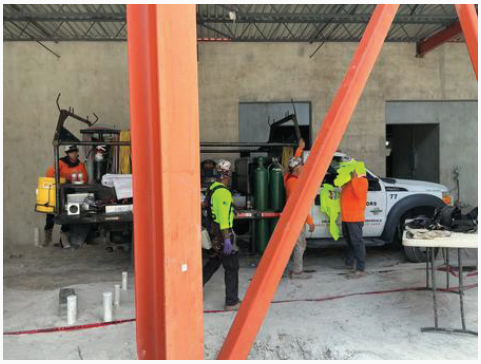


7BD880A0-2B40-4A24-A0C4-46E730FC0DD2.jpeg



7600DF02-35CB-405A-B27C-6D23567C2FE6.jpeg



C22AEF11-5EAC-4947-8FA3-1C2EB13753D8.jpeg

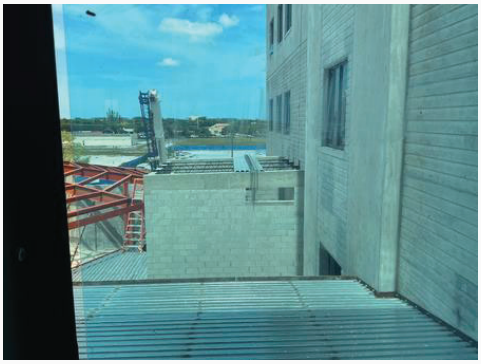

D4D0BEFA-5E4A-4BC9-AFFF-54D2B25331ED.jpeg


2.




FBC46DE1-2EEB-4859-AF6D-5C4244BAB555.jpeg



F69F642E-F2C2-42ED-AD76-DBDB8819B55D.jpeg

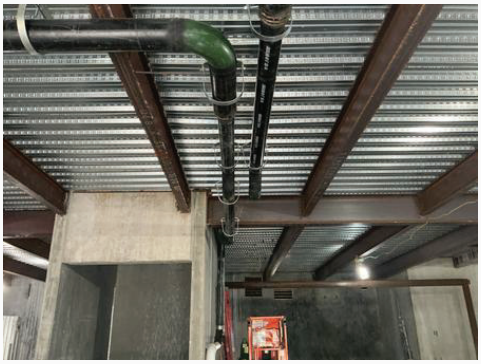


9E77F845-D85A-47F4-9AB4-6D597C037D63.jpeg

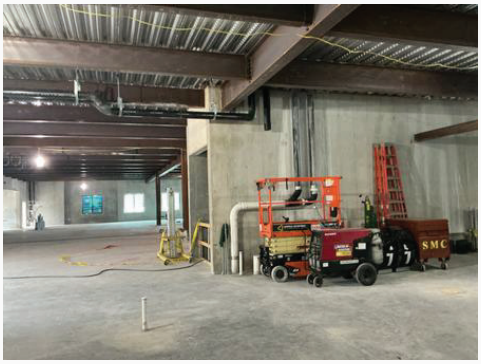

1E0A251D-C048-462A-8241-DAEDED9A4D98.jpeg

3.

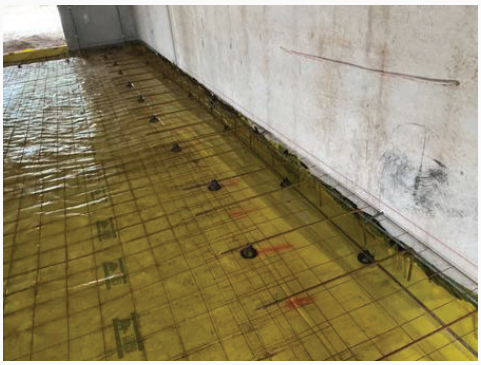

6F83A965-2C50-4B9A-A82C-668EF3D9E8AB.jpeg



A4FE09CA-E417-4092-90D5-09A69BACCD1A.jpeg



32901D48-C005-421D-BD86-F9C53DEDB85B.jpeg




4093A545-9FFE-401F-BC18-EB7B4C28843C.jpeg




D60B8CB0-37D5-4DF4-9F40-1F6E0906D358.jpeg



15C3E174-786E-4ECD-8507-09532ABBB9D6.jpeg

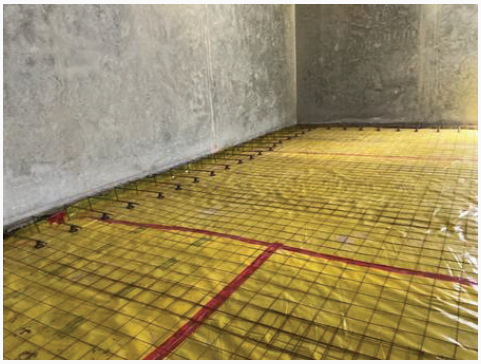

8844D8F2-4E40-437C-A669-0F696F68E555.jpeg

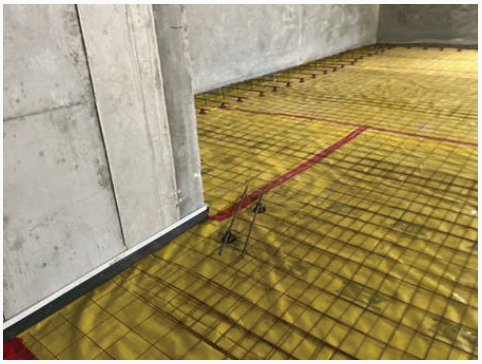

3EFFDF76-C479-4407-9F2F-DD977D314E34.jpeg



56981EE0-ABA3-45E7-93A2-8C7A9700A4E9.jpeg




966A30A6-97F8-4578-9EF7-D02006A4EE62.jpeg



33C36737-C258-42A7-B8DA-983079023B62.jpeg

4.

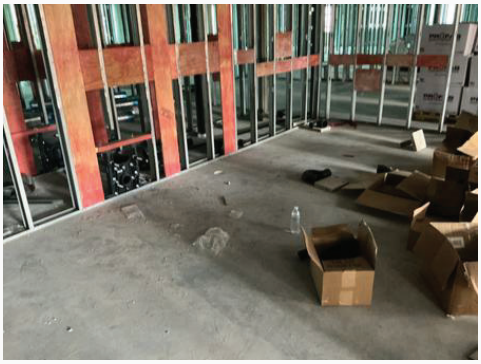

C5186EDE-2019-446B-9457-8CEA4CF4BA72.jpeg

5.



DA9798EB-5495-4BC3-A70E-EF72E20B7A6E.jpeg



27A6D961-B04E-4651-8BFC-08F69554B14E.jpeg



61194731-6865-4AC3-AF11-165F9AF7F0D5.jpeg



EC0859D3-1511-45A1-99A7-61104EE3E833.jpeg

By

Date

Copies To

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

Subcontractor Non-Compliance Notice #1

Kaufman Lynn Construction, Inc.
3185 S. Congress Avenue
Delray Beach, Florida 33445
Phone: 561-361-6700
Fax: 561-361-6979

Project: 1189 - Greenacres Emergency Operations Center
Greenacres
Greenacres, Florida

Date Issued: 08/06/2026

POOR WORKMANSHIP OR DEFECTIVE WORK (FAILURE TO TIMELY CORRECT FAILURES)

Please accept notice that you have failed to comply with the material terms and obligations your subcontract agreement. Specifically, you have provided deficient workmanship or failed to correct or repair defect work on a timely basis.

THIS IS A SAMPLE LETTER OF NON-COMPLIANCE: DESCRIPTION OF OFFENSE GOES HERE.

Please provide sufficient assurances or otherwise cure any deficiencies noted herein including providing a proposed recovery schedule with accurate delivery and completion of repair dates within seventy-two (72) hours unless a different time to cure or remedial action is identified in this Notice. Please note, Kaufman Lynn Construction does not waive and hereby reserves the right to pursue damages and reimbursement of expenses or costs including retaining other subcontractors to repair or replace prior work or retain additional subcontractors to supplement or complete your work as authorized under the Subcontract Agreement.

In the meantime, please do not hesitate to contact our project team or Kaufman Lynn Construction's Chief Legal Officer, Joshua Atlas, to discuss the concerns raised in this communication.

ASSIGNEE	STATUS	RESPONSE DATE	NOTES
Andrew McGrath **(Kaufman Lynn Construction, Inc.)**	Pending		

Kaufman Lynn Construction, Inc.
3185 S. Congress Avenue
Delray Beach, Florida 33445
P: 561-361-6700
F: 561-361-6979

Project: 1189 Greenacres Emergency Operations Center
Greenacres
Greenacres, Florida

Submittal #01 30 00-1.0 - SAMPLE SUBMITTAL
01 30 00 - Administrative Requirements

Revision	0	**Submittal Manager**	Andrew McGrath (Kaufman Lynn Construction, Inc.)
Status	Open	**Date Created**	Aug 6, 2026
Issue Date	Aug 6, 2026	**Spec Section**	01 30 00 - Administrative Requirements
Responsible Contractor	Kaufman Lynn Construction, Inc.	**Received From**	Andrew McGrath (Kaufman Lynn Construction, Inc.)
Received Date	Aug 6, 2026	**Submit By**	Aug 6, 2026
Final Due Date	Sep 10, 2026	**Lead Time**	
		Cost Code	
Location		**Type**	Informational
Submittal Package			

Approvers Andrew McGrath (Kaufman Lynn Construction, Inc.), JoNae Cromartie (Song & Associates, Inc), Tammy Murray (Song & Associates, Inc), Aryana Robinson (Song & Associates, Inc)

Ball in Court Andrew McGrath (Kaufman Lynn Construction, Inc.)

Distribution Andrew McGrath (Kaufman Lynn Construction, Inc.), Aryana Robinson (Song & Associates, Inc), Neil Richardson (Kaufman Lynn Construction, Inc.), Tammy Murray (Song & Associates, Inc)

Description

STAMP INFO

Show Stamp on PDF	Yes	**Stamp Response**	
Other Name		**Stamp Date**	
Stamp By Person			

Notes

Submittal Workflow

Name	Sent Date	Due Date	Returned Date	Response	Attachments
General Information Attachments					
Andrew McGrath		Aug 13, 2026		Pending	
Andrew McGrath		Aug 27, 2026		Pending	
JoNae Cromartie		Sep 10, 2026		Pending	
Tammy Murray		Sep 10, 2026		Pending	
Aryana Robinson		Sep 10, 2026		Pending	

KAUFMAN LYNN CONSTRUCTION
100% EMPLOYEE OWNED

PCPCO #030

Kaufman Lynn Construction, Inc.
3185 S. Congress Avenue
Delray Beach, Florida 33445
Phone: 561-361-6700
Fax: 561-361-6979

Project: 1164 - PBSO Dist 1 Marine Unit Bldg
785 N Jog Road
West Palm Beach, Florida 33413

BMS Monitoring of Generator

TO:	Palm Beach County 2633 Vista Parkway West Palm Beach Florida, 33411-5604	**FROM:**	Kaufman Lynn Construction, Inc. 3185 S. Congress Avenue Delray Beach Florida, 33445
PCO NUMBER/REVISION:	030 / 0	**CONTRACT:**	1164-01 - GMP
STATUS:	Approved	**CREATED BY:**	Matthew Holloway **(Kaufman Lynn Construction, Inc.)**
SCHEDULE IMPACT:	0 days	**DATE CREATED:**	8/19 /2025
		TOTAL AMOUNT:	$24,117.20

POTENTIAL CHANGE ORDER TITLE: BMS Monitoring of Generator

CHANGE REASON: Owner Initiated

POTENTIAL CHANGE ORDER DESCRIPTION: *(The Contract Is Changed As Follows)*
CE #114 - RFI #133: BMS Monitoring of Generator
RFI #133: BMS Monitoring of Generator. All work requested by ESS/ISS. We had approved permitted drawings and everything was installed. The below work was done after the fact per Owner direction.

- Pomeroy Cost = $7,272.00
  - Testing required
  - SPD installation
  - Lobby smoke removal
  - Generator monitoring removal
- Lucto Cost = $14,776.00
  - (1) 6" water bell
  - (4) new individual monitor modules
  - (1) lot of Class A wiring
  - (2) high voltage surge protectors/suppressors
  - (3) double circuit low voltage surge protection/suppressors
  - (1) Class A expansion card
- Total with Markup = $24,117.20

ATTACHMENTS:
641865-22 BMS Monitoring Revised 2.pdf _PBSO Lucto CO#3 Lucto-Frontier Added Scope for ESS Changes.pdf

#	SubJob	Cost Code	Description	Type	Amount
1	N/A	15-500 - H.V.A.C,	RFI #133: BMS Monitoring of Generator	Subcontractor	$ 7,272.00
2	N/A	15-300 - Fire Protection	RFI #133: BMS Monitoring of Generator	Subcontractor	$ 14,776.00
				Subtotal:	$22,048.00
			[redacted]		[redacted]
				GL Insurance: 1.38% Applies to All Line Items	$ 304.26
				P&P Bond: 1.15% Applies to All Line Items	$ 253.55
				Fee: 5.00% Applies to All Line Items	$ 1,102.40
				Grand Total:	**$24,117.20**

Example only. Final numbers to be recalculated without Builders Risk

BY SIGNING BELOW, OWNER AUTHORIZES CONTRACTOR TO PROCEED AND AGREES TO ALL TERMS INCLUDING PAYMENT AS DESCRIBED IN THIS POTENTIAL CHANGE ORDER.

Song & Associates, Inc	**Palm Beach County**	**Kaufman Lynn Construction, Inc.**
1545 Centrepark Drive North	2633 Vista Parkway	3185 S. Congress Avenue
West Palm Beach, Florida 33401	West Palm Beach Florida 33411-5604	Delray Beach Florida 33445
SIGNATURE **DATE**	**SIGNATURE** **DATE**	**SIGNATURE** **DATE**

Kaufman Lynn Construction, Inc.
3185 S. Congress Avenue
Delray Beach, Florida 33445
P: 561-361-6700
F: 561-361-6979

Project: 1189 Greenacres Emergency Operations Center
Greenacres
Greenacres, Florida

RFI #PC-54: Window Tag 9

Revision	0	**Status**	Closed on 04/28/26
To	Aryana Robinson (Song & Associates, Inc) JoNae Cromartie (Song & Associates, Inc)	**From**	Beatriz Alfonso (Kaufman Lynn Construction, Inc.) 3185 S. Congress Avenue Delray Beach, Florida 33445
Date Initiated	Apr 9, 2026	**Due Date**	Apr 14, 2026
Location		**Project Stage**	Bidding
Cost Impact		**Schedule Impact**	
Spec Section		**Cost Code**	
Drawing Number	A-802, A-201A	**Reference**	
Linked Drawings			
Received From	Beatriz Alfonso (Kaufman Lynn Construction, Inc.)	**Sub Job**	
Copies To	Nathan Coker (Kaufman Lynn Construction, Inc.), JoNae Cromartie (Song & Associates, Inc), Emily Jones (Kaufman Lynn Construction, Inc.), Roberto Martinez (Kaufman Lynn Construction, Inc.), Andrew McGrath (Kaufman Lynn Construction, Inc.) , Neil Richardson (Kaufman Lynn Construction, Inc.) , Aryana Robinson (Song & Associates, Inc)		

Activity

Question

Question from Beatriz Alfonso Kaufman Lynn Construction, Inc. *on Wednesday, Apr 8, 2026 at 11:57 AM EDT*

Window Schedule Sheet A-802 is missing info for Tag W9 shown in partial 1st floor plan Sheet A-201A. Please provide.

Official Response

Response from JoNae Cromartie Song & Associates, Inc *on Wednesday, Apr 15, 2026 at 04:32 PM EDT*

Please see attached updated pdf with the plan sheets added as requested to see all new storefront tags

Attachments
Answered RFI# PC-54-Window Tag 9.pdf

SUBSTITUTION REQUEST FORM

TO: _____Date: _____
Consultant

RE:

Project: Greenacres Municipal Operations Center **Project No.:** 1189

We hereby submit for your consideration the following product as a substitution to the specified item for the above project.

Specification Section: _____Paragraph:

Specified Item:

Specified Manuf.: _____

Drawing No.: _____Drawing Title: _____

Location of Product Use:

1. Does the substitution affect dimensions shown on Drawings? Yes ___ No ___
   If yes, attach drawings with affected changes clearly marked.

2. Will the change have an effect on other disciplines: Yes ___ No ___
   If yes, explain: _____
   _____

3. What effect does substitution have on schedule? _____

4. Will the Contractor be offering a credit for the proposed substitution? If yes, how much? Yes _____$ _____ No_____

5. Reason for substitution: _____
   _____
   _____
   _____
   _____

6. Is the substitution equal to or better than the specified product in all aspects?
   Yes _____ No _____

7a. If the acceptance of the substitution requires a revision or redesign of any part of

the Work, will the Contractor be providing the redesign?
Yes _____ No _____ N/A _____

7b. If the acceptance of the substitution requires a revision of any part of the Work by the City's Design Professional, will the Contractor pay the City's Design Professional to do the redesign?
Yes _____ No _____ N/A _____

8. List significant variations of proposed substitution with specified product:

Attach complete technical data including descriptive literature and performance data. Submit sample of material where feasible. Include complete information on changes to Drawings, warranty information and previous project information where this product was utilized. Without this information, request will be returned unreviewed.

CERTIFICATION

The undersigned does hereby certify that the proposed substitution is equal to or superior to the specified item in function, performance, design, appearance, and quality, and is compatible with interfacing materials.

Submitted by:

Contractor Sub-Contractor

For Use by Consultant:

( ) Accepted ( ) Not Accepted ( ) Accepted a Noted ( ) Resubmit

Consultant Signature Date

Remarks:

Accepted by City of Greenacres Project Manager

Signature Date

KAUFMAN LYNN CONSTRUCTION

3185 South Congress Avenue
Delray Beach, FL 33445
o 561.361.6700 | **f** 561.361.6979

www.kaufmanlynn.com
CGC 021732

WARRANTY / GUARANTEE

Job Description: **City of Greenacres – Municipal Operations Center**

5770 Melaleuca Lane, Greenacres, FL 33463

Warranty / Guarantee Period: For a period of one (1) year from **{Enter Date}.**

We hereby guarantee and warrant that we have performed the work included in our contract in accordance to the Drawings, Specification, and in accordance to our contract agreement.

Should any defects develop with the work during the warranty period, repair or replacement shall be made to this work at no expense to the owner.

The owner shall give the contractor written notice of defective work. Commencement on said defective work shall commence within 72 hours after receipt of written notification.

This warranty excludes remedy for damage or defect caused by abuse, modifications made that were not executed within the contract agreement, improper or insufficient maintenance, improper operation, acts of God, or normal wear or tear under normal usage.

KAUFMAN LYNN CONSTRUCTION

Name: _____

Signature: _____

Date: _____

Material and Workmanship Warranty

Project:

Owner:

Architect:

Contractor: Kaufman Lynn Construction

Subcontractor:

Address:

Phone:

E-mail:

Scope of Work Provided:

Subcontractor warrants its Work against any and all defects in materials and workmanship for a period of **one (1) year** from the date of Final Completion, as issued by Owner for the Project, unless the warranty period is extended pursuant to the Contract Documents or for such other period of time as may be proscribed by Florida Statutes, whichever is longer.

Subcontractor guarantees and warrants that all Work performed under this Subcontract is in strict compliance with the Contract Documents and in such a manner as to preserve all warranties required by the Contract Documents.

The Subcontractor warrants that the Owner is a direct beneficiary of this warranty and all manufacturer warranties required to be provided pursuant to the Contract Documents. All required warranties must be freely assignable by the Owner to any person with an interest in the Project, including any current or future owners of the Project. The Subcontractor shall attach to this Warranty all manufacturer's warranties required by the Contract Documents pertaining to its scope of work.

Nothing contained herein shall be construed to establish a period of limitation with respect to other obligations the Subcontractor has under the Contract Documents. Establishment of the one- year period for correction of Work relates only to the specific obligation of the Subcontractor to correct the Work, and has no relationship to the time within which the obligation to comply with the Contract Documents may be sought to be enforced, nor to the time within which proceedings may be commenced to establish the Subcontractor's liability with respect to the Subcontractor's obligations other than specifically to correct the Work.

Name:_____

Title:_____

Signature:_____

Item Summary

Meeting Date: August 17, 2026

From:

Subject: Rambo Park Parking. - Andrea McCue, City Manager.

Background

Analysis

Financial Information

Legal

Staff Recommendation

Attachments:

None

Department Report

Meeting Date: August 17, 2026

From: Michele Thompson, Director

Subject: Community Recreation Services.

Background

Analysis

Financial Information

Legal

Staff Recommendation

Attachments:

1. July Department Repor(1)

Department Report

MEETING DATE: August 17, 2026

FROM: Michele Thompson, Director, Community & Recreation Services

SUBJECT: Community & Recreation Services Dept. – July Report

ADMINISTRATION

PERFORMANCE MEASUREMENT	THIS PERIOD	FY 2026 TO DATE	FY 2026 BUDGET
No. of Contracts Executed/Renewed	0	4	4
No. of Collaborative Partnerships/Opportunities	13	79	50
No. of Vendor/Independent Contractor Agreements	0	86	61
No. of Educational Scholarship Applications R'cd	-	25	25
No. of Community Events Coordinated	2	11	14
No. of Event Participants	7,000	26,564	36,000
No. of Little Free Libraries (LFL) *Replacement Units / #*Story Walk* Boards	1	30/5	30/2
No. of Business Sponsorships	1	16	20
No. of Schools/Attendance for "Read for the Record"	-	10/1,025	18/1,500

FACILITY RENTALS

FACILITY RENTALS	THIS PERIOD	FY 2026 TO DATE	FY 2026 BUDGET
Fields/Concession Stands	58	625	750
Pavilions	25	228	500
Center Facility	37[1]	518[1]	750
Monthly Center Attendance	2,785	30,072	52,000

150[1] Additional Free Rentals: **101** Gym: Open Gym/YP/Tai Chi/OAP; **14** Banquet Hall: Ballroom/PBSO/Fire Rescue/YP/OAP/Mexican Consulate Event/Business Roundtable Event/Coding 101; **17** Room 1: OAP; **3** Room 2: Spotlighters, OAP; **10** Room 3: OAP/AARP/ESOL; **5** Room 4: ESOL/Mexican Consulate Event/Back2School Event; **0** Freedom Park

TOTAL DEPARTMENT REVENUE

FACILITY RENTALS REVENUE	THIS PERIOD	FY 2026 TO DATE	FY 2025 PROJECTED
Total Revenue Generated	$17,451.75	$339,583.23	$344,000

ATHLETICS

YOUTH ATHLETICS	THIS PERIOD	FY 2026 TO DATE	FY 2026 PROJECTED
FY26 Co-ed Fall Soccer (10/19/25-12/5/25) • Registration Period 8/1/25 – 9/19/25	0	255	280
FY26 Co-ed Winter Basketball (12/1/25-3/6/26) • Registration Period 9/2/25 – 10/30/25	0	157	160
FY26 Co-ed Spring Soccer (2/23/26-5/15/26) • Registration Period 1/5/26 – 2/20/26	0	239	280
Co-ed Basketball Skill Development Program • 8-week session: 4/2/26 - 5/21/26 (Thurs.) • Registration Period 2/12/26 - 3/19/26	0	55	100

FOOD DISTRIBUTION	NO. SERVED
Restoration Bridge, Int. – Nov. 12th @ City Hall	1,000
House of Grace – Dec. 20th @ City Hall (w/ toy drive)	467
Restoration Bridge, Int. - May 1st @ Community Center	1,219

OLDER ADULT PROGRAMS

SOCIAL ACTIVITIES	PARTNERS/SPONSORS	NO. OF PARTICIPANTS YTD
Daily Meal Program; Zumba Games/Bingo; Special Events; Educational Sessions Mon. - Fri. (5 x 30)	Area on Aging; PBC Clerk of the Court (Property Fraud); Dedicated Sr. Med. Ctr.; Dr.'s Choice; PACE; PR2U; Firebush; Zumba; HealthSun; Humana; Universal Coaching; University of Miami; WellCare Monthly In-kind Services Provided = $680	3,711

FY26 EVENTS & SPONSORSHIPS

EVENTS	SPONSORS/PARTNERS	FY 2026 EXPENSE	FY 2026 ACTUAL	FY2026 ATTENDEES
Trunk or Treat	PBSO	N/A	N/A	4,000
FR Pancake Breakfast w/Santa 12/7/25	GAFR	-	-	800
HIP & 100th Kick-off (Fri & Sat), 12/12-12/13/25	Waste Management The Glasser Family	$38,055	48,914	7,000
Sundaes with Santa 12/19/25	The Glasser Family	$3,044	$2,643	52
Daddy/Daughter Dance 2/7/26	The Glasser Family	$9,337	$3,621	95
Sunday Sounds (1st Concert) 2/22/26	The Glasser Family	$8,048	$10,000	450
FR Chili Cook-Off 3/1/26	GAFR The Glasser Family	$7,665	$7,547	2,500+
Eggs'stravaganza 4/4/26	The Glasser Family; WM; Tapatia; State Farm	$28,196	$23,544	4,500+
100th Birthday Bash 5/24/26	Burger King; Greenacres Bowl; The Glasser's; Pinecrest Bakery; Auto Nation; WM; UHC; Gehring Group; Adolphe Law Group; IAFF Local 2928; iThink Fin	$22,377	$24,829	2,000
Ignite the Night 7/4/26	WM; FPL; The Glasser Family	$83,048	$81,609	7,000+
Back-2-School -School Supply Distribution 7/24/26	NCJW – Valencia Shores; The Glasser Family	$8,292	$6,197	10 Schools
Senior Resource Fair 9/26/26	Wawa; HealthSun	$500		
Sunday Sounds Presents – Sabor Y Exito 9/27/26	WM; The Glasser Family	$8,048		

FY26 Event Actuals = Direct + In-direct – Event Sponsors & Revenues

Department Report

Meeting Date: August 17, 2026

From:

Subject: Development and Neighborhood Services.

Background

Analysis

Financial Information

Legal

Staff Recommendation

Attachments:

1. DNS July Dept Report

Department Report

MEETING DATE: July 20, 2026

FROM: Denise Malone, AICP, Development & Neighborhood Services Director

SUBJECT: July 1, 2026, through July 31, 2026

Development & Neighborhood Services Department

My Government Online Software (MGO)
Implementation continued for the new MGO software online platform to replace the New World and Energov modules. MGO Permitting, contractor registration, business tax receipts, and code compliance modules are actively being used. The remaining module for planning and zoning is anticipated to be active and in use the upcoming couple of months.

Planning, GIS, & Engineering Division

NEW CASES

Shirdi Sai Baba Temple – 4761 Myrtle Drive (SP-12-02D, SE-12-01A)
A request for a Special Exception Amendment and a Major Site and Development Plan Amendment to construct a two-story multi-purpose building. (Submitted 7/14/26; Staff Completeness Review in progress.)

Buena Vista Plaza Master Sign Plan – 3747 S Military Trail (MSP-26-03)
A request for a Master Sign Plan (MSP-26-03) for 3747 S Military Trail. (Submitted 7/14/26; Staff Completeness Review in progress.)

Raising Cane's Restaurant – Mil-Lake Plaza – 3969 S Military Trail (SP-25-01A, & PCD-81-02O)
A request for a Minor Site and Development Plan Amendment (SP-25-01A) and a Commercial Planned Development (PCD) Amendment (PCD-81-02O) to remove excess surface parking and increase the amount of landscaped open space for the approved Raising Cane's Restaurant project. (Submitted 7/29/2026; Staff Completeness Review in progress.)

ZTA-26-02 – Business Flex & Motels and Hotels
A City-initiated Zoning Text Amendment to establish Business Flex and to clarify the regulations and standards for Motels and Hotels use. (Scheduled for the 8/13/26 PZB Meeting.)

CURRENT PLANNING CASES

Boatman Landings – 4656 Boatman Street (ANX-25-01, CPA-26-01, ZC-26-01, SP-25-03, MSP-25-04, and PLT-26-01)
A request for a voluntary Annexation (ANX-25-02), a Small-Scale Future Land Use Map Amendment changing the Future Land Use designation of the subject property from County MR-5 Residential Medium Density Residential to City Residential Medium Density (RS-MD) (CPA-26-01), a Rezoning of the subject property from County RM-Multifamily Medium Density to City Residential Medium Density (RM-2) (ZC-26-01), a Site and Development Plan (SP-25-03), a Master Sign Plan (MSP-25-04), and a Preliminary Plat (PLT-26-01) to allow the development and subdivision of the ±1.07-acre parcel located at the southwest corner of Boatman Street and Nyack Lane into a seven (7) unit townhouse development. (ANX, CPA, ZC, SP and MSP scheduled for the 9/10/26 PZB Meeting.)

Barclay Square Master Sign Plan – 2902 S Jog Road (MSP-24-08)
A request for a Master Sign Plan (MSP-24-08) for Barclay Square. (Revisions made to Approval Letter; in its final review.)

Buttonwood Plaza Master Sign Plan – 3016-3094 S Jog Road (MSP-24-07)
A request for a Master Sign Plan Amendment (MSP-24-07) for the Buttonwood Plaza. (Revisions made to Approval Letter; in its final review.)

Greenacres Plaza Master Sign Plan Amendment – 3905-3985 S Jog Road (MSP-25-02)
A request for a Master Sign Plan Amendment (MSP-25-02) for Greenacres Plaza. (Approved July 15, 2026)

Greenacres Sunoco and Office/Retail – 3067 S Jog Road (SP-96-05D and MSP-26-02)
A request for Major Site and Development Plan Amendment (SP-96-05D) and a Master Sign Plan (MSP-26-02) to allow for the construction of a new 6,000 sq ft office/retail building with a 786 sq ft mezzanine. (Completeness letter sent March 11, 2024, resubmittal received September 30, 2024, comments were provided on November 1, 2024. Resubmittal received August 20, 2025. (Approved at the June 15, 2026, City Council meeting.)

Ice Cream La Bendicion – 560 Jackson Avenue (SP-24-04 and MSP-25-03)
A request for Site and Development Plan (SP-24-04) and Master Sign Plan (MSP-25-03) approval to construct an 882 sq ft two story building with ice cream/raspado shop on the ground floor and one dwelling unit on the second floor. (Heard on June 18, 2026, DRC Meeting; awaiting resubmittal.)

Raising Cane's Restaurant – Mil-Lake Plaza – 3969 S Military Trail (SE-25-01, SP-25-01, & PCD-81-02N)
A request for Special Exception (SE-25-01), Site and Development Plan Amendment (SP-25-01), and a Master Plan Amendment (PCD-81-02N) for the construction of a 3,153 sq ft drive-through restaurant on the outparcel located at the southeast corner of the Mil-Lake Plaza. (Approved at the June 15, 2026, City Council meeting.)

Symphony Court – 5217 & 5163 S Military Trail (ANX-25-03, CPA-25-04, and ZC-25-04)
A request for a voluntary annexation (ANX-25-03) of 2 parcels of land totaling 8.91 acres, a Small-Scale Future Land Use Amendment (CPA-25-04) from Palm Beach County Medium Residential 5 to City Residential High Density and a Rezoning (ZC-25-04) from PBC Agricultural Residential to City Residential High. (Approved 4-0 at the 6/11/26 PZB Meeting; Approved 5-0 at the 7/20/26 Council Meeting on First Reading; scheduled for 8/3/26 Council Meeting for Second Reading.)

Talented Teen Club – 305 Swain Boulevard (SP-26-01)
A request for a Minor Site Plan Amendment to add a new 500 square foot pre-fab building on the property to support existing operations. (Heard on June 18, 2026, DRC Meeting; corrections required, awaiting resubmittal from the applicant.)

Temple Beth Tikvah – 4550 S Jog Rod (CPA-25-03, ZC-25-03, & SP-87-02F)
A request for Small-Scale Future Land Use Amendment (CPA-25-03) from Residential Low Density (RS-LD) to Commercial (CM), a Rezoning from Residential Low Density (RL-3) to General Commercial (CG), and a Minor Site Plan Amendment (SP-87-02F) to provide for the expansion of the existing adult daycare use from 70 participants to 251 participants. (Completeness Review Comment Letter issued on January 14, 2026; Extension Request Letter from the applicant received on February 12, 2026; Extension Request Letter #2 and #3 received. Resubmitted May 28, 2026; Heard at the July 16, 2026, DRC Meeting and DRC Comments have been issued; Corrections required, awaiting resubmittal.)

Truist Bank (River Bridge Centre Outparcel) – 6702 Forest Hill Blvd (SP-87-07A)
A Minor Site and Development Plan Amendment for modifications to the landscaping. (Approved on July 10, 2026.)

West Pines Preserve – 4860 Melaleuca Lane (CPA-26-03, ZC-26-02, BA-26-02, and SP-26-03)
A request for a Future Land Use Map Amendment (CPA-26-03), from Residential Low Density (RS-LD) to Residential High Density (RS-HD); a Rezoning (ZC-26-03) from the current Residential Medium-Density 2 (RM-2) on the northern parcel and Residential Low-Density 1 (RL-1) District on the southern parcel to the proposed Residential High-Density (RH) District; a Variance (BA-26-02) request from the minimum side yard setback of 20 feet to proposed 10 feet; and a Site and Development Plan (SP-26-03) for an 83-unit Townhouse Development on 8.476 acres. (Staff Completeness Review Letter issued on July 22, 2026; Staff meeting with applicant scheduled for August 5, 2026, to discuss Completeness Review comments.)

SITE PLAN AMENDMENTS

Buttonwood Plaza (EV Charging Stations) – 3016 South Jog Road (SP-84-05J)
A request for a Minor Site Plan Amendment to add four (4) electric vehicle (EV) charging stations to the plaza. (DRC technical comments sent July 10, 2026.)

Canalakes (Recreation Pod) – 3107 Poolside Drive (PUD-80-01F)

A request for a Minor Planned Unit Development Amendment (PUD-80-01F) to replace the spa (hot tub) with a splash pad. (Completeness comments sent June 22, 2026.)

Chase Bank (River Bridge Centre Outparcel) – 6710 Forest Hill Blvd (SP-87-08B)
A request for a Minor Site and Development Plan Amendment to modify the landscape plan. (Completeness comments sent July 21, 2026.)

Garden Square – 6645 Chickasaw Road (SP-23-03A, BA-26-01, and PLT-26-02)
A request for a Minor Site and Development Plan Amendment (SP-23-03A) to revise the elevations, an Administrative Variance (BA-26-01) to reduce the required side yard setbacks, and a Preliminary Plat (PLT-26-02) to allow the development and subdivision of the forty-four (44) unit townhouse development. (Comments provided June 23, 2026, and pending applicant response and resubmittal.)

TEXT AMENDMENTS

CPA-26-02 – Urban Corridor and Redevelopment Initiatives
A City-initiated Comprehensive Plan Text Amendment pertaining to mixed-use and urban corridor redevelopment initiatives and modify density and intensity standards in targeted areas. (June 11, 2026 PZB Meeting (Approved 4-0); Scheduled for First Reading on July 20, 2026. Proposed text amendment transmitted to the FL Department of Commerce on 7/27/26, pending response within 30 days of transmittal; tentatively scheduled for Second Reading on 9/9/26.)

ZTA-26-01 – Urban Corridor and Redevelopment Initiatives
A City-initiated Zoning Text Amendment to modify the development standards in targeted areas, including building height design guidelines and parking. (June 11, 2026 PZB Meeting (Approved 4-0); Scheduled for First Reading on July 20, 2026; tentatively scheduled for Second Reading on 9/9/26.)

RESIDENTIAL DEVELOPMENT PROJECTS

Blossom Trail (Nash Trail)
All Project plans approved. Final Engineering Permit issued, Construction Bond and Contract in place. Master Building Permits have been issued for the Townhouse and Single-Family units. Submittals of individual building permit applications in progress.

NON-RESIDENTAL DEVELOPMENT PROJECTS

Church of God 7th Day of Palm Beach – 3535 South Jog Road
All approvals have expired. Special Exception, site and associated development plans, building and engineering permit applications, and outside agency approvals would be required to be submitted to seek/obtain development approval. Adjacent single-family house has complied, and the code enforcement case closed out. House of Worship site has three (3) Special Magistrate board orders accruing fines at $250 day/order. Foreclosure proceedings commenced with March 17, 2026 Special Magistrate Hearing.

GIS

GIS
Staff continues to make updates to the publicly available GIS applications on the city website. As maps and apps are updated, the website links will change accordingly.

The GIS team has completed the GIS needs assessments and plans to meet with the City Manager at the end of August to discuss findings, begin prioritizing projects and develop project timelines. Following the meeting, the GIS team will follow up with all departments to provide updated timelines and coordination efforts.

TEMPORARY USE PERMITS

2026-223 – Publix (Outdoor Storage) – 6294 Forest Hill Boulevard
A request from HGR Construction, Inc., representing Publix, to allow for temporary storage containers to be located on site to store materials for their interior renovation project. (TUP issued July 14, 2026.)

TU-2026-1468 – Blossom Trail Model Home – 5189 Begonia Circle
A request from DR Horton for a model home to be used for showing at 5189 Begonia Circle within the Blossom Trail Planned Unit Development. (TUP issued July 27, 2026.)

TU-2026-1469 – Blossom Trail (Model Home) – 5193 Begonia Circle
A request from DR Horton for a model home to be used for showing within the Blossom Trail Planned Unit Development. (TUP issued July 27, 2026.)

TU-2026-1469 – Blossom Trail (Model Home) – 5193 Begonia Circle
A request from DR Horton for a model home to be used for showing within the Blossom Trail Planned Unit Development. (TUP issued July 27, 2026.)

2026-449 – Blossom Trail (Model Home) – 5509 Begonia Circle
A request from DR Horton for a model home to be used for showing within the Blossom Trail Planned Unit Development. (TUP issued July 27, 2026.)

2026-450 – Blossom Trail (Model Home) – 5507 Begonia Circle
A request from DR Horton for a model home to be used for showing within the Blossom Trail Planned Unit Development. (TUP issued July 27, 2026.)

2026-451 – Blossom Trail (Model Home) – 5505 Begonia Circle
A request from DR Horton for a model home to be used for showing within the Blossom Trail Planned Unit Development. (TUP issued July 27, 2026.)

2026-607 – Blossom Trail (Construction Signs) – 5901 Begonia Circle
A request from DR Horton for construction signs to be used for the duration of Blossom Trail residential Planned Unit Development construction. (TUP issued July 27, 2026.)

2026-560 – Walmart (Outdoor Storage) – 6294 Forest Hill Boulevard
A request from the general contractor, HGR Construction, Inc., representing Walmart, to allow for eight (8) temporary storage containers to be located on site to store materials for their interior (2026-0696) and exterior alterations. (DRC Comments issued July 21, 2026.)

2026-638 – Walmart (Construction Fence) – 6294 Forest Hill Boulevard
A request from HGR Construction, Inc., representing Walmart, to allow for a construction fence to be installed to store their materials for their interior (2026-0696) and exterior renovation projects. (DRC Comments issued July 21, 2026.)

LIVE ENTERTAINMENT PERMITS

Staff is coordinating with PBSO for reports of any incidents observed and reported for alcohol serving establishments open after 2 am or operating without benefit of a Live Entertainment Permit. Follow-up is being provided and any noncompliance issues addressed with businesses.

LE 2025-2583 – Coco Mambo LLC – 3745 South Military Trail
A request for a Live Entertainment Permit for no more than four (4) nights per week from 7:00 pm to 1:00 am. (Code Enforcement Violation Notice sent via Certified Mail on June 30, 2026.)

LE 2025-2959 – El Sabor Latino – 2202 South Jog Road
A request for a Live Entertainment Permit for daily from 8:00 pm to close of business. (Code Enforcement Violation Notice sent via Certified Mail on June 30, 2026.)

LE 2024-2729 – El Valle Hondu-Mex Restaurant – 4992 10th Avenue North
A request for a Live Entertainment Permit for Friday and Saturday's from 9:00 pm to 1:30 am and for scheduled sports games. (Code Enforcement Violation Notice sent via Certified Mail on June 30, 2026.)

LE 2025-2353 – Reggae Jerk of the Palm Beaches LLC – 2178 Jog Road – In Progress
A request for a Live Entertainment Permit to host quarterly "Family and Friends Fish Fry" events until 1:30 a.m. on event dates. (Code Enforcement Violation Notice sent via Certified Mail on June 30, 2026; Life Safety Plan received by Staff on July 14, 2026.)

2026-313 – Radical Root LLC – 6376 Forest Hill Boulevard
A request for a Live Entertainment Permit to periodically host local artists/musicians, DJ's and other similar acts on a weekly basis from 8:00 PM to 1:00 AM. (Scheduled for August 20, 2026, DRC Meeting.)

FY 2026 Data:

APPROVALS ISSUED	CURRENT PERIOD	FYTD 2026	FY 2026 BUDGET
Annexation	0	0	2
Comprehensive Plan Amendment	0	0	3
Zoning Changes	0	0	3
Special Exceptions	1	2	4
Site Plans	1	2	5
Site Plan Amendments	0	8	8
Variances	0	2	3
Zoning Text Amendments	0	2	4
Master Sign Plan	0		5
INSPECTION TYPE	**CURRENT PERIOD**	**FYTD 2026**	**FY 2026 BUDGET**
Landscaping	3	33	80
Zoning	3	16	50
Engineering	6	45	50

* Assumes progress of proposed Developments such that inspections are requested.

Building Division

Building Department Report
(July 1, 2026 – July 31, 2026)

1) ADMINISTRATION:

a) Researched and completed Eighty-Seven (87) lien searches providing open and/or expired permit information.
b) Researched and completed Thirty -Six (36) records requests for historical permits.

2) PERMITS/INSPECTIONS:

PERMITS/INSPECTIONS	DURING THIS PERIOD NewWorld	DURING THIS PERIOD MGO	FYTD 2026
New Applications Received / Permits Created	17	280	2,245
Applications Approved	5	238	1,138
Applications Canceled/ VOID	3	0	40
Applications Denied	0	0	1
Applications Reopened	12	0	30
Permits Issued	20	238	1,923
Permits Completed	46	41	1,401
Permits Canceled	3	0	67
Permits Reopened	0	0	112
Permits Expired	1	0	119
Inspections Performed	94	207	3,792
Construction Value of Permits Issued	$145,659.11	$ 427,422.89	$30,654,422.5
Construction Reinspection Fees	$250.00	$0	$135,553.41
Extension/Renewal Fees	$779.53	$0	$4,242.42
CO's Issued	6	0	36
CC's Issued	0	0	0
Temporary CO's Issued	0	0	7

3) BUSINESS AND CONTRACTOR REGISTRATION:

(See Attached Summary Reports)

4) PERMIT APPLICATIONS IN PLAN REVIEW – PRINCIPAL NEW OR REMODEL PROJECTS:

PROJECT	ADDRESS	SIZE	DESCRIPTION	PERMIT#
Dunkin Donut	3098 S J Rd	1593	Interior Remodel	2026-683
TWH	5004 Marigold Way		New TWH	2026-515
TWH	5006 Marigold Way		New TWH	2026-514
TWH	5010 Marigold		New TWH	2026-512
TWH	5012 Marigold		New TWH	2026-511
TWH	5014 Marigold		New TWH	2026-510
TWH	5202 Marigold		New TWH	2026-498
TWH	5204 Marigold		New TWH	2026-497
TWH	5206 Marigold		New TWH	2026-496
TWH	5208 Marigold		New TWH	2026-495
TWH	5210 Marigold		New TWH	2026-494
TWH	5212 Marigold		New TWH	2026-493
TWH	5214 Marigold		New TWH	2026-492
TWH	5216 Marigold		New TWH	2026-491
Habitat for Humanity	4639 Lake Worth Rd		Partition Walls	2026-517
Dollar Tree	6358 Forest Hill Blvd	12057	Interior Remodel	2026-524
AHR Property	4752 S Jog Rd		Interior Reno Walls	2026-566
Applebees	6707 Forest Hill Blvd	3,128	Interior Exterior Remodel	2026-0684
Murphy Oil USA	6270 Forest Hill Blvd	2,824	Convenience Store	2025-2411
SFH	425 Swain Blvd	1,608	New SFH	2025-1959

5) PROJECTS IN PROGRESS – PRINCIPAL REMODELING/RENOVATION:

PROJECT	ADDRESS	SIZE	DESCRIPTION	PERMIT #
Asian Restaurant	2902 S Jog Rd		Interior Renovation	2026-391
Culvers	6120 Lake Worth Rd		Interior Remodel	2026-1166
Walmart	6294 Forest Hill Blvd		Interior Exterior Remodel	2026-0696
Publix Liquor	4805 S Military	1,130	Interior Remodel	2026-0307
Phonexi Mngmt	6135 B Lake Worth Rd		Interior buildout	2026-0784
Heritage Career Institute	4568 Lake Worth Rd		Interior Remodel	2026-0395
Fire Station	5095 S Haverhill Rd		Bunkhouse Conversion	2025-2360

6) PROJECTS IN PROGRESS – PRINCIPAL NEW CONSTRUCTION:

PROJECT	ADDRESS	SIZE	DESCRIPTION	PERMIT #
Mobile Home	960 Bayivew Rd	1,152	New Mobile Home	2025-2909
Blossom Trial	5901 Begonia Cir	3,926	Clubhouse	2025-2421
SFH	5010 Begonia		New SFH	2026-502
SFH	504 Swain Blvd	1,685	New SFH	2025-2270
TWH	6202 Begonia Cir		New TWH	2026-0505
TWH	6204 Begonia Cir		New TWH	2026-0504
TWH	6206 Begonia Cir		New TWH	2026-0503
TWH	6208 Begonia Cir		New TWH	2026-0502
TWH	6210 Begonia Cir		New TWH	2026-0501
TWH	6212 Begonia Cir		New TWH	2026-0500

TWH	6214 Begonia Cir		New TWH	2026-0499
TWH	6216 Begonia Cir		New TWH	2026-0498
SFH	5077 Petunia Way		New SFH	2026-0793
SFH	5081 Petunia Way		New SFH	2026-0495
SFH	5085 Petunia Way		New SFH	2026-0496
SFH	5089 Petunia Way		New SFH	2026-0497
SFH	5189 Begonia Cir	2,034	New SFH	2026-0426
SFH	5193 begonia Cir	3,059	New SFH	2026-0427
TWH	5501 Begonia Cir	1,472	New TWH	2026-0490
TWH	5503 Begonia Cir	1,446	New TWH	2026-0491
TWH	5505 Begonia Cir	1,446	New TWH	2026-0492
TWH	5507 Begonia Cir	1,446	New TWH	2026-0493
TWH	5509 Begonia Cir	1,472	New TWH	2026-04494
Santa Catalina Bldg A	3145 S JOG RD	7,325	New Construction Development of Medical Offices	2024-2721
Santa Catalina Bldg B	3197 S JOG RD	7,325	New Construction Development of Medical Offices	2024-2722

Business Listing Report

Business BTR New Between 7/1/2026 To 7/31/2026

Generated 8/4/2026

BTR Number	BTR Type	Business	Licensee	Address	Phone	Extension	Email Address	Start of Business	End of Business
Business BTR New									
Food									
BTR-2026-180	Business Tax Receipt	TL Caribbean Restaurant LLC	TL Caribbean Restaurant LLC, TERCIUS JEUDY	5371 10th Ave N Suite 8, Greenacres FL 33463	(954) 729-4703		tlcaribbeanrestaurantsllc@gmail.com	7/8/2026	
Food Totals: 1									
General Service									
BTR-2026-173	Business Tax Receipt	Grace Care Home Health	Grace Care Home Health LLC, Geraldine Marquez Cuesta	3900 Woodlake Blvd 207-1, Greenacres FL 33463	(561) 704-1413		gracecarehomehealth@yahoo.com	7/6/2026	
BTR-2026-178	Business Tax Receipt	AutoBase, Inc.	AutoBase, Inc., Thomas Manqan	5139 Lake Worth Road , Greenacres FL 33463	(305) 606-7716		Tom@AutoBaseCorp.com	7/8/2026	
BTR-2026-179	Business Tax Receipt	VL BEAUTE LLC - INREP LLC	INREP LLC, MARIO REYES	4608 S JOG RD , GREENACRES FL 33467	(754) 333-1797		ADMIN@INREP.NET	7/8/2026	
BTR-2026-190	Business Tax Receipt	JLZ Vending Inc.	JLZ Vending Inc., Jeff Ward	5000 Lake Worth Road 503-504W, Greenacres FL 33463	(561) 512-5820		jeffward4362@gmail.com	7/31/2026	
BTR-2026-191	Business Tax Receipt	TRUE SOLUTIONS INSURANCE AND MULTI SERVICES LLC	TRUE SOLUTIONS INSURANCE AND MULTI SERVICES LLC, WILFRIS PIERRE	5700 Lake Worth Rd , Greenacres FL 33463	(561) 334-7919		pierrewilfris@gmail.com	7/31/2026	
BTR-2026-193	Business Tax Receipt	Nails spa by ANA INC	Nails spa by ANA INC, Thuy Cao	3951 jog road Suit 127, Greenacres FL 33467	(561) 806-9079		thuycao94ana@icloud.com	7/31/2026	
General Service Totals: 6									
Home Based									
BTR-2026-175			Mishica Thomas	5044 Nautica Lake Cir , Greenacres FL 33463	(561) 506-7755		triplesqueeze7@gmail.com	7/6/2026	
BTR-2026-183	Business Tax Receipt	MAQOR POOLS LLC	MAQOR POOLS LLC, Yurlenis penaloza	1641 Crooked Stick Way , Greenacres FL 33413	(561) 635-6099		DNASERVE@DNASERVICESS.COM	7/13/2026	
BTR-2026-184		General House Solutions LLC	General House Solutions LLC, Maria L Lopez Marin	1055 Salmon Isle , Greenacres FL 33413	(561) 632-3042		elsi@nelpiservices.net	7/17/2026	
BTR-2026-185	Business Tax Receipt		SM Premier Services LLC, Susana Martinez	3914 La Rambla , Greenacres FL 33467	(561) 506-2011		smpremierservices@outlook.com	7/23/2026	
BTR-2026-188	Business Tax Receipt	Thomas Quality Construction LLC	Thomas Quality Construction LLC, Patrick Thomas	5044 Solar Point Dr. , Greenacres FL 33463	(754) 779-1843		thomasqualityc@gmail.com	7/29/2026	
BTR-2026-189	Business Tax Receipt	HCS Pool Service Inc	HCS Pool Service Inc, Pedro Donado	142 Martin Ave. , Lake Worth FL 33463	(786) 367-6101		Hcspoolservice@gmail.com	7/30/2026	
Home Based Totals: 6									
Professionals									

BTR-2026-177	Business Tax Receipt	Los Compadres Barbershop LLC (Borges Mesa)	Los Compadres Barbershop LLC, Rodolfo Borges Mesa	4180 S Jog RD STE 2, Lake Worth FL 33467	(561) 772-0560	borgesrodolfo514@icloud.com	7/8/2026
BTR-2026-181	Business Tax Receipt	Los Compadres Barbershop LLC (Rosario Almonte)	Los Compadres Barbershop LLC, Darwin Elisaul Rosario Almonte	4180 Jog Rd 2, Greenacres FL 33463	(347) 602-0501	darwin2989@gmail.com	7/8/2026
BTR-2026-182	Business Tax Receipt	Los Compadres Barbershop LLC (German)	, Weslin Gil German	4180 S Jog Rd 2 , Greenacres FL 33467	(561) 403-8975	Gilweslin23@gmail.com	7/8/2026

Professionals Totals: 3

Rental

BTR-2026-176	Rentals	Rental-2191 White Pine D	Smart Agency SAS LLC, Doralba Tellaz Vargas	2191 White Pine Cir D, Greenacres FL 33415	(561) 290-5991	tellezdoralba@gmail.com	7/8/2026

Rental Totals: 1

Business BTR New Total: 17

CITY OF GREENACRES
Licensing Revenue Summary Report

Licensing Revenue Summary Report - Summary
From Date: 7/1/2026 - To Date: 7/31/2026

	Charge Code	No. of Billing Transactions	No. of Adjustment Transactions	Billed Amount	Adjustments	Net Billed
Food	25% Late Fee	1	0	$31.91	$0.00	$31.91
	Collection Fee	1	0	$25.00	$0.00	$25.00
	Delinquent over 150 Days Fee	1	0	$100.00	$0.00	$100.00
	Food	1	0	$127.63	$0.00	$127.63
	Food Service Annual Fire Inspection - Up to 10 Seats	1	0	$76.58	$0.00	$76.58
	Food Totals:	**5**	**0**	**$361.12**	**$0.00**	**$361.12**
General Retail	Food	2	0	$354.20	$0.00	$354.20
	General Retail	2	0	$720.89	$0.00	$720.89
	General Retail/General Service/Industrial/Wholesale Annual Fire Inspection - Greater than 500 Sq. Ft.	2	0	$576.70	$0.00	$576.70
	General Retail Totals:	**6**	**0**	**$1,651.79**	**$0.00**	**$1,651.79**
General Service	25% Late Fee	2	0	$68.27	$0.00	$68.27
	Collection Fee	5	0	$125.00	$0.00	$125.00
	Cosmetology & Barber	1	0	$40.61	$0.00	$40.61
	Delinquent over 150 Days Fee	5	0	$500.00	$0.00	$500.00
	General Retail/General Service/Industrial/Wholesale Annual Fire Inspection - Greater than 500 Sq. Ft.	4	0	$278.92	$0.00	$278.92
	General Retail/General Service/Industrial/Wholesale Annual Fire Inspection - Less than 500 Sq. Ft.	4	0	$240.00	$0.00	$240.00
	General Service	19	0	$2,091.96	$0.00	$2,091.96
	Initial Annual Fire Inspection	2	0	$150.00	$0.00	$150.00
	Zoning Review Fee	3	0	$150.00	$0.00	$150.00
	General Service Totals:	**45**	**0**	**$3,644.76**	**$0.00**	**$3,644.76**
Home Based	25% Late Fee	1	0	$20.35	$0.00	$20.35
	Home Based	18	0	$1,302.26	$0.00	$1,302.26
	Zoning Review Fee	4	0	$200.00	$0.00	$200.00
	Home Based Totals:	**23**	**0**	**$1,522.61**	**$0.00**	**$1,522.61**

CITY OF GREENACRES

Licensing Revenue Summary Report

Licensing Revenue Summary Report - Summary
From Date: 7/1/2026 - To Date: 7/31/2026

nsurance	Professional/Office	25	0	$1,455.65	$0.00	$1,455.65
	Insurance Totals:	**25**	**0**	**$1,455.65**	**$0.00**	**$1,455.65**
rofessionals	25% Late Fee	1	0	$30.51	$0.00	$30.51
	Collection Fee	4	0	$100.00	$0.00	$100.00
	Cosmetology & Barber	6	0	$203.06	$0.00	$203.06
	Delinquent over 150 Days Fee	4	0	$400.00	$0.00	$400.00
	Professional/Office	4	0	$427.11	$0.00	$427.11
	Professionals Totals:	**19**	**0**	**$1,160.68**	**$0.00**	**$1,160.68**
Rental	25% Late Fee	2	0	$20.30	$0.00	$20.30
	Collection Fee	3	0	$75.00	$0.00	$75.00
	Delinquent over 150 Days Fee	3	0	$300.00	$0.00	$300.00
	Rental Property	35	1	$1,449.74	$40.61	$1,409.13
	Rental Totals:	**43**	**1**	**$1,845.04**	**$40.61**	**$1,804.43**
	Grand Total:	**166**	**1**	**$11,641.65**	**$40.61**	**$11,601.04**

Code Compliance Division

Code Compliance Report

(July 1, 2026, through July 31, 2026)

CODE ENFORCEMENT	DURING THIS PERIOD	FYTD 2026
Inspections Related to Active Code Cases	30	209
New Cases Started	24	139
Cases Complied	11	44
Current Open Cases	532	2086
Notices Sent	34	333
Illegal Signs Removed from right-of-way	255	2693
Inspections Not Related to Active Code Cases	30	237
Complaints Received and Investigated	11	63

Department Report

Meeting Date: August 17, 2026

From: Philip Harris, Director

Subject: Economic Development.

Background

July 2026 represented another month of strong progress for the City of Greenacres' economic development efforts. The Economic Development Department continued advancing strategic priorities focused on redevelopment and investment attraction, small business development, workforce readiness, regional and international partnerships, and expanded opportunities for residents and entrepreneurs.

During the month, the Department continued engaging developers and hospitality investors, successfully facilitated the Mexican Mobile Consulate in Greenacres, expanded entrepreneurial education and technical assistance, strengthened partnerships with the business community, and advanced workforce development programming.

As Greenacres celebrates its Centennial Year, these initiatives reflect the City's continued transformation into a more connected, competitive, and business-friendly community. Through intentional partnerships and proactive economic development strategies, Greenacres continues building momentum toward sustainable investment, job creation, business growth, and an enhanced quality of life.

1. REDEVELOPMENT AND INVESTMENT OUTREACH

Corridor Redevelopment and Hotel Investment

Throughout July, the Department continued strategic discussions with developers, property owners, investors, and hospitality representatives regarding redevelopment opportunities along the Lake Worth Road commercial corridor.

Particular emphasis was placed on advancing potential hotel investment opportunities, including discussions involving Hilton affiliated development interests and Cobblestone Hotels. The Department continues working to identify appropriate sites, connect property owners with prospective investors, and position Greenacres for additional hospitality investment.

In addition to hotel development, discussions continued regarding mixed-use, multifamily residential, retail, and workforce housing opportunities that complement the City's long-term redevelopment vision.

These efforts support several important City objectives, including:

- Expanding and differentiating the municipal tax base;
- Encouraging redevelopment of underutilized commercial properties;
- Attracting new private-sector investment;
- Creating employment opportunities;
- Expanding hospitality and visitor-serving amenities; and
- Strengthening the long-term economic vitality of the Lake Worth Road corridor.

The continued engagement of developers and investors demonstrates growing confidence in the Greenacres market and reflects the City's proactive approach to creating an environment where quality development and investment can move forward.

2. STRATEGIC PARTNERSHIPS AND COMMUNITY ENGAGEMENT

Mexican Consulate of Miami – Mobile Consulate Initiative

On July 11, 2026, the City of Greenacres successfully hosted the Mexican Mobile Consulate at the Greenacres Community Center in partnership with the Consulate General of Mexico in Miami.

The initiative brought essential consular and community services directly to Greenacres and surrounding communities, reducing the need for residents to travel to the Consulate's headquarters in Miami-Dade County.

Services and resources included:

- Passports and consular identification services;
- Voter registration assistance;
- Civil registry and dual-nationality resources;
- Legal and immigration information;
- Health and wellness resources;
- Financial education; and
- Community outreach and resource connections.

The initiative extended beyond traditional consular services. Through collaboration with Prospera, bilingual economic development resources were made available to connect entrepreneurs and residents with information related to access to capital, entrepreneurship, business planning, marketing, employment opportunities, and small business technical assistance.

Following the event, the Consulate General of Mexico in Miami formally recognized the City of Greenacres for its collaboration and support. In correspondence dated July 17, 2026, Consul General Rutilio Escandón Cadenas expressed gratitude to Mayor Charles Shaw and the City for providing the Greenacres Community Center and noted that the

City's collaboration was essential to successfully bringing consular services closer to the Mexican community in Greenacres and surrounding areas.

The Consul General also specifically recognized the professionalism and commitment of the City's Economic Development Department and staff in facilitating the partnership and serving as an institutional liaison between Greenacres and the Consulate.
This successful initiative demonstrates the City's ability to leverage international and community partnerships to improve access to services while simultaneously creating pathways to entrepreneurship and economic opportunity.

3. BUSINESS ASSISTANCE, ENTREPRENEURSHIP, AND BUSINESS VISIBILITY
Buy Local. Shop Greenacres. – New Business Spotlight Initiative
In July, the Economic Development Department officially launched the City's first "Buy Local. Shop Greenacres." business spotlight, expanding Greenacres' innovative digital marketing efforts to support and promote locally owned retailers and service-based businesses.

Building upon the success of the award-winning "Dine Local. Savor Greenacres." campaign, *Buy Local. Shop Greenacres* is a new digital media series designed to showcase the small businesses that contribute to Greenacres' unique character and economy. From salons and boutiques to entertainment venues, barbershops, and other locally owned establishments, the initiative provides participating businesses with professional promotional exposure at no cost.

The campaign supports the City's broader economic development objectives by:

- Increasing visibility for locally owned businesses;
- Encouraging residents and visitors to spend locally;
- Strengthening the City's small business ecosystem;
- Promoting businesses and experiences that are unique to Greenacres;
- Expanding the City's digital reach; and
- Reinforcing Greenacres' distinctive "Only in Greenacres" identity.

The inaugural spotlight featured VYDA Salon & Spa, located at 2182 South Jog Road. Owner Gissela Tafur and her team provide a variety of beauty, wellness, and self-care services to the Greenacres community.

The launch represents another important evolution in the City's approach to economic development, using creative digital storytelling and the City's communications platforms to become an active marketing partner for local businesses.

New Business Grand Opening – Pho Hoa
On July 17, 2026, City leadership and staff participated in the official ribbon-cutting ceremony welcoming Pho Hoa to Greenacres at Riverbridge Plaza, 6716 Forest Hill Boulevard.

Pho Hoa brings an internationally recognized Vietnamese dining concept to the City's

growing and culturally diverse restaurant community. The restaurant specializes in authentic Vietnamese pho prepared with fresh ingredients and traditional recipes. The name *"Hòa,"* meaning "harmony," reflects the restaurant's philosophy of balancing tradition and innovation, flavor and nutrition, and Vietnamese culture.

The opening of Pho Hoa represents another positive addition to Greenacres' commercial landscape and further expands the dining experiences available to residents and visitors.

The City congratulates the Pho Hoa team on its investment in Greenacres and welcomes the restaurant to our growing business community.

Florida State University Jim Moran Institute Small Business Bootcamp
The Department continued promoting a new entrepreneurial development opportunity in partnership with the Jim Moran Institute for Global Entrepreneurship at Florida State University.

Applications were promoted for the West Palm Entrepreneurship and Adversity Program (WPEAP), an intensive six-week Community Bootcamp scheduled to begin August 15, 2026.

The program is designed to assist aspiring entrepreneurs and existing small business owners seeking to launch, stabilize, or grow their businesses. Participants will receive practical instruction and resources related to:

- Entrepreneurship;
- Marketing;
- Financial management;
- Business operations;
- Strategic planning;
- Mentoring and consulting; and
- Community business resources.

Connecting Greenacres entrepreneurs with high-quality educational and technical resources strengthens the City's entrepreneurial pipeline and supports the long-term sustainability of locally owned businesses.

Prospera – Digital Presence to Increase Sales Seminar
During July, the Department partnered with Prospera to host a business development seminar focused on "Digital Presence to Increase Sales."

The seminar provided entrepreneurs and small business owners with practical guidance on marketing strategies, digital tools, artificial intelligence, customer engagement, and techniques for increasing their online visibility.

Participants were also able to ask questions, exchange ideas, network with fellow

entrepreneurs, and establish connections with business-development professionals.

The strong participation demonstrated the entrepreneurial energy that continues to grow within Greenacres. Through partnerships such as Prospera, the City continues providing accessible and responsive resources designed to help businesses start, grow, and succeed.

SCORE Business Mentoring
The Department continued its partnership with SCORE, providing confidential one-on-one business mentoring sessions at City Hall on the third Thursday of each month. SCORE's volunteer business professionals provide entrepreneurs and existing business owners with expertise related to startup planning, business strategy, expansion, financial management, and operational challenges.

Together, the City's partnerships with SCORE, Prospera, and the Jim Moran Institute provide entrepreneurs with a continuum of assistance, from developing an initial business concept to strengthening and expanding an established enterprise.

4. BUSINESS RETENTION, EXPANSION, AND COLLABORATION
Open for Business: City Leaders Roundtable
On July 30, 2026, the City partnered with the Black Chamber of Commerce of Palm Beach County to host Open for Business: City Leaders Roundtable at the Greenacres Community Center.

The event brought together municipal leaders, procurement professionals, business owners, entrepreneurs, and community partners to strengthen connections between local government and the business community.

The roundtable provided businesses with valuable information regarding:

- Municipal procurement and contracting;
- Vendor registration;
- Certification opportunities;
- Public-sector purchasing processes;
- Upcoming projects and contracting opportunities;
- Business development resources; and
- Direct connections with municipal representatives.

The partnership created an important forum for moving beyond traditional networking toward meaningful connections, access to information, and expanded economic opportunities.

The City values its continued collaboration with the Black Chamber of Commerce of Palm Beach County and remains committed to ensuring that small businesses and entrepreneurs have greater awareness of and access to opportunities within local government.

5. Workforce Development
NextUp Skilled Trades: Speed Networking & Career Connection
During July, the Department continued planning for the NextUp Skilled Trades: Speed Networking & Career Connection Event, scheduled for August 26, 2026, at the Greenacres Community Center.

The initiative is being developed in partnership with PBC Design & Trades Networking Mixer and the National Kitchen & Bath Association's Treasure Coast Chapter to connect students, job seekers, and adults considering career changes with professionals from the construction, skilled trades, architecture, engineering, and design industries.

The event is designed to expose participants to career pathways that offer opportunities for long-term professional and economic advancement.

Programming will include:

- An industry-focused presentation;
- Interactive question-and-answer opportunities;
- Speed networking with industry professionals;
- Career pathway information;
- Workforce and educational resources; and
- Direct professional connections.

The initiative is particularly focused on high school, college, and trade school students, as well as adults interested in entering or transitioning into skilled-trade and design-related careers.

Meet industry professionals. Explore career pathways. Build your future.
This initiative reflects the Department's broader workforce development strategy of connecting residents with industries experiencing workforce demand while helping employers build stronger talent pipelines.

CONCLUSION
July 2026 demonstrated continued and measurable momentum for economic development in Greenacres. From advancing hotel and redevelopment opportunities along Lake Worth Road to successfully hosting an international consular initiative, expanding entrepreneurial assistance, strengthening business partnerships, and developing new workforce pathways, the Department continues moving strategic initiatives from relationships to opportunities and from opportunities to results.

These accomplishments demonstrate the value of collaboration among local government, businesses, educational institutions, nonprofit organizations, regional partners, and international stakeholders.

As Greenacres celebrates its Centennial Year, the Economic Development Department

remains focused on building upon this momentum by attracting quality investment, supporting existing businesses, developing the City's future workforce, and creating opportunities that strengthen economic prosperity and quality of life.

Analysis

Financial Information

Legal

Staff Recommendation

Attachments:

None

Department Report

Meeting Date: August 17, 2026

From:

Subject: Fire Rescue.

Background

Analysis

Financial Information

Legal

Staff Recommendation

Attachments:

1. Fire Rescue Report July

Department Report

MEETING DATE: August 07, 2026

FROM: Phillip Konz, Fire Chief


SUBJECT: Fire Rescue July

FR CALLS

CALLS	MONTHLY TOTALS
Total Alarms dispatched in July	549
Average alarms per day	19.61
Total calls this fiscal year	6,252


In July 2026, 385 patients were treated for Emergency Medical related services. Of those patients, 46 were in the City of Atlantis. These requests vary from a single unit responding to help an individual who has fallen to the floor, to a cardiac arrest necessitating multiple units, along with a mix of personnel, advanced skills and equipment.

Service Calls, Cancels, and Public Assists totaled 47. The requests include, but are not limited to, people locked out of home, water evacuation, animal problems, police assist, defective elevator, and canceled due to wrong address.

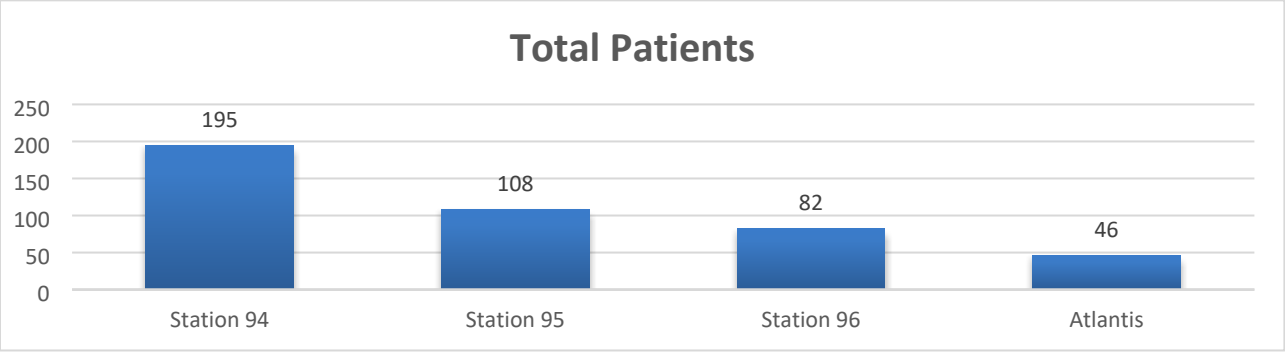


ALS/BLS

Fire Rescue transported 313 patients to a hospital or 80% of the patients we were called to treat. The majority of those (204) required Advanced Life Support procedures. ALS emergencies require additional personnel, specialized equipment, and skills. Often, an EMT or Paramedic will be taken from the ALS Engine to accompany the one person in the rear of the Rescue to assist with life-saving therapies.

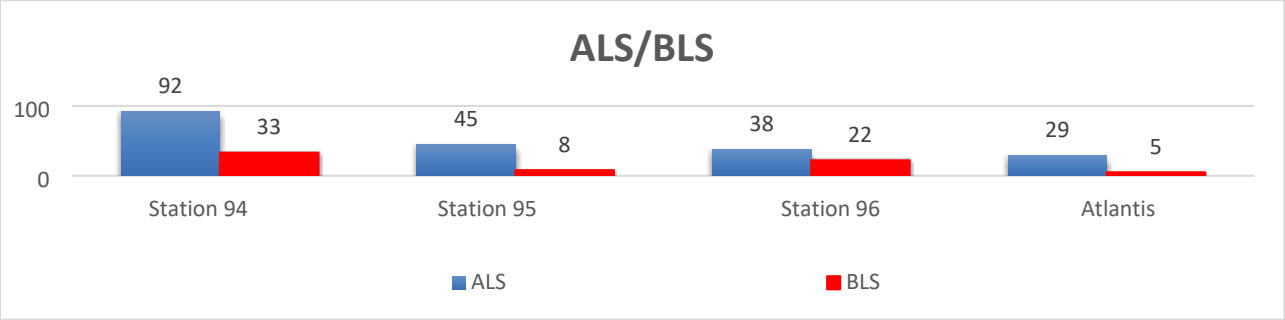


FIRE RESPONSES

Fire Rescue responded to 52 calls for a fire or smoke-related emergency. There were three (3) calls requiring an escalated response to a car, brush, or refuse fire; six (6) were in a residential or commercial structure.

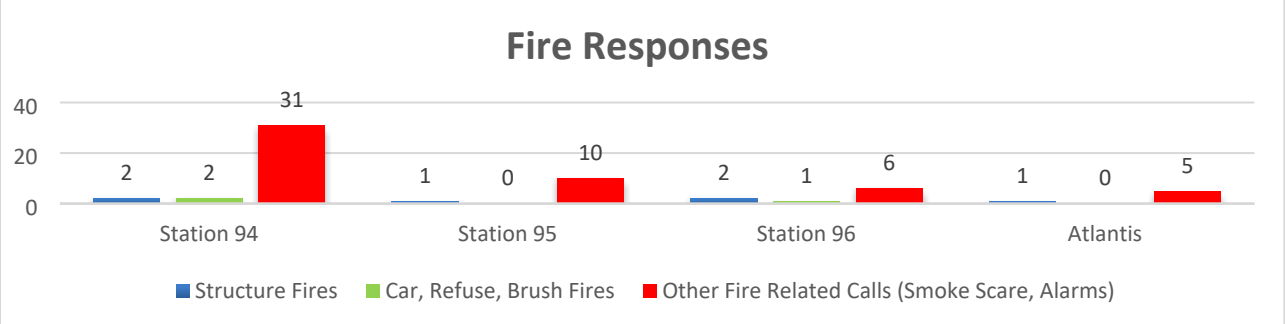

MUTUAL AID




Mutual aid is the sending or receiving of emergency resources (apparatus, personnel) to or from another entity or agency upon request. No community has sufficient resources to handle every emergency of all sizes. Therefore, neighboring agencies work together through a system called Mutual Aid. That system is designed to be limited to large events that tax the resources beyond the normal capabilities of the community.

FIRE MARSHAL

Fire Prevention and Protection focuses on protecting people and property from fire through fire safety inspections, fire plans review, fire cause and origin investigations, and public education. In addition, the Fire Marshal provides fire safety lectures, attends land development meetings, and testifies at code enforcement hearings.

Inspections	201
Plans Review	29
People Displaced due to Fire Incidents	0

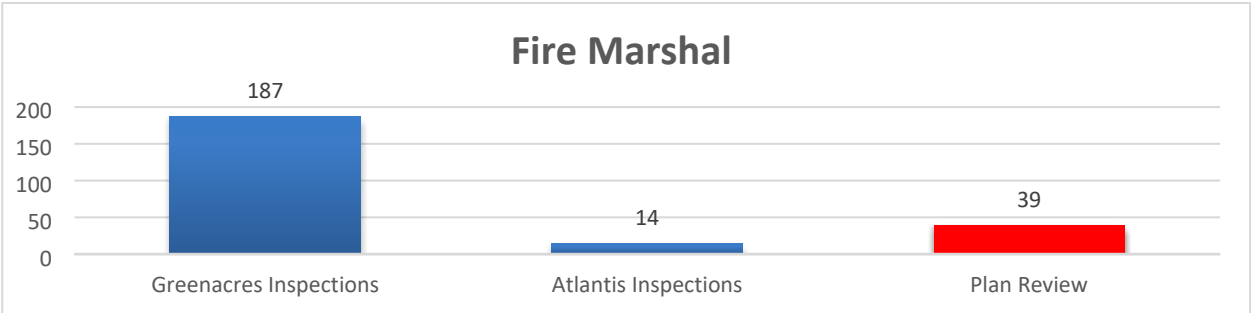

SPECIAL SERVICES

Blood Pressure Screenings	2
Presentations, Station Tours/Attendees	2/10
People Trained in CPR	0

Department Report

Meeting Date: August 17, 2026

From:

Subject: Finance.

Background

Analysis

Financial Information

Legal

Staff Recommendation

Attachments:

1. 11 Finance Dept Report - July 2026

Department Report

MEETING DATE: August 17, 2026

FROM: Teri Lea Beiriger, Director of Finance

SUBJECT: Department of Finance Activity Report

DEPARTMENT HIGHLIGHTS

The following report provides activity within the Department of Finance for the reporting period from July 1 through July 31, 2026:

- Continued to work on efficiencies to better serve our internal and external customers.

- General Operations
  - Continued Fixed Assets process improvements, working with the summer intern to revise inventory spreadsheets and forms.
  - Continued to collaborate with IT staff, credit merchant providers, and software teams to implement credit card pass through fees changes for CRS department.
  - Begin the PEMT Cost Reporting process.
  - Continued the budget process at the department level.
  - Set millage and budget hearing dates; submit to the Department of Revenue (DR420, DR420MMP) for eTRIM compliance.

- Grants
  - Submitted applications for the following grants:
    - FL DEP Septic to Sewer 2027 LWLI (State).
  - Submitted quarterly grant reports for:
    - American Rescue Plan
    - FEMA SAFER 2024
    - Firefighters Supplemental 2026
    - FL DEP 2023 - 2024 Orig. Section South Phase I
    - FL DEP 2025 - 2026 Orig. Section South Phase III
    - FL DOE 2023 Youth Program Capital Outlay (State) Approp.
    - HMGP Gladiator Lake 2018
    - Opioid settlement 2022

Department Report

Meeting Date: August 17, 2026

From:

Subject: Information Technology.

Background

Analysis

Financial Information

Legal

Staff Recommendation

Attachments:

1. 2026_07 IT Dept July Report

Department Report

MEETING DATE: August 17, 2026

FROM: Georges Bayard, Director, Information Technology

SUBJECT: Department of Information Technology – July 2026 Activity Report

DEPARTMENT HIGHLIGHTS

The following report provides the highlights of activity within the Information Technology Department for the reporting period from July 1, 2026 – July 31, 2026.

1. Final configuration of the City's public website on the new CivicPlus platform has been completed. Due to a delay in implementation of an important feature, Go-Live has been pushed back to August 13, 2026.
2. Implementation of the new CivicPlus Recreation Management application is nearing completion. User training has been under way and integration with the new payment processor Forte has been completed and is now in testing. Go-Live is expected to take place in August.
3. Work continues in consultation with Info-Tech on development of an Information Security Program, to encompass a cybersecurity incident response plan, AI policy, Backup & Disaster Recovery Plan, and more.
4. Staff installed overhead speakers and coordinated installation of six new Comcast cable boxes for the new bunk rooms at Fire Rescue Station 95.
5. Installation of mobile printers in Code Compliance vehicles and user training has been completed.
6. The IT Application Specialist is continuing production of training video clips for staff to highlight useful features of the City's enterprise applications.
7. The team welcomed our new IT Support Specialist, Isaiah Reid.
8. The Director and staff attended the Florida Local Government Information Systems Association (FLGISA) annual conference.
9. Monthly KnowBe4 simulated phishing email test results:

   Links clicked: 6; attachments opened: 3; QR codes scanned: 0. Phish-prone users (vulnerable to email phishing attacks): 4.66%, no change from 4.66% in the previous month.

SERVICE DESK REQUESTS

July 2026

DEPARTMENT	CURRENT PERIOD	FY 2026 YTD	FY 2026 BUDGET
Administration	15	108	-
Community & Recreation Services	4	52	-
Development & Neighborhood Svcs.	11	163	-
Finance	6	54	-
Fire Rescue	14	98	-
Information Technology	3	26	-
Public Works	3	27	-
Purchasing	0	8	-
Youth Programs	17	47	-
Total Service Desk Requests	**73**	**583**	**750**

IT Department Monthly Activity Report - July, 2026

Number of Total Tickets


73

Tickets


Count of Number




Tickets by Employee

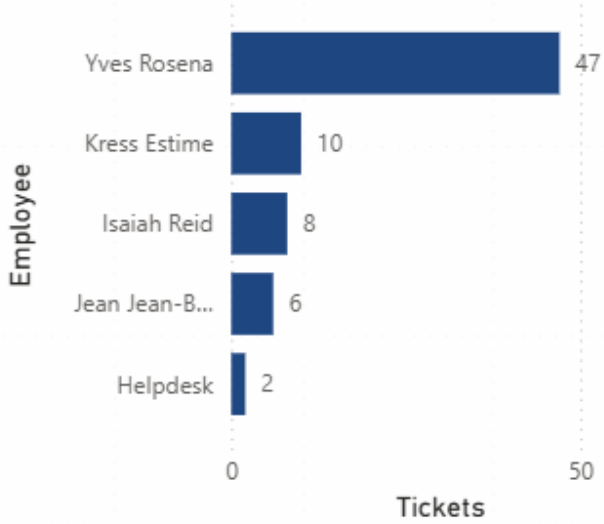


Tickets by Day

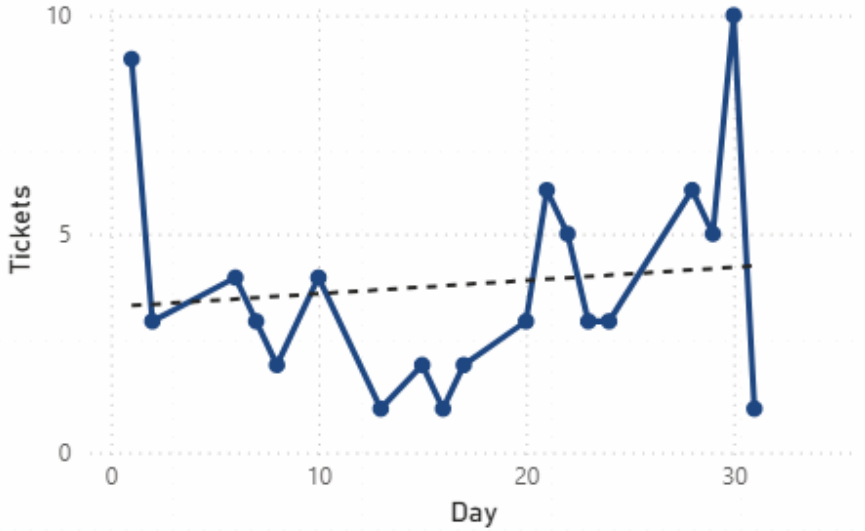


Tickets by State

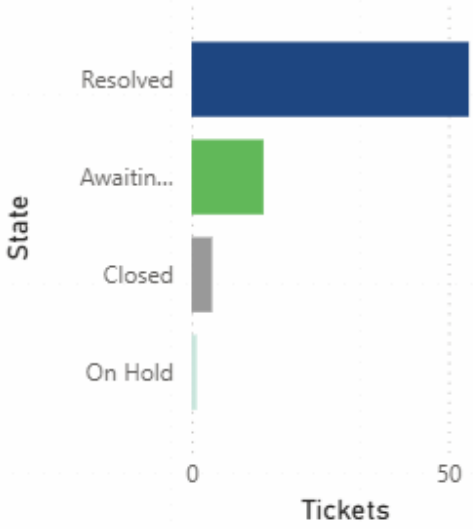

Tickets by Category

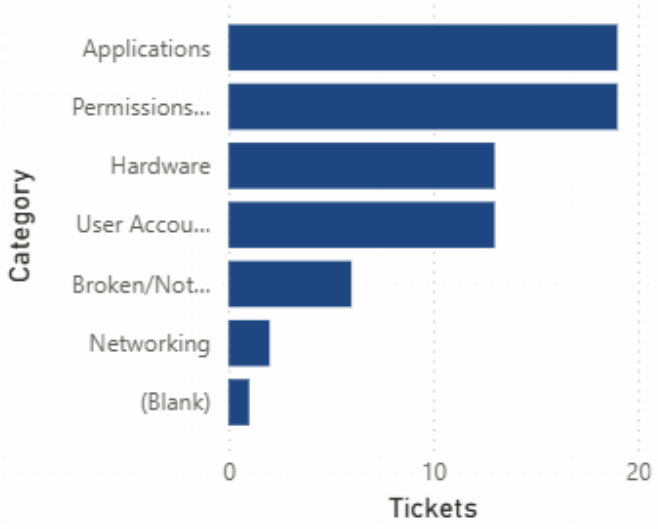

Tickets by Employee

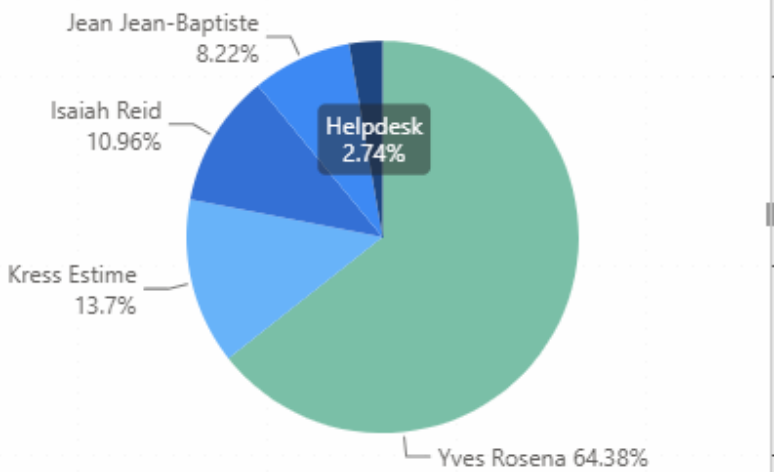

Department Report

Meeting Date: August 17, 2026

From:

Subject: Palm Beach Sheriff's Office, District 16.

Background

Analysis

Financial Information

Legal

Staff Recommendation

Attachments:

1. D16 Monthly Report - July 2026 (2)

Department Report

MEETING DATE:

FROM: Captain Craig Turner, PBSO District 16

SUBJECT: PBSO District 16 – July 2026 Report

CAD CALLS

CAD CALLS	MONTHLY TOTALS
Business / Residence Checks (Self-Initiated)	1,628
Traffic Stops (Self-Initiated)	796
Calls for Service (Excluding 1050's & 1061's)	1,563
All CAD Calls - Total	**3,987**
Total Calls for Service – FY 2026 (October 2025 – September 2026)	39,998

Data Source: CADS/Premier 1
*Omit Miscellaneous Calls

Note: P1 is a dynamic system. Meaning that #'s can change from what was previously reported in the event there is a location or call type re-classification/modification.

SUMMARY

During the month, there were 3,987 generated calls within the district and 61% of these calls were self-initiated.

TRAFFIC ACTIVITY

DISTRICT 16 PERSONNEL	
Total Citations	**Total Warnings**
370	392

Data Source: D16 Office Staff/Monthly Report

PBSO MOTORS UNIT	
Total Citations	**Total Warnings**
345	185

Data Source: D16 Office Staff

COMMUNITY POLICING EVENTS

- Summer Camp
- Ignite the Night

STREET CRIMES UNIT

- **C/N 26-075226** – District 16 Street Crime Unit conducted a traffic stop on a gray Nissan. The passenger was found to have an active warrant from the Palm Beach County Sheriff's Office. The suspect was taken into custody without incident and charged accordingly.
- **C/N 26-074581 / C/N 26-074543 -** District 16 Street Crime received probable cause to arrest a suspect for two vehicle burglaries in the city of Greenacres. Surveillance was conducted at multiple locations and the suspect was ultimately located. The suspect was interviewed and charged accordingly.
- **C/N 26-078559 -** District 16 Street Crime Unit assisted road patrol with locating a suspect in reference to a 31D. Surveillance was conducted and suspect was located leaving a car dealership in District 1. The suspect was apprehended and charged accordingly.
- **C/N 26-063666** – District 16 Street Crime Unit received probable cause to arrest a suspect for burglary of an occupied dwelling and petit theft. District 16 Street Crime Unit conducted surveillance and located suspect. The suspect was taken into custody and charged accordingly.


PROPERTY DETECTIVES


- **C/N 26-074543** - On July 4, 2026, the victim who reported that an unknown male attempted to enter her vehicle by pulling on the driver's door. The vehicle was locked, and the suspect walked off her property. On July 8, 2026, a latent report revealed the latent recovered belonged to the suspect. The victim confirmed she does not know who the suspect is. PC was established, and District 16 Street Crime Unit was assigned to assist, and the suspect was later located. A post-Miranda confession was obtained of the suspect's involvement.
- **C/N 26-074581** - On July 4, 2026, the victim reported that an unknown male entered her unlocked vehicle and stole her wallet, which contained her Navy Federal credit and debit cards. Multiple fraudulent charges were made and denied. The suspect depicted in the video surveillance is the same suspect in the above case. Street Crime Unit was assigned to assist, and the suspect was later located. A post-Miranda confession was obtained of the suspect's involvement.
- **C/N 26-063666 –** On May 25, 2026, a residential burglary occurred in the City of Greenacres and a pressure washer was stolen. Detectives obtained several residential search warrants and PC This case is cleared by arrest.
- **C/N 26-069324 –** During the overnight hours of June 12th, 2026 burglaries occurred to the lawn maintenance trailers parked at Pro Green Services. Approximately $12,000 in lawn equipment was stolen during the burglaries.


Detectives identified the suspect vehicle and partnered with SFCAT to obtain a Broward County tracking warrant. On June 26th, 2026, the suspects committed an additional burglary in District 1 area. Detectives responded and interviewed the suspects who were uncooperative. The suspect's phones were gathered for evidence and their vehicles were sealed and towed to Sisters lot. Additional warrants forthcoming. Two phone dump warrants were obtained, relay request submitted, and phones taken to digital forensics. Two cell site warrants obtained and placed the suspects on scene.

DATA ANALYSIS

The data included in this report is charted and graphed to illustrate and compare changes over a specific time period. These charts and graphs are utilized to assist in determining crime trends and to measure enforcement efforts. This data is utilized in conjunction with other analysis to develop directed patrol and various enforcement activities. The analysis included on these pages is presented as a brief highlight to explain the salient points of this report.

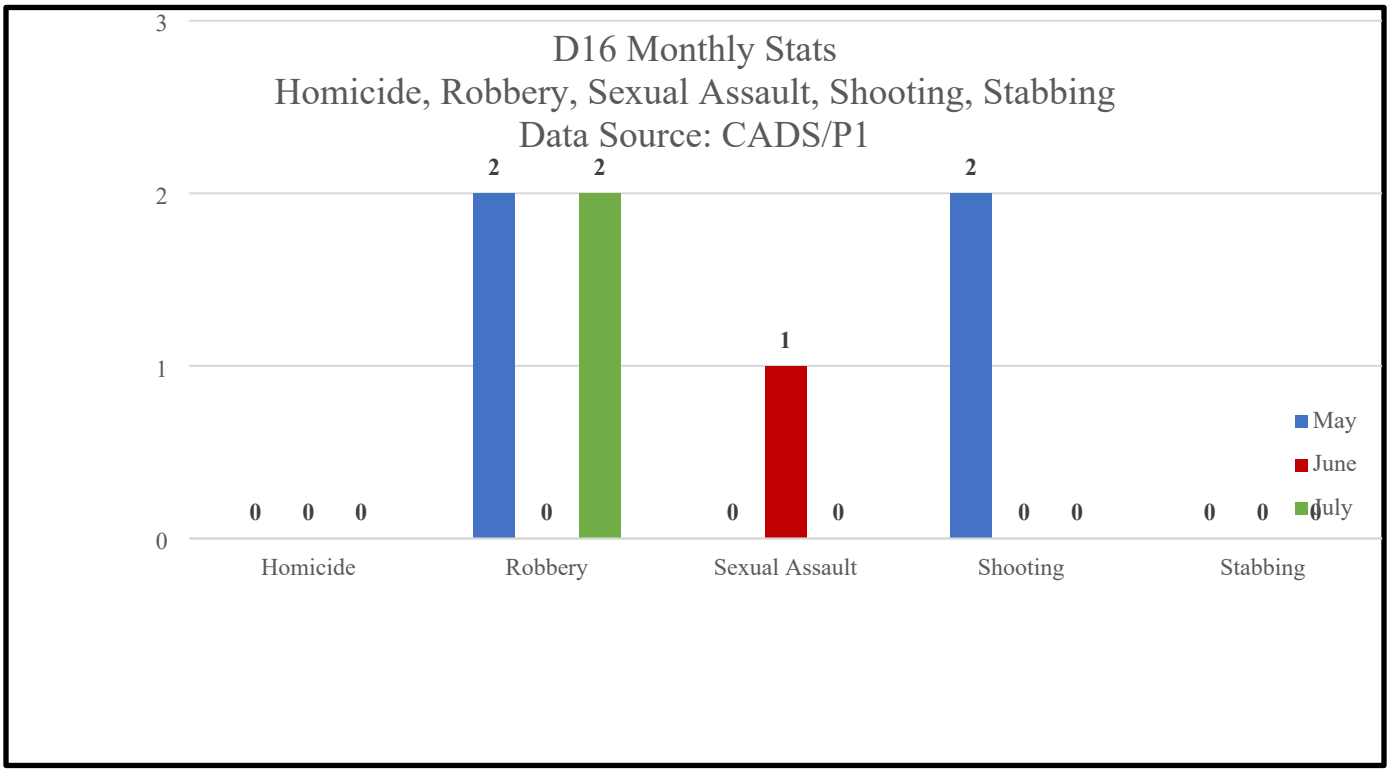


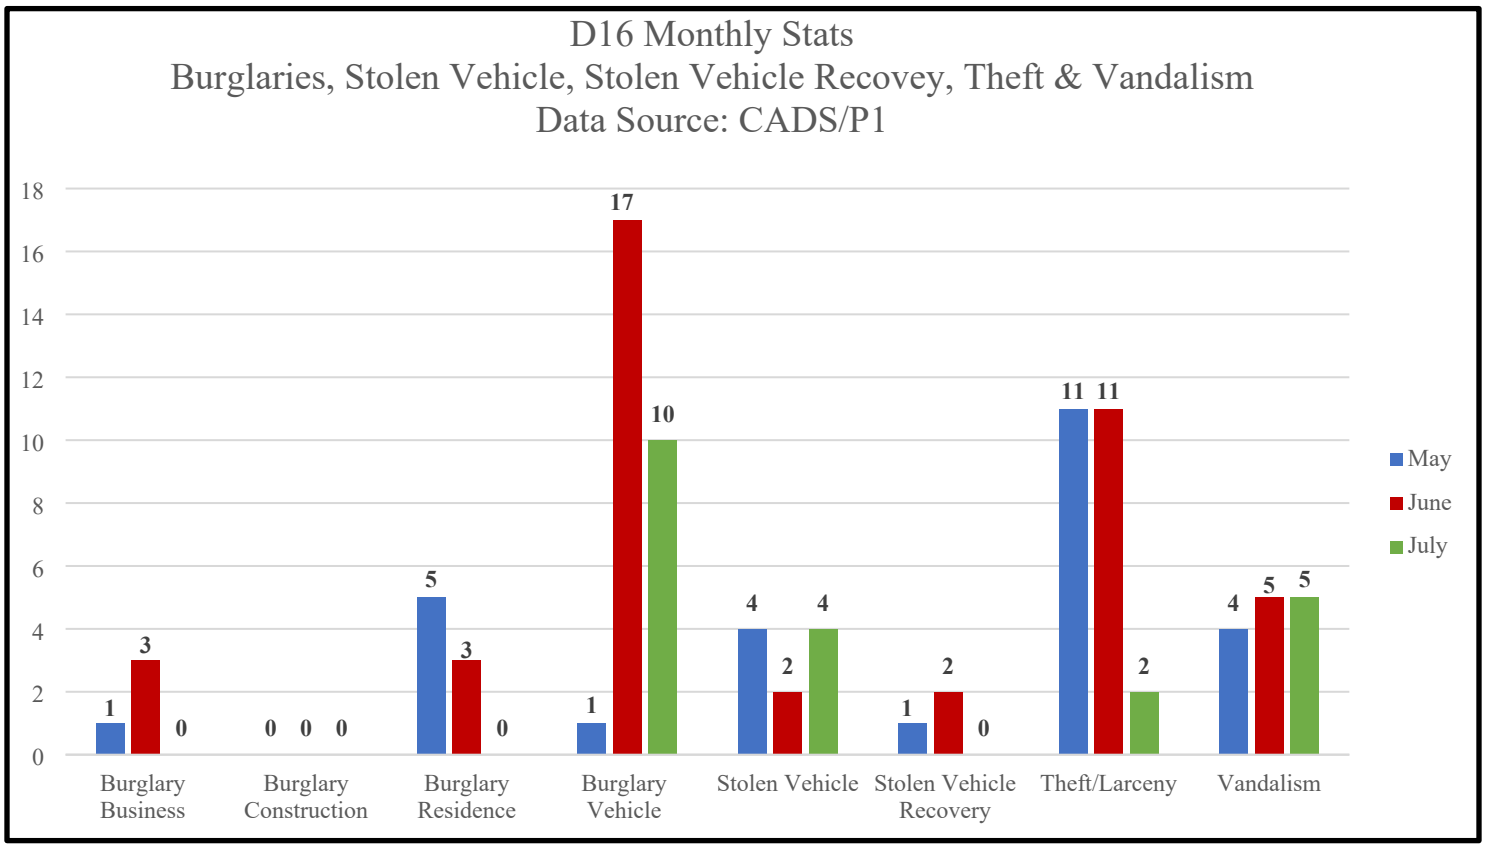

D16 Monthly Stats
Burglaries, Stolen Vehicle, Stolen Vehicle Recovey, Theft & Vandalism
Data Source: CADS/P1
18
16
14
12
10
8
6
4
2
0
1
3
0
0
0
0
5
3
0
1
17
10
4
2
4
1
2
0
11
11
2
4
5
5
Burglary Business
Burglary Construction
Burglary Residence
Burglary Vehicle
Stolen Vehicle
Stolen Vehicle Recovery
Theft/Larceny
Vandalism
May
June
July

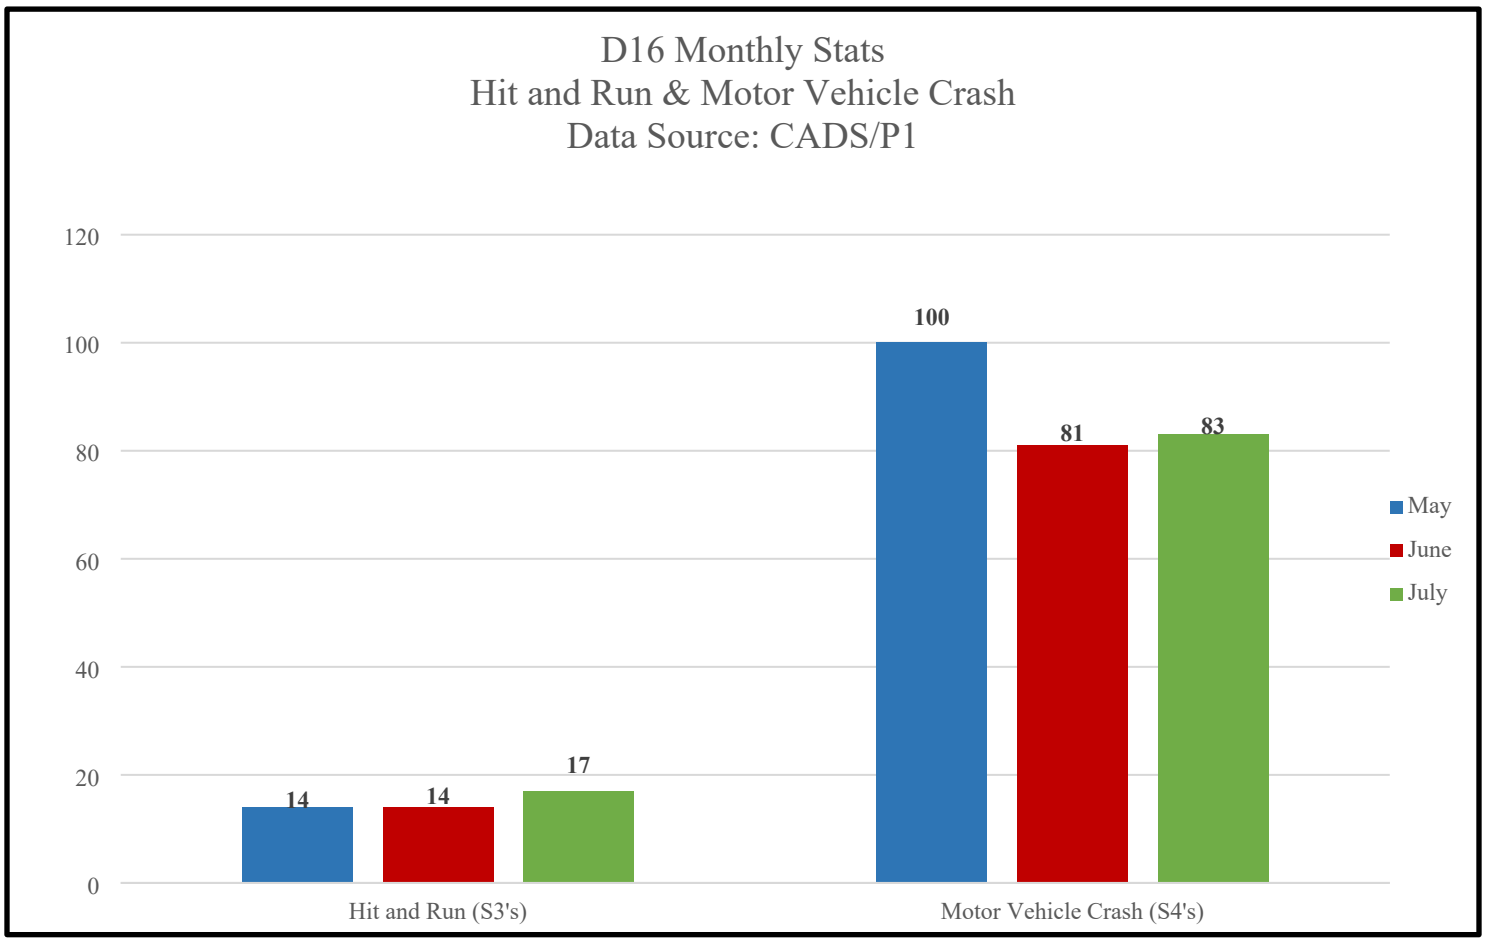
D16 Monthly Stats
Hit and Run & Motor Vehicle Crash
Data Source: CADS/P1
120
100
80
60
40
20
0
14
14
17
100
81
83
Hit and Run (S3's)
Motor Vehicle Crash (S4's)
May
June
July

TOP ACCIDENT LOCATIONS FOR JULY 2026 - CASE NUBER INCIDENTS (S3's, 4's & 5V)

Pin Map of Locations

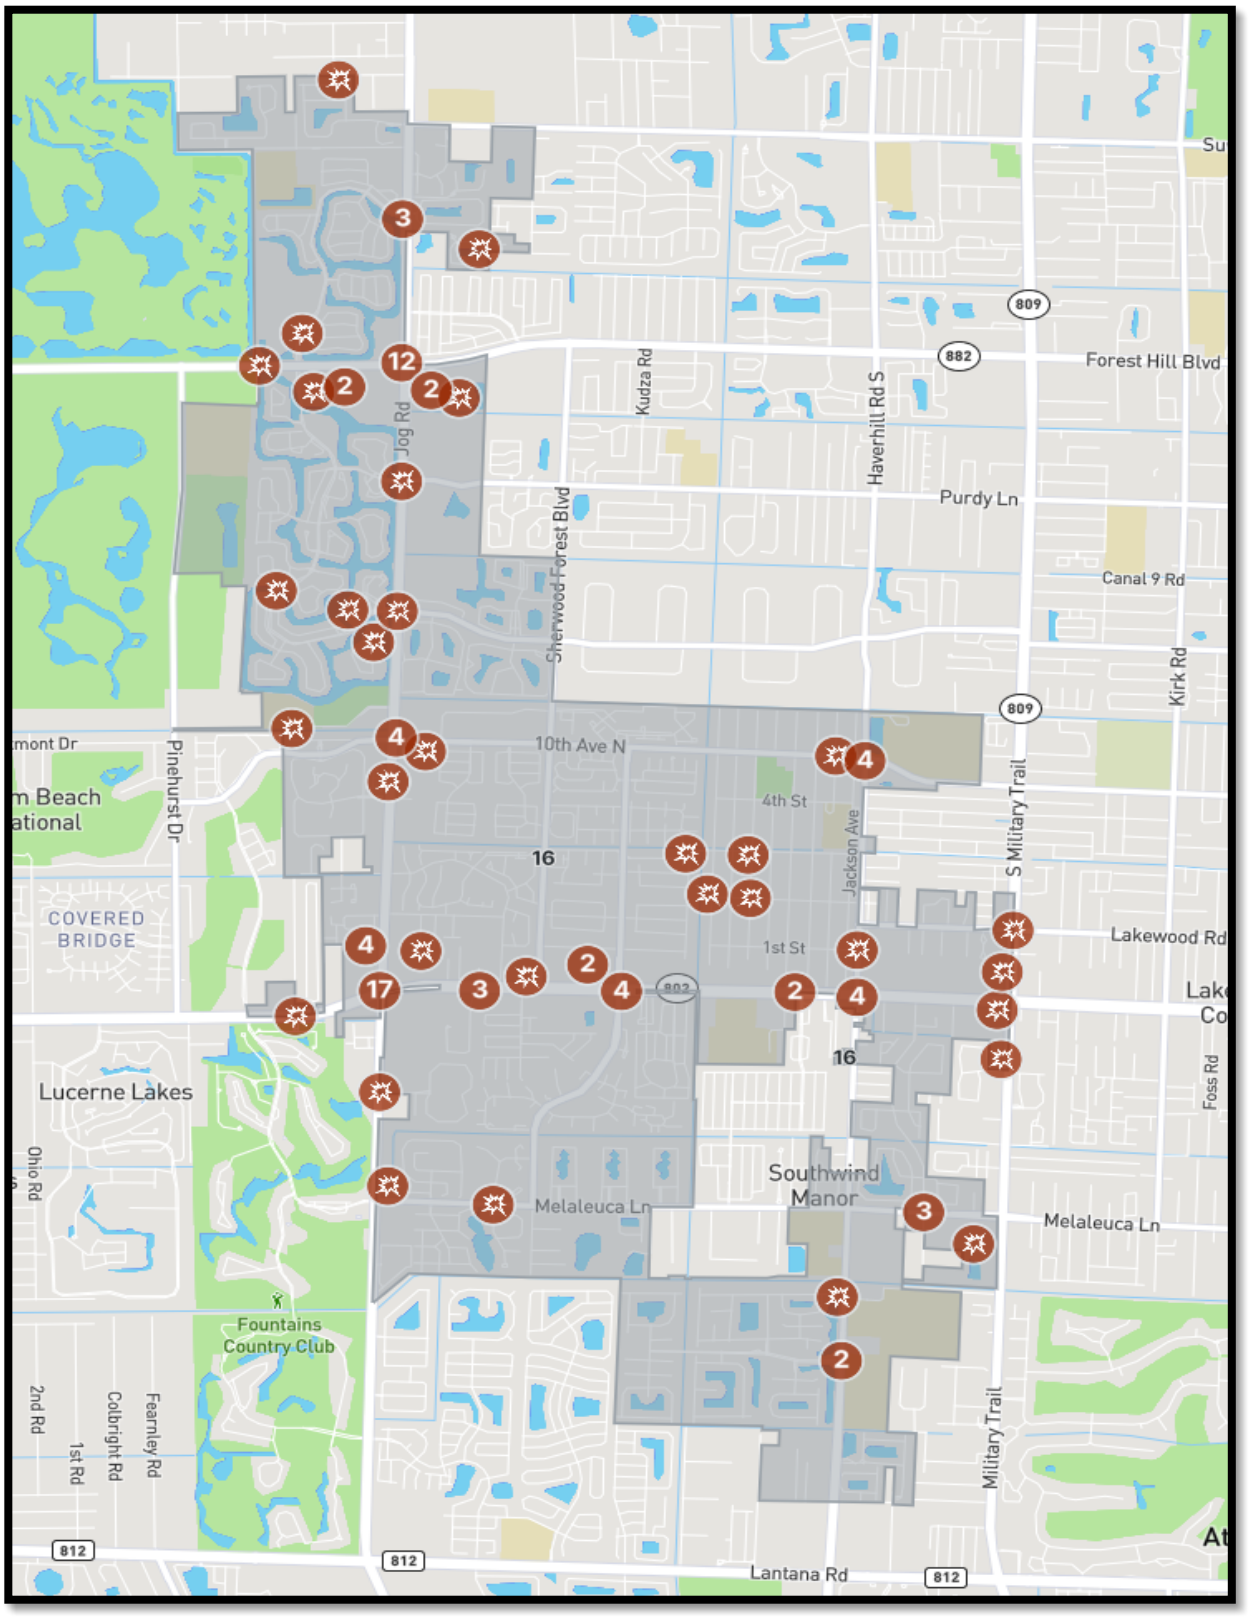

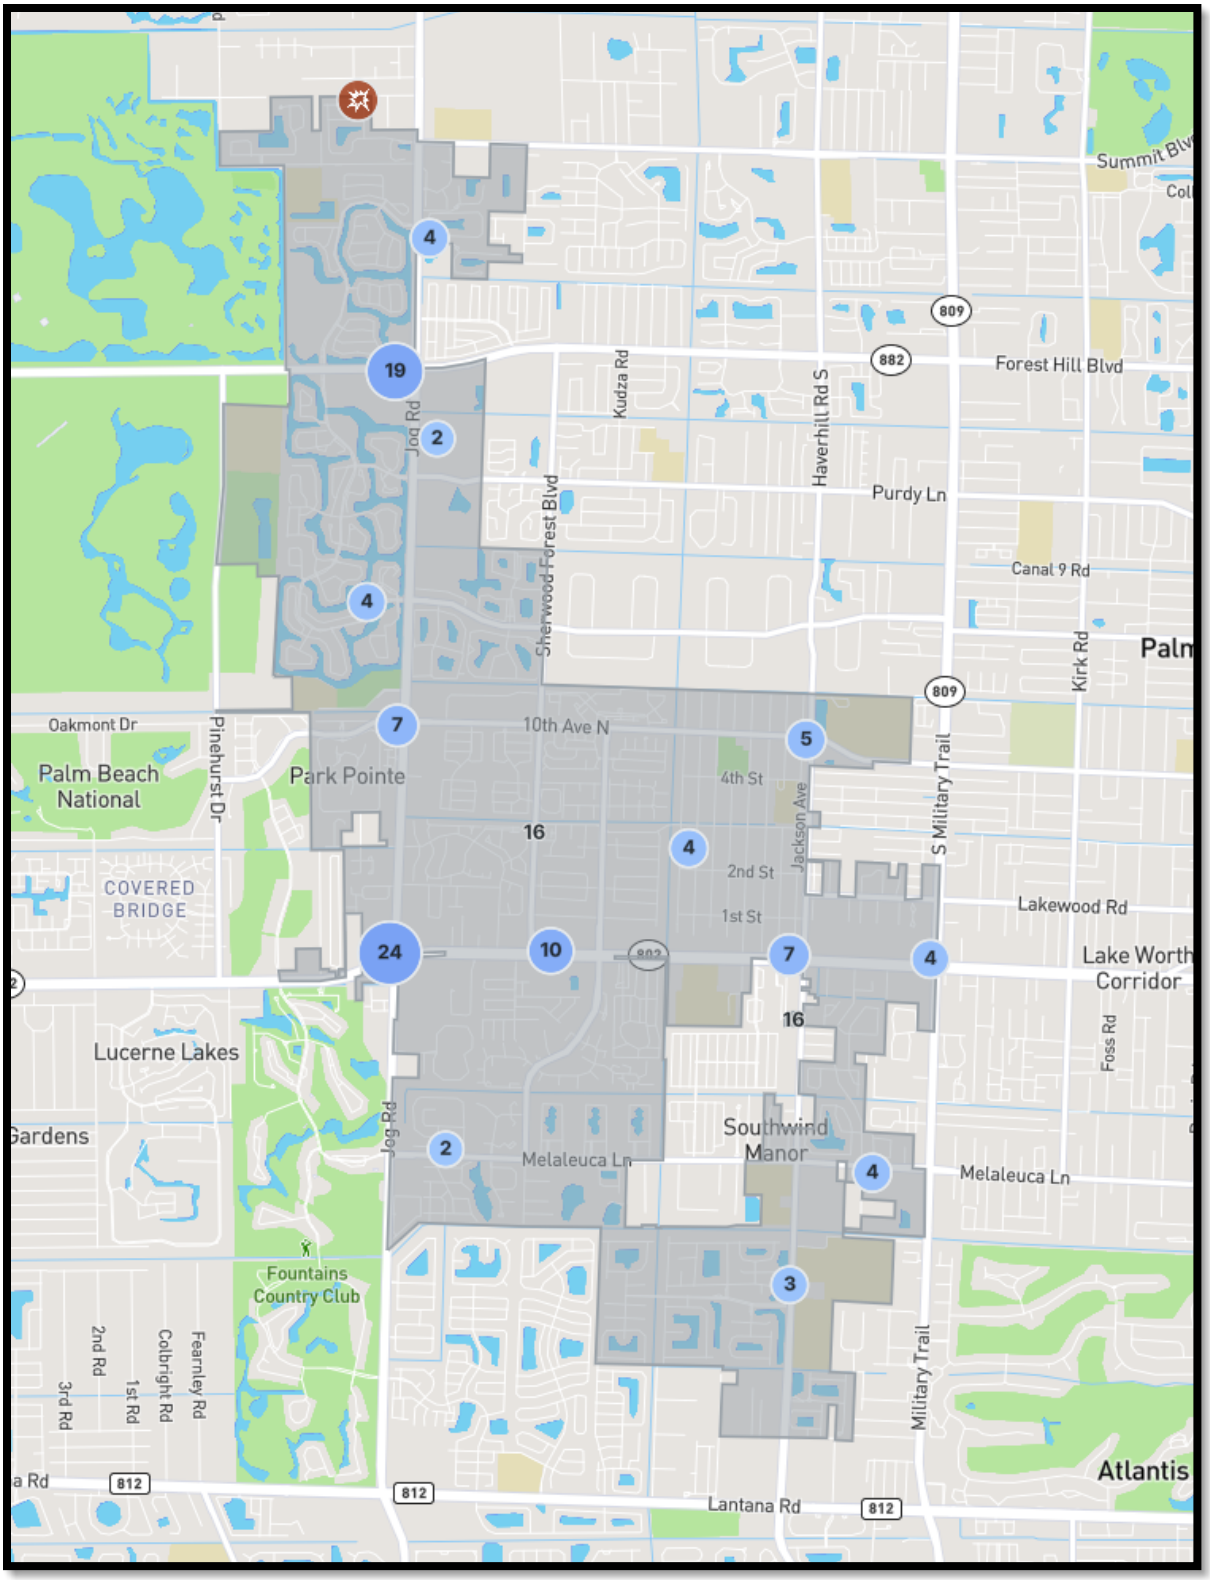
Summit Blvd
Forest Hill Blvd
809
882
Kudza Rd
Haverhill Rd S
Purdy Ln
Canal 9 Rd
Sherwood Forest Blvd
Jog Rd
Kirk Rd
Palm
Oakmont Dr
Pinehurst Dr
Palm Beach National
Park Pointe
10th Ave N
4th St
2nd St
1st St
Jackson Ave
S Military Trail
Lakewood Rd
COVERED BRIDGE
Lake Worth Corridor
Foss Rd
Lucerne Lakes
Gardens
Southwind Manor
Melaleuca Ln
Fountains Country Club
2nd Rd
3rd Rd
1st Rd
Colbright Rd
Fearnley Rd
Military Trail
Atlantis
812
Lantana Rd
19
4
2
7
5
16
24
10
3

Department Report

Meeting Date: August 17, 2026

From:

Subject: Public Works.

Background

Analysis

Financial Information

Legal

Staff Recommendation

Attachments:

1. PW Report July2026-

Department Report

MEETING DATE: August 17, 2026

FROM: Carlos Cedeño, Public Works Director

SUBJECT: Public Works Department Report

DEPARTMENT HIGHLIGHTS

Listed below is a summary of the activities undertaken by the Public Works Department during the period of July 1, 2026 through July 31, 2026.

1. ADMINISTRATION:

- CIP updates:
  - 500 Perry Building Demolition and New Playground (CIP#305-032): Permits and site plan approval have been issued for the demolition.
  - Fire Rescue Staff Lounge (CIP# 304-191) Project is 85% complete.
  - Public Works Building Steel Columns Rehabilitation (CIP#304-020) is 30% complete.

2. ROADS AND DRAINAGE MAINTENANCE

- Staff conducted nighttime FPL streetlight inspections throughout the City and reported outages to FPL for repairs.
- Staff assisted with the set up and break-down of the Ignite the Nite event.
- Removed holiday banners from street poles and made necessary repairs.
- Staff performed sidewalk and root grinding in the Villa del Trio and within the Original Section (along Martin Avenue).

3. VEHICLE MAINTENANCE

- Monthly bus inspections were conducted.
- Staff performed preventative maintenance cycle of Fire Rescue vehicles.
- Two (2) Public Works replacement vehicles were received, upfitted and put into service.

4. BUILDING SERVICES

- Staff worked on punch list items to continue transition into new Youth Programs Facility.
- Preventative maintenance service cycle for the HVAC systems was conducted.
- Supervisor coordinated annual City-wide inspections of potable water and fire suppression back flows.
- Staff performed building generator inspections were performed.

5. PARKS MAINTENANCE

- Coordinated the installation of a total of eleven (11) solar lights throughout Arbor Park, Freedom Park and Dillman Trail.
- Staff assisted with the set up and break-down of the Ignite the Nite event.

Department Report

Meeting Date: August 17, 2026

From:

Subject: Purchasing.

Background

Analysis

Financial Information

Legal

Staff Recommendation

Attachments:

1. July

Department Report

MEETING DATE: August 17, 2026

FROM: Monica Powery, Director, Purchasing

SUBJECT: Department of Purchasing Activity Report

DEPARTMENT HIGHLIGHTS

The following report provides the highlights of activity within the Department of Purchasing for the reporting period from July 1 through July 31.

a. The Director and Buyer attended the NFBPA South Florida Inaugural Civic Excellence Symposium & Awards on July 24, 2026. This event provides education from expert-level panelists, celebrating community spirit, and recognizing outstanding civic contributions. Attendees gained powerful insights, connect with changemakers, and elevate your impact in public service.

b. Solicitations In Progress – Professional Sound System with Stage & Video Wall for City Events; Tents for City Events; Inflatables for City Events; and Miscellaneous Electrical Services for Building and Park Facilities.

DEPARTMENT ACTIVITY

ACTIVITY	CURRENT PERIOD	FY 2026 YTD
Purchase Orders Issued	47	694
Purchase Order Amounts	$853,087.16	$38,291,286.96
Solicitations Issued	-	8
Solicitations in Progress	4	-
Central Store Requests	3	36
Contracts Managed	78	78
Purchasing Card Purchases	282	3,246
Purchasing Card Transactions	$61,063.37	$522,126.89
No. of Training Sessions Conducted	-	4

Department Report

Meeting Date: August 17, 2026

From:

Subject: Youth Programs.

Background

Analysis

Financial Information

Legal

Staff Recommendation

Attachments:

1. July 2026 Report

Youth Programs Department Monthly Report

MEETING DATE: August 17, 2026

FROM: Jowie Mohammed, Director of Youth Programs

SUBJECT: July 2026 Department Report

PROGRAMMING

- Our Summer Camp program launched on June 4th, operating Monday through Friday from 7:30 a.m. to 5:30 p.m. Camp includes full meal service, providing campers with breakfast, a hot lunch, and snacks.
- July field trips include Museum of Discovery, Calypso Bay, Bowling, Build-A-Bear, Butterfly World, Bedner's Farm, Astro Skate, Cici's, Chuck E. Cheese, and much more.
- Photos of July camp can be found on YouTube.

PERFORMANCE MEASURMENTS

PERFORMANCE MEASUREMENT	AVERAGE THIS PERIOD	FY 2026 TO DATE
Summer Camp # of Participants	132	132
# of Participants in Sierra Club ICO	0	48
# of Part's in TOP Program	0	20
# of Licenses Coordinated	1	1
# of MOU's Coordinated	2	2
# of Part.'s in Teen Advisory Council (TAC)	0	8
# of Com. Serv. Learning Projects coordinated	1	2
# of After-hour events coordinated	0	2
# of Presidential Volunteer Service Hours	0	8120

FINANCIAL INFORMATION

GRANTS COORDINATED	AVERAGE THIS PERIOD	FY 2026 TO DATE
Early Learning Coalition	$23,942.03	$142,869.31
Parent & Registration Fees	$6,135.00	$162,468.84
Youth Services Department SEL Grant	$0.00	$22,394.40
Textile Funds	$0.00	$1,750.00
Community Foundation Grant	$0.00	$25,000.00
SCSP	$7,800.00	$9,750
